START

009574

DOE/RL-90-20
Draft A

Remedial Investigation/ Feasibility Study Work Plan for the 100-KR-1 Operable Unit, Hanford Site, Richland, Washington

Date Published
May 1990

JUN 1990
RECEIVED
EDMC

United States
Department of Energy
P.O. Box 550
Richland, Washington 99352

Approved for Public Release

Reference herein to any trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof.

ACRONYMS

ACL	Alternate concentration limits
ADI	Acceptable daily intake
ALARA	As low as reasonably achievable
ARAR	Applicable or relevant and appropriate requirement
AS	Nonmetallic ion analysis
ATSM	American Society of Mechanical Engineers
ATSDR	Agency for Toxic Substances and Disease Registry
BTDS	BWIP technical data system
BWIP	Basalt waste isolation project
CAA	Clean Air Act
CCS	Commitment control system
CDR	Conceptual design report
CEQ	Council on Environmental Quality
CERCLA	Comprehensive Environmental Response, Compensation and Liability Act of 1980, as amended
CFR	Code of federal regulations
CLP	Contract liability program
CMD	Corrective measures design
CMI	Corrective measures implementation
CMS	Corrective measures study
CPP	CERCLA past practice
CRDL	Contract-required detection of limits
CRP	Community relations plan
CZMA	Coastal Zone Management Act
D&D	Deactivation and decontamination
DAC	Derived air concentration
DCG	Derived concentration guides
DHHS	Department of Health and Human Services
DMP	Data management plan
DOE	U.S. Department of Energy
DOE-RL	U.S. Department of Energy-Richland Operations Office
DOI	U.S. Department of Interior
DQO	Data quality objective
DST	Double shell tank
DW	Dangerous waste
EE&T	Environmental engineering and technology
EA	Environmental assessment

Ecology	Washington State Department of Ecology
ECTS	Environmental compliance tracking system
EDMS	Environmental Data Management Center
EEI	Environmental investigations and instructions
EIS	Environmental impact statement
EMI/MAG	Electromagnetic induction/magnetometer
EMSL	Environmental Monitoring Support Laboratory
EPA	U.S. Environmental Protection Agency
ERDA	Energy Research and Development Administration
ERT	Environmental response team
ESA	Endangered Species Act
FS	Feasibility study
FSP	Feasibility sampling plan
FTS	Financial tracking plan
GC	Gas chromatography
GEU	Geotechnical engineering unit
GM	Gamma monitor (probe)
GPR	Ground penetrating radar
HCN	Hydrogen cyanide
HECR	Hanford environmental compliance report
HEHF	Hanford Environmental Health Foundation
HEIS	Hanford environmental information system
HGWDB	Hanford ground water data base
HISS	Hanford inactive site survey
HMS	Hanford Meteorological Station
HP	WHC Health Physics Department
HPT	Health physics technologists
HRS	Hazard ranking system
HSO	Health and safety officer
HSP	Health and safety plan
HSWA	Hazardous and Solid Waste Amendments (of 1984)
HSWMUR	Hanford site waste management units report
HWMA	Hazardous Waste Management Act
HMPD	Hanford multi-purpose dosimeters
HWVP	Hanford waste vitrification plant
IC	Ion chromotography
ICRP	International Council of Radiation Protection
IM	Interim measure
IRA	Interim response actions
IRIS	Integrated risk information system

IRM	Information resources management
IS&FP	Industrial safety and fire protection
ISV	In-situ vitrification
ITS	In-tank solidification
LAER	Lowest achievable emission rate
LAP	Laboratory analytical protocol
LLWPA	Low-Level Waste Policy Act of 1980
LLWPAA	Low-Level Waste Policy Amendment Act of 1985
MS	Metals and radiation analysis
MCL	Maximum contaminant level
MCLG	Maximum contaminant level goal
MCS	Management control system
MDL	Minimal detection limit
MHRS	Modified hazard ranking system
Mou	Memorandum of understanding
MSDS	Material safety data sheet
msl	Mean sea level
NARM	Naturally occurring radioactive materials
NCP	National oil and hazardous substances contingency plan
NCRP	National council of radiation protection
NEPA	National Environmental Policy Act
NESHAPS	National emission standards for hazardous air pollutants
NIOSH	National Institute for Occupational Safety and Health
NOAA	National Oceanic and Atmospheric Administration
NOD	Notice of deficiency
NPDES	National pollution discharge elimination system
NPL	National priorities list
NQA	Nuclear quality assurance
NR	Not reported
NRC	National Regulatory Commission
O&M	Operation and maintenance
ORE	Occupational radiation exposure
OSHA	Occupational Safety and Health Act of 1970
OSM	(Westinghouse Hanford) Office of sample management
OSWER	Office of solid waste and emergency response
OVA	Organic vapor analyzer
PA/SI	Preliminary assessment/site inspection
PARCC	Precision, accuracy, representativeness, completeness and comparability
PCB	Polychlorinated biphenyl

PDMS	Program data and management system
PELs	Permissible exposure limits
PJSP	Pre-job safety plan
PMP	Project management plan
PNL	Pacific Northwest Laboratory
PNRS	Preliminary natural resource survey
PPE	Personal protective equipment
PUREX	Plutonium/uranium extraction (plant)
QA	Quality assurance
QAPI	Quality assurance program index
QAPP	Quality assurance project plan
QC	Quality control
QCBSDB	Quality control blind standards data base
QI	Quality instruction
QR	Quality requirement
R&D	Research and development
RA	Risk assessment
RAD	Radionuclides of concern
RAS	Routine analytical services
RCR	Review comment record
RCRA	Resource Conservation and Recovery Act
RCW	Revised Code of Washington
RD	Remedial design
RE	Relative error
RFA	RCRA facility assessment
RfD	Reference dose
RFI	RCRA facility investigation
RFI/CMS	RCRA facility investigation/corrective measures study
RI	Remedial investigation
RI/FS	Remedial investigation/feasibility study
RM	Radiation monitor
RMCl	Recommended maximum contaminant level
ROD	Record of decision
RPP	RCRA past practice
RPT	Radiation protection technologist
RSR	Radiation shipping records
RWP	Radiation work permit
SAP	Sampling and analysis plan
SARA	Superfund Amendments and Reauthorization Act of 1986
SAS	Special analytical services

SC	Site characterization
SCBA	Self-contained breathing apparatus
SDWA	Safe Drinking Water Act
SITE	Superfund innovation technology evaluation
SOP	Standard operating procedure
SOW	Statement of work
SPS	Sample preparation system
STEL	Short-term exposure limit
SST	Single-shell tank
SVS	Semi-volatile organic analysis
SWDA	Solid Waste Disposal Act
SWP	Special work permit
TAG	Technical assistance grant
TAL	Target analyte list
TBC	To-be-considered
TBD	To-be-determined
TCL	Target compound list
TLV	Threshold limit value
TOC	Total organic carbon
TRIS	Training records information system
TS	Physical analysis
TSCA	Toxic Substances Control Act
TSD	Treatment, storage, and disposal
TWA	Time-weighted average
UN	Unplanned release not to an existing disposal facility
UPR	Unplanned release to an existing disposal facility
USWB/USDA	U.S. Weather Bureau/ U.S. Department of Agriculture
VOA	Volatile organic analysis
VOC	Volatile organic compounds
WA	Wilderness Act
WAC	Washington Administrative Code
WIDS	Waste identification data system
WIMS	Warehouse inventory management system
WPPSS	Washington public power supply system
WRAP	Waste receiving and processing
WSRA	Wild and Scenic Rivers Act

THIS PAGE INTENTIONALLY
LEFT BLANK

DOE/RL-90-20
DRAFT A

WORK PLAN

9 0 0 5 2 1 1 1 0 9

THIS PAGE INTENTIONALLY
LEFT BLANK

CONTENTS

1.0 Introduction . . . . . WP 1-1
1.1 Purpose and Scope of RI/FS . . . . . WP 1-5
1.2 Project Goals . . . . . WP 1-6
1.3 Organization of Work Plan . . . . . WP 1-11
1.4 Quality Assurance . . . . . WP 1-12

2.0 Operable Unit Background Setting . . . . . WP 2-1
2.1 Operable Unit Site Description . . . . . WP 2-1
2.1.1 Location . . . . . WP 2-1
2.1.2 History of Operations . . . . . WP 2-3
2.1.3 Facility Identification . . . . . WP 2-3
2.1.4 Waste-Generating Processes . . . . . WP 2-13
2.1.5 Decontamination and Deactivation . . . . . WP 2-20
2.1.6 Interactions with Other Operable Units . . . . . WP 2-21
2.1.7 RCRA Site Interactions . . . . . WP 2-21
2.2 Physical Setting . . . . . WP 2-22
2.2.1 Topography . . . . . WP 2-22
2.2.2 Geology . . . . . WP 2-22
2.2.3 Hydrogeology . . . . . WP 2-53
2.2.4 Surface Hydrology . . . . . WP 2-77
2.2.5 Meteorology . . . . . WP 2-88
2.2.6 Environmental Resources . . . . . WP 2-90
2.2.7 Human Resources . . . . . WP 2-98

3.0 Initial Evaluation . . . . . WP 3-1
3.1 Known and Suspected Contamination . . . . . WP 3-1
3.1.1 Sources . . . . . WP 3-2
3.1.2 Soil . . . . . WP 3-13
3.1.3 Ground Water . . . . . WP 3-23
3.1.4 Surface Water and River Sediment . . . . . WP 3-23
3.1.5 Air . . . . . WP 3-25
3.1.6 Biota . . . . . WP 3-25
3.1.7 Site Conceptual Model . . . . . WP 3-34
3.2 Potential Applicable or Relevant and Appropriate Requirements . . . . . WP 3-42
3.2.1 Chemical-Specific Requirements . . . . . WP 3-43
3.2.2 Action-Specific Requirements . . . . . WP 3-48

3.2.3 Location-Specific Requirements . . . . . WP 3-48
3.2.4 Other Criteria and Guidance . . . . . WP 3-48
3.2.5 Waivers . . . . . WP 3-57
3.2.6 Proposed Regulations . . . . . WP 3-58
3.3 Preliminary Risk Assessment . . . . . WP 3-58
3.3.1 Conceptual Exposure Pathway . . . . . WP 3-59
3.3.2 Primary Toxicity Assessment . . . . . WP 3-62
3.3.3 Contaminant Characteristics . . . . . WP 3-62
3.3.4 Risk Quantification . . . . . WP 3-65
3.4 Preliminary Remedial Action Objectives and Remedial Action Alternatives . . . . . WP 3-66
3.4.1 Remedial Action Objectives . . . . . WP 3-66
3.4.2 General Response Action . . . . . WP 3-67
3.4.3 Remedial Technologies and Process Options . . . . . WP 3-68
3.4.4 Remedial Action Alternatives . . . . . WP 3-71

4.0 Work Plan Approach and Rationale . . . . . WP 4-1
4.1 Decision Types . . . . . WP 4-2
4.1.1 Data Users . . . . . WP 4-2
4.1.2 Available Information . . . . . WP 4-3
4.1.3 Conceptual Models . . . . . WP 4-3
4.1.4 RI/FS Objectives and Decisions . . . . . WP 4-4
4.2 Data Uses and Needs . . . . . WP 4-5
4.2.1 Data Uses . . . . . WP 4-6
4.2.2 Data Types . . . . . WP 4-6
4.2.3 Data Quality Needs . . . . . WP 4-7
4.2.4 Data Quantity Needs . . . . . WP 4-15
4.2.5 Sampling and Analyses Options . . . . . WP 4-15
4.2.6 PARCC Parameters . . . . . WP 4-16
4.3 Data Collection Program . . . . . WP 4-16
4.3.1 General Rationale . . . . . WP 4-17
4.3.2 General Strategy . . . . . WP 4-18
4.3.3 Investigation Methodologies . . . . . WP 4-20
4.3.4 Data Evaluation and Decision Making . . . . . WP 4-25

5.0 Remedial Investigation/Feasibility Study Tasks . . . . . WP 5-1
5.1 Project Management . . . . . WP 5-2
5.1.1 General Management . . . . . WP 5-2
5.1.2 Meetings . . . . . WP 5-2
5.1.3 Cost and Schedule Control . . . . . WP 5-3

5.1.4 Data Management . . . . . WP 5-3
5.1.5 Progress Reports . . . . . WP 5-3
5.2 Operable Unit Characterization . . . . . WP 5-4
5.2.1 Task 1 - Project Management . . . . . WP 5-6
5.2.2 Task 2 - Source Investigation . . . . . WP 5-6
5.2.3 Task 3 - Geologic Investigations . . . . . WP 5-23
5.2.4 Task 4 - Surface Water and Sediment Investigations . . . . . WP 5-25
5.2.5 Task 5 - Vadose Zone Investigation . . . . . WP 5-25
5.2.6 Task 6 - Ground Water Investigations . . . . . WP 5-35
5.2.7 Task 7 - Air Investigations . . . . . WP 5-35
5.2.8 Task 8 - Ecological Investigations . . . . . WP 5-36
5.2.9 Task 9 - Cultural Resource Investigations . . . . . WP 5-39
5.2.10 Task 10 - Data Evaluation . . . . . WP 5-40
5.2.11 Task 11 - Base Line Risk Assessment . . . . . WP 5-40
5.3 FS Phase I/II - Remedial Alternatives Development . . . . . WP 5-46
5.3.1 Task 1 - Project Management . . . . . WP 5-46
5.3.2 Task 2 - FS Phase I Alternatives Development . . . . WP 5-47
5.3.3 Task 3 - FS Phase II - Remedial Alternatives Screening . . . . . WP 5-52
5.3.4 Task 4 - FS Phase I/II Report: Remedial Alternatives Development . . . . . WP 5-55
5.4 RI Phase II - Treatability Investigation . . . . . WP 5-56
5.4.1 Task 1 - Operable Unit Characterization . . . . . WP 5-56
5.4.2 Task 2 - Treatability Investigation Work Plan . . . . . WP 5-58
5.4.3 Task 3 - Treatability Investigation Implementation and Data Evaluation . . . . WP 5-62
5.4.4 Task 4 - RI Phase II Report . . . . . WP 5-65
5.5 FS Phase III - Detailed Analysis of Remedial Alternatives . . . . . WP 5-65
5.5.1 Task 1 - Definition of Remedial Alternatives . . . . . WP 5-66
5.5.2 Task 2 - Detailed Analysis of Alternatives . . . . . WP 5-66
5.5.3 Task 3 - Comparison of Remedial Alternatives . . . . WP 5-69
5.5.4 Task 4 - Feasibility Study Report . . . . . WP 5-70
5.5.5 Task 5 - Corrective Action Plan . . . . . WP 5-70

6.0 Project Schedule . . . . . WP 6-1

7.0 Project Management . . . . . WP 7-1

8.0 References . . . . . WP 8-1

Plate 1 Contour Map of the 100-K Area . . . . . Pocket

Attachment 1 Sampling Analysis Plan for the 100-KR-1 Operable Unit
Attachment 2 Health and Safety Plan for the 100-KR-1 Operable Unit
Attachment 3 Project Management Plan for the 100-KR-1 Operable Unit
Attachment 4 Data Management Plan for the 100-KR-1 Operable Unit
Attachment 5 Community Relations Plan for the 100-KR-1 Operable Unit

FIGURES

1-1 Hanford Site . . . . . WP 1-2
1-2 Map of the 100-K Area Showing the Surface and Ground Water Operable Units . . . . . WP 1-3
1-3 The RI/FS Process at Hanford . . . . . WP 1-9
2-1 Location Map of the 100-KR-1 Operable Unit . . . . . WP 2-2
2-2 Map of the Operable Unit as it Existed During Active Operations . . . . . WP 2-5
2-3 Cooling Water Circuits in the 100-K Area . . . . . WP 2-15
2-4 Generalized Geologic Cross Section of the Hanford Site . . . WP 2-24
2-5 Summary of Stratigraphic Units in the Pasco Basin . . . . . WP 2-25
2-6 Distribution of the Ringold Formation Section Types . . . . . WP 2-26
2-7 Ringold Type Facies at the Hanford Site and Vicinity . . . . . WP 2-27
2-8 Structural Geology of the Pasco Basin . . . . . WP 2-29
2-9 Top of Basalt Contours . . . . . WP 2-31
2-10 Well Location Map and Locations of Geologic Cross Sections, 100-K Area and Vicinity . . . . . WP 2-35
2-11 Well Location Map and Locations of Geologic Cross Sections, 100-K Area . . . . . WP 2-37
2-12 Graphic Logs for Wells K-10, 6-81-62, 199-B3-2 . . . . . WP 2-72
2-13 Geologic Cross Section A-A', 100-K Area . . . . . WP 2-43
2-14 Geologic Cross Section B-B', 100-K Area (Sheet 1) . . . . . WP 2-45
2-15 Geologic Cross Section B-B', 100-K Area (Sheet 2) . . . . . WP 2-47
2-16 Contour Map of the Top of the Ringold Formation, 100-K Area . . . . . WP 2-51

2-17 Water Table Contour Map of the Unconfined Aquifer in 1989, 100-K Area . . . . . WP 2-69
2-18 Hydrographs of Select 100-H Area Wells . . . . . WP 2-72
2-19 Water Table Contour Map of the Unconfined Aquifer in 1967 100-K Area . . . . . WP 2-75
2-20 Ground Water Elevation vs. Time, 100-K Area . . . . . WP 2-78
2-21 Profile of the Columbia River . . . . . WP 2-84
2-22 Flooded Area at the Hanford Site for the Probable Maximum Flood . . . . . WP 2-86
2-23 Flooded Area at the Hanford Site Resulting from a Hypothetical 50 Percent Breach of Grand Coulee Dam . . . WP 2-87
2-24 Hanford Site Wind Roses . . . . . WP 2-89
2-25 Wildlife, Fish and Bird Statistics at the Hanford Site . . . . . WP 2-93
3-1 Waste Site Locations in the 100-KR-1 Operable Unit . . . . . WP 3-3
3-2 Sample Locations Inside the 107-K Retention Basins . . . . WP 3-7
3-3 Location of Soil Samples from the 116-K-1 Crib and 116-K-2 Trench . . . . . WP 3-11
3-4 Test Hole Locations for Soil Samples Outside the 107-K Retention Basins . . . . . WP 3-18
3-5 Soil Sample Locations from the 116-K-1 and 116-K-2 Area for the 1987 Environmental Surveillance Report . . . . . WP 3-24
3-6 Hanford Site and Surrounding Community Air Sampling Locations . . . . . WP 3-26
3-7 Terrestrial Flora Site Sampling Locations 100-KR-1 Operable Unit . . . . . WP 3-29
3-8 Median (3 Standard Deviations) ^{90}Sr, ^{137}Cs, $^{239,240}Pu$, and U Concentrations in Vegetation at Onsite and Offsite Locations . . . . . WP 3-30
3-9 Terrestrial Fauna Sampling Locations Near 100-K Area . . . WP 3-32
3-10 Median Concentration of ^{90}Sr in Bone and ^{137}Cs in Muscle of Cottontail Rabbits in the 100-K Area . . . . . WP 3-33
3-11 Site Conceptual Model-Contaminant Sources Release Mechanisms, Environmental Transport and Potential Receptors for 100-KR-1 . . . . . WP 3-35
3-12 Conceptual Model of Vadose System at the 100-K Area . . . . WP 3-39
3-13 General Response Actions, Technologies, and Process Options Available . . . . . WP 3-69
4-1 Decision Tree for RI/FS Ground Water Sampling . . . . . WP 4-26

4-2 Decision Making Tree for RI/FS Soil, Surface Water, Sediment, Air, and Biota Sampling . . . . . WP 4-27
5-1 Proposed Sampling Locations for 100-KR-1 Source Investigation . . . . . WP 5-14
5-2 Proposed Sampling locations for Soil Investigations . . . . . WP 5-28
5-3 Components of the Risk Assessment Process . . . . . WP 5-42
6-1 Phase I RI/FS Schedule for Hanford Site RI/FS Projects . . . WP 6-2

TABLES

2-1 100-Area Production Reactor Locations by Area . . . . . WP 2-2
2-2 Overview of 100-K Area Operations History . . . . . WP 2-3
2-3 Facilities Within the Boundaries of the 100-KR-1 Operable Unit . . . . . WP 2-5
2-4 Hanford Criteria for Unrestricted Release Adopted for 100-KR-1 Operable Unit Facilities . . . . . WP 2-6
2-5 Washington State List of Endangered and Threatened Flora Species Having the Potential to be Found on the Hanford Site (Endangered Vascular Plants/Threatened Vascular Plants) . . . . . WP 2-21
2-6 Washington State List of Endangered and Threatened Fauna Species Having the Potential to be Found on the Hanford Site (Endangered Birds/Threatened Mammals) . . . . . WP 2-22
3-1 Profiles of Waste Sites Within the 100-KR-1 Operable Unit . . . . . WP 3-2
3-2 Summary of Radionuclide Inventories in the 107-K Retention Basins in 1978 . . . . . WP 3-8
3-3 Radionuclide Concentrations in Soil Samples Inside the 107-K Retention Basins . . . . . WP 3-9
3-4 Radionuclide Concentrations in Soil Samples Inside and Adjacent to the 116-K-1 Effluent Crib . . . . . WP 3-10
3-5 Radionuclide Concentrations in Soil Samples Along the 116-K-2 Trench . . . . . WP 3-12
3-6 Radionuclide Concentrations in Soils outside the 107-K Retention Basins . . . . . WP 3-14
3-7 Summary of Radionuclide Inventory In and Near 116-K-1 Crib and 116-K-2 Trench . . . . . WP 3-15

3-8 Radionuclide Concentrations In Soils Outside the 116-K-1 Crib and 116-K-2 Trench . . . . . WP 3-17
3-9 Concentrations of Radionuclides Detected In 116-K-1 and 116-K-2 Waste Site Surface Soils for the 1987 Environmental Surveillance Report . . . . . WP 3-16
3-10 Air Quality Data for Eastern Washington and the Hanford Site . . . . . WP 3-17
3-11 Radioactive Airborne Emissions from 100-K Area . . . . . WP 3-34
Hanford Site, 1988 . . . . . WP 3-32
3-12 Radionuclide Concentrations Detected in 100-K Area Vegetation . . . . . WP 3-38
3-13 Average Radionuclide Concentrations (pCi/g) Detected in 100-K Area Vegetation 1981 through 1987 . . . . . WP 3-39
3-14 Terrestrial Fauna Radionuclide Concentrations 100 Areas . . . . . WP 3-40
3-15 Contaminants of Concern in the 100-KR-1 Operable Unit . . . WP 3-42
3-16 Radiological Drinking Water Standards . . . . . WP 3-43
3-17 Annual Average Standard for Manmade Radionuclides in Drinking Water . . . . . WP 3-44
3-18 Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements . . . . . WP 3-46
3-19 Selected Location-Specific Potential Applicable or Relevant and Appropriate Requirements . . . . . WP 3-53
3-20 Half-Lives of Selected Radionuclides of Interest to the 100-KR-1 Operable Unit . . . . . WP 3-61
3-21 Unit Bioconcentration Factors for Selected Contaminants of the 100-KR-1 Operable Unit . . . . . WP 3-62
4- 1 Data Objectives for the 100-KR-1 Work Plan . . . . . WP 4-5
4- 2 Analytical Levels for Collecting Needed Data Types in 100-KR-1 . . . . . WP 4-8
4- 3 Data Types, Measurements and Required Analytical Levels for 100-KR-1 . . . . . WP 4-9
5- 1 Proposed Samples for 100-KR-1 Source Investigation . . . . . WP 5-15
5- 2 100-KR-1 Operable Unit Chemical and Physical Analyses . . WP 5-17
5- 3 Proposed Samples for 100-KR-1 Vadose Investigation . . . . . WP 5-29

THIS PAGE INTENTIONALLY
LEFT BLANK

1.0 INTRODUCTION

More than 1,500 waste sites have been identified on the Hanford Site. Most of the waste sites are located within one of four geographic areas on the Hanford Site that are referred to as the 100, 200, 300, and 1100 Areas. Figure 1-1 shows the location of these areas. Each area has been placed on the National Priorities List (NPL) under the Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA). The waste sites were grouped into four areas on the basis of type of facility and operation. For example, the 100 Areas generally are equivalent to the inactive nuclear reactor sites. Each area is further subdivided into operable units according to waste disposal practices, geology, hydrogeology, and other pertinent site characteristics. A total of 78 operable units have been identified. This process is continuing, and the total number of operable units, as well as the individual waste sites within each operable unit, is subject to change. For example, the 100-KR-1 operable unit is an assemblage of individual waste units associated with the KE and KW Reactors, which are located in the 100 Area.

This work plan and the attached plans establish the objectives, procedures, tasks, and schedule for conducting a CERCLA remedial investigation/feasibility study (RI/FS) for the 100-KR-1 operable unit. The 100-KR-1 operable unit is one of three source operable units within the 100-K Area. The location of the operable units within the 100-K Area is presented in Figure 1-2. Source operable units include facilities that are potential sources of radiological or hazardous substance contamination. In addition to the three source operable units, the ground water underlying the entire 100-K Area is considered as a separate operable unit. The RI/FS work plan for the 100-KR-1 source operable unit is being developed concurrently with the RI/FS work plan for the 100-KR-4 ground water operable unit. Work plans for the other two source operable units at the 100-K Area will be developed at a later date.

This work plan was developed in accordance with the *Hanford Federal Facility Agreement and Consent Order* and the associated *Action Plan* (Ecology et al. 1989). All work conducted under this work plan will conform to the conditions set forth in the agreement and consent order.

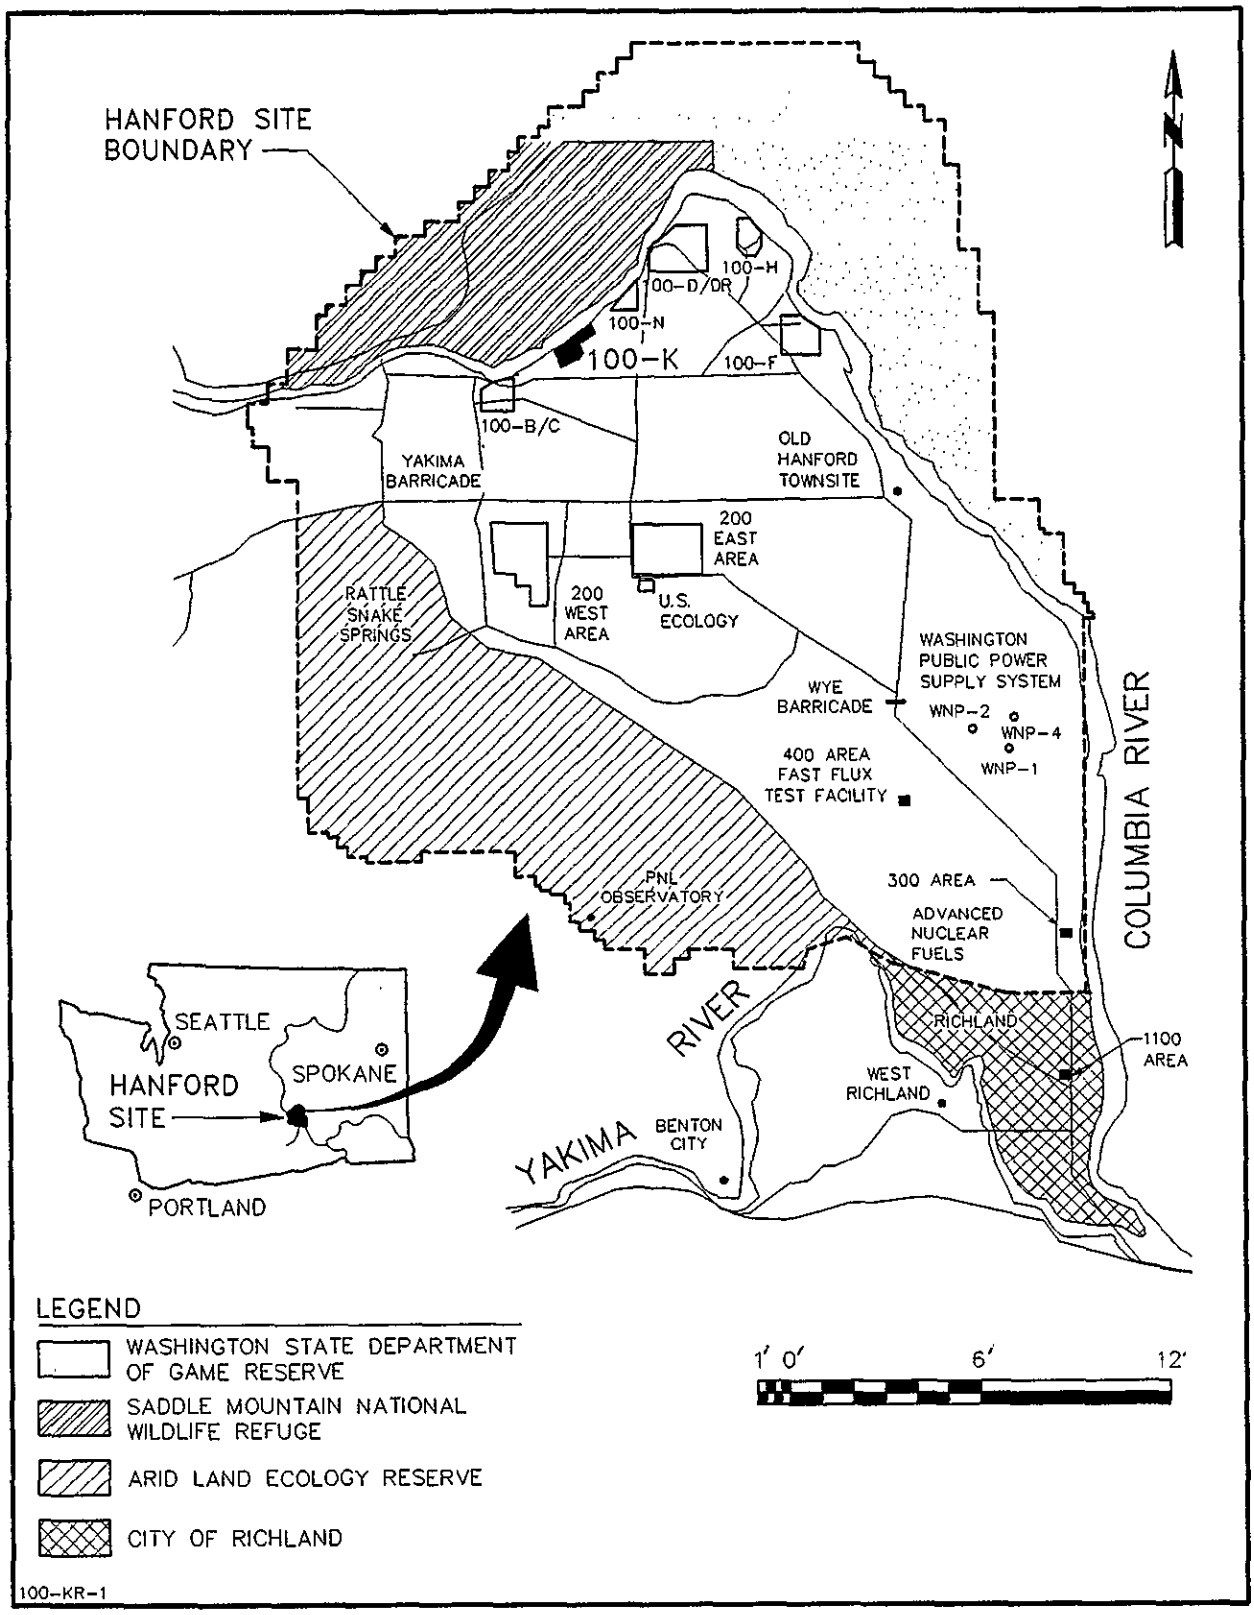

Figure 1-1. Hanford Site.

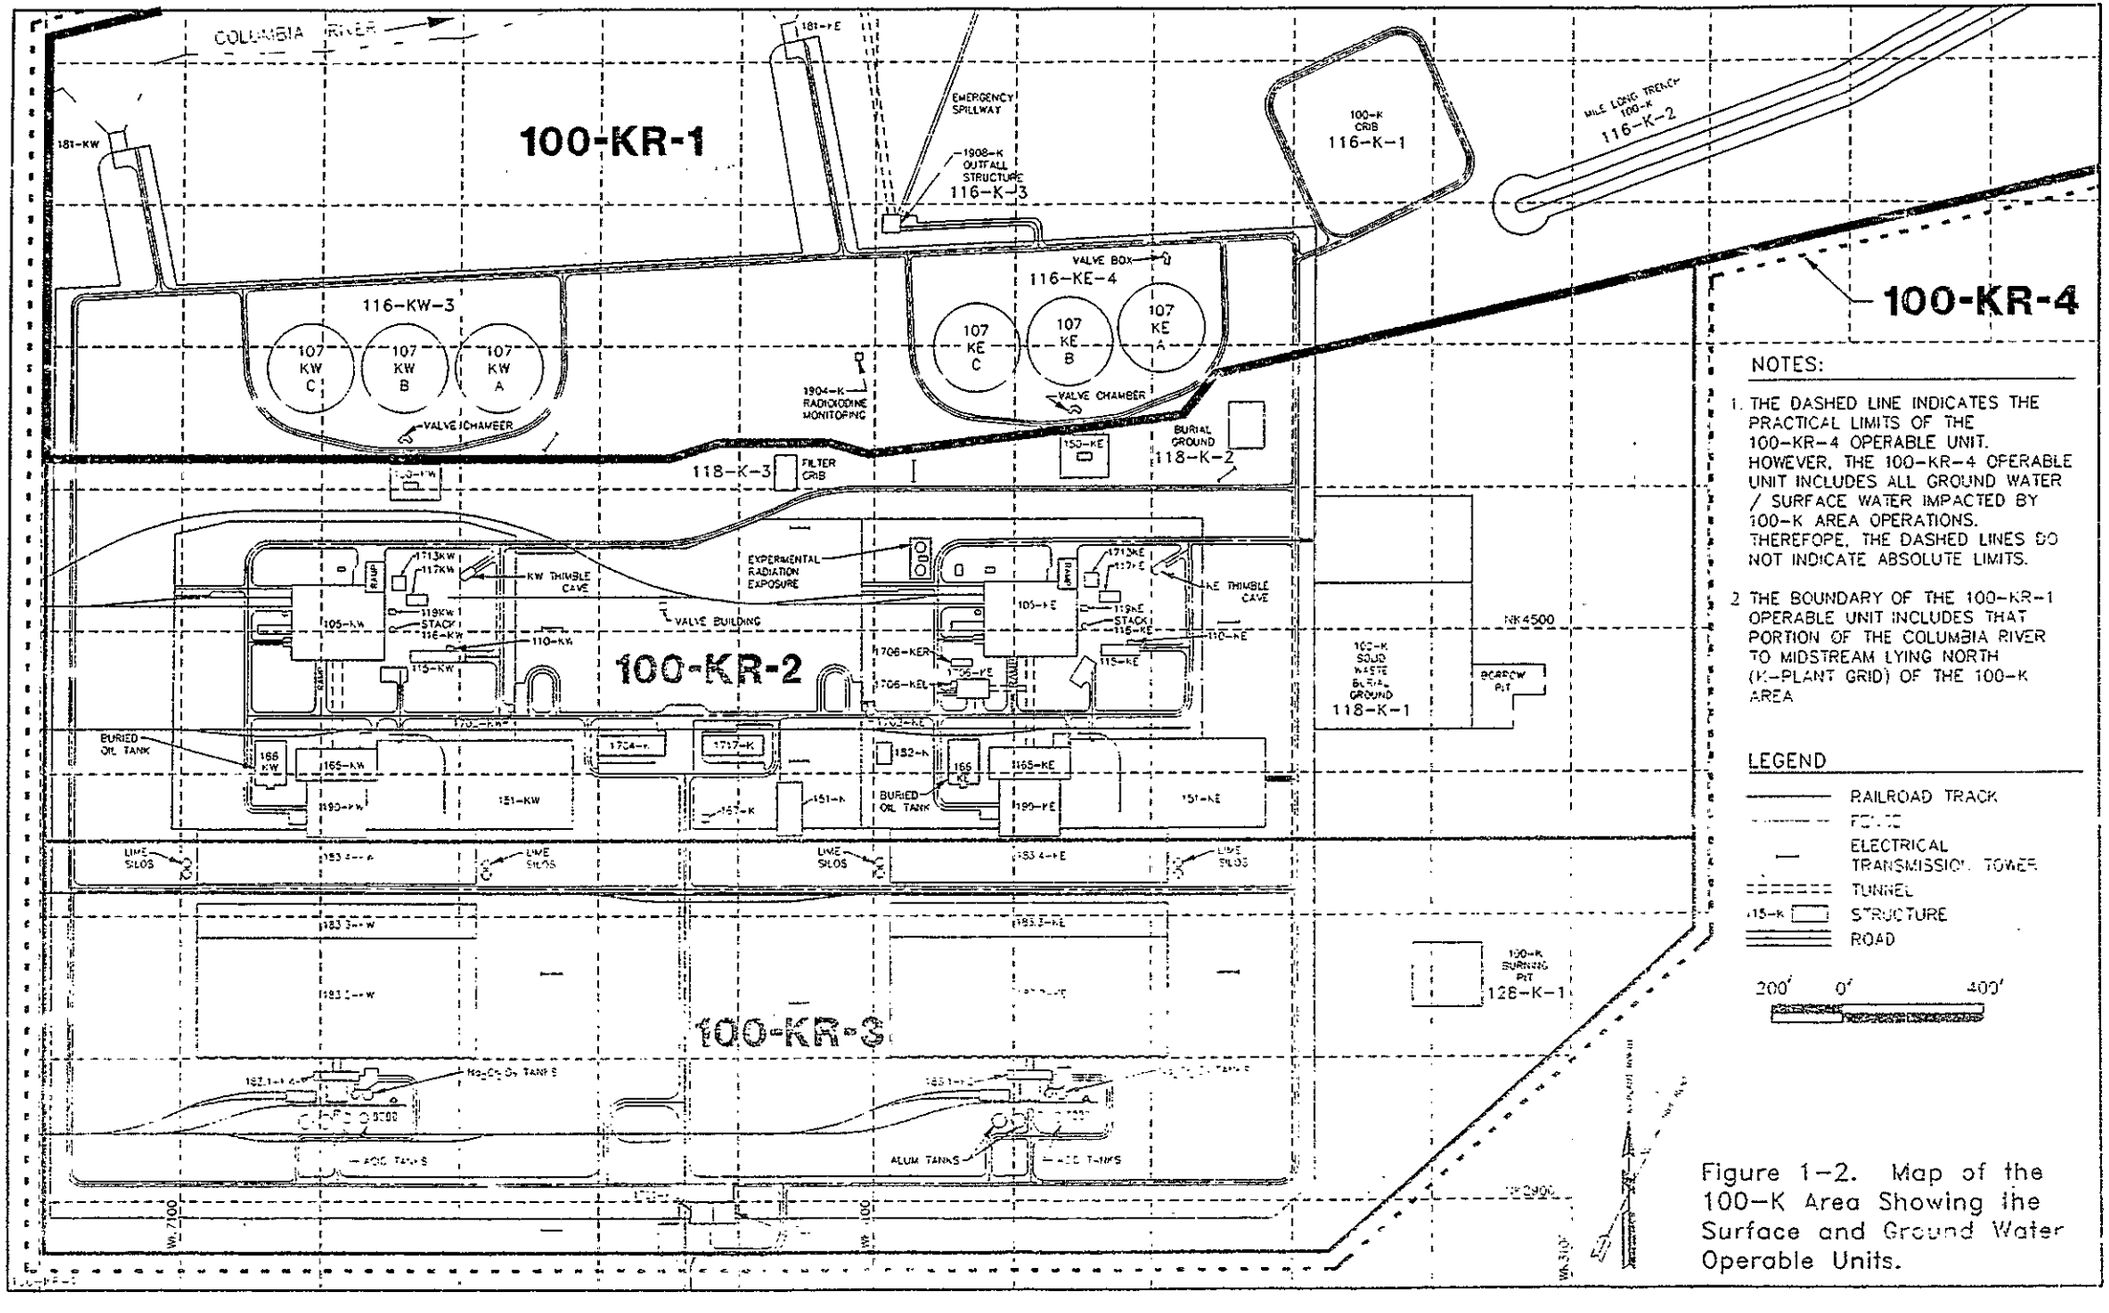

Figure 1-2. Map of the 100-K Area Showing the Surface and Ground Water Operable Units.

THIS PAGE INTENTIONALLY
LEFT BLANK

Pursuant to the consent order, relevant U.S. Environmental Protection Agency (EPA) guidance documents were consulted in the preparation of this work plan, including:

- *Draft Guidance for Conducting Remedial Investigations and Feasibility Studies Under CERCLA* (EPA 1988a)
- *Data Quality Objectives for Remedial Response Activities* (EPA 1987)
- *Superfund Exposure Assessment Manual* (EPA 1988b)
- *Risk Assessment Guidance for Superfund, Volume I, Human Health Evaluation Manual* (EPA 1989a).
- *Risk Assessment Guidance for Superfund, Volume II, Environmental Evaluation Manual* (EPA 1989b).

1.1 PURPOSE AND SCOPE OF RI/FS

In the summer of 1988, EPA proposed the 100 Areas at the U.S. Department of Energy (DOE) Hanford Site for inclusion on the NPL (EPA 1988c). In anticipation of this proposal being finalized, EPA, the Washington Department of Ecology (Ecology), and DOE agreed on the division of the 100 Areas into operable units for the purpose of increasing the manageability of the site characterization and remediation processes (WHC 1989a). On October 4, 1989, EPA issued its final rule that included the placement of the 100 Areas on the NPL, effective November 3, 1989.

The 100-KR-1 operable unit is considered a source operable unit because it contains a liquid waste disposal trench, effluent crib, an outfall structure, and retention basins. The scope for the 100-KR-1 investigation includes these sources of contamination and the associated contamination of soils above the water table (the vadose zone), air and terrestrial biota.

All ground water, surface water, river sediment, and aquatic biota investigations for the entire 100-K Area will be carried out in accordance with the 100-KR-4 work plan, which is being prepared concurrently with the 100-KR-1 work plan.

The purpose of collecting data in an RI/FS is clearly stated in the EPA's *Draft Guidance for Conducting Remedial Investigations and Feasibility Studies Under CERCLA* (1988a):

> "The objective of the RI/FS process is not the unobtainable goal of removing all uncertainty, but rather to gather information sufficient to support an informed risk management decision regarding which remedy appears to be most appropriate for a given site."

The amount of media-specific information needed to support the remedy selection process is dependent in part on the potential future use of the 100-K Area. This potential future use will determine the accessibility of humans and biota to the waste and contaminated media. Although DOE intends to maintain active institutional control of the Hanford Site in perpetuity, an uncontrolled use scenario has been assumed for the development of the RI data-gathering tasks.

Preliminary investigations of radiological contamination that resulted from past practices at the 100-K Area have been conducted by Dorian and Richards (1978). The information and findings of these studies have been used extensively in this work plan. Although a significant amount of data is available to describe certain site conditions, additional information is necessary to develop an acceptable understanding of the nature and extent of potential risks and to develop a suitable range of remedial action alternatives for the 100-KR-1 operable unit. Additional information also is necessary to substantiate existing data that may not be complete, currently evaluated, or validated.

1.2 PROJECT GOALS

The goals of the 100-KR-1 RI are to provide sufficient information needed to evaluate future use exposures in the risk assessment, and develop and evaluate a range of remedial alternatives in the FS that could provide for continued restricted use or an unrestricted future use of the 100-K Area. The 100-KR-1 RI will be conducted in a phased manner. However, if sufficient data are gathered in the initial phase, subsequent work will not be warranted. In addition, the RI will be implemented concurrently with the 100-KR-4 RI. It is expected that the 100-KR-4 RI will provide useful data for the 100-KR-1 RI and FS.

Data-gathering goals of the 100-KR-1 RI are to:

- Identify the contaminants (radiologic and hazardous substances) that occur in the vadose zone and have the potential to be released to the unsaturated soil, air, and terrestrial biota. (Releases to the ground water, surface water, river sediment and aquatic biota will be addressed in the 100-KR-4 work plan.)

- Determine the nature, areal extent, and concentrations of contaminants in these media.

- Identify contaminant migration pathways and potential receptors.

- Identify the potential risks to human health and the environment posed by radioactive and hazardous substances. In particular, identify imminent threats and dangers to human health and the environment during the initial phase of the RI.

- Compile the information necessary to develop and evaluate remedial alternatives and to select preferred remedial actions.

The goal of the 100-KR-1 FS is to evaluate potential remedial actions that encompass a range of appropriate waste management options by developing, screening, and analyzing remedial alternatives. The ultimate goal of the RI/FS is to allow the selection and subsequent implementation of a cost-effective remedial action plan that ensures the protection of public health and the environment. After public review of the RI and FS reports, DOE, EPA, and Ecology will select an appropriate remedy and document this choice in a record of decision (ROD). This will be followed by design, implementation, and monitoring of the chosen remedial action.

The RI/FS process, shown in Figure 1-3, is divided into five phases: two RI phases (operable unit characterization and treatability investigation) and three FS phases (remedial alternatives development, screening, and analysis). According to the action plan of the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989), the following four primary documents will be prepared and distributed for public review and comment: Phase II RI report and Phase I, II and III FS reports. The data collected during the initial RI phase will provide the information needed to develop and evaluate remedial alternatives in the FS. The initial alternatives evaluation in the FS may, in turn, identify the need for additional data collection during the second phase of the RI.

THIS PAGE INTENTIONALLY
LEFT BLANK

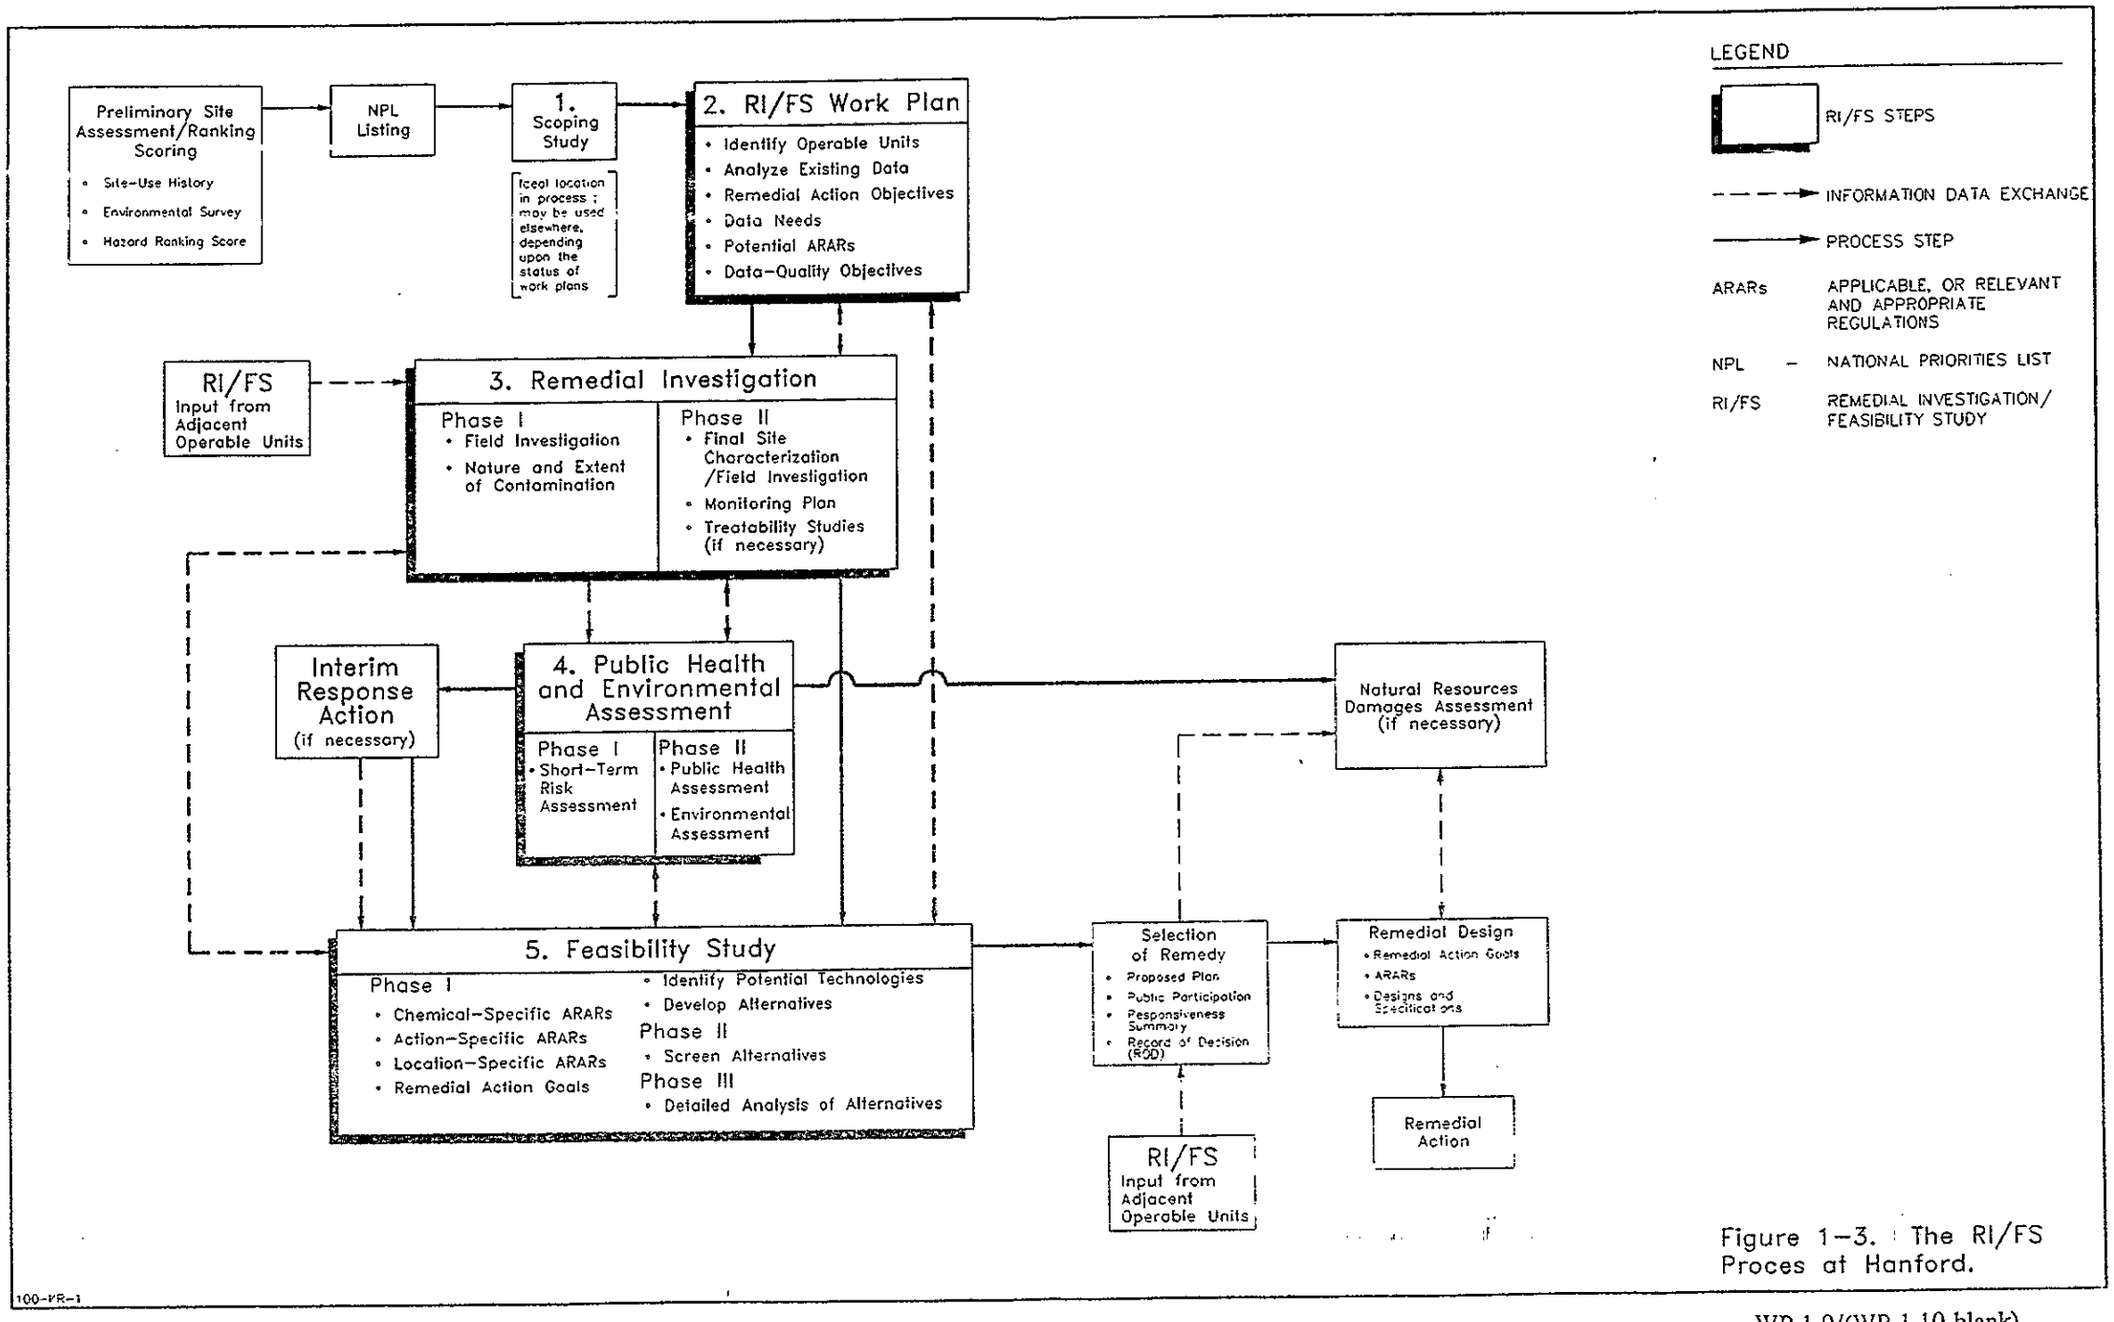

Figure 1–3. The RI/FS Proces at Hanford.

THIS PAGE INTENTIONALLY
LEFT BLANK

1.3 ORGANIZATION OF WORK PLAN

The RI/FS work plan is based on a knowledge of conditions at the 100-KR-1 operable unit that has been acquired from a review of the reference materials listed in Chapter 8.0, a walkover of the operable unit by members of the work plan team, and conversations with a former employee at the 100 Areas. The work plan will be modified and updated throughout the RI/FS process as additional information becomes available. In this manner, the work plan will provide efficient and effective directions consistent with project goals. A dynamic work plan will also serve to help document the rationale for project decisions and conclusions and thereby provide assistance in making subsequent remedial action decisions. In particular, it is recognized that by the time this work plan is implemented, valuable data presumably will be available from RI/FS and Resource Conservation and Recovery Act of 1976 (RCRA) facility investigation/corrective measures study (RFI/CMS) projects at other 100 and 300 Area operable units.

Eight chapters, including this introduction, are included in the work plan. Chapter 2.0 presents the physical and environmental setting of the 100-K Area and its surroundings. The history and current understanding of the waste generation, transfer, storage, and disposal processes and facilities within the 100-KR-1 operable unit are also summarized in Chapter 2.0.

Available data on potential contaminant exposure pathways are reviewed in Chapter 3.0 to develop a conceptual model for the operable unit. Waste sources, quantities, and characteristics are identified, along with the current understanding of the extent of contamination in the various environmental media. Federal and state standards, requirements, criteria, or limitations that may be considered potentially applicable or relevant and appropriate requirements (ARAR) are identified, potential impacts to public health and the environment are assessed, and preliminary remedial action objectives are presented.

Chapter 4.0 summarizes what is known and, more importantly, what is not known, about the 100-KR-1 operable unit. By comparing the data needed to conduct an RI/FS with the data that are available now, the RI tasks can be defined.

Chapter 5.0 presents the activities necessary to conduct the two phases of the RI (operable unit characterization and treatability investigation) and the three phases of the FS (remedial alternatives development, screening, and analysis). Detailed activities for the treatability investigation are not described, because such activities

will depend on the information gathered during the site characterization phase of the RI and the results of the initial phases of the FS.

A project schedule is presented in Chapter 6.0. Modifications to the schedule may be required as new information is obtained prior to or during project implementation. Chapter 7.0 refers to the project management plan, which discusses the organization and responsibilities required to implement the RI/FS activities. References used to develop the work plan are provided in Chapter 8.0.

Attachments to this work plan include support plans that are necessary to manage, conduct, and control the RI/FS project. The attached plans are:

- Attachment 1: Sampling and Analysis Plan (SAP) comprising
  Part 1: Field Sampling Plan (FSP) and
  Part 2: Quality Assurance Project Plan (QAPP)
- Attachment 2: Health and Safety Plan (HSP)
- Attachment 3: Project Management Plan (PMP)
- Attachment 4: Data Management Plan (DMP)
- Attachment 5: Community Relations Plan (CRP).

Each of the plans is meant to be used in conjunction with the work plan and the other plans, thus minimizing duplication of information.

1.4 QUALITY ASSURANCE

The 100-KR-1 work plan and its supporting plans (i.e., the SAP, FSP, QAPP, PMP, DMP, and HSP) have been developed to meet specific EPA guidelines for format and structure, within the overall QA program structure mandated by DOE-Richland Operations Office (DOE-RL) for all activities at the Hanford Site.

The hierarchy of QA program documents applicable to this project follows:

- DOE-RL Order 5700.1A, *Quality Assurance* (DOE-RL 1983): This directive establishes broadly applicable QA program requirements, based on American National Standard Institute/American Society of Mechanical Engineers (ANSI/ASME) *NQA-1, Quality Assurance Program Requirements for Nuclear Facilities* (ANSI/ASME 1986), for all projects conducted on the Hanford Site.

- *Westinghouse Hanford Company Quality Assurance Manual,* WHC-CM-4-2 (WHC 1989b): This document describes the program and procedures to be used to implement DOE-RL Order 5700.1A for all activities conducted by Westinghouse Hanford on the Hanford Site.

- Westinghouse Hanford QA program plan for CERCLA RI/FS activities: This plan describes the means selected to implement WHC-CM-4-2 for CERCLA RI/FS environmental investigations, while accommodating the specific requirements for project plan format and content agreed on in the Hanford Federal Facility Agreement and Consent Order (Ecology et al. 1989). The guidance contains a complete matrix of procedural resources [from WHC-CM-4-2 (WHC 1989b) and from WHC-CM-7-7 (WHC 1989c), and from other sources] that may be drawn on to support lower-tier operable unit-specific project plans.

- 100-KR-1 QAPP: Included as Part 2 of the 100-KR-1 SAP, the QAPP supports the FSP. The QAPP defines the specific means that will be used to ensure that the sampling and analytical data obtained as part of the Phase 1 RI will be defensible and will effectively support the purposes of the investigation. As required for CERCLA RI/FS activities, the structure and content of the QAPP is based on *Interim Guidelines and Specifications for Preparing Quality Assurance Project Plans* (EPA 1983). Where required, the QAPP invokes appropriate procedural controls from WHC-CM-7-7 (WHC 1989c) for CERCLA RI/FS activities or developed to accommodate the unique needs of this investigation.

THIS PAGE INTENTIONALLY
LEFT BLANK

2.0 OPERABLE UNIT BACKGROUND SETTING

This section presents a summary of the pertinent physical and historical setting, for the 100-KR-1 operable unit.

2.1 OPERABLE UNIT SITE DESCRIPTION

2.1.1 Location

The Hanford Site is located in south central Washington state. The 100-K Area is located in the north central part of the Hanford Site, within Benton County, Washington, and is situated along the southern shoreline of the Columbia River (Figure 1-1). The area lies approximately 25 mi (40 km) northwest of the city of Richland, Washington. The 100-KR-1 operable unit is adjacent to the Columbia River shoreline between River Miles 380 and 382 (Figure 2-1).

The operable unit covers an area of approximately 0.23 mi^2 (0.6 km^2) and is located within Sections 5 and 6 of Township 13 N, Range 26 E and Sections 31 and 32 of Township 14 N, Range 26 E and lies between Hanford south/north coordinates N75,200 and N84,200 and west/east coordinates W71,650 and W63,650 respectively. The 100-K Area was laid out on its own grid system, known as the 100-K Area grid, which is rotated 27° 09'59" counterclockwise from Hanford (true) north to the 100-K Area north. This system can be translated and rotated from the general Hanford grid using coordinate transform equations.[1] The coordinate boundaries for the area are approximately south/north coordinates N^K 4,900 and N^K 10,400 and east/west coordinates W^K (-)1,900 and W^K 7,600, respectively.

---

[1] $N^K = 0.8897\,N^H + 0.4566W^H - 94{,}331$
$W^K = -0.4566N^H + 0.8897W^H - 20{,}884$
Where: N^K = North, K Area coordinates
W^K = West, K Area coordinates
N^H = North, Hanford coordinates
W^H = West, Hanford coordinates

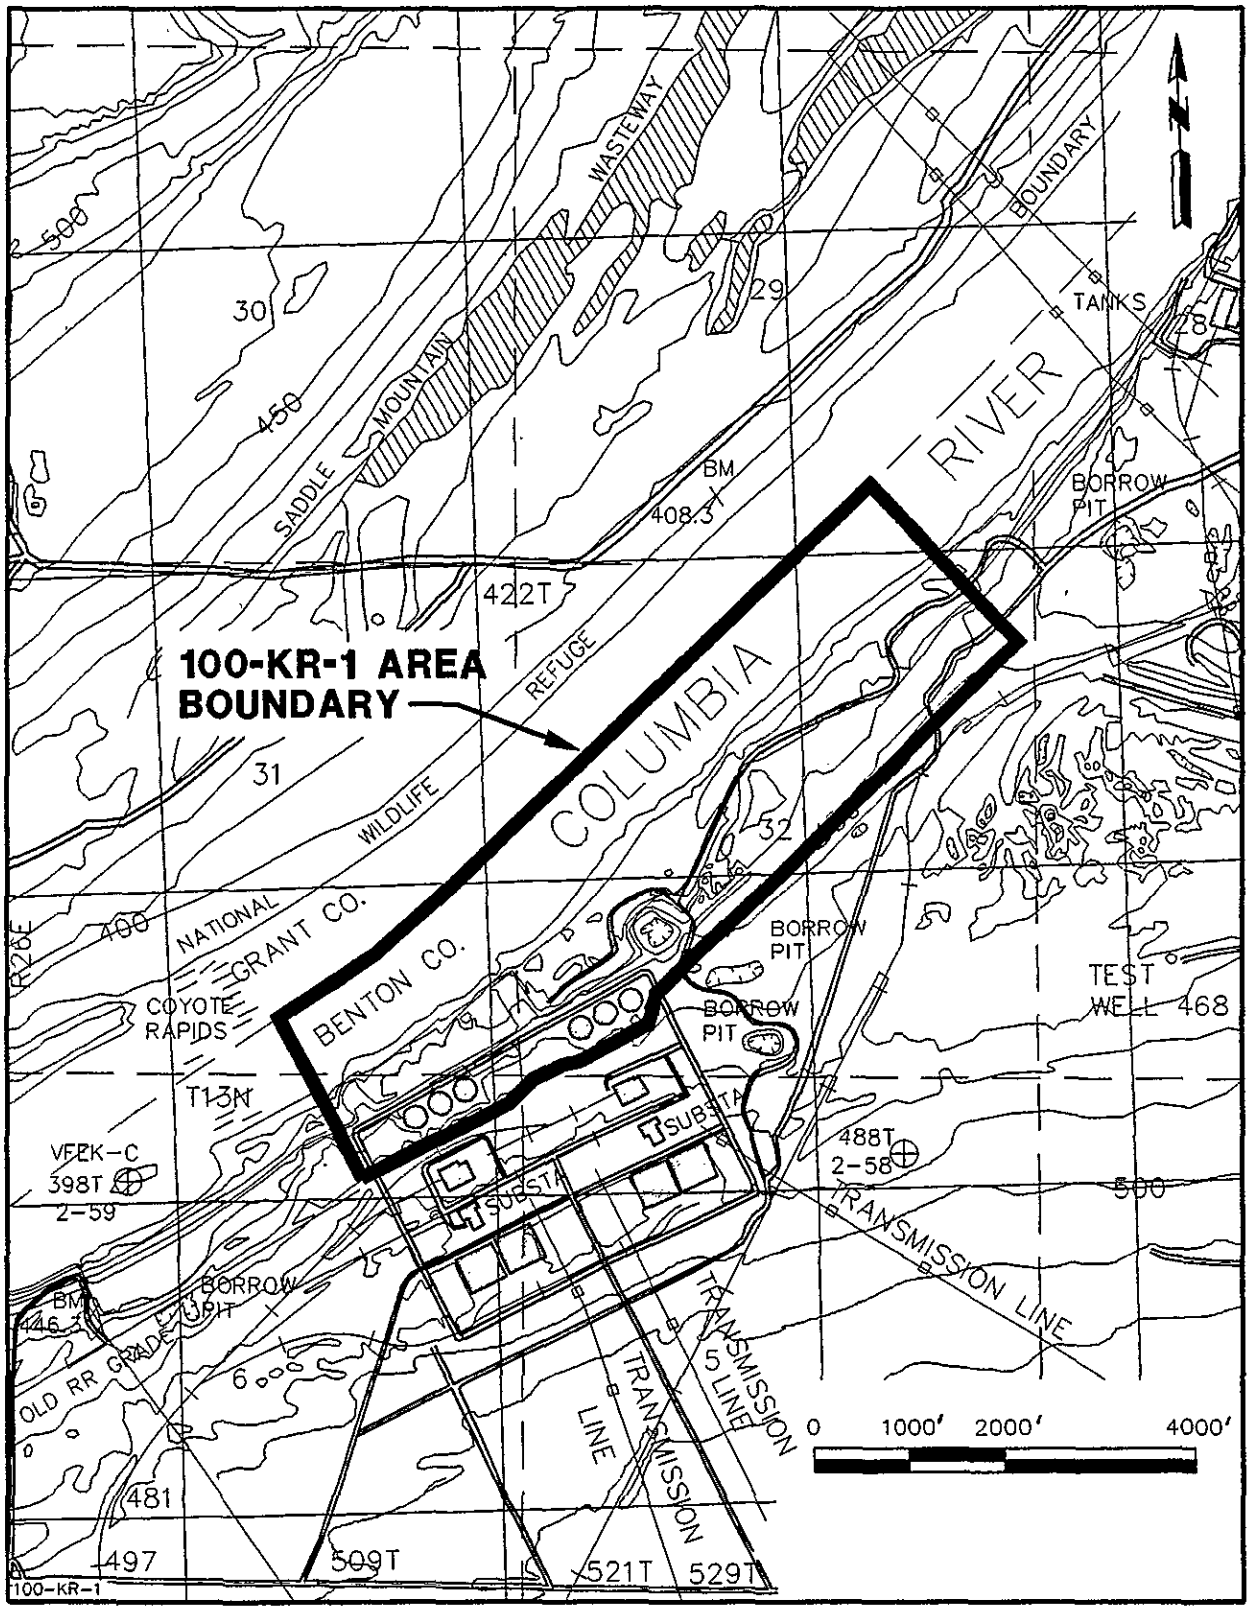

Figure 2-1. Location Map of the 100-KR-1 Operable Unit

2.1.2 History of Operations

Between 1943 and 1963, nine water-cooled, graphite-moderated plutonium production reactors were built along the Columbia River upstream from the now abandoned town of Hanford. Eight of these reactors (B, C, D, DR, F, H, KE, and KW) have been retired from service and are under evaluation for decommissioning. The ninth reactor (N reactor) in the 100-N Area is currently on cold standby.

The KW and the KE reactors and support facilities were constructed between 1952 and 1954. The KW reactor operated from 1955 through 1970 at which time it was retired from service. The KE reactor operated from 1955 until 1971 and was then retired from service. Although a few ancillary structures were shared by the reactor facilities, in general the major support operations were duplicated. Table 2-1 summarizes the history of 100-K Area operations.

Currently, there are several active facilities within the 100-K Area. They include the 105-KE and 105-KW fuel storage basins used to store spent fuel from the N reactor; the alum tanks adjacent to building 183.1-KE; research and development performed in 1706-KE; buildings used for site management; one pumphouse; one water treatment facility; and septic tanks and leach fields used for disposal of sanitary waste.

To minimize the potential spread of radioactive isotopes from the reactors and associated facilities, a plan for decontamination and deactivation of the reactors was implemented after reactor operations ceased. Deactivation generally consisted of removing equipment, electrical hardware, piping, and other items from the buildings and flushing and/or wiping pipes and equipment with decontamination agents.

2.1.3 Facility Identification

The facilities within the 100-K Area as they existed during active operations are shown in Figure 2-2 and listed in Table 2-2. The majority of the buildings remain standing. Buildings demolished and/or removed are noted in Table 2-2. The table includes the original facility identification number, facility name, years in service, purpose, and description where known.

Table 2-1. History of 100-K Area Operation.

Date	Event
1954	Construction completed on 105-KW and 105-KE reactors
1955-1970	105-KW reactor in operation to produce plutonium
1955-1971	105-KE reactor in operation to produce plutonium
1970-1971	Reactors shut down, systems deactivated and decontaminated. A major part of deactivation was removal of the fuel
1973-1974	105-KE and 105-KW reactor basins cleaned and equipment modified to store N reactor irradiated fuel storage
1974	105-KE basin leak detected
1974-mid-1976	105-KE and 105-KW basin cooling systems modified to closed system cooling
1975	N reactor irradiated fuel storage begins in 105-KE and 105-KW reactor basins
1975-1977	Study performed to establish radionuclide levels in 100-K Area vadose (Dorian and Richards 1978)
1980	105-KE basin leak isolated and repaired
1987-1988	Preliminary assessment/site investigation completed; 100 Areas nominated to National Priorities List (NPL)
1989	Shipments of N reactor irradiated fuel cease

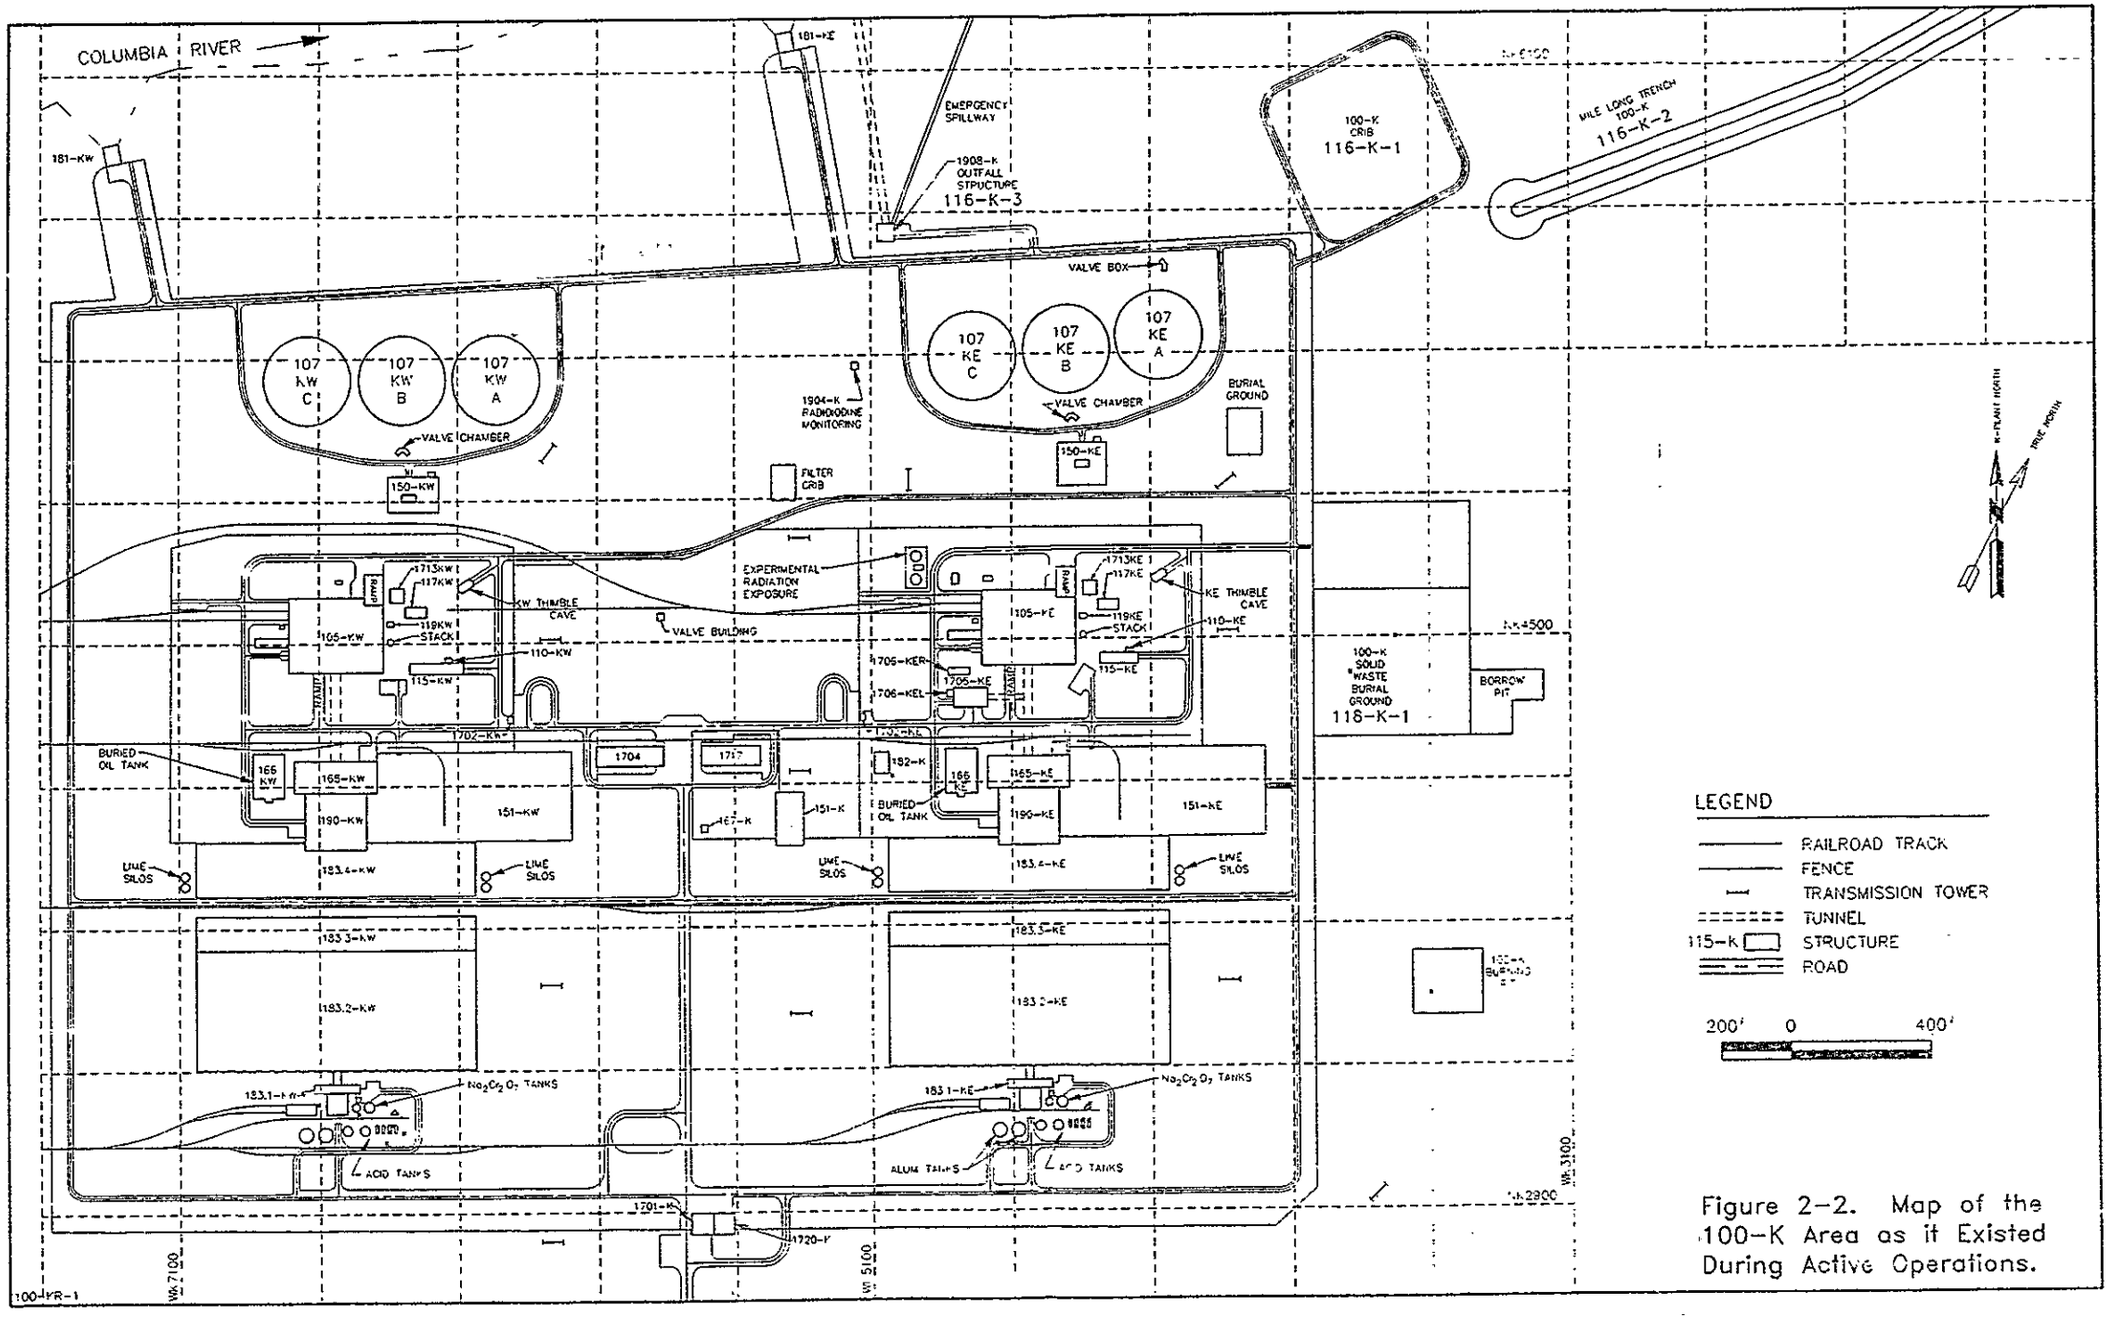

Figure 2-2. Map of the 100-K Area as it Existed During Active Operations.

THIS PAGE INTENTIONALLY
LEFT BLANK

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
100-KR-1 OPERABLE UNIT				
181-KE	River pump-house	1955-Present	Pump river water to water treatment plant	Reinforced-concrete intake structure
181-KW	River pump-house	1955-1970	Pump river water to water treatment plant	Reinforced-concrete intake structure
1908-K	Outfall structure	1955-Present	Control effluent discharge from 107-KE & 107-KW retention basins	Reinforced-concrete structure; two steel inlet pipes, two 84-in. steel effluent pipes, overflow channel
1904-K	Radioiodine Monitor Building	1955-1971	Monitor radioactivity of effluent	Unknown
107-KE	Retention basins	1955-1971	Provide retention of reactor cooling water prior to discharge into river	Three 250-ft-diameter, 9,000,000-gal, welded carbon steel tanks, mounted on a reinforced-concrete foundation
107-KW	Retention basins	1955-1970	Provide retention of reactor cooling water prior to discharge into river	Three 250-ft-diameter, 9,000,000-gal, welded carbon steel tanks, mounted on a reinforced-concrete foundation
116-K-2	Effluent trench	1955-1971	Percolation of radioactive reactor cooling effluent	4,000 x 50-ft, gravel-lined percolation trench including four overflow areas
116-K-1	Effluent crib	1955	Percolation of radioactive reactor cooling effluent	200 x 200 x 20-ft percolation crib

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
100-KR-2 OPERABLE UNIT				
105-KE/KW	Reactor buildings	KE 4/55-1/71 KW 1/55-2/70	Provide housing for KE-reactors and ancillary facilities	Reinforced-concrete and steel multi-story structure; houses reactor, control room, offices, lunch room, spent fuel storage, ventilation systems
115-KE/KW	Gas recircula-tion building	1955-1971 Demolished in 1988	Houses gas circulating pumps and associated equipment and reactor gas coolant system	Single-story reinforced-concrete structure; tunnel connects to 105 reactor building; considered a major contaminated structure
110-KE/KW	Gas storage appurtenant to 115-KE/KW building	1955-1971	Gas storage for 115-KE and 115-KW building	Reinforced-concrete
116-KE/KW	Reactor exhaust stacks	1955-1971 Top 125 ft. Decontami-ated in 1982, partially dismantled in 1988	Discharged reactor building exhaust air	Reinforced monolithic concrete, 30 x 22-ft-diameter at base; top 125-ft dismantled, rubble was placed in remaining base of stacks
117-KE/KW	Exhaust air filter building	1955-1971 Demolished 1988	Filter ventilation air from reactor buildings; houses air filters and airflow control system	Reinforced-concrete building built mostly underground, 59 ft X 39 ft X 35 ft high; connected by tunnels to 105 reactor building and 116 exhaust stack; structure demolished and buried in-situ in 1988
100-K Burial ground	100-K Area waste burial ground	1954-1973	Burial of solid waste from the 100-K Area	1,200 x 600 ft 100-K Area burial ground; contains numerous trenches and pits; surface routinely treated with herbicide, contains large radionuclide inventory

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
151-KE/KW	Electrical substation area	1955-Present	Provide power distribution	Approximately 3 acres of land containing transformers and switch gear
165-KE/KW	Power control buildings	1955-present	Houses powerhouse, control room, valve pit and electrical switch gear for water supply building	Single-story concrete structure; the building consists of the pump room and valve pit, electrical area, oil-fired steam plant and control room; tunnel from 183 water filter plant to 105 reactor building; the 165-KE oil boiler provides heat for the remaining facilities in the 100-K Area
166-KE/KW	Fuel oil storage and pumps appurtenant to 165-KE/KW building	1955-1971	Storage and pump facilities for fuel oil for the oil-fired steam plant in the 165-KE/KW buildings	Underground 1,650,000-gal fuel oil storage bunkers
167-K	Cross-tie tunnel vent	1955-Present	To provide ventilation between 190 KE and 190 KW	A vent constructed of wood, steel and concrete
182-K	Emergency water pump building	1955-1971	Provides emergency pumping capacity from the clearwells to the 105-reactors; houses three diesel engine driven pumps, air compressors, fuel tanks, batteries and charging equipment	Steel-framed structure with concrete foundation and transite walls; two 17,500-gal fuel tanks are appurtenant to this structure
190-KE/KW	Main pump-houses	KE 1955-present KW 1955-1971	Provides primary coolant for the 105 reactors; houses process and service water pumps, powerhouse, electrical substation, valve pit and control room	Single-story building with concrete basement and floors, steel frame and transite walls; 190-KW, deactivated in 1971; 190-KE, presently used to supply water to the fuel storage basins, fire protection and domestic water needs

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
1608-KE/KW	Wastewater pumphouses	KE 1955-1971 KW 1955-1970	Collection supply and pump station for potential contaminated liquids from the 105 reactor buildings; pumped effluent to the reactor effluent lines	Concrete or steel
1702-KE/KW	105-Area badge houses	1955-1980's	Security and personnel dosimetry	Single-story, concrete and steel frame with transite walls
1704-K	Administrative building	1954-present	Provides office space and first aid center	Single-story, concrete and steel frame with transite siding
1706-KE	Testing facilities	1955-present	Provides out-of-reactor facilities in support of in reactor testloops and single pass tubes	Single-story, concrete and steel frame with transite siding; full basement; provides water treatment facilities and instrumentation for eight reactor tubes used to study corrosion and effects of water treatment on effluent
1706-KER	Testing facilities	1955-present	Provides out-of-reactor facilities in support of in reactor testloops and single pass tubes	Single-story, concrete and steel frame with transite walls shielded cells below grade
1706-KEL	Laboratory	1955-present	Lab for 1706-KE and 1706-KER testing facilities	Single-story concrete and steel frame
1713-KE	Shop building	1954-1980s	Storage	Sheet metal with concrete floor

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
1713-KER	Warehouse	1950s-1970s	Storage	Sheetmetal with concrete floor
1713-KW	Warehouse	1950s-1970s	Storage	Sheetmetal with concrete floor
1717-K	Maintenance shops	1954-present	Maintenance shops and light equipment maintenance	Single-story, concrete and steel frame with transite siding; used for carpenter, millwright, welding, paint and automotive service station
150-KE/KW	Heat recovery facilities	KE 1955-1971 KW 1955-1970	Heat recovery from cooling water effluent	Unknown
100-KR-3 OPERABLE UNIT				
1701-K	Area badge house	1954-1980s	Security and personnel dosimetry	Single-story, concrete and steel frame, structure with transite walls; adjoins 1720-K building
1720-K	Area headquarters	1954-Present	Headquarters for security patrol, mail operations	Single-story, concrete and steel frame construction with transite siding; adjoins 1701-K building
183 KE/KW Facilities	Water treatment facility	KE: 1955-Present KW: 1955-1970s	Process water and domestic water treatment	See 183.1, 183.2, 183.3, 183.4 and 183.5 structures described below
183.1 KE/KW	Headhouse and chlorine building	1950s-1970s	Contains a lab sample room, chlorinator room, switchgear room and operational area housing chemical feed equipment, storage tanks, water softeners and pumps	Single-story, concrete and steel frame structure with transite siding

Table 2-2. Facilities Within the 100-K-Area (AEC-GE, 1964).

Facility designation	Name	Years in service	Facility purposes	Facility description
183.2 KE/KW	Flocculation and sedimenta-tion	1950s-1970s	Water treatment	Open-air concrete basins, with mixing chambers, agitators, flumes; each facility (KE/KW) covers about 288,000 ft^2
183.3 KE/KW	Filter basin	1950s-1970s	Water filtration	Concrete basin containing a granular media filter with about 65,000 ft^2 of surface area; gravity flow through filter
183.4 KE/KW	Clearwells	1950s-1970s	Treated water storage	Concrete basin used to store treated water; two clearwells of 9,000,000-gal capacity are used at each 105 reactor
183.5 KE/KW	Lime houses	1950s	Lime storage, and feeding lime to filtered water in clearwells	Transite and steel
183.6 KE/KW	Feeder buildings	1950s-1970s	These facilities were cross tie buildings between the KE and KW areas	Concrete and steel

Two primary numbering systems have been used in the 100-K Area. Under the original Hanford numbering system, facilities were given a unique number (e.g., 105-KE for the KE Reactor and 105-KW for the KW Reactor). Most waste units were not assigned a unique number, but were instead referred to by the number of the nearby facility (e.g., 105-KE percolation French drain). The Waste Information Data System (WIDS) was initiated in 1980 as an organized waste site identification system. The waste sites and some facilities were assigned waste site designation numbers (e.g., 116-KE-3 for the 105-KE percolation French drain) by WIDS.

2.1.4 Waste-Generating Processes

Wastes produced in the 100-K Area have been generated from the operation of the reactors and support facilities. Known waste streams affecting the 100-KR-1 operable unit are summarized below (Stenner et al. 1988):

- Reactor process liquid wastes and cooling water effluent
- Miscellaneous radioactive liquid wastes
- Radioactive sludge
- Herbicides to control vegetation.

2.1.4.1 Reactor Cooling Water System. The major component of liquid radioactive wastes generated in the 100-K Area resulted from the reactor cooling water circuits.

Reactor cooling water was pumped from the Columbia River. The water was treated and circulated in a single pass through each reactor. The cooling water exiting the reactor contained activation products from the reactor and also chemicals added during the water treatment process. Once through the reactor building, cooling water passed through a retention basin system and was then discharged to the river. At times, ruptured fuel elements contaminated the cooling water which was then diverted to the 116-K-2 trench (Dorian and Richards 1978). The cooling water circuit for the 100-K Area reactors is shown in Figure 2-3. The KE reactor cooling water system is described more fully in the following paragraphs. The KW reactor cooling water system is similar.

THIS PAGE INTENTIONALLY
LEFT BLANK

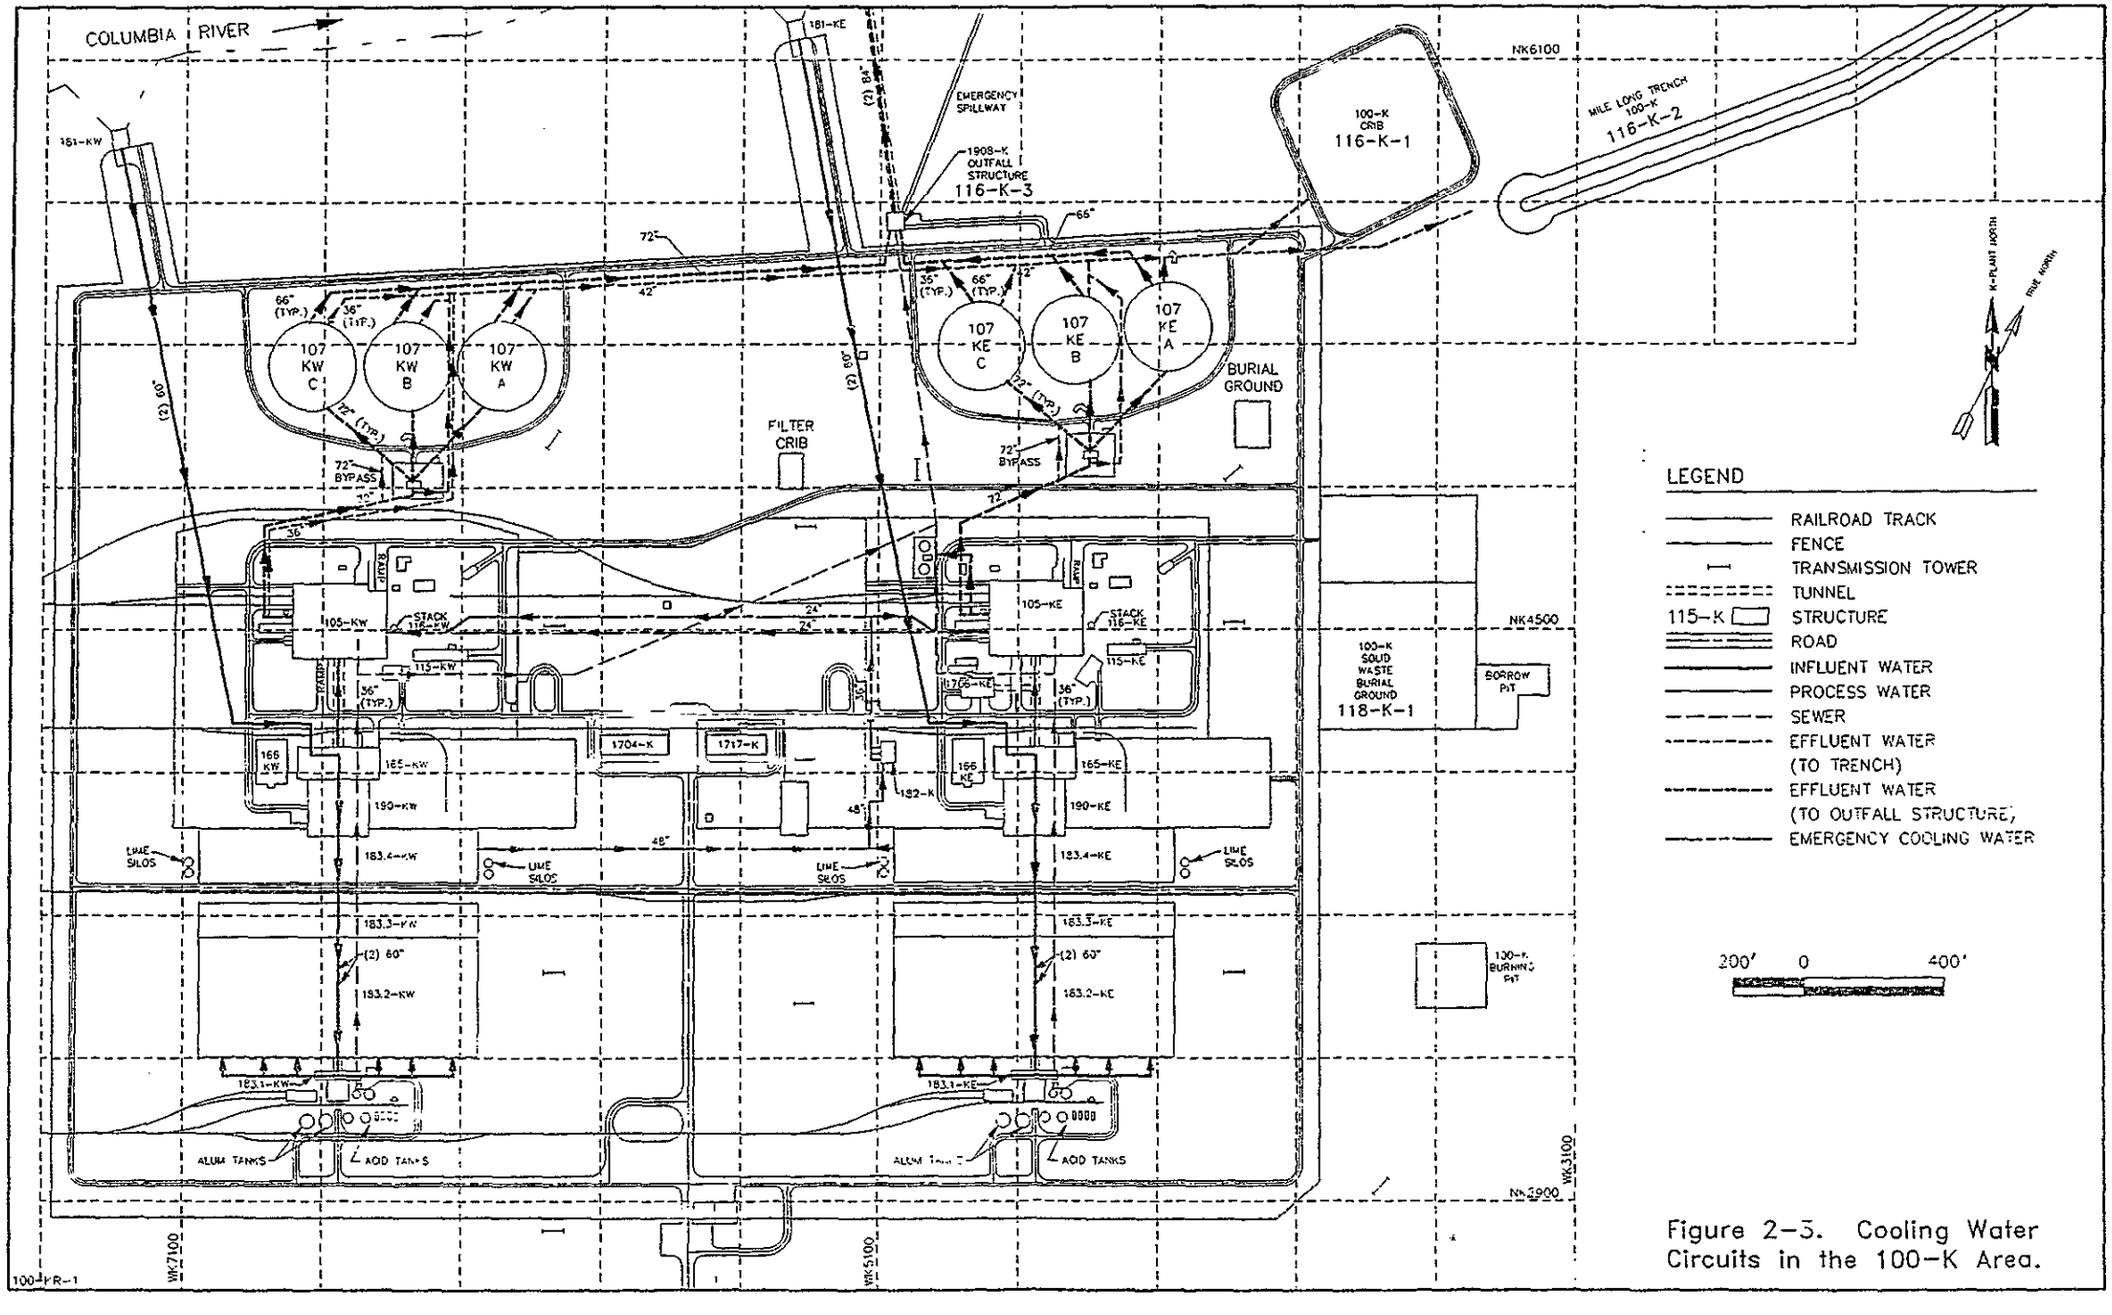

Figure 2-3. Cooling Water Circuits in the 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

Columbia River water from the 181-KE river pumphouse was pumped to the water treatment facility in the 183-KE complex. At the 183-KE complex, the river water was treated with chemical additives to remove suspended matter and retard corrosion. These additives included alum and polyelectrolytes to enhance the removal of suspended solids by flocculation and filtration respectively; sulfuric acid to control pH; and chlorine to control algae growth in the settling basins. The alum was produced by mixing sulfuric acid and bauxite. Commercially produced alum was stored southwest of the 183.1-KE treatment buildings as a backup. Concentrated sulfuric acid and bauxite were stored in steel tanks just outside the buildings. The chemical additives were introduced as the water passed down a flume into a mixing chamber (183.2-KE). From the chamber, the water traveled to a basin equipped with paddlewheel flocculators. After passing through the flocculators, the cooling water for the reactor then passed to one of six settling basins. Lime could be added at this point to adjust the pH of the system.

The water was then filtered through one of 12 rapid sand filters (183.3-KE). The filters were backwashed periodically, and backwash water from the filters was discharged to a process sewer. Before the advent of the National Pollutant Discharge Elimination System Permit Program, backwash water may have been discharged directly to the river, as indicated in the *1963 Hazards Summary Report*, (GE 1964; Figure III-1). Water exiting from the filters was piped to two subsurface 9,000,000-gal (3.4×10^7L) clearwells (183.4-KE) for each reactor. Sodium dichromate was added to the clearwell discharge prior to the coolant pump to inhibit corrosion of reactor piping.

The coolant pumps delivered the water to a distribution header in the 165-KE building, then to the reactor. Water that entered the reactor contained alum, chlorine, sodium dichromate, and residual impurities naturally present in river water that were not removed during treatment.

There were several flow paths through each reactor, the primary one being through the inside of 3,220 individual process tubes. A second pathway went through cooling pipes located in the thermal and biological shields. Other less voluminous flow paths through the reactors included circulation through the foundation and the horizontal control rods (20 per reactor) that penetrated the reactor core. The cooling water from all flow pathways was recombined before leaving the reactor building. Reportedly, cooling water flow through the reactor was about 200,000 gal/min (12,600 L/s).

Due to the thermal energy transfer from the reactor core, cooling water exited the reactor at a near-boiling temperature. The water was passed through riser pipes on each side of the rear of the reactor, then to a crossover pipe located above the reactor, and finally to a "downcomer." The water entering the downcomer cascaded downward through 30 rectangular flow channels, resulting in partial cooling. The water was discharged from the reactor building through cooling water effluent lines to the three 107-KE retention basins.

The 107-KE retention basins are three 9,000,000-gal (3.4 x 10^7L), steel, open-air tanks used to cool the water and to let short-lived radioisotopes decay prior to release to the river. The basins originally operated on a cycle system whereby one basin would be filling with effluent, a second basin would be holding the effluent for cooling and short-lived radionuclide decay, and the third basin would be draining to either the river outfall or to the 116-K-1 crib for soil column percolation (in case of a fuel cladding failure). The cycling practice, however, was abandoned shortly after 105-KE reactor startup when this method of operation caused an outfall line to float and break. The outfall lines were anchored and the basin cycling system was then changed to send the coolant effluent to two basins in parallel. The third basin was usually empty and ready to receive fuel cladding failure effluent. Average retention time in the basins was approximately 1.5 h according to the *1963 Hazards Summary Report* (GE 1964).

Under normal operations, water from the retention basins was discharged through the 1908-K outfall structure to two 84-in. (213 cm) steel pipes discharging at the center bottom of the Columbia River. In the event that the discharge pipes became inoperable, the overflow from the outfall structure discharged directly to the shore of the river through a concrete-lined emergency spillway. The emergency spillway was seldom used. During the years of reactor operation, there were frequent ruptures of the fuel cladding while fuel elements were in the process tubes. When this occurred, the cooling water effluent became significantly contaminated and was diverted to the 116-K-2 trench.

2.1.4.2 Reactor Process Liquid Wastes and Cooling Water Effluent. The cooling water became irradiated while in the reactor by three mechanisms:

- The high neutron flux in the reactor activated elements in the cooling water and created radioisotopes such as ^{41}Ca, ^{51}Cr, and ^{65}Zn. Most of those radioisotopes are relatively short-lived and have since decayed to negligible levels except for ^{41}Ca.

- Activation products from the piping, other reactor components, and fuel cladding were picked up by the cooling water. Significant radioisotopes included ^{3}H, ^{14}C, ^{60}Co, ^{63}Ni, ^{152}Eu, ^{154}Eu and ^{155}Eu.

- Fuel element fission products such as ^{90}Sr and ^{137}Cs and transuranics such as $^{239/240}Pu$ were introduced into the cooling water during fuel-cladding failures. Concentrations of radionuclides in the reactor cooling water were low during normal operations.

The contaminated effluent containing debris from a fuel cladding failure was diverted to a 4,100-ft (1,250-m) long trench, 116-K-2, which replaced the 116-K-1 crib in 1955. The 116-K-1 crib was reportedly used only once since it failed to percolate.

Discharges in addition to the contaminated effluent discharged into the 116-K-2 trench included retention basin leaks, which released cooling water to the area in and around the basins, lines, and flood plain at a rate as high as 10,000 to 20,000 gal/min (63 to 126 L/s). During reactor operations, evidence of water pooling on the ground adjacent to the retention basins was frequently noted (Dorian and Richards 1978). Effluent water in the basins also leaked through the valves into the lines which drained to the trench, causing the trench to fill and sometimes overflow.

2.1.4.3 Miscellaneous Radioactive Liquid Wastes. There were several sources of radioactive liquid waste in addition to the reactor cooling water system. These miscellaneous wastes were disposed to small cribs and drains as well as to the 116-K-2 trench by the reactor cooling water effluent piping. Miscellaneous liquid radioactive wastes combined with cooling water effluent include:

- Radioactive wastes generated by research and development activities (reactor loop studies) in the 1706-KE and 1706-KER buildings and disposed in the 116-KE-2 trench

- Water from the hot water system, circulated through process tubes during reactor downtimes

- Cooling water system cleaning waste, consisting of a diatomaceous earth slurry used to scour the corrosive film from the reactor piping and tubes.

During reactor operation and shutdowns, large quantities of decontamination solutions were used routinely to remove radionuclides from facility equipment and

surfaces. Known decontamination solutions included chromic, citric, oxalic, nitric and sulfamic acids, and fluoride. Reportedly other chemicals, including organic solvents, were also pumped through the cooling water effluent system. The majority of these decontaminant solutions were disposed to the 116-K-2 trench.

2.1.4.4 Radioactive Sludge. Large volumes of radioactive sludge were generated during reactor operations and accumulated in the cooling water effluent system pipes, in the 105-K fuel storage basins, in the 107-K retention basins, and in water traps located in the 115-K gas treatment facilities.

Sludges generally consisted of fine particulate matter which originated from dissolved and suspended solids in the river water, pipe slag, dust, failed fuel elements, and other undefined solids. The sludge was contaminated with radionuclides and various chemicals.

2.1.4.5 Herbicide Use. During a 1990 site visit to the 100-K Area, it was reported that herbicides had been used to control vegetation growth. According to past employees, herbicides were not used much during operating years because problem areas were remediated by scraping and adding topsoil. In the 1970s, herbicides and ground sterilants were used for both ground and aerial applications.

2.1.5 Decontamination and Deactivation

Although the area continues to be used, some of the 100-K Area facilities have undergone initial stages of decontamination and deactivation. The success of past decontamination and deactivation efforts using current standards and future contaminant potential has not been addressed in this work plan. However, such an evaluation will be part of the RI and may, in the future, become an integral part of the RI/FS process.

After reactor shutdown in the early 1970s, efforts were undertaken to control airborne radioactivity and to protect wildlife and plants from contacting contaminants. Examples of these efforts included

- Covering bottom and sides of the northeast end of 116-K-2 to prevent access by wildlife

- Installing a 2-in. (5-cm) water line to supply water to the southwest end of 116-K-2 trench. The water supply was designed to keep the trench covered with water to prevent airborne transport of radionuclides
- Backfilling 116-K-2 trench to grade
- Patching observable leaks in 107-K retention basins
- Installing various devices (whistles, vibrators, screens) in and near the 107-K basins to minimize attractive nuisance problems with wildlife
- Decontaminating 107-K retention basin walls and covering the floors with 2 ft (0.6 m) of dirt
- Covering of the bottom and sides of the 116-K-1 crib with dirt.

2.1.6 Interactions with Other Operable Units

As shown in Figure 1-2, the 100-KR-1 operable unit is bordered on the southeast by the 100-KR-2 operable unit. In general, the waste sites and structures in 100-KR-1 are outside the actual operating facilities; 100-KR-2 contains reactor and reactor support facilities; and 100-KR-3 contains the water treatment activities. It should be noted that, due to the length of the 116-K-2 crib and resultant impact to ground and surface water, the 100-KR-1 operable unit extends more than 1 mi (1.6 km) downriver from the reactors.

The RI/FS activities are for 100-KR-1 and 100-KR-4 operable units. Where possible, activities will be coordinated to increase efficiency and cost effectiveness. Major RI/FS activities for the 100-KR-2 and 100-KR-3 units will be implemented later according to the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989). Information gained from the 100-KR-1 RI/FS work will benefit activities in adjacent units.

2.1.7 RCRA Site Interactions

According to Appendix B of the action plan of the agreement, the 100-K Area has a facility (1706-KE) that treats RCRA waste in a waste accumulation tank, an ion exchange column, a solidification unit (evaporator) and condensate tank (Ecology et

al. 1989). However, according to Appendix C of the action plan, none of the listed past-practice waste disposal units at the 100-K Area have been assigned corrective action authority under RCRA, but they have been designated CERCLA past practice units.

2.2 PHYSICAL SETTING

2.2.1 Topography

The 100-KR-1 operable unit is located southwest of the Columbia River under a gently sloping bench. This reach of the river is within the structural and topographic feature known as the Pasco Basin. The reactor unit is 500 to 1,000 ft (150 to 300 m) from the Columbia River. Ground elevation at the site varies from 400 to 500 ft (120 to 150 m) above mean sea level.

The land surface slope averages 100 ft/mi (49 m/km) toward the northwest to the boundary of the 100-KR-1 operable unit. Just north of the 107-K retention basins the slope steepens with a drop in the land surface of about 40 ft (12 m), to a river terrace that lies 10 to 15 ft (3 to 5 m) above the typical water level of the river. In this area, the average water surface elevation of the river is about 395 ft (120 m) above mean sea level (USGS 1986a). Topography for the 100-K Area and vicinity is shown in Plate 1.

2.2.2 Geology

This section discusses regional and site geology. The regional discussion covers the general geology of the Pasco Basin and Hanford Site. Site geology covers the 100-K Area and its immediate vicinity.

2.2.2.1 Regional Geology. The geology of the Pasco Basin has been studied extensively in recent years, primarily for the Basalt Waste Isolation Project and other facility siting studies (e.g., Liikala et al. 1988). A summary of this existing work pertinent to the region of the 100 Areas is presented.

2.2.2.1.1 Stratigraphy of the Hanford Site. The Hanford Site lies in the Columbia Plateau, which is a broad plain formed by the Miocene Columbia River Basalt Group between the Cascade Mountains to the west and the Rocky Mountains to

the east. In the central and western parts, the basalt is underlain predominantly by Tertiary continental sedimentary rocks and overlain by late Tertiary and Quaternary fluvial and glaciofluvial deposits. A generalized geologic cross section of the Hanford Site is shown in Figure 2-4. The principal geologic units beneath the Hanford Site are, in ascending order: the Columbia River Basalt Group with interbeds of the Ellensburg Formation; the Ringold Formation; and the Hanford formation. In some portions of the Hanford Site, a Plio-Pleistocene unit occurs between the Ringold and Hanford formations, but this unit is apparently absent north of the Gable Butte/Gable Mountain structure. Locally, Pleistocene/Holocene alluvium, colluvium, and eolian deposits veneer the surface. A summary of the stratigraphic units present in the Pasco Basin is shown in Figure 2-5.

2.2.2.1.2 Columbia River Basalt Group. The tholeiitic flood basalts of the Columbia River Basalt Group form the bedrock of the Pasco Basin. This thick sequence of basalt was formed between 6 and 17 million years before present when large flows of lava erupted from fissures in the southeastern portion of the Columbia Plateau. The Columbia River Basalt Group is subdivided into five formations (Ledgerwood et al. 1978; Swanson et al. 1979) and consists of more than 42,000 mi^3 (174,000 km^3) of basalt covering more than 64,000 mi^2 (166,000 km^2) (Tolan et al. 1987). Beneath the Pasco Basin, this basalt sequence may be as much as 14,000 ft (4,267 m) thick. Flows of the Columbia River Basalt Group are interbedded with and overlain by Miocene-Pliocene epiclastic and volcaniclastic sediments of the Ellensburg formation (Swanson et al. 1979).

2.2.2.1.3 Ringold Formation. Following cessation of the Columbia River Basalt volcanism, sediments of the Ringold Formation accumulated in the Pasco Basin. The sediments were deposited between 8.5 and 3.7 million years before present in a fluvial/flood plain environment (Myers et al. 1979) to reach a thickness of more than 1,200 ft (366 m). The Ringold Formation overlies the Columbia River Basalt throughout most of the Hanford Site.

Within the Pasco Basin, the Ringold Formation has been classified into three stratigraphic section types (Tallman et al. 1981). The distribution of these section types is shown in Figure 2-6 and their descriptions summarized on Figure 2-7. Section Type I, located throughout the central Pasco Basin, is subdivided into four textural units: (1) sand and gravel of the basal Ringold unit; (2) clay, silt, and fine sand with minor gravel lenses of the lower Ringold unit; (3) occasionally cemented sand and gravel of the middle Ringold unit; and (4) silt and fine sand of the upper Ringold unit (Tallman et al. 1981). The section Type I is not thought to be present beneath the 100-K Area. Section Type II consists of predominantly silt, sand, and

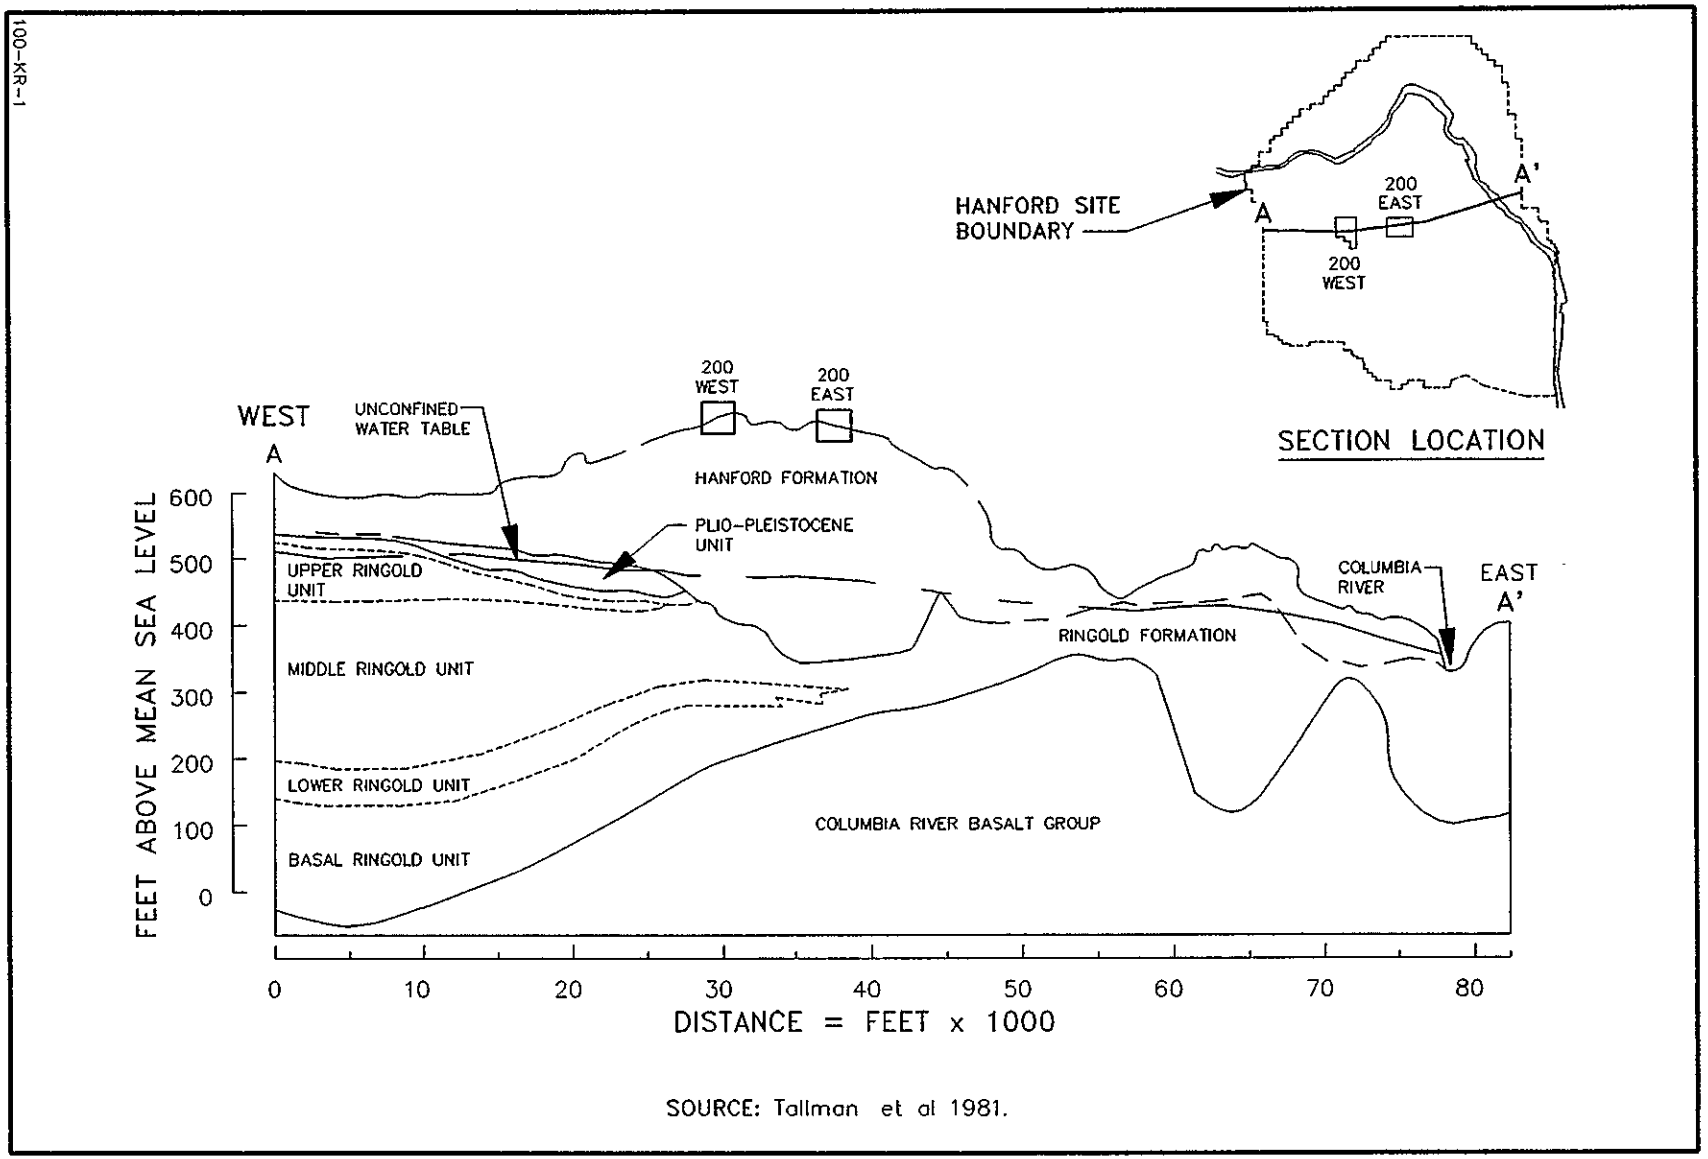

SOURCE: Tallman et al 1981.

Figure 2-4. Generalized Geologic Cross Section of the Hanford Site.

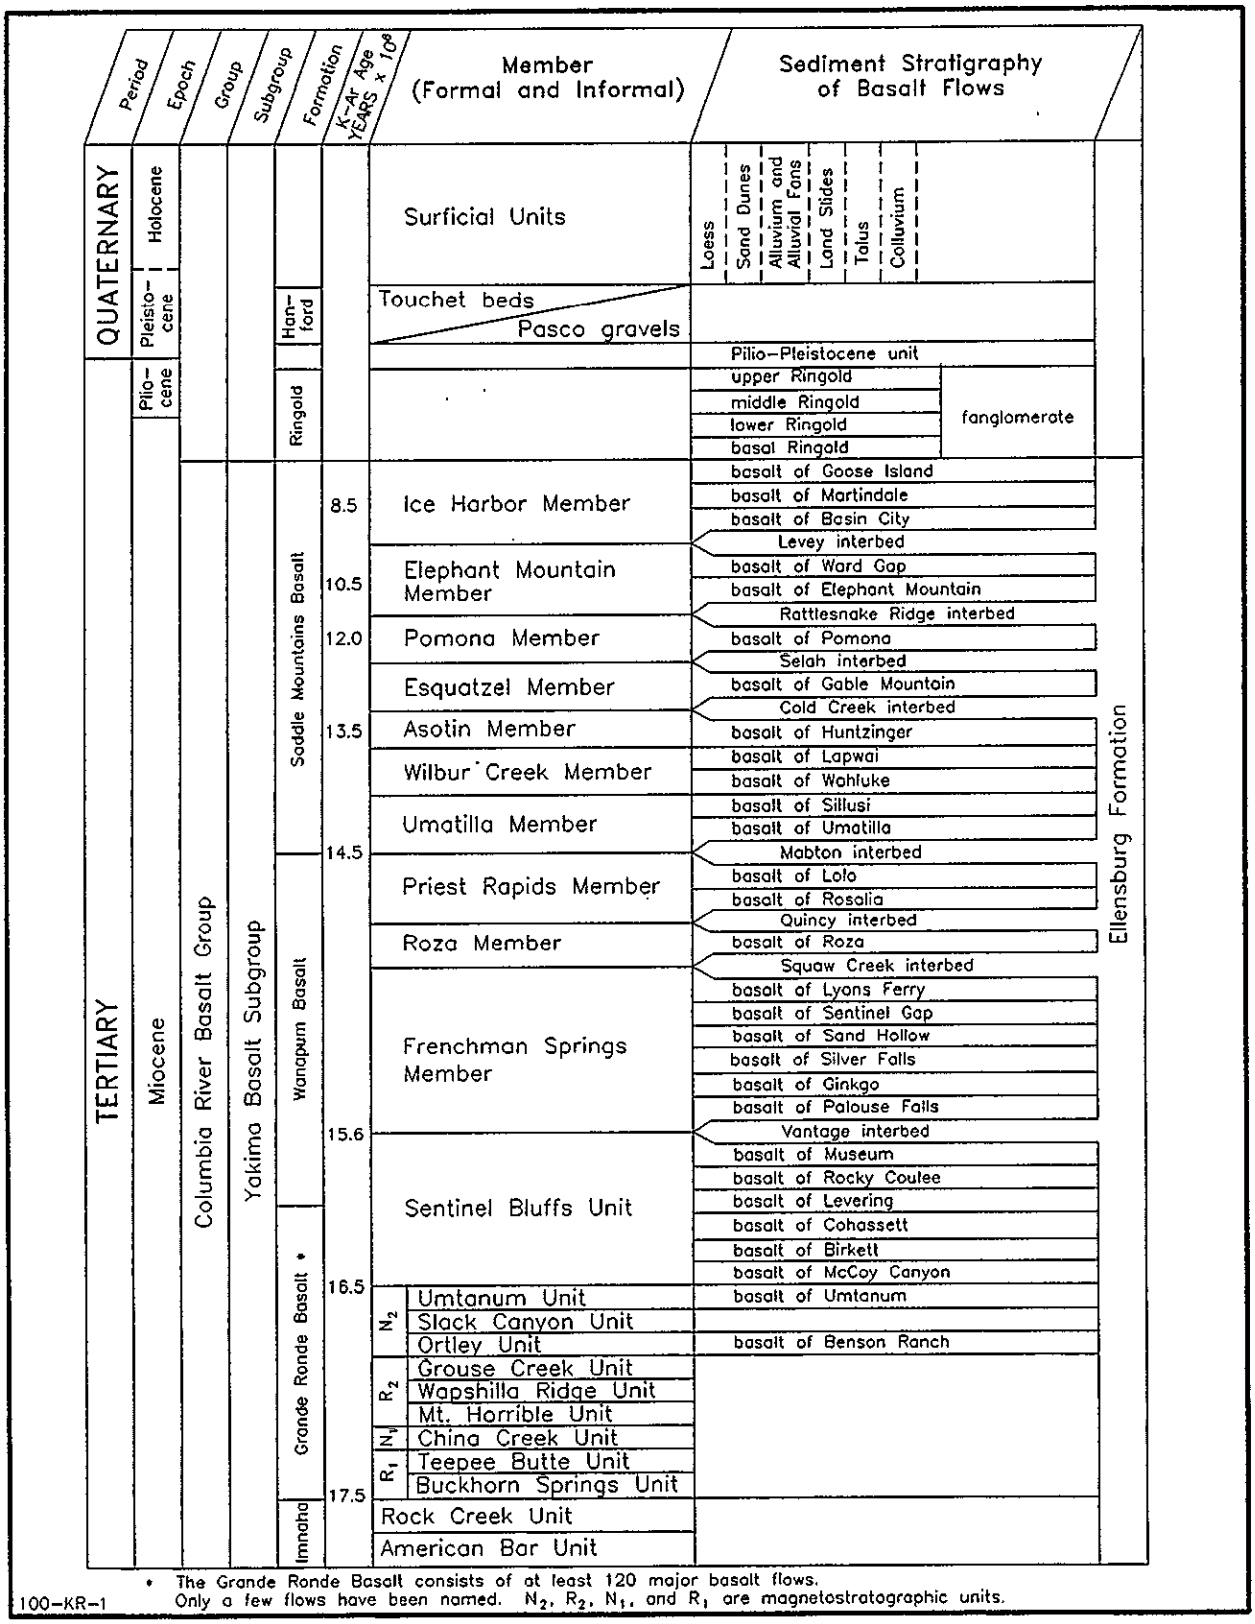

* The Grande Ronde Basalt consists of at least 120 major basalt flows. Only a few flows have been named. N_2, R_2, N_1, and R_1 are magnetostratographic units.

Figure 2-5. Summary of Stratigraphic Units in the Pasco Basin.

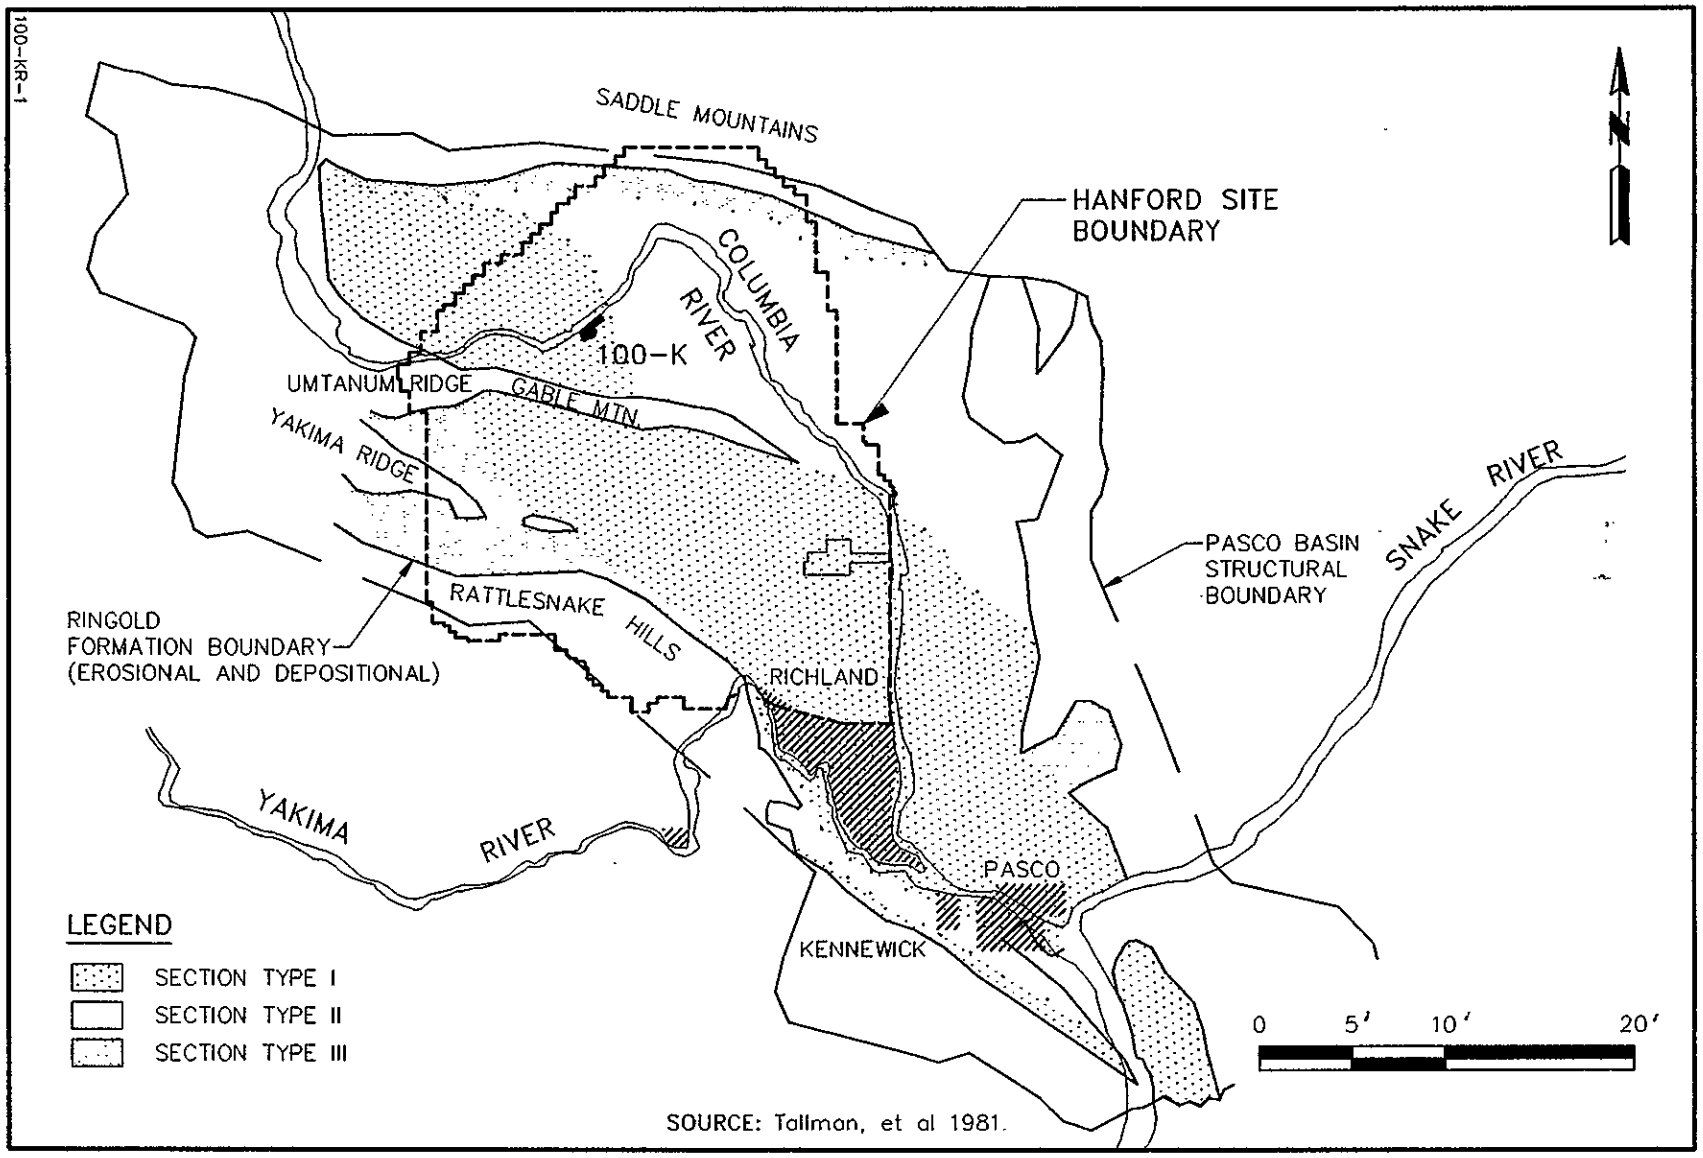

Figure 2-6. Distribution of The Ringold Formation Section Types.

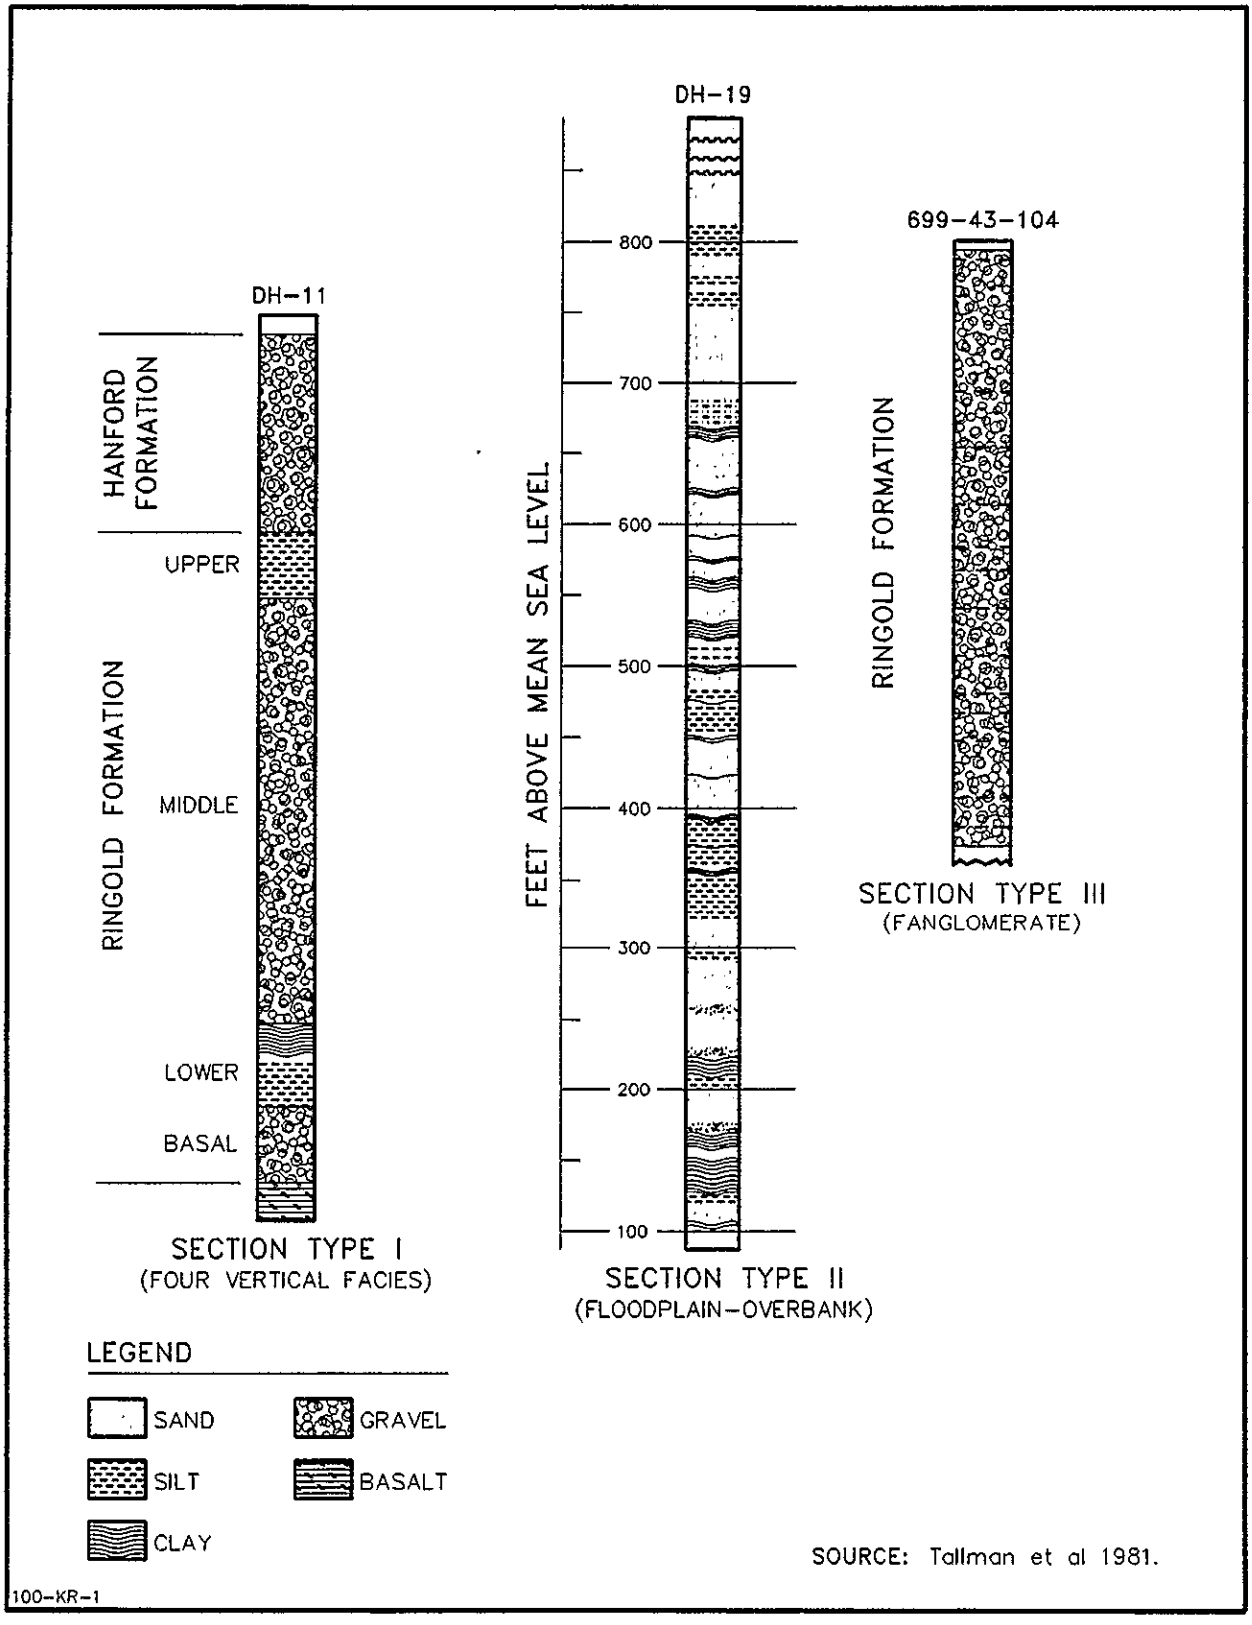

Figure 2-7. Ringold-Type Facies at the Hanford Site and Vicinity (after Tallman et al. 1981).

clay with minor gravel lenses, and is found north and east of Gable Mountain. Section Type III is composed of talus, slope wash, and sidestream deposits that are along the flanks of anticlinal ridges and interfinger with the central basin deposits.

2.2.2.1.4 Hanford Formation. The Hanford formation (an informal geologic unit) lies unconformably on the eroded surface of the Ringold Formation, and locally, the basalt bedrock. The Hanford formation consists of cataclysmic flood sediments that were deposited when ice dams in western Montana and Idaho were breached, and massive volumes of water spilled abruptly across eastern and central Washington. The floods scoured the land surface, locally eroding the Ringold Formation, upper basalt flows, and interbeds. Thick sequences of sediments were deposited by several episodes of Pleistocene flooding, with the last major flood sequence dated about 12,000 years before present (Fecht et al. 1985).

Cataclysmic flood deposits have locally been divided into two main facies, termed the "Pasco Gravels" facies and the "Touchet Beds" facies. The Pasco Gravels facies are composed of poorly sorted gravels and coarse sand indicative of a high-energy depositional environment. The Touchet Beds facies consist of rhythmically bedded sequences of graded silt, sand, and minor gravel units (Myers et al. 1979). These sediments are limited to areas where slack-water conditions existed.

2.2.2.1.5 Surficial Deposits. Eolian sediments, consisting of loess, active and inactive sand dunes, alluvium, and colluvium, locally veneer the surface of the Hanford Site.

2.2.2.1.6 Geologic Structure. The structural geology of the Pasco Basin is illustrated on Figure 2-8. The major structural feature of the region is a sub-parallel series of west- to northwest-trending folds known as the Yakima Fold Belt. Umtanum Ridge and Cold Creek Valley west of the Site are examples of structurally controlled anticlinal ridges and synclinal valleys. Gable Butte and Gable Mountain on the Hanford Site represent the eastward extension of the Umtanum Ridge structure (Fecht 1978, p. 17). More localized information indicates that the 100-K Area site lies in Wahluke syncline, a down-warped valley between the Gable Mountain and the Saddle Mountain anticlines. The orientation of this syncline and the elevations of the top of basalt near the 100-K Area are shown on Figure 2-9 (Myers et al. 1979).

2.2.2.2 Site Geology. The geologic setting underlying the 100-K Area is based on regional data for the Pasco Basin and the Hanford Site and preliminary interpretation of geologic information from wells drilled in and adjacent to the 100-K Area. Twenty-nine wells were drilled in the 100-K Area, nine wells drilled in the adjacent

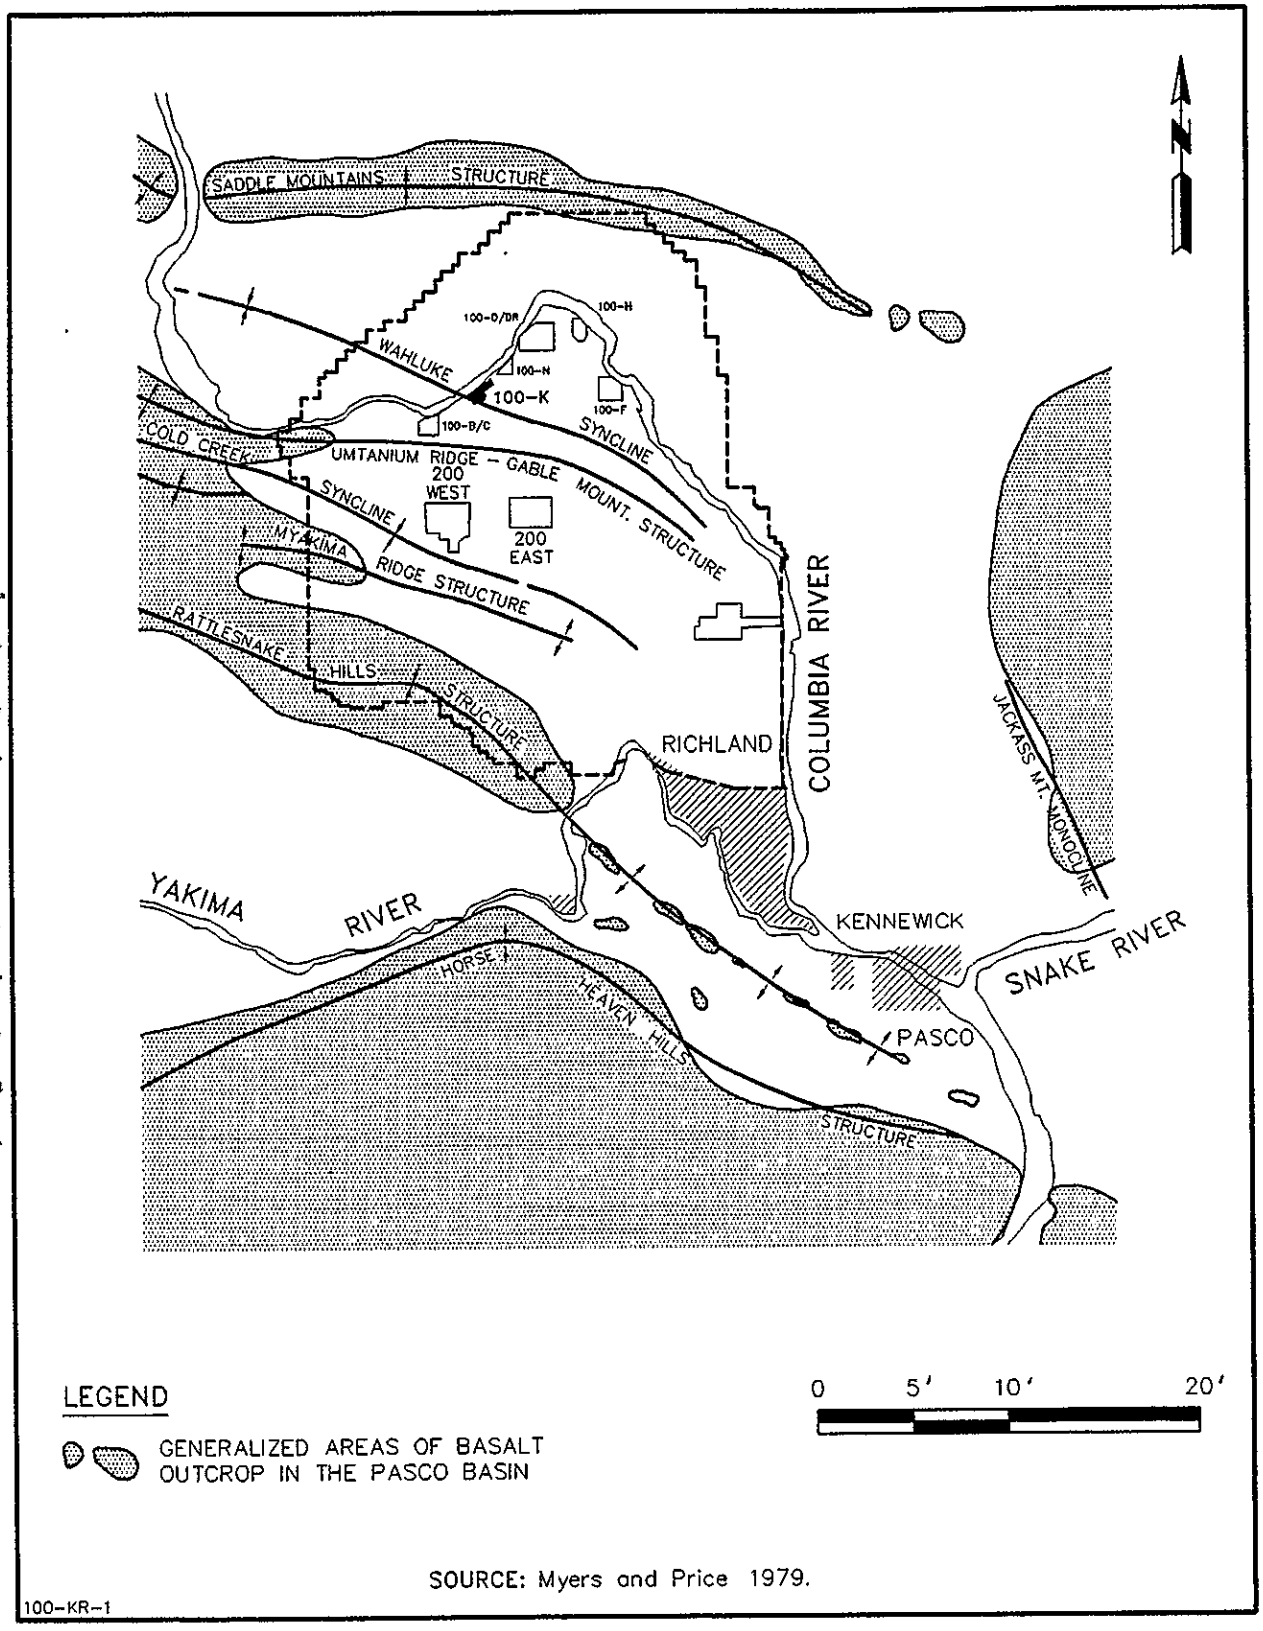

Figure 2-8. Structural Geology of the Pasco Basin.

THIS PAGE INTENTIONALLY
LEFT BLANK

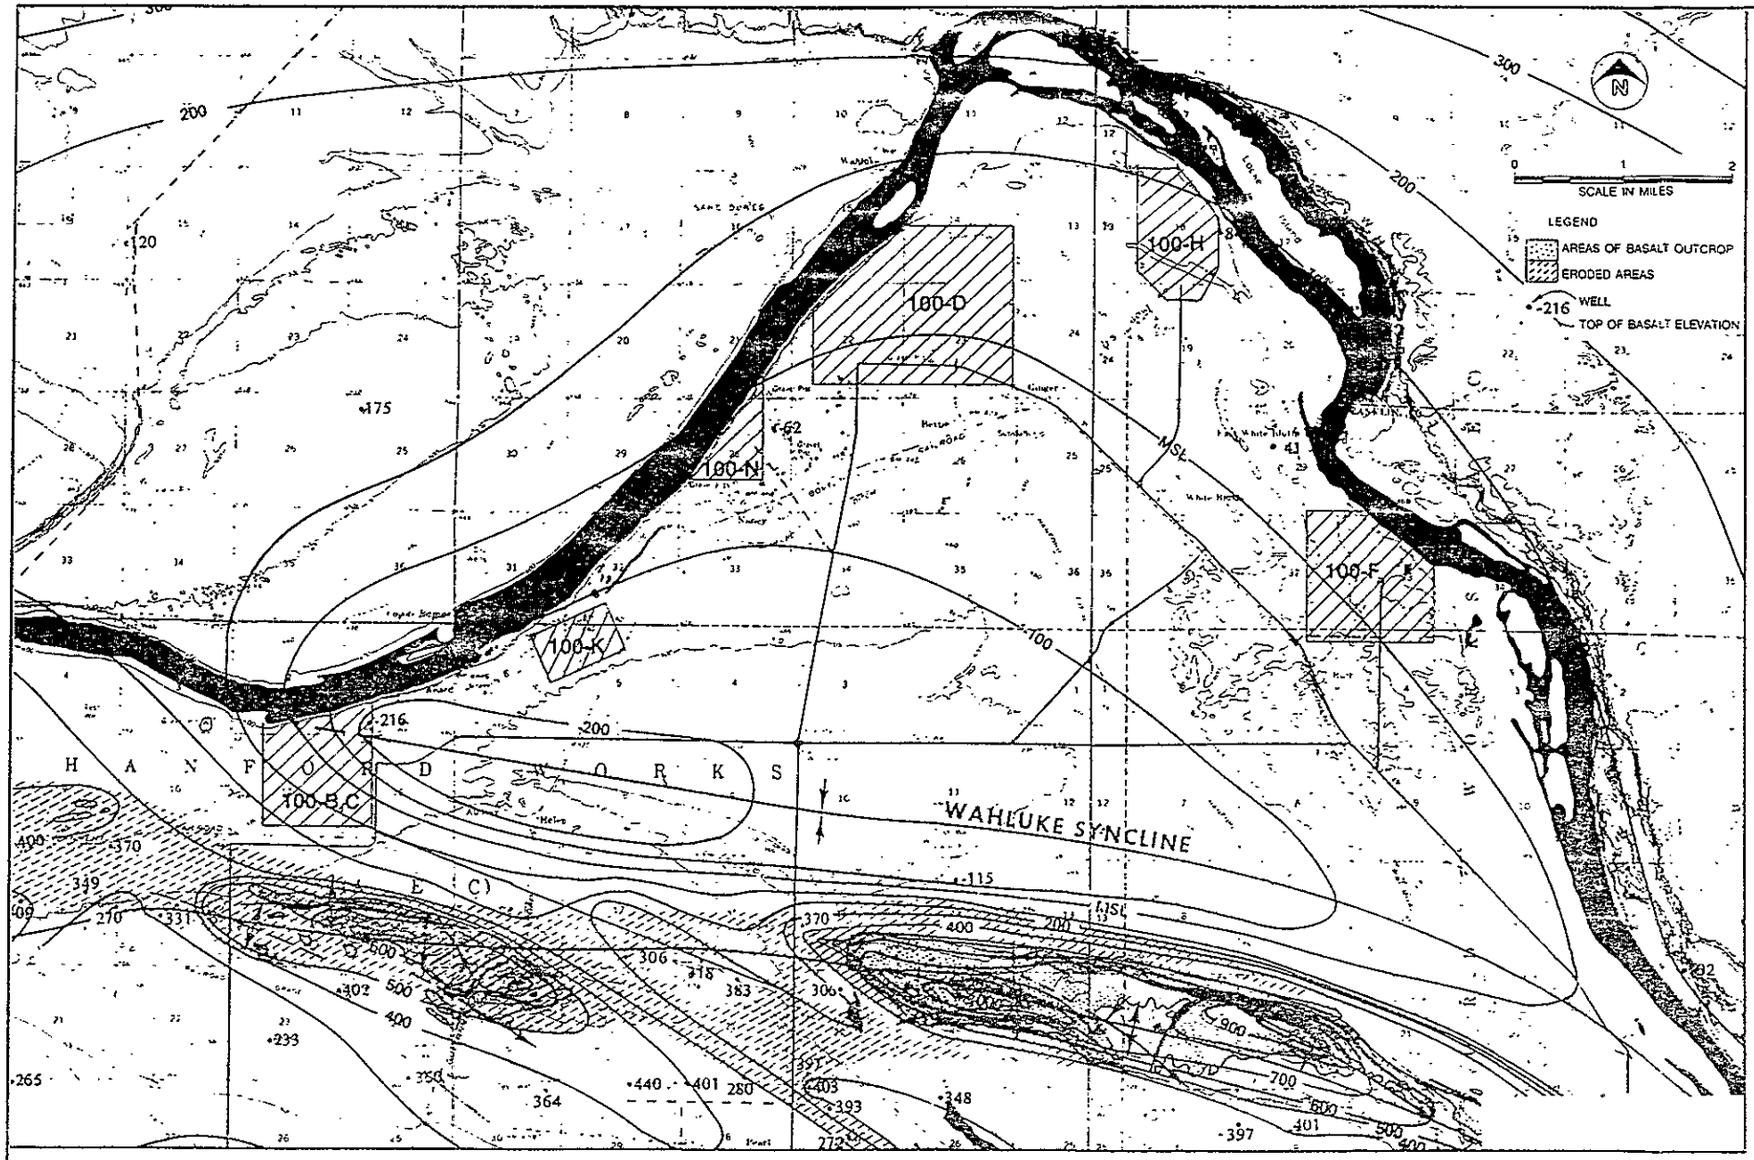

Figure 2-9. Top of Basalt Contours.

THIS PAGE INTENTIONALLY
LEFT BLANK

600 Area and one well in the 100-B/C Area. The locations of these wells are shown in Figure 2-10 (100-K Area and adjacent 600 Area) and Figure 2-11 (detail of 100-K Area). Construction information for these wells is summarized on Table 2-3.

Most of the 100-K Area wells penetrate only the uppermost portions of the geologic section, with all but five wells extending less than 100 ft (33 m) beneath ground surface. There are no drill holes in the 100-K Area which extend beyond 160 ft (53 m) below ground surface. Wells in the 600 Area are likewise limited to the upper geologic section. One exception is Well 699-81-62, which is completed in basalt at a depth of about 1,011 ft (308 m) below surface. (A handwritten note on the geologic log indicates it was deepened to 1,471 ft [748 m].) This well is located about 3,000 ft (915 m) east of the main portion of the 100-K Area. Another deep well, 199-B3-2, is located about 3,000 ft (915 m) southwest of the 100-K Area in the 100-B/C Area and is about 790 ft (240 m) deep. Information on the deeper subsurface conditions beneath the 100-K Area has been inferred primarily from these two wells. Figure 2-12 provides a graphic comparison between a centrally located 100-K Area well (199-K-10) and the two deep wells.

Well numbering conventions in the remainder of the report have been abbreviated. The full number for wells within the 100-K Area would be 199-K-#, which has been shortened K-# or K#, e.g., 199-K-1 is referred to as K1 (in some reports, the abbreviation 1-K-# has also been used). The full numbers for the wells in the 600 Area around the 100-K Area have also been shortened, e.g., 6-78-72, rather than 699-78-72.

2.2.2.2.1 Site Stratigraphy. The geology in the 100-K Area consists of three principal formations and other surficial units of interest to this site investigation. From oldest to youngest, the site stratigraphy includes the Saddle Mountains Basalt of the Columbia River Basalt Group (intercalated with the Ellensburg Formation sediments), the Ringold Formation, and the Hanford formation. Surficial deposits include river sediments and fill. Geologic cross sections, which are based on interpretation of the drillers' logs and notes, are presented on Figures 2-13 and 2-14. (The locations of the cross sections are shown on Figures 2-10 and 2-11.) These cross-sections address only the uppermost portions of the stratigraphic section (less than 200 ft [60 m] deep) because of database limitations. As mentioned previously, interpretation of the deeper stratigraphic units is based on information from two adjacent deep wells outside of the 100-K Area (Wells 6-81-62 and 199-B3-2).

THIS PAGE INTENTIONALLY
LEFT BLANK

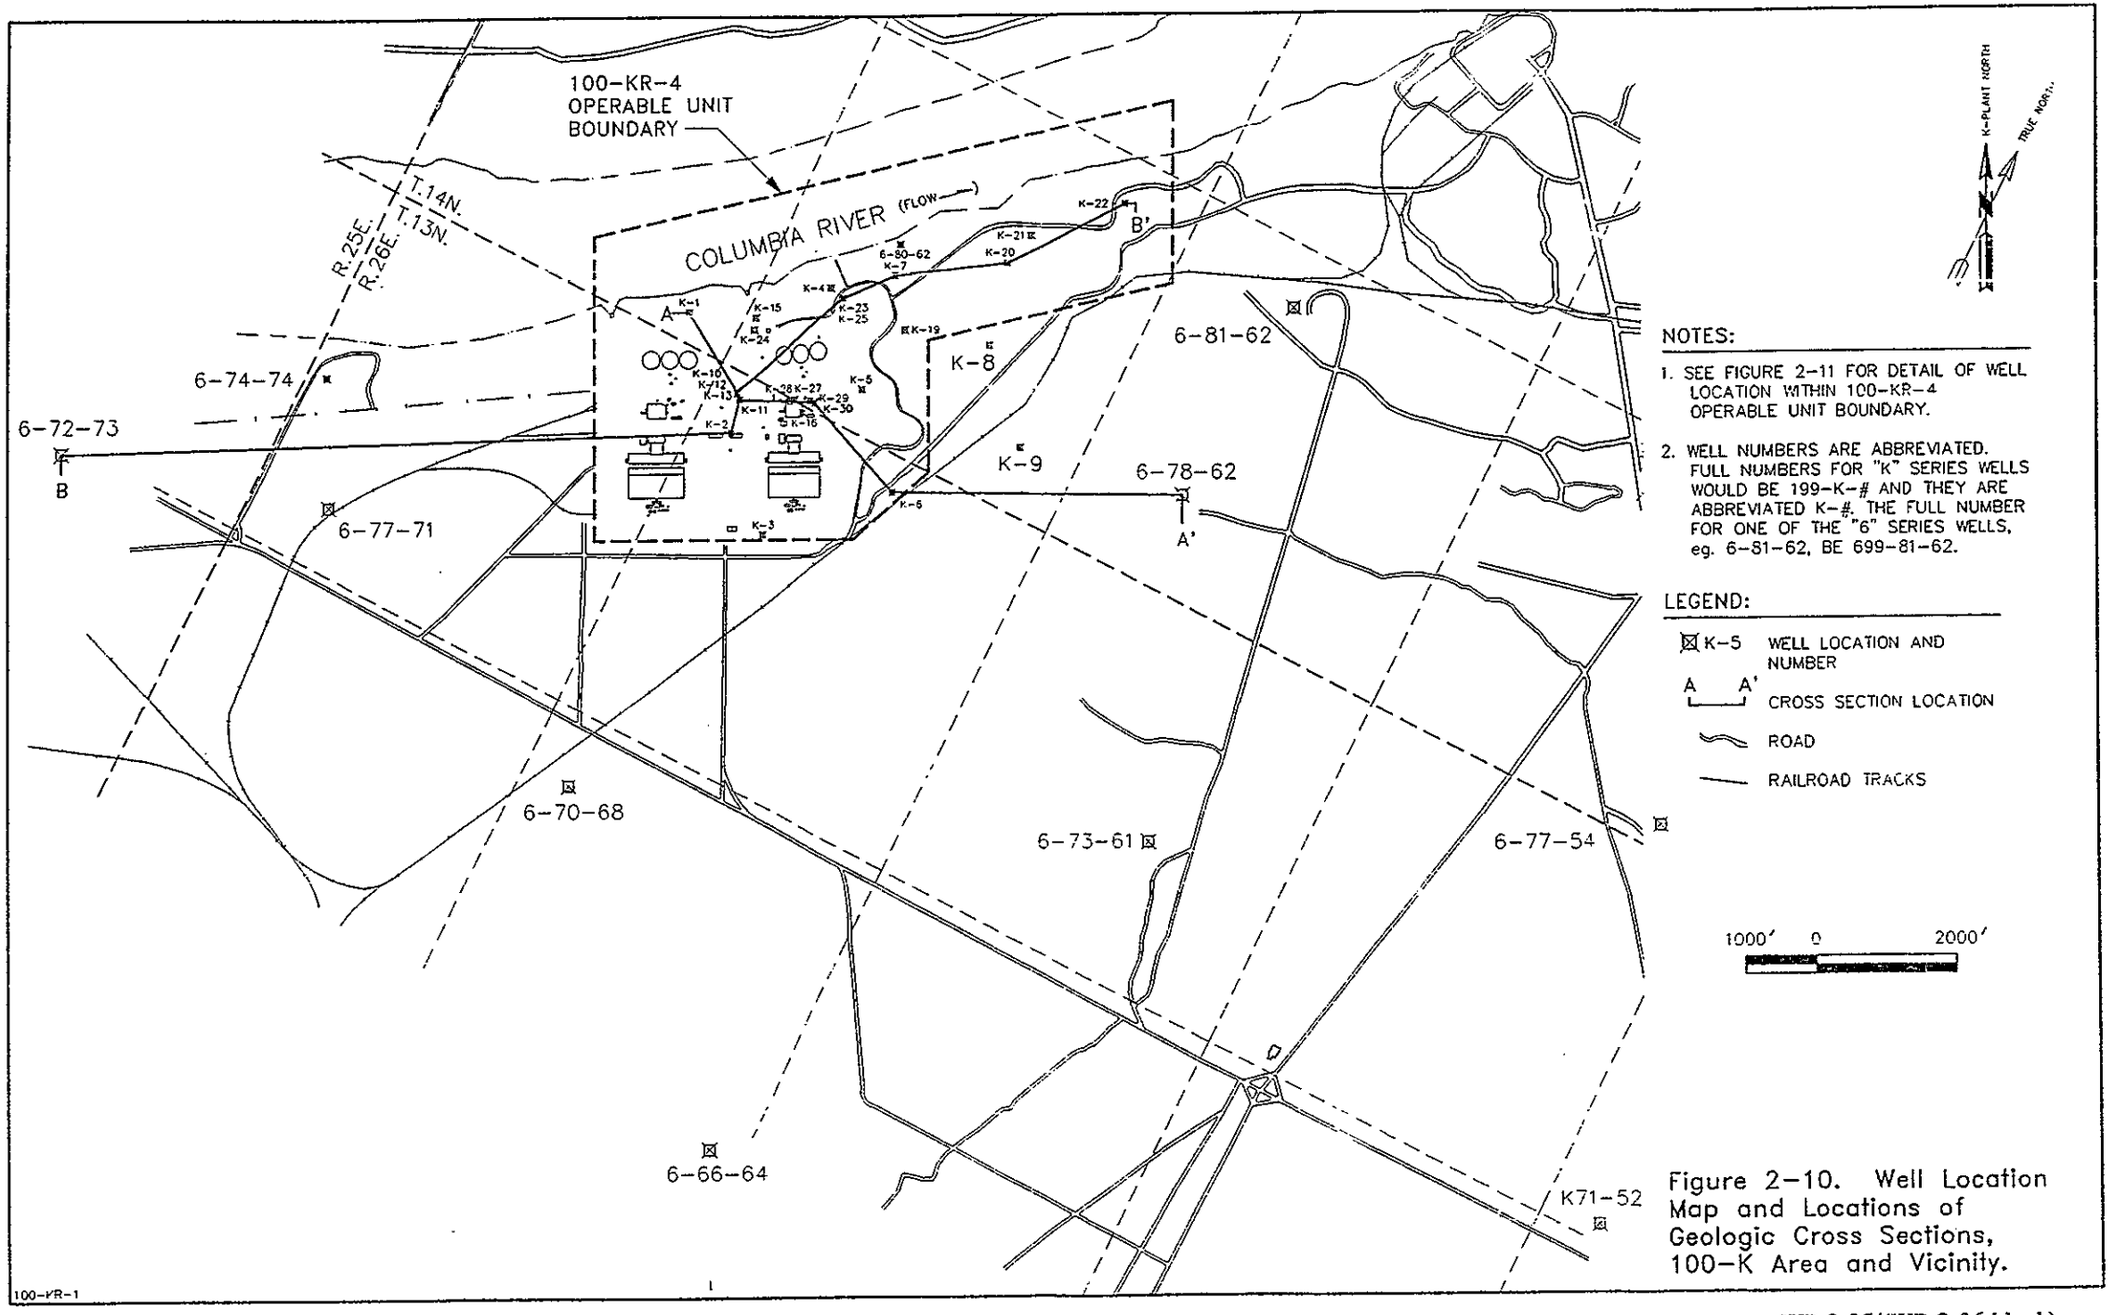

Figure 2-10. Well Location Map and Locations of Geologic Cross Sections, 100-K Area and Vicinity.

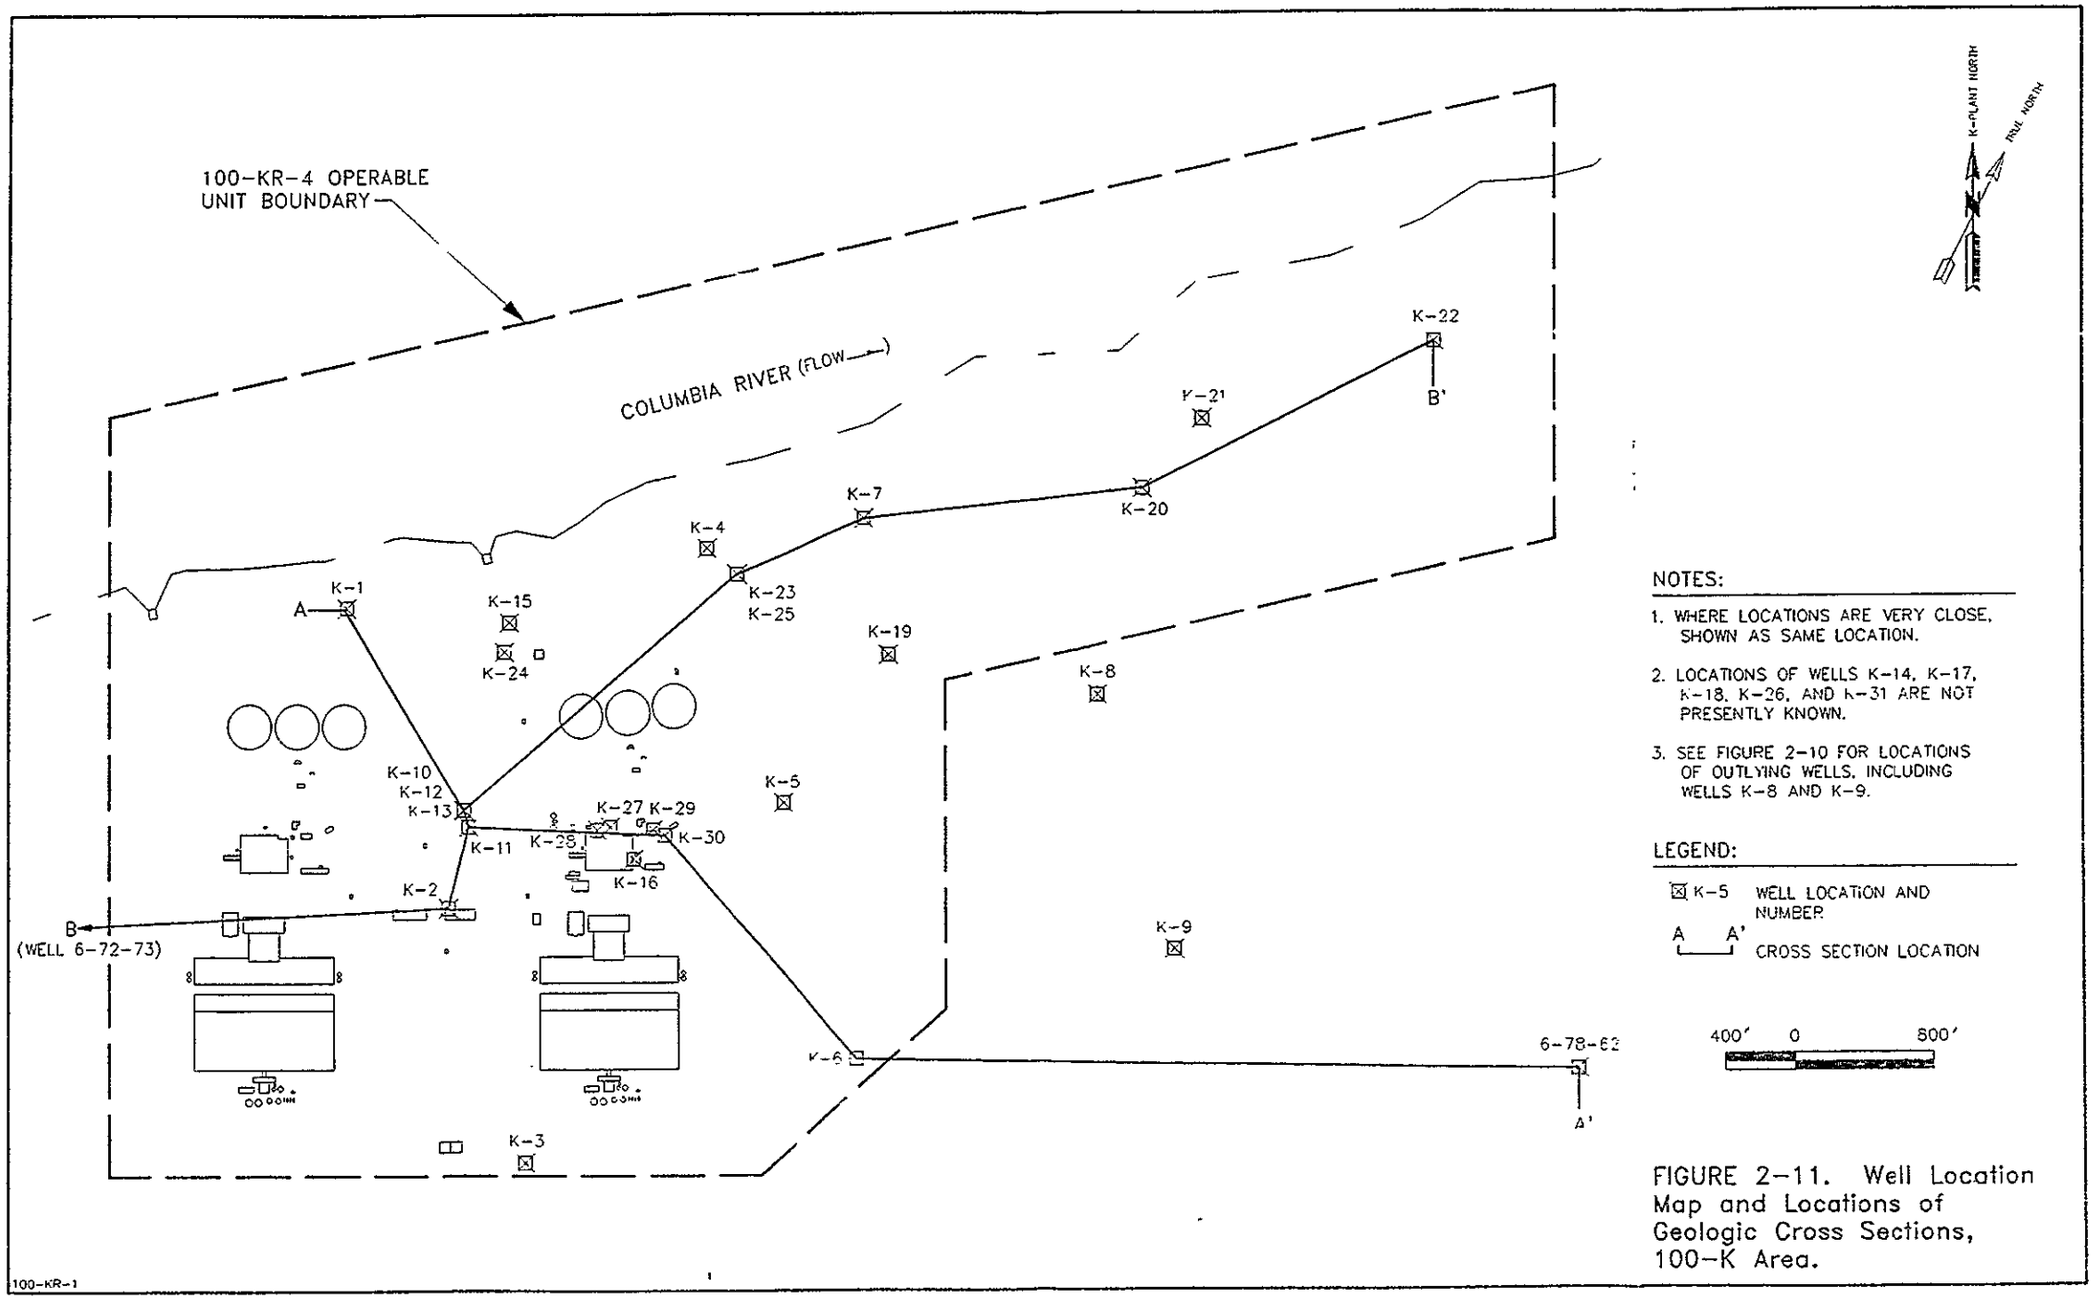

FIGURE 2-11. Well Location Map and Locations of Geologic Cross Sections, 100-K Area.

Table 2-3. Construction Information for Wells in the Vicinity of the 100-K Area.
Page 1 of 2

Well[a] Number	Hanford Coordinates[b] West	Hanford Coordinates[b] North	Casing Elevation (ft, msl)	Casing Diameter (in.)	Well Depth (ft)	Screened Interval From (ft)	Screened Interval To (ft)	Date Completed	Comments
100-KR-1 Operable Unit									
K-1[c]	69930	76800	405.00	8	107	---[d]	---	3/31/52	Casing removed
K-4	68220	78052	405.00	8	40	---	---	3/31/52	Casing removed
K-7	67480	78620	406.00	8	42	---	---	2/28/52	Casing removed
K-13	68803	76104	464.00	12	138	---	---	3/31/53	Oil in well
K-19	67000	78000	422.17	8	51	10	50	4/30/55	P-Submrsbl
K-20	66125	79500	422.57	8	48	10	50	5/31/55	P-Submrsbl
K-21	66000	80000	421.73	8	16	10	50	5/31/55	---
K-22	65000	81000	421.68	8	49	10	50	5/31/55	P-Submrsbl
K-23	68000	78000	405.00	8	25	65	80	2/28/56	---
K-24	69000	77000	467.00	8	50	---	---	12/31/52	---
K-25	68000	78000	405.00	8	76	50	75	8/31/53	---
100-KR-2 Operable Unit									
K-2	68628	75569	469.00	6	40	---	---	2/28/52	Casing removed
K-5	67175	76975	460.00	6	40	---	---	1/31/52	Casing removed
K-10	68800	76100	466.66	12	170.2	155	165	8/31/52	---
K-11[e]	68733	76030	467.66	6	170	69	160	8/31/52	P-Sub T.D. 138 ft
K-15	69050	77160	408.00	6	150	---	---	4/30/43	---
K-16	67800	76300	404.00	8	50	---	---	2/28/53	---
K-27	68000	76400	~465	6	90	65	85	9/30/79	P-Submrsbl
K-28	68060	76350	~465	6	88	63	88	9/30/79	P-Submrsbl
K-29	67775	76500	~465	6	89	65	85	9/30/79	P-Submrsbl
K-30	67700	76500	~465	6	89	---	---	10/31/79	P-Submrsbl
100-KR-3 Operable Unit									
K-3	67582	74493	495.00	6	40	---	---	8/31/52	Casing removed
K-6	66131	75889	480.00	6	40	---	---	1/31/52	Casing removed
K-12	68803	76104	466.55	6	159	118	138	9/30/52	---
600 (Background)									
K-8	65733	78371	455.00	6	40	---	---	2/28/52	Casing removed
K-9	64688	77295	470.00	8	40	---	---	2/28/52	Casing removed
6-66-64	64249	66483	505.92	6	120	96	116	6/30/72	P-Submrsbl
6-70-68	68357	70123	526.21	8	149	126	147	7/31/54	P-Submrsbl
6-72-73[e]	73222	72038	482.57	8	202	60	176	9/30/61	P-Sub T.D. 133 ft
6-73-61[f]	60527	73195	531.53	8	150	107	146	9/14/62	P-Submrsbl
6-74-74	74075	73650	438.00	6	65				Collapsed(?)

Table 2-3. Construction Information for Wells in the Vicinity of the 100-K Area.
Page 2 of 2

Well[a] Number	Hanford Coordinates[b] West	North	Casing Elevation (ft, msl)	Casing Diameter (in.)	Well Depth (ft)	Screened Interval From (ft)	To (ft)	Date Completed	Comments
6-78-62[e]	62300	77750	469.88	8	150	70	120	5/31/57	P-Sub T.D. 109 ft
6-80-62	62000	81900	440.00	---	---	---	---	---	---
6-81-62	62072	80813	441.46	2	1011[g]	1280	1322	3/31/73	---
B/C Area									
B3-2	71752	78818	442.59	8	790	635	645	8/53	Deep-Basalt
Wells Not Currently Located by Coordinates									
K-14	---	---	469	---	---	---	---	---	---
K-17	---	---	406	8	75	---	---	9/53	---
K-18	---	---	409	8	60	---	---	10/54	---
K-26	---	---	464	8	55	---	---	8/53	---
K-31	---	---	---	---	---	---	---	---	

Sources:

Notes:

[a] Well numbers are abbreviated. Full numbers for "K" series wells would be 199-K-# and they are sometimes abbreviated 1-K-#. The "6" series wells, e.g., 6-81-62, would be 699-81-62.

[b] Well locations are shown on Figure 2-10 and 2-11.

[c] No information is currently available for wells K14, K17, K18, K26 and K31.

[d] Dashes (---) indicate data not available.

[e] Well depth from drillers log at time of drilling. Several boreholes were sanded in at time of pump installation therefore revised depth indicated in comments column.

[f] Log for 6-73-61 originally designated as 699-74-60.

[g] A handwritten note on the geologic log indicates this well was deepened to 1,471 ft.

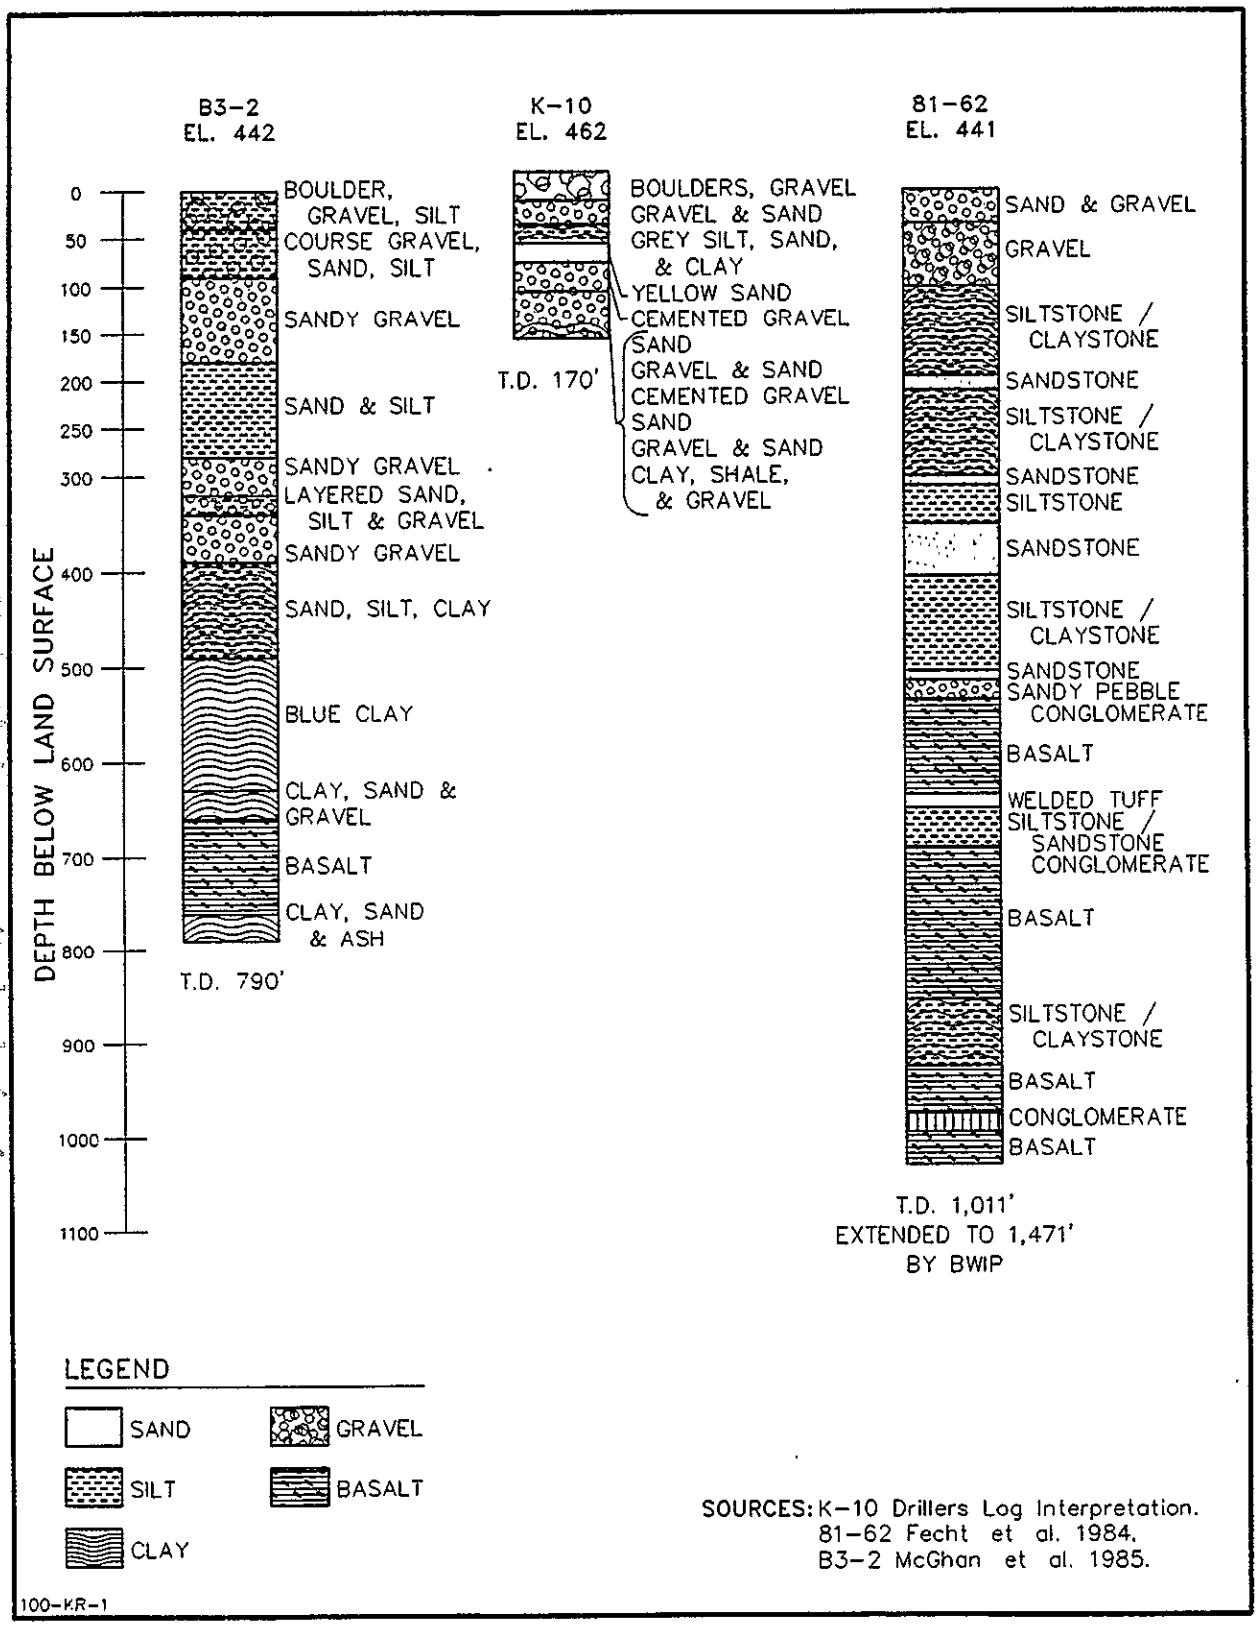

Figure 2-12. Graphic Logs for Wells K-10, 6-81-62, 199-B3-2.

THIS PAGE INTENTIONALLY
LEFT BLANK

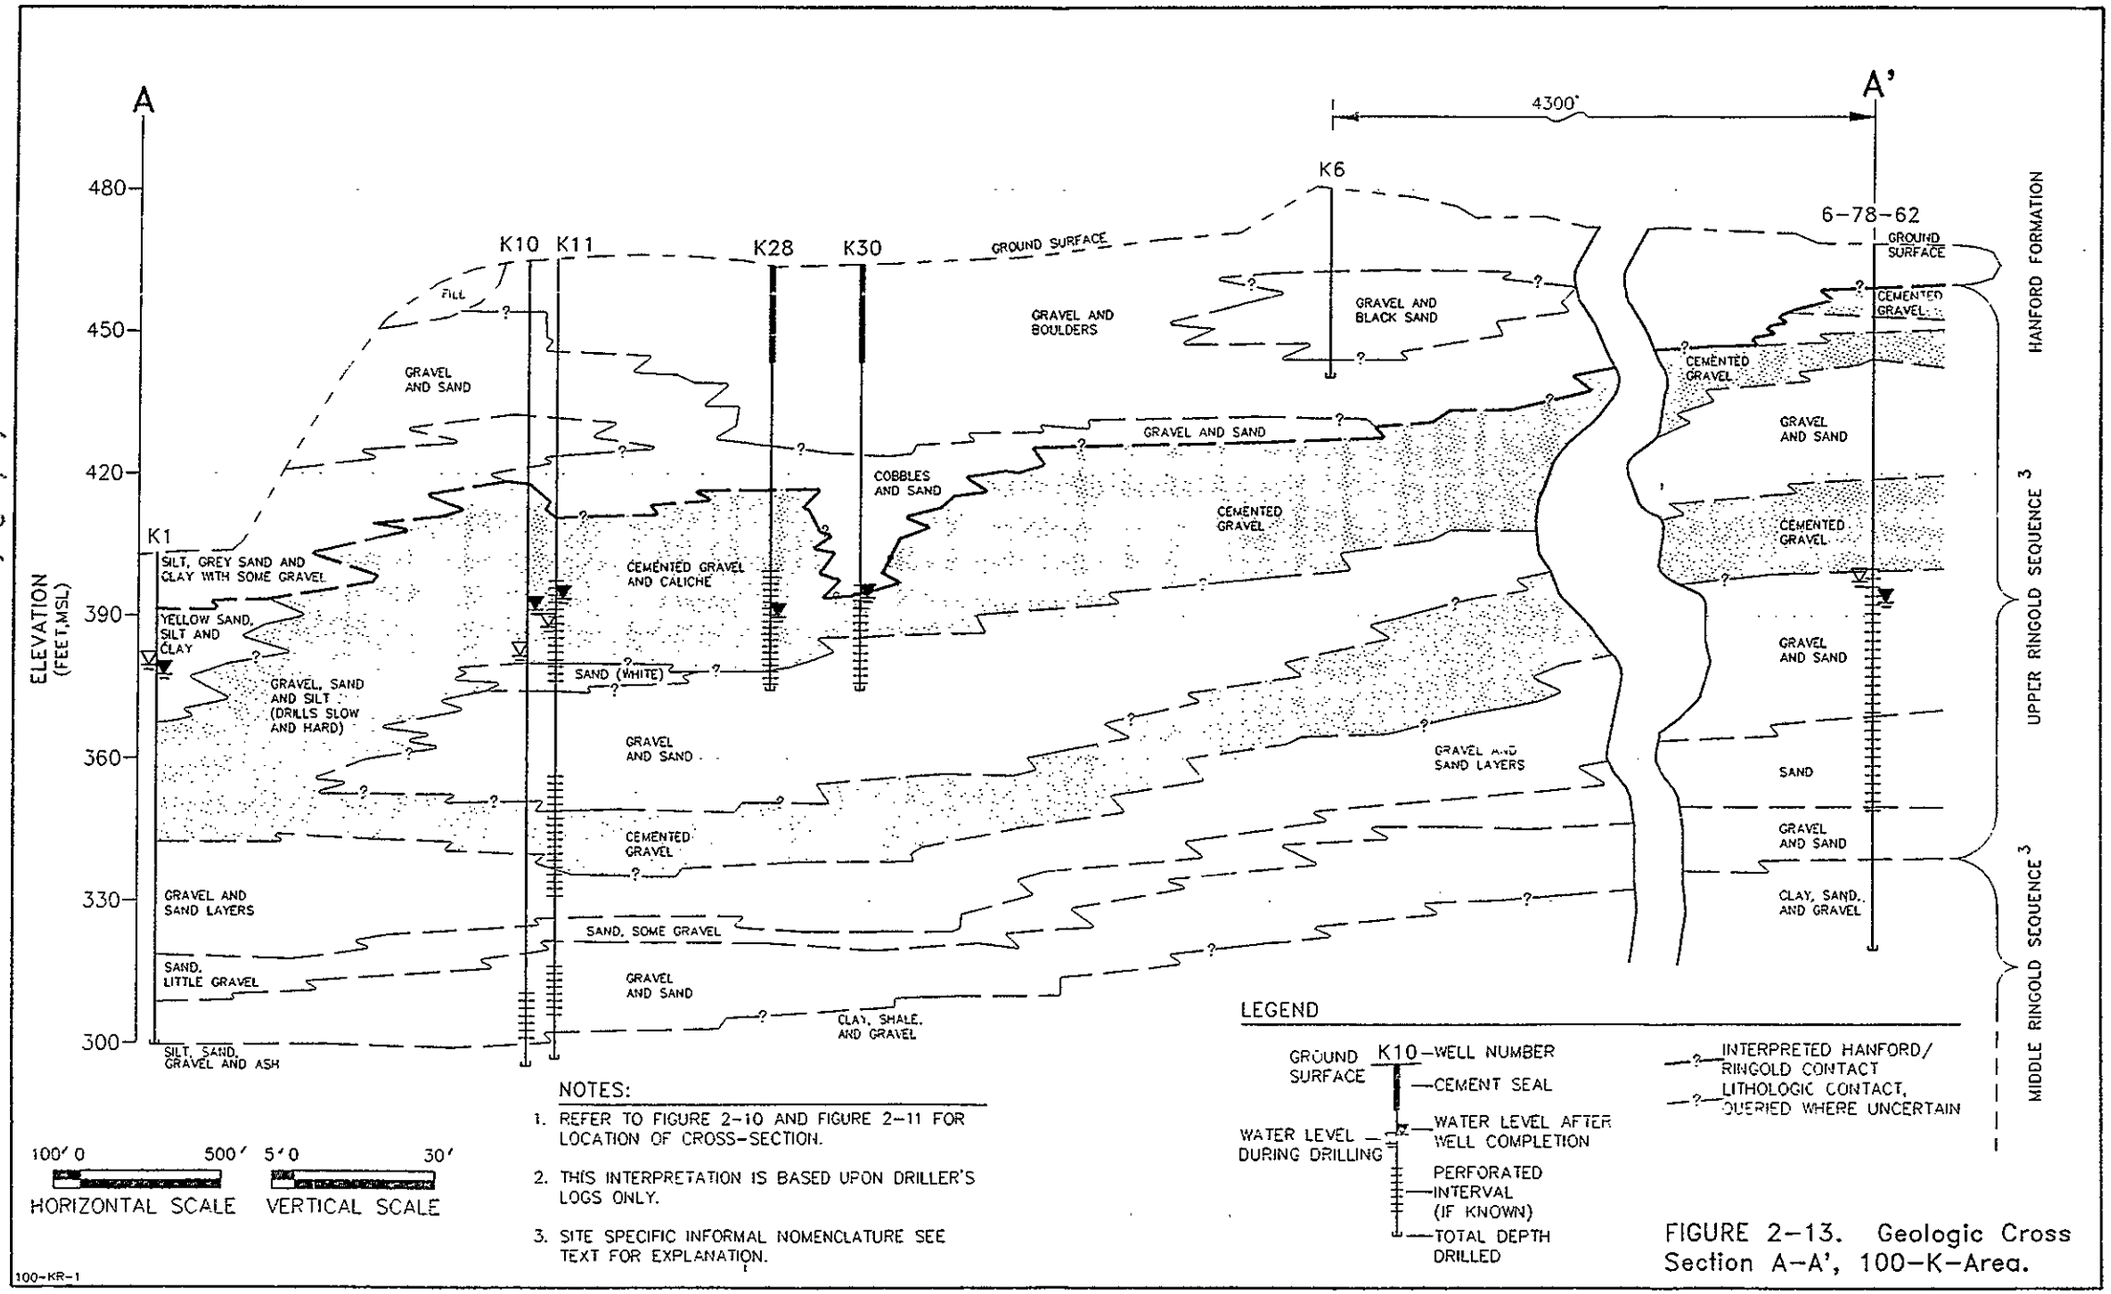

NOTES:

1. REFER TO FIGURE 2-10 AND FIGURE 2-11 FOR LOCATION OF CROSS-SECTION.
2. THIS INTERPRETATION IS BASED UPON DRILLER'S LOGS ONLY.
3. SITE SPECIFIC INFORMAL NOMENCLATURE SEE TEXT FOR EXPLANATION.

LEGEND

GROUND SURFACE — K10 — WELL NUMBER
CEMENT SEAL
WATER LEVEL DURING DRILLING — WATER LEVEL AFTER WELL COMPLETION
PERFORATED INTERVAL (IF KNOWN)
TOTAL DEPTH DRILLED
INTERPRETED HANFORD/RINGOLD CONTACT
LITHOLOGIC CONTACT, QUERIED WHERE UNCERTAIN

FIGURE 2-13. Geologic Cross Section A-A', 100-K-Area.

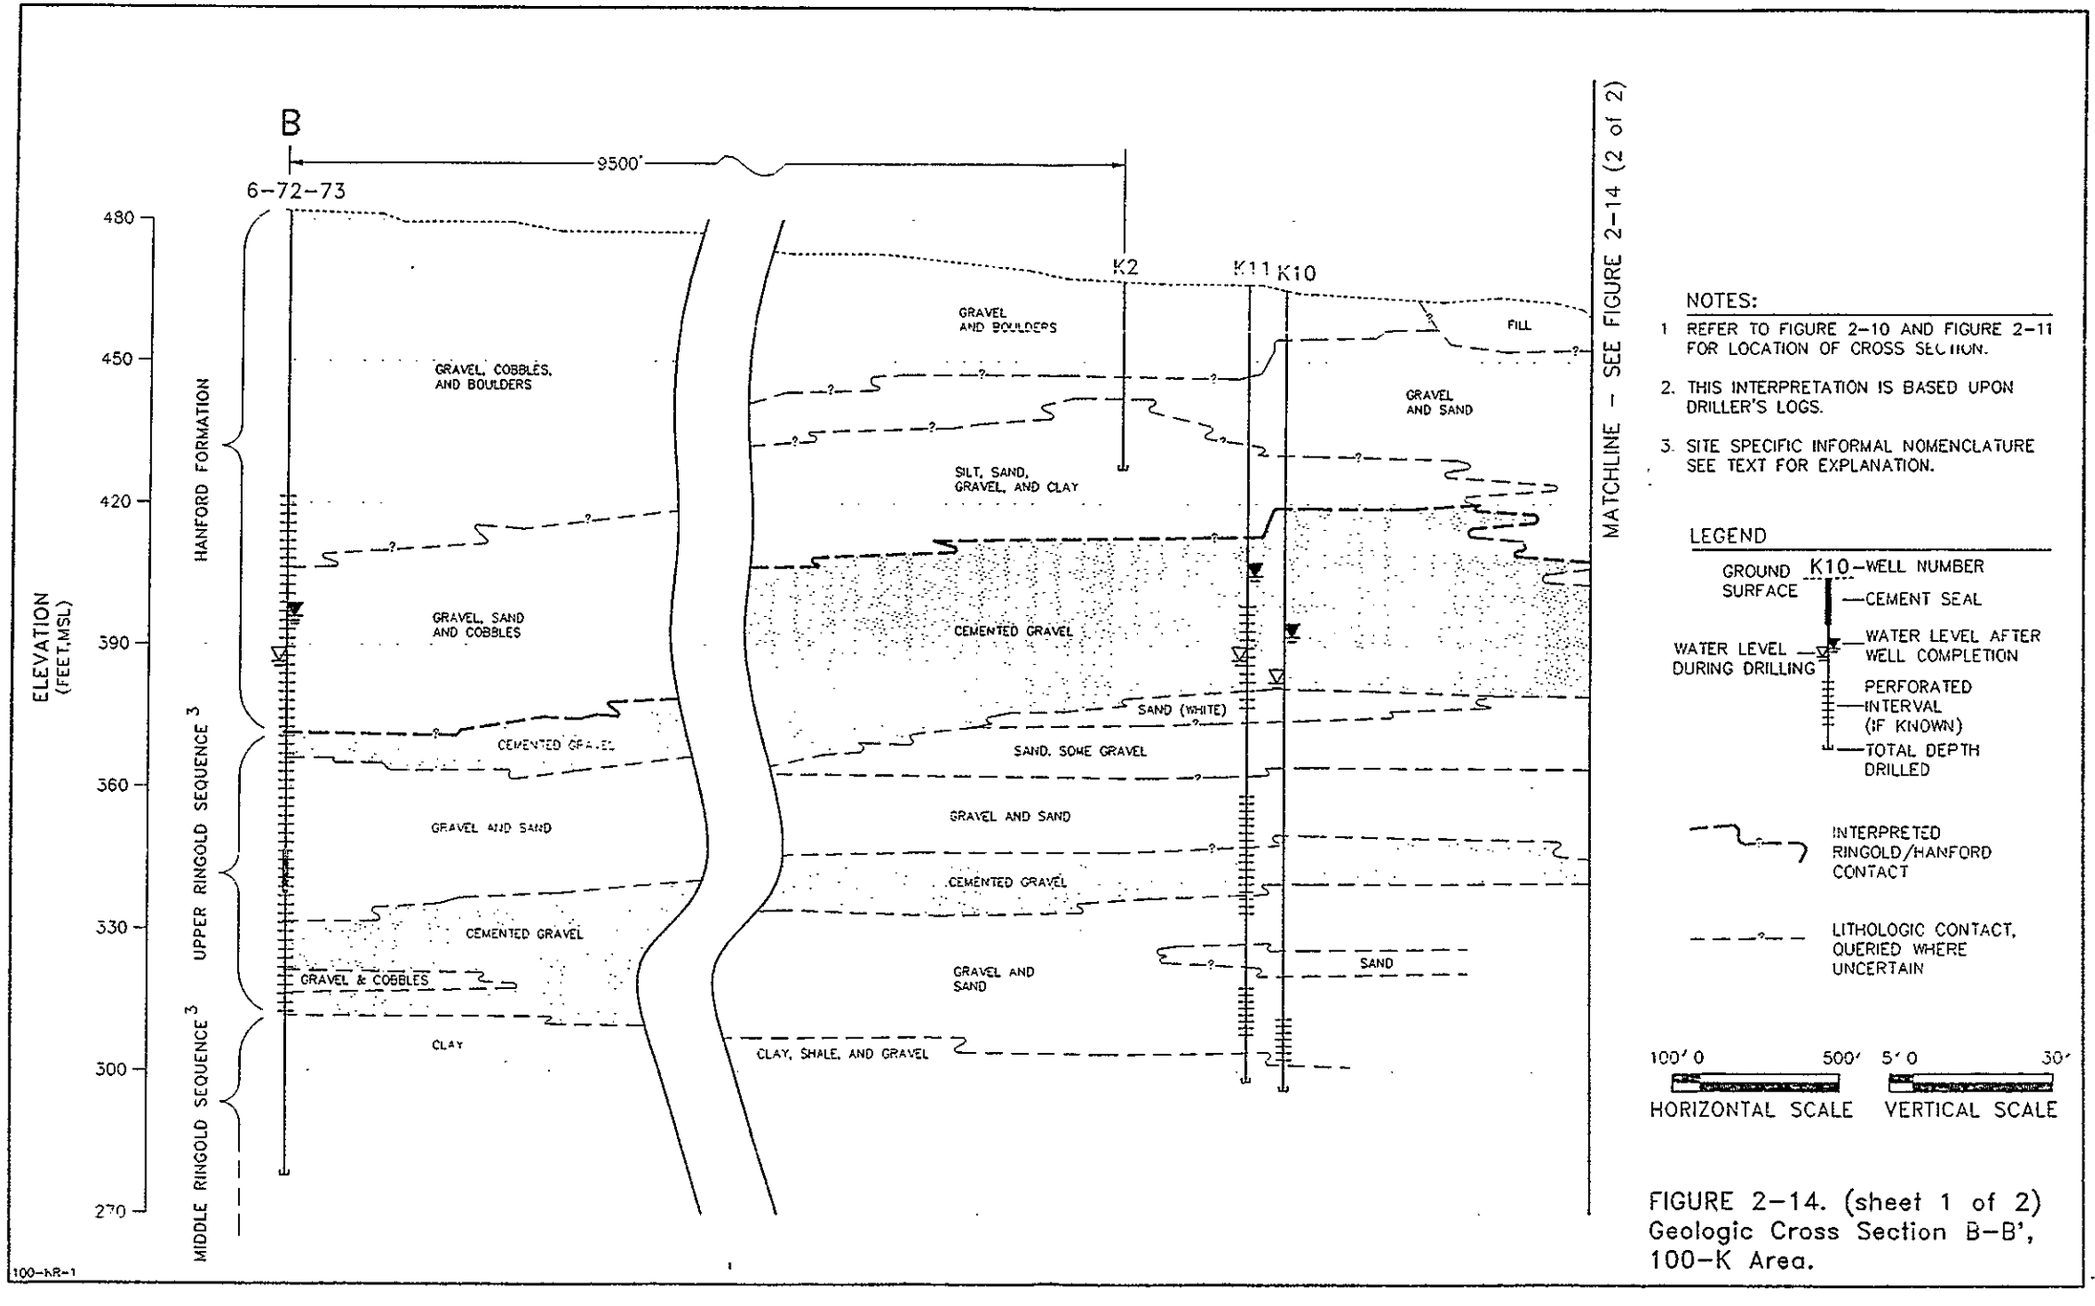

NOTES:

1. REFER TO FIGURE 2-10 AND FIGURE 2-11 FOR LOCATION OF CROSS SECTION.
2. THIS INTERPRETATION IS BASED UPON DRILLER'S LOGS.
3. SITE SPECIFIC INFORMAL NOMENCLATURE SEE TEXT FOR EXPLANATION.

LEGEND

GROUND SURFACE — K10 — WELL NUMBER
— CEMENT SEAL
WATER LEVEL DURING DRILLING — WATER LEVEL AFTER WELL COMPLETION
— PERFORATED INTERVAL (IF KNOWN)
— TOTAL DEPTH DRILLED

INTERPRETED RINGOLD/HANFORD CONTACT

LITHOLOGIC CONTACT, QUERIED WHERE UNCERTAIN

100' 0 500' HORIZONTAL SCALE

5' 0 30' VERTICAL SCALE

FIGURE 2-14. (sheet 1 of 2) Geologic Cross Section B-B', 100-K Area.

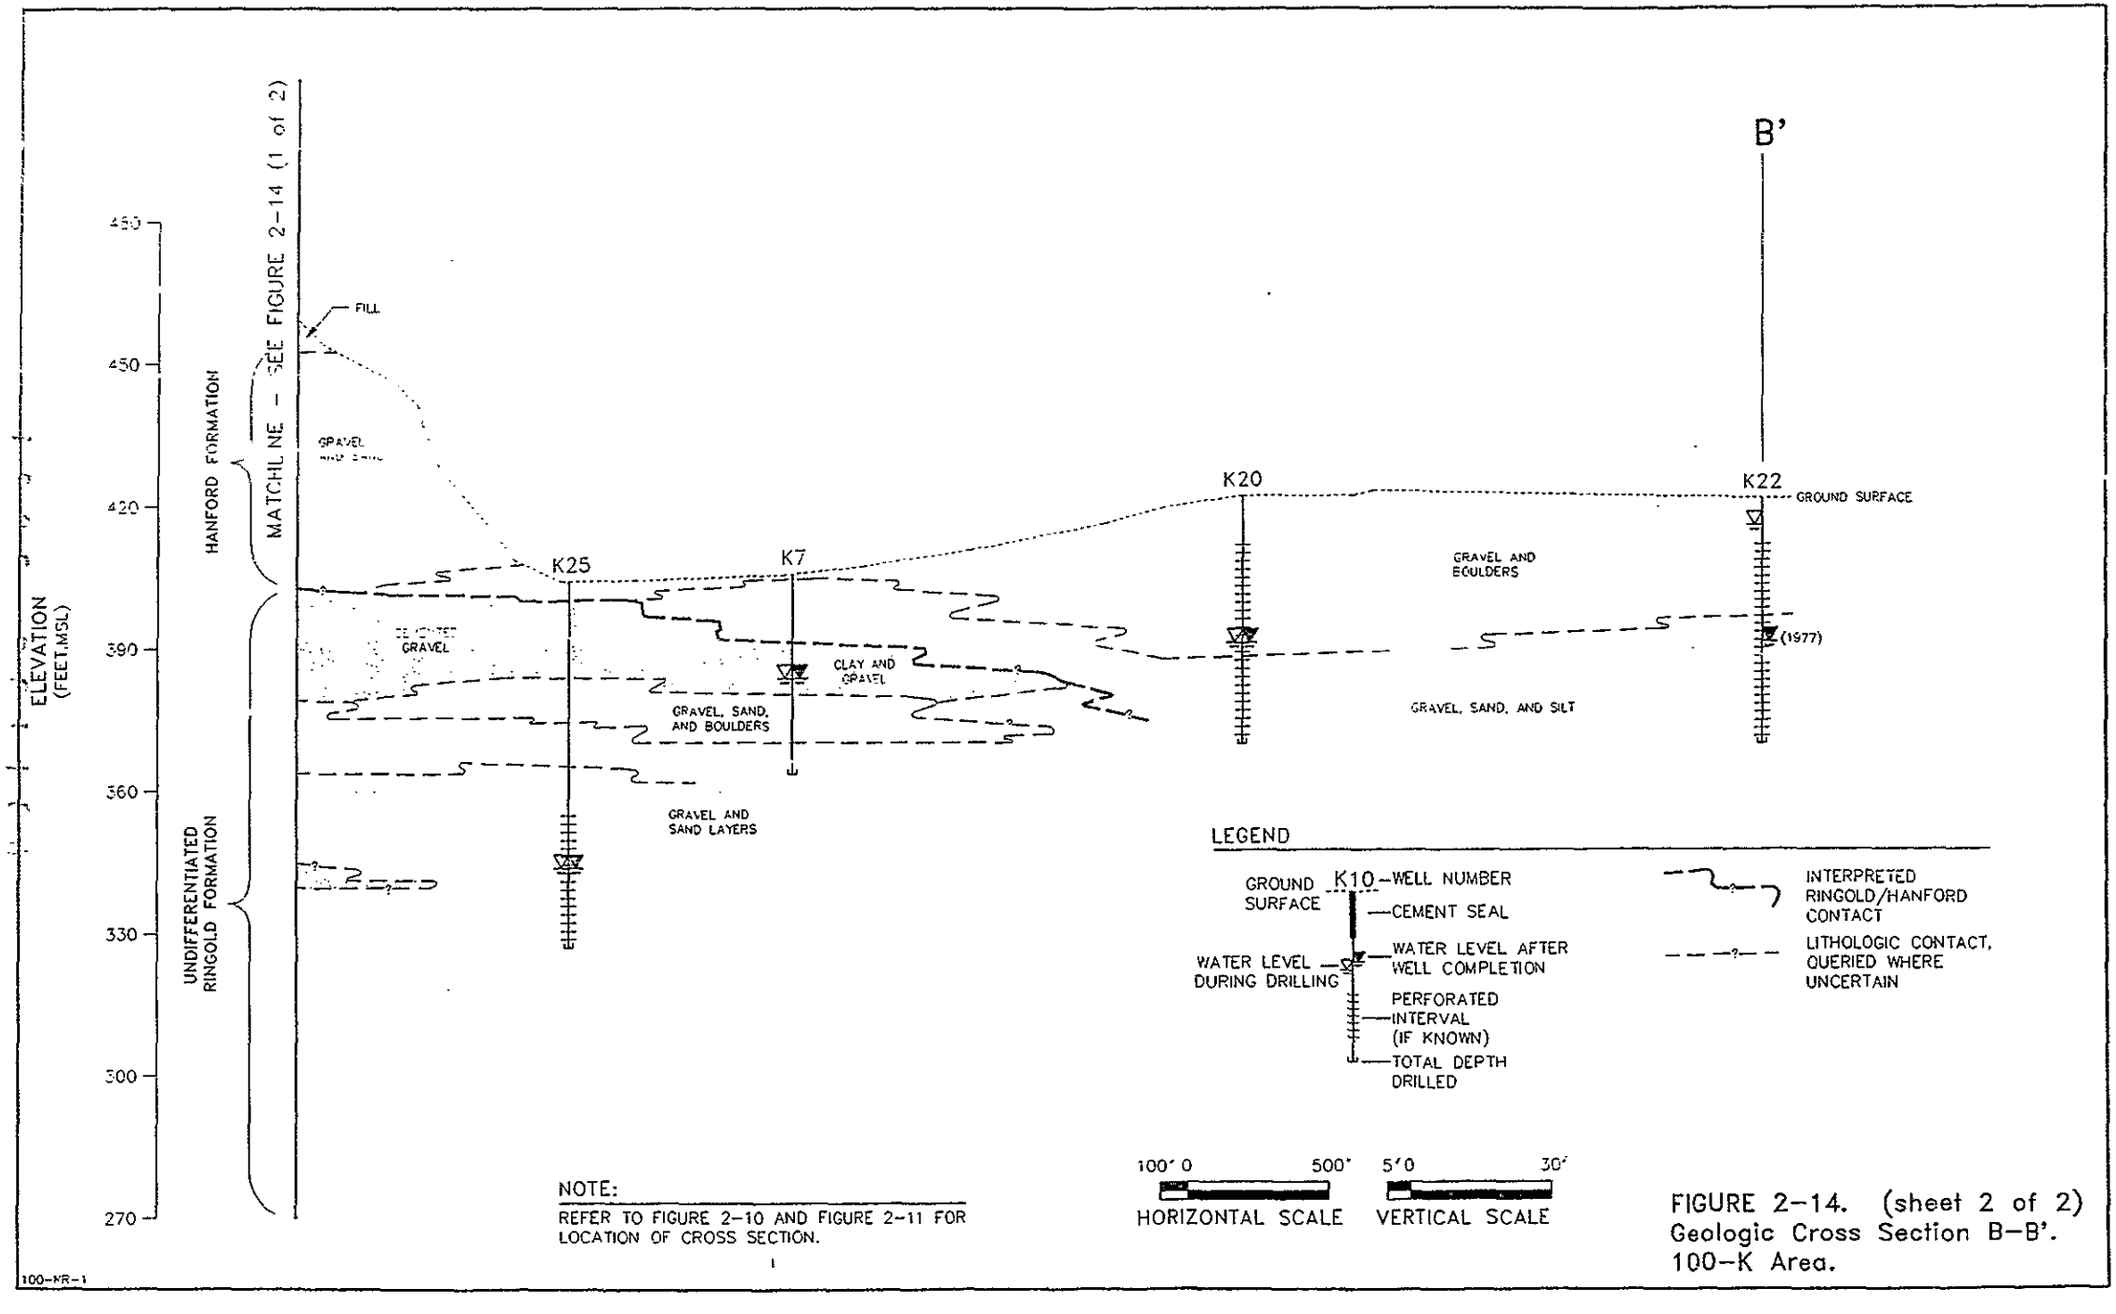

NOTE:

REFER TO FIGURE 2-10 AND FIGURE 2-11 FOR LOCATION OF CROSS SECTION.

FIGURE 2-14. (sheet 2 of 2) Geologic Cross Section B–B'. 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

2.2.2.2.1.1 Saddle Mountains Basalt. The upper surface of the Saddle Mountains Basalt is expected to be approximately 525 ft (160 m) below ground surface. A contour map of the top of the Saddle Mountains Basalt is provided in Figure 2-9. The regional geologic setting suggests that the uppermost basalts to be encountered are flows of the Elephant Mountain Member. Information from Wells 6-81-62 and 199-B3-2 indicates the upper basalt will be about 100 ft (30 m) thick. Beneath these flows, the Rattlesnake Ridge sedimentary interbed of the Ellensburg Formation was encountered in the two deep wells. The interbed was logged in Well 199-B3-2 as clay/sand/ash and as tuff/siltstone/sandstone/conglomerate in Well 6-81-62. (Well 199-B3-2 apparently did not penetrate the entire interbed.) These sediments are expected to be about 40 ft (12 m) thick in the 100-K Area and overlie basalt flows of the Pomona Member.

2.2.2.2.1.2 Ringold Formation. The Ringold Formation beneath the 100-K Area is composed of interbedded fluvial deposits consisting of gravels, sands, silts, and clays and is probably a mixture of Section Type I and II described in Section 2.2.2.1.3. The Ringold Formation is not fully penetrated by wells in the 100-K Area. The two adjacent deep wells (199-B3-2 and 6-81-62) indicate that the thickness of the Ringold Formation is about 480 ft (145 m). This is based on the interpretationthat the drillers' descriptions of cemented gravels and sands about 70 to 85 ft (21 to 26 m) below ground surface represent the upper Ringold contact.

The Ringold Formation is subdivided into three informal, site-specific units, in the vicinity of the 100-K Area; a lower Ringold sequence, a middle Ringold sequence, and an upper Ringold sequence. The sediment sequences are differentiated based on lithologies. These designations are not to be confused with other Ringold Formation classifications elsewhere in the Pasco Basin such as the Upper, Middle, Lower, and Basal Ringold units of the Type I facies of Tallman et al. (1981). The classification of Tallman et al. was developed principally for the Ringold Formation within the 200 Areas (south of Gable Mountain) and does not easily fit the Ringold Formation in the 100-K Area.

The deepest Ringold unit (lower sequence) is expected to consist predominantly of gravels and sands (possibly sandstone and conglomerate) based on information from Wells 1-B3-2 and 6-81-62. The thickness of this unit is expected to be between 20 ft (6 m) and 65 ft (20 m).

The lower sequence of sands and gravels is overlain by the middle Ringold sequence, which consists of silts and clays with minor lenses of sands and gravels. The lowermost portion of this sequence is composed of a relatively thick section of

clay, commonly referred to in drillers' logs as "green" or "blue clay." The thickness of the "blue clay" is expected to range between 105 and 140 ft (32 to 43 m). Another clay layer of interest is light-colored and found in the uppermost portion of the sequence (see Figures 2-13 and 2-14). This layer may be continuous across the site and may be approximately 40 ft (12 m) thick. The thickness of the entire middle sequence ranges between approximately 410 and 450 ft (125 to 137 m).

The upper sequence of the Ringold Formation is characterized by alternating layers of consolidated and unconsolidated coarse sediments (sands and gravels). The consolidated soils are described in the drillers' logs and notes as caliche, cemented gravel, or gravel, sand and silt that drill slow and hard (hereafter referred to as "cement gravels"). The cemented gravels appear to be continuous across the site and may even extend to Coyote Rapids, which have been mapped as Ringold Formation sediments and described as being associated with a "caliche" layer (Brown 1962). A calcrete layer may be associated with the top of the uppermost cement gravel, but this occurrence cannot be verified at this time. The thickness of this sequence of sands and gravels is approximately 80 ft (24 m) below the 100-K Area.

Using the criteria that the top of the cemented gravels represents the contact between the Ringold and Hanford formations, a contour map of the top of the Ringold Formation was prepared for this work plan (Figure 2-15). Significant elevation differences (50 ft [16 m]) are apparent and may be representative of an erosional (paleo-drainage) system or scouring from catastrophic floods.

2.2.2.2.1.3 Hanford Formation. The Hanford formation lies above the Ringold Formation and varies between 30 and 70 ft (9 to 20 m) in thickness. The variation in thickness depends largely upon topography with thinning of the formation following terracing toward the Columbia River. Also, as mentioned above, the contact with the Ringold Formation is unconformable and varies in elevation between well locations. The Hanford formation consists largely of unsorted gravel, sands and boulders, which are typically unconsolidated.

2.2.2.2.1.4 Other Surficial Deposits. Adjacent to the Columbia River, recent alluvium is continually deposited and reworked. The magnitude of river flow and abundance of sediment ranging to boulders gives rise to a varied alluvial sequence.

Nearly the entire surface of the operable unit with the exception of some locations along the steeply pitching river banks has been disturbed by grading or excavation. Fill materials are largely comprised of native materials. The extent of fill is greatest near the river bank terrace or at berms established adjacent to the 116-KE

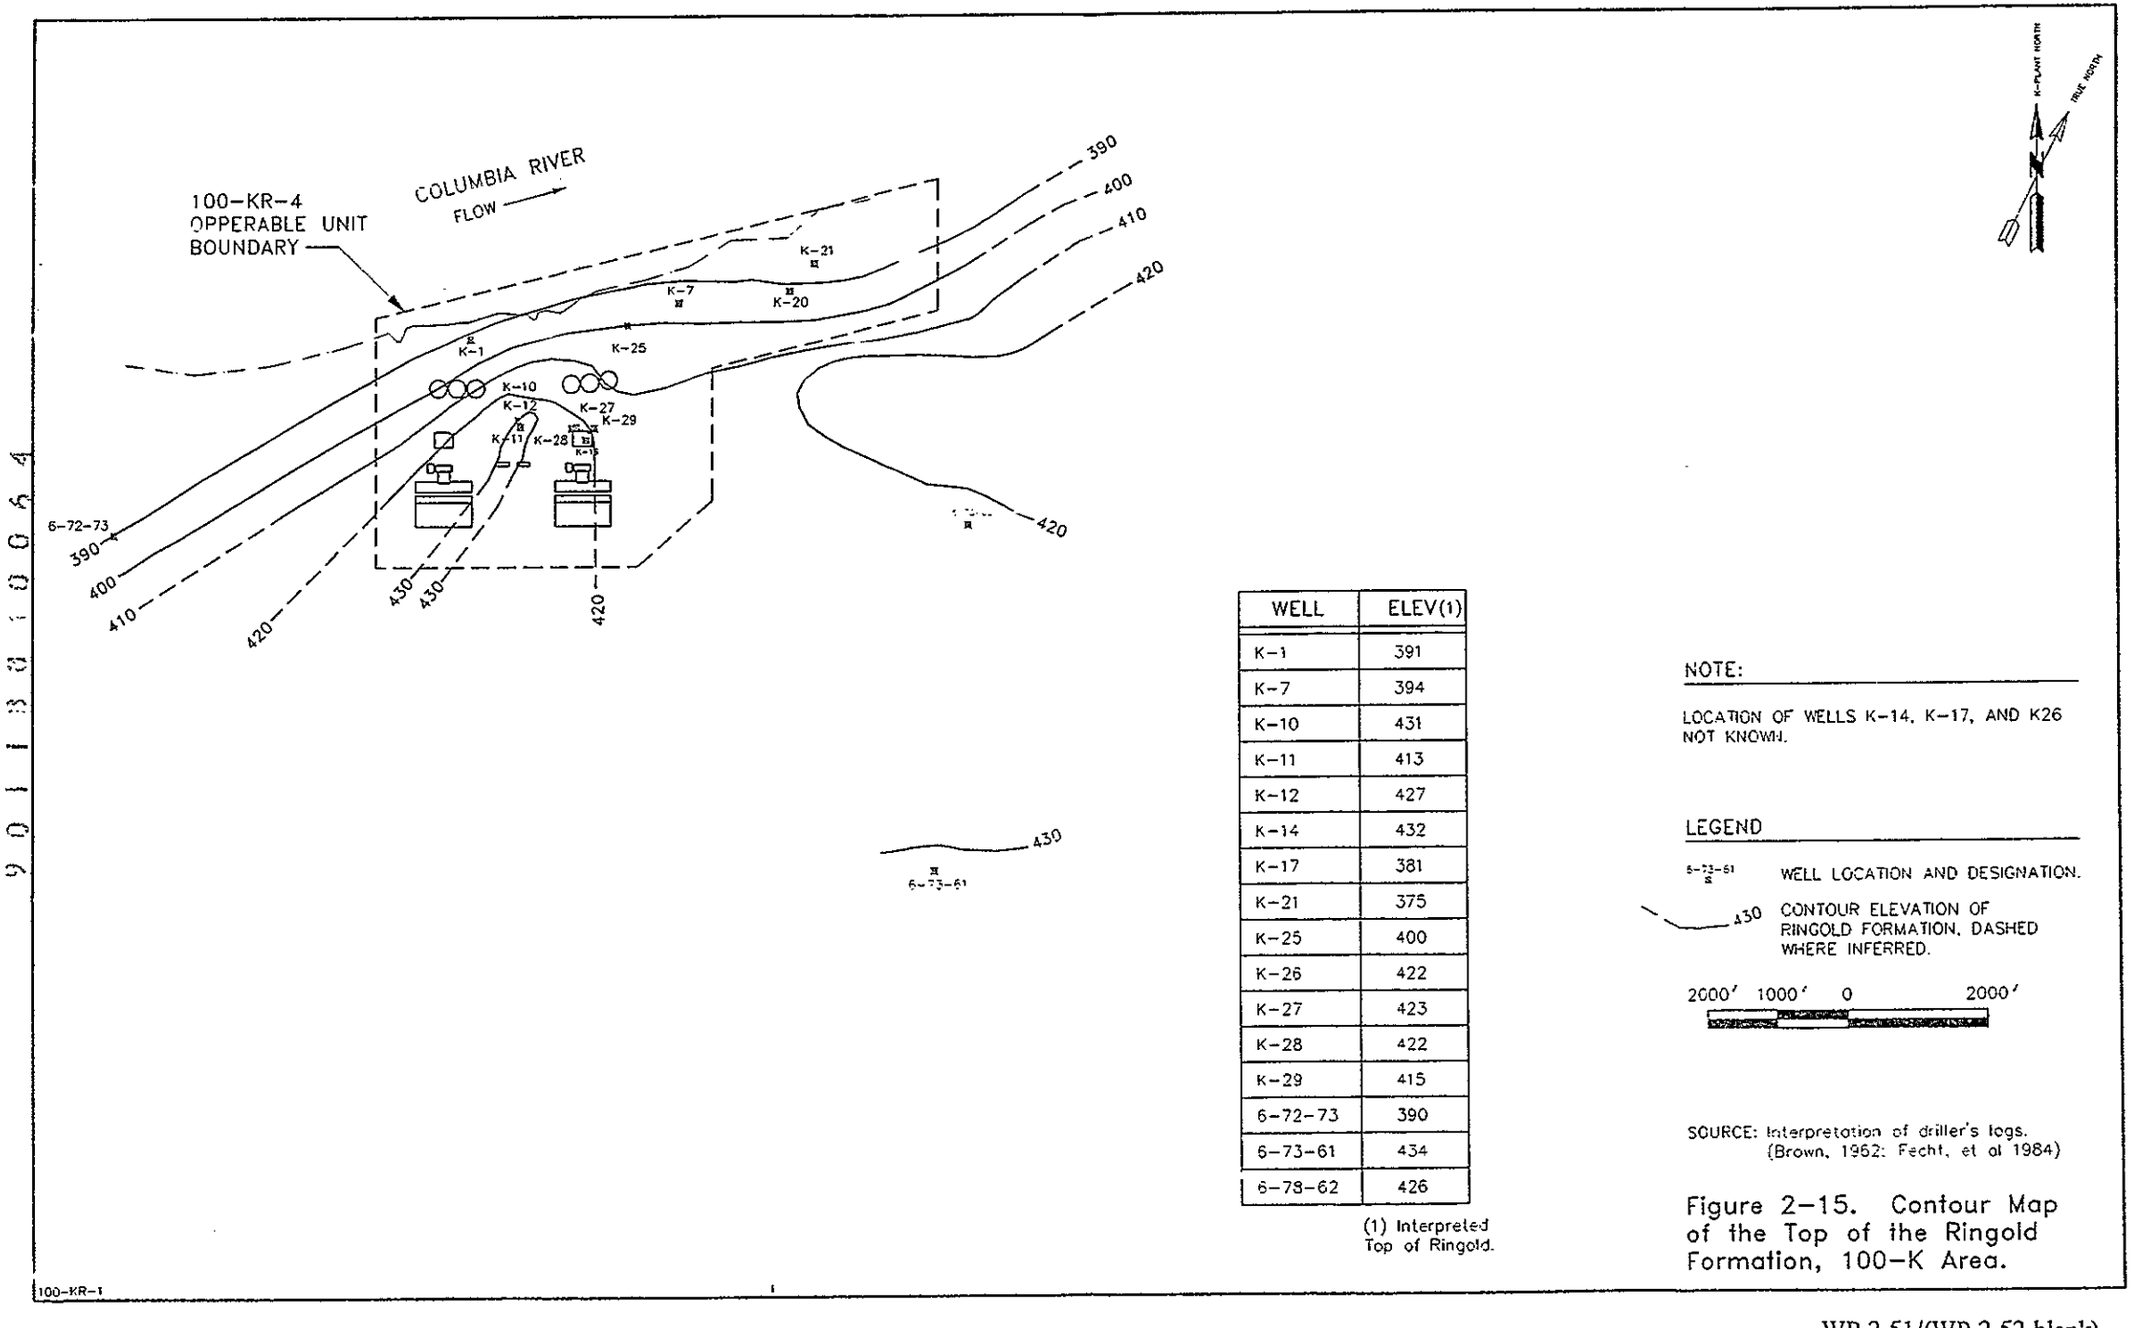

WELL	ELEV(1)
K-1	391
K-7	394
K-10	431
K-11	413
K-12	427
K-14	432
K-17	381
K-21	375
K-25	400
K-26	422
K-27	423
K-28	422
K-29	415
6-72-73	390
6-73-61	434
6-73-62	426

(1) Interpreted Top of Ringold.

Figure 2-15. Contour Map of the Top of the Ringold Formation, 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

and KW retention basins, the 116-K-1 pond berm and local fill areas from washouts along the 116-K-2 trench. Comparisons of topographic maps from before and after reactor construction indicate that as much as 10 ft (3 m) of fill may have been placed underneath the retention basins. Recent information is provided by the Coyote Rapids 7.5 minute quadrangle map (USGS 1986b). Older information is from a topographic map numbered M-1600-K, Sheet 1 prepared by General Electric for the USAEC. One of the well logs (for Well K15) also indicates at least 10 ft (3 m) of casing had to be added to the top of the well casing before fill was brought into the area.

2.2.2.2.2 Site Structural Geology. Site-specific structural features cannot be identified from existing or current interpretations of the 100-K Area site geology. Interpretation based upon regional features indicate that 100-K Area is situated on the northern limb of the Wahluke Syncline regionally described as gently dipping to the south (Figure 2-9).

2.2.3 Hydrogeology

A regional overview of the hydrogeology of the Hanford Site is presented in the first part of this section. This information provides a background setting for a more detailed discussion of the hydrogeology of the 100-K Area, which is included in the second part of this section.

2.2.3.1 Regional Hydrogeology. The Hanford Site lies near the center of the Pasco Basin, which is a sub-basin of the Columbia Basin. Ground water at the site occurs under both unconfined and confined conditions.

The unconfined aquifer is contained primarily within sedimentary deposits of the Ringold and Hanford formations. The base of the unconfined aquifer is defined either by the clay zones of the lower Ringold Formation or by the top of Columbia River Basalts where the lower Ringold Formation is absent.

The depth to ground water beneath most of the Hanford Site is generally 200 to 300 ft (61 to 91 m). However, north of Gable Mountain in the 100 Areas, the water table is shallower (Liikala et al. 1988). A regional water table contour map of the unconfined aquifer is presented in Plate 1. Ground water generally moves eastward across the Hanford Site toward the Columbia River, which receives ground water discharge from the unconfined aquifer along much of its length. The general eastward flow is interrupted by ground water mounds that occur near the 200 Areas as a result of artificial recharge from onsite disposal of cooling water. The unconfined aquifer is

naturally recharged by precipitation, runoff from higher elevations, and influent reaches of the Yakima and Columbia rivers. Beneath the Hanford Site, most of the shallow ground water originating from natural recharge flows to the Hanford Site from the higher elevations along Rattlesnake Ridge down toward the Cold Creek and Dry Creek Valleys.

The confined aquifers of the regional ground water flow system are contained in the rubbley interflow zones and in the associated sedimentary interbeds within the Columbia River Basalt Group. Intermediate or local confined systems may also occur in the Ringold Formation, where clay units act as aquitards.

The Hanford Site lies within the regional discharge zone of the Pasco and Columbia basins. Therefore, in a general regional sense, vertical ground water movement is upward in response to increasing hydraulic head with depth.

2.2.3.2 Hydrogeology of the 100-K Area. As with the geologic information, site-specific hydrogeologic information for the 100-K Area has been developed based upon information from 29 wells drilled within or immediately adjacent to the 100-K Area (K1 through K7 and K10 through K31). In addition, 10 other wells (K8, K9, 6-66-64, 6-70-68, 6-72-73, 6-73-61, 6-74-74, 6-78-62, 6-80-62, 6-81-62) are located in the 600 Area close enough to the 100-K Area to be of use in characterizing the 100-KR-1 operable unit. The locations and construction details for the wells relied upon for this work plan are shown in Figures 2-10 and 2-11 and Table 2-3, respectively. Because numerous wells have been installed in and around the 100-K Area, efforts have been made to review and interpret the available data from the wells (if only in a qualitative sense) in order to provide the most efficient plan for additional work at the site.

The history of well installation in the 100-K Area and vicinity is summarized in Table 2-4. Lithologic data from boring logs are available for nearly all 100-K Area wells. Hydrologic information, such as water level measurements and aquifer test data, is limited but is sufficient for preliminary definition of hydrostratigraphic units and ground water flow directions beneath the 100-K Area. Where site-specific information is not available, reference has been made to information available for other sites. In particular, all but one of the wells in the 100-K Area and immediate vicinity are shallow, i.e., penetrate only the upper portion of the unconfined aquifer.

Ground water information is also available from surveys of springs or seeps along the shoreline of the Columbia River. There are an estimated 14 seeps along the riverbank assigned to the 100-K Area reach of the Columbia River (McCormack and

Carlile 1984). The locations of the seeps are shown on Figure 2-16 and the seep characteristics are described in Table 2-5.

Table 2-4. History of Well Installation in the 100-K Area

Time Frame	Well #	Purpose
1943	K15	Unknown (rediscovered in 1953)
1952	K1 to K14, K24	
1953	K16, K17, K25	Presumably installed to evaluate overall conditions of 100-K Area
1954	K18	
1955	K19 to K22	
1979	K27 to K30	Four wells to determine impact from 105-KE fuel storage basin
1986	K31	Supplement 1979 wells
1966-1981	"6" Series Wells	Installed to evaluate overall conditions of 100 Areas

2.2.3.2.2 100-K Area Hydrostratigraphy. The conceptual hydrostratigraphic column for the 100-K area is included in Table 2-6. Comparison of the hydrostratigraphic and stratigraphic units is provided by this table. The hydrostratigraphic interpretation for the 100-K Area is based on available borehole logs as compared with known regional conditions. Because of the greater potential impact of the waste sites on shallow ground water, the hydrostratigraphic units are discussed in descending order starting from ground surface. The designation (A, B, C, and D) of the various layers have been provided for clarity and are not related to other nomenclature used to describe the Hanford Site hydrostratigraphy.

The available borehole logs, most of which were prepared by the drillers, generally lack detailed geologic description or classification of the subsurface material encountered. However, the logs correlate with general descriptions of the typical lithologic section for the Hanford Site. Several of the wells were installed by the same drillers, who made detailed notes; therefore, the logs are consistent and useful. In addition, the drillers frequently noted depth(s) of water occurrences and provided qualitative assessments of the water occurrence (such as gain, loss or sufficient water for drilling). Based on this information, there appear to be higher permeability zones that correlate with lithologic variations, indicating potential variations in lateral and vertical ground water (and contaminant) movement.

In the conceptual hydrostratigraphy discussed below, units within the upper Ringold sequence are designated "producing layers" and "lower permeability layers" because there are insufficient data to judge whether the lower permeability layers act as confining or semiconfining units. The hydrostratigraphic units within the middle

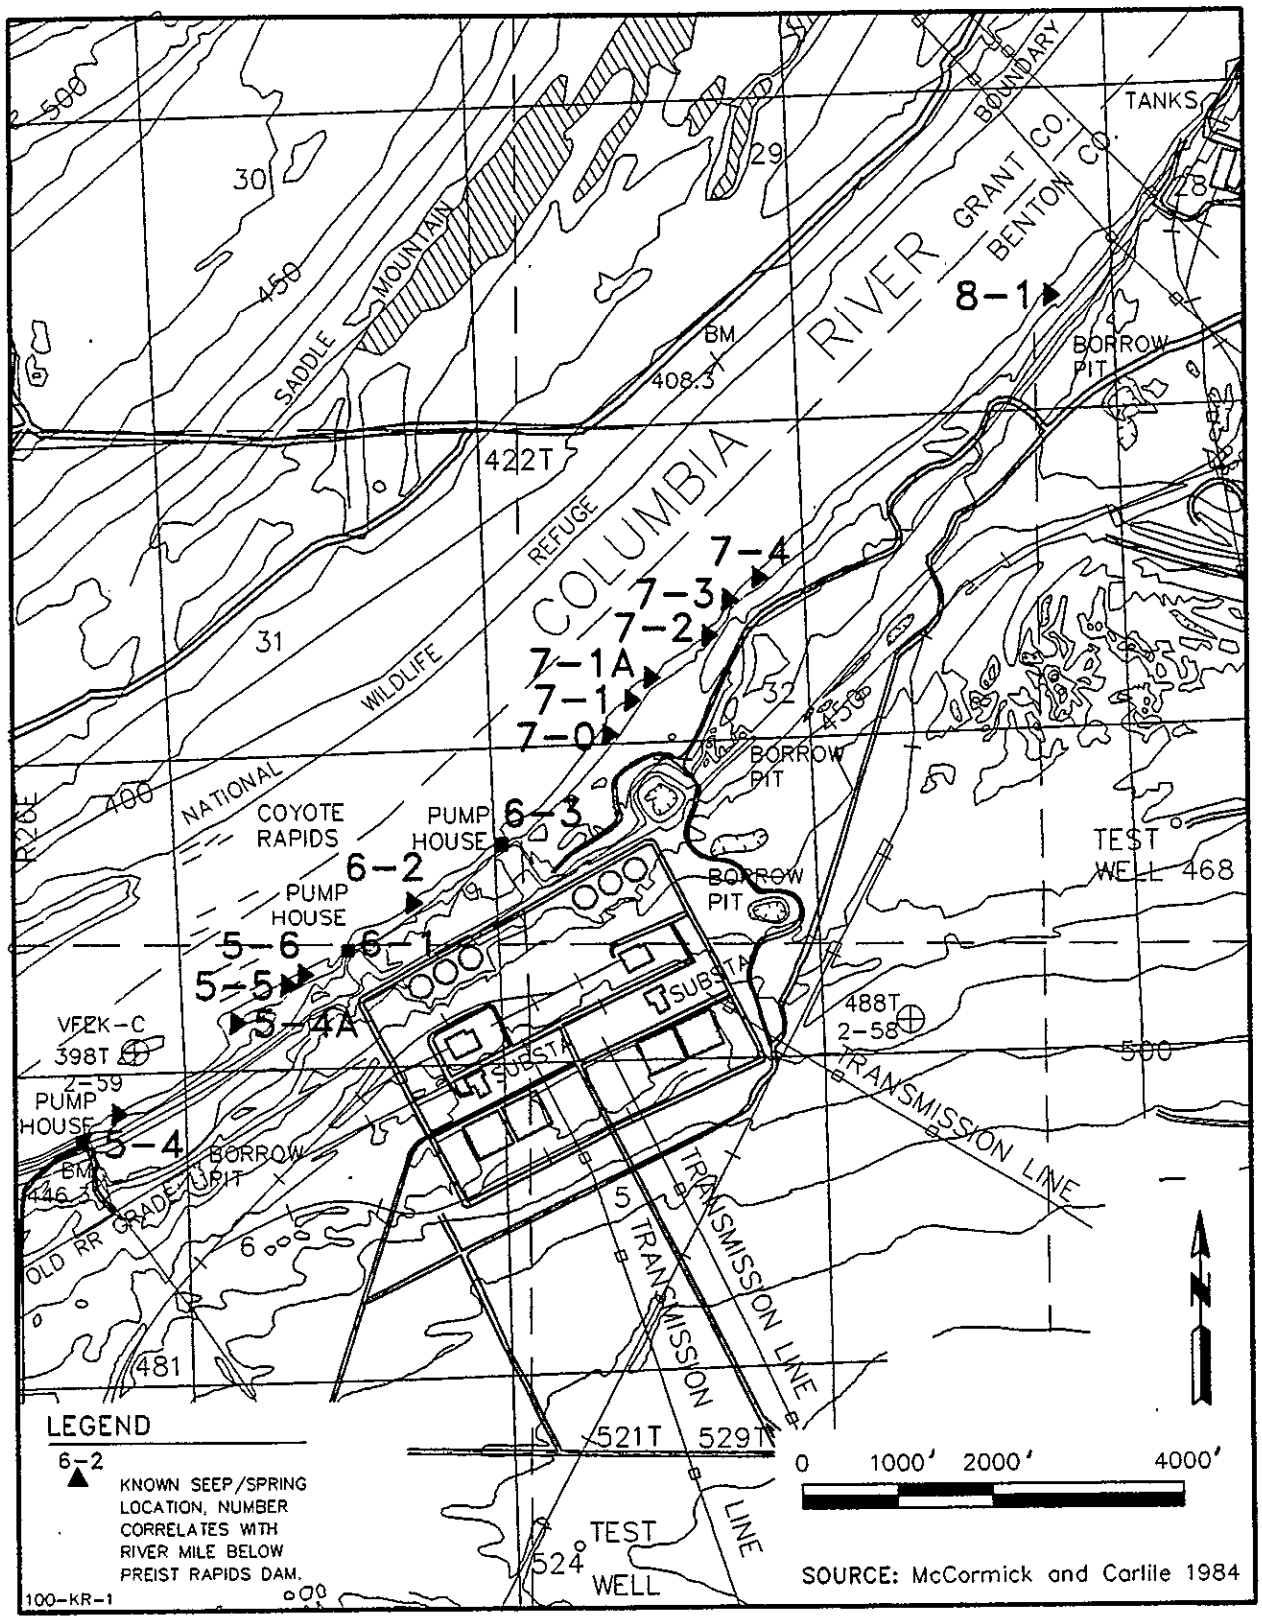

Figure 2-16. Location of Seeps Along the Columbia River Shoreline Near 100-K Area.

Table 2-5. Shoreline Seeps Inspection Record in Vicinity of 100-K Area

Location[a]	Location[b]	Designation[c]	Description[d]
5.25	382.85	5-4	17.3°C, moderate flow, several small springs at river's edge 60 yd DS RM 5-3.
5.6	382.5	5-4A	12.3°C, low flow, 100 yd DS RM pump station.
		5-5	10.2°C, moderate flow, 50 yd DS 5-4A, percolating.
5.9	382.2	5-6	12.8°C, moderate flow, continuous to RM 6 (50 yd).
6.0	382.1	6-1	12.9°C, moderate flow, percolating continuous for 50 ft. 150 yd DS RM 6.
6.2	381.9	6-2	10.1°C, low flow, percolating stream, 75 yd DS boat launch area.
		6-3	8.8°C, low flow, 75 yd DS 100-KW intake.
6.8	381.3	7-0	13.2°C, heavy flow, inside narrow inlet extending inland 10 yd from river's edge, 200 yd DS 100-KE intake, inlets surrounded large boulders and cobble; 20 ft DS is another inlet, low flow 12.0°C.
6.9	381.2	7-1	11.9°C, moderate to low flow, emanating from small boulders at DS inlet from small point, 4 ft from river's edge, 100 yd DS is another area low flow 12.5°C (at RM 7).
7.0	381.1	7-1	13.8°C, heavy flow, 5 yd from river's edge, cobble and boulders, 150 ft DS RM 7, on small point; 10 yd DS is 2nd area heavy flow 13.0°C; 30 yd DS is 3rd area heavy flow 14.6°C, 6 ft from river's edge; 36 yd total DS 7-1 4th area 15.1°C, broad area of springs (directly below K-19 well)- unnumbered well with water in it here. - at K trench overflow, broad area, low flow 12.2°C (BM site sign) - 8:10 a.m.
7.25	380.85	7-2	15.4°C, moderate flow, area 15 ft wide, small inlet at DS end of depressed K trench overflow area, 6 ft from river's edge.
		7-3	11.2°C, moderate flow, 100 ft S no trespass sign 100 ft DS from 7-3 intermittent flow DS from 7-3.

Table 2-5. Shoreline Seeps Inspection Record in Vicinity of 100-K Area

Location[a]	Location[b]	Designation[c]	Description[d]
7.3	380.80	7-4	11.8°C, very heavy flow, forms small pool, boulder area 15 ft from river's edge, bank broad and flat.
8.25	379.85	8-1	12.0°C, low flow, in grooves perpendicular to river, 15 yd from river's edge, flat cobble shore, 500 yd DS RM 8 - 60 ft DS 8-1 12.2°C, percolating vertically from hole between rocks 1 ft from river's edge - 930 a.m. 11.9°C below no trespass sign 5 ft from river's edge.

a) River Mile (RM) per McCormack and Carlisle, 1984
b) Converted RM to correspond to standards USGS designation
c) Spring Designation per McCormack and Carlisle, 1984
d) DS-Downstream

Note: This table includes seeps from River Miles 5.3 through 7.5. This portion of the river was selected by McCormack and Carlisle (1984) to encompass the sections of shoreline adjacent to the 100-K Area.

Table 2-6. Conceptual 100-K Area Hydrostratigraphy

Hydrostratigraphy	Stratigraphy	Approximate Depth (ft. below surface)	Lithologic Description
Unsaturated			
Vadose zone	fill/alluvium	0-5	Reworked gravel with sand
	Hanford formation	5-45	Cobbles, boulders, gravel, and sand
	Upper Ringold Sequence	45-70	Cemented gravel and sand
Water table			
Saturated			
Lower Permeability Layer A (uppermost water-bearing unit)	Upper Ringold Sequence	70-85	Cemented gravel and sand, unconsolidated silt and clay
Producing Layer A	Upper Ringold Sequence	85-115	Gravel and sand
Lower Permeability Layer B	Upper Ringold Sequence	115-125	Cemented gravel and sand
Producing Layer B	Upper Ringold Sequence	125-165	Gravel and sand
Confining Layer C	Middle Ringold Sequence	165-185(?)	Light-colored clay/shale/ash
Confined Aquifer C	Middle Ringold Sequence	185(?)-400	Siltstone, claystone and sandstone
Confining Layer D	Middle Ringold Sequence	400-505	Green to black siltstone/claystone
Confined Aquifer D	Lower Ringold Sequence	505-525	Sandstone and conglomerate
Basalt Confining Layer	Elephant Mountain Member Basalt Flow(s)	525-645	Basalt
Basalt Interbed Aquifer	Rattlesnake Ridge Interbed (Ellensburg Formation)	645-685	Welded tuff, siltstone, sandstone and conglomerate

Note: The depths and descriptions of the upper hydrostratigraphic units (into confining layer C) are based on interpretations from the driller's log and notes for Well K-10 which is centrally located in the 100-K Area. The deeper hydrostratigraphic units and depths are based upon interpretations of driller's log and notes for Well 6-81-62 located about 3,000 ft (915 m) east of the main portion of the 100-K Area.

Ringold sequence are designated "confining layers" and "confined aquifers" based on information from drillers' logs and similar hydrostratigraphy elsewhere on the Hanford Site.

The hydraulic characteristics presented below are based primarily on Hanford Site conditions (regional information) because only limited information is available specifically for the 100-K Area. However, the reported ranges of values do give an idea of the relative permeabilities of the hydrostratigraphic units. Conditions within the 100-K Area are expected to be within the reported ranges because of stratigraphic similarities between the 100-K Area and the Hanford Site region.

2.2.3.2.2.1 Vadose Zone. Several different stratigraphic units occur within the vadose zone, including fill, loess, alluvium, the Hanford formation and the Ringold Formation. Because the water table occurs within the uppermost cemented gravel underneath much of the site, which has been interpreted as the upper portion of the Ringold Formation, this zone has also been included in the vadose zone. The thickness of the vadose zone varies from about 20 to 80 ft (6 to 24 m) across the site due to topographic variations as shown on the geologic cross sections (Figures 2-13 and 2-14). The vadose zone may have been reduced in thickness historically due to ground water mounding during site operations.

Water contents at depth in vadose zone sediments at the Hanford Site are generally low, ranging from 2 to 7% by weight in coarse-grained soils and 7 to 15% in silts (Gee and Heller 1985). Measurements of matrix potential (i.e., the energy required to extract water from a soil against the capillary and adsorptive forces of the soil matrix) at depths greater than 30 ft (9 m) suggest that water in the deeper sediments is slowly draining to the water table (Hseih et al. 1973).

2.2.3.2.2.2 Lower Permeability Layers 'A' and 'B' (Upper Ringold Sequence). Lower permeability layers 'A' and 'B' correspond to layers of cemented gravel underlying the site (Section 2.2.2.2). The 'A' layer is the saturated portion of the uppermost cemented gravel. Based on conditions encountered during installation of Well K10, it is about 15 ft (4 to 5 m) thick. From the drillers' notes, the depth at which water was encountered during drilling apparently corresponded to the water level in the well upon completion. Therefore, this layer may only be semiconfining or there may not be of sufficient hydraulic head to raise the potentiometric surface relative to this layer. The 'B' layer is about 10 ft (3 m) thick in Well K10 and is separated from the 'A' layer by more permeable sands and gravels. The hydraulic characteristics of these layers are discussed below with those for confining layer 'C'.

The position of the lower permeability 'A' and 'B' layers relative to the water table and their thicknesses of these layers are variable. East of the 100-K Area, e.g., toward Well 6-78-62, both of these layers are apparently shallower and thus they are in the vadose zone. Locally, the 'A' and 'B' layers may merge as in Well K1 (Figure 2-13). Also, the continuity of these layers (or the degree of cementing) may change resulting in variations to ground water and contaminant flow.

The potential effect of the cemented gravel layers on contaminant movement is evident in the variations in cation exchange capacities (CEC). Available CEC data are summarized on Table 2-7, along with the lithologic descriptions of the samples. Significant increases in CEC values, which could indicate decreased contaminant mobility, correspond to layers in which caliche or clay were noted.

2.2.3.2.2.3 Producing Layers 'A' and 'B' (Upper Ringold Sequence). These layers correspond to the relatively more permeable sands and gravels generally noted by the drillers beneath the cemented gravels. The upper producing layer is about 30 ft (9 m) thick but may be locally absent (Well K1) near the river. The lower producing layer is about 20 ft (7 m) thick in Well K10. The hydraulic characteristics of these layers are discussed below with those for confined aquifer 'C'.

2.2.3.2.2.4 Confining Layer 'C' (Middle Ringold Sequence). At the three deeper Ringold well locations in the 100-K Area (Wells K1, K11, and 6-78-62), a light-colored layer variously described as clay, shale, ash with silt, sand, and gravel was encountered. The drillers noted a significant reduction in water production in this layer. None of the three wells fully penetrates the layer. At about the same depth in Well 6-81-62, a lighter colored siltstone layer about 40 ft (12 m) thick was encountered. Because of the significantly reduced production capacity of this layer, it has been considered to have a potential impact on ground water and contaminant movement by restricting vertical migration.

2.2.3.2.2.5 Producing Layer 'C' (Middle Ringold Sequence). None of the 100-K Area wells was drilled into this layer. This layer has been assumed to exist between confining layers 'C' and 'D', of the Ringold Formation (a thickness of about 200 ft [60 m]). Based on variations in lithology encountered in Well 6-81-62, there are probably alternating producing and confining layers corresponding to alternating lithologies within this zone.

At present, information specific to the upper producing layers in the Ringold Formation ('A', 'B' and 'C') is only available for producing layer 'B'. This information is from testing of Well K10 which is completed in producing layer 'B'.

Table 2-7. Cation Exchange Capacities

Well Number	Depth of Sample (ft below surface)	Grain Size: Material above 2mm (%)	Grain Size: Sand (%)	Grain Size: Silt (%)	Grain Size: Clay (%)	Cation Exchange Capacity (meq/100g)	Lithology (from driller's log)
Wells Within 100-KR-1 Operable Unit							
K-19	10	42	54	1.9	1.9	1.4	Gravel and boulders
	15	28	60	7.7	4.9	2.0	Gravel
	20	31	54	9.0	5.8	1.5	Gravel
	25	26	59	9.4	5.9	1.4	Gravel
	30	30	59	7.8	4.2	1.1	Gravel
	35	54	45	0.4	0.9	0.5	Gravel
	40	88	8	1.7	1.0	0.3	Gravel and boulders
	45	29	65	0.9	4.5	1.6	Gravel
K-25	5	35	50	9.9	5.0	3.7	Clay
	10	32	51	11.3	5.5	4.3	Clay and gravel
	15	10	62	20.1	8.7	6.0	Clay and gravel
	20	59	38	1.7	0.9	1.5	Gravel
	25	75	25	0.1	0.3	0.9	Gravel and boulders
	30	31	65	2.5	1.1	1.7	Sand and coarse gravel
	35	21	73	5.9	0.1	1.6	Sand and coarse gravel
	40	41	53	4.3	1.6	1.3	Coarse gravel, boulders and fine sand
	45	57	40	2.4	0.8	1.3	Sand and coarse gravel
	50	59	39	1.2	0.6	0.6	Sand and coarse gravel
	55	52	44	2.9	1.2	1.2	Coarse gravel and sand
	60	50	48	1.9	1.0	1.1	Coarse gravel and sand
	65	60	39	0.9	0.6	0.7	Gravel and sand
	70	49	45	3.6	2.3	0.8	Gravel and sand
	75	59	40	0.7	0.8	0.4	Gravel and sand
K-26	5	21	70	6.3	3.0	4.9	No log available
	10	33	57	7.0	2.9	4.4	
	15	45	54	1.1	0.4	3.4	
	20	32	51	12.0	5.0	5.4	
	25	29	53	13.8	4.5	5.9	
	30	39	55	3.7	2.5	1.2	
	35	24	59	12.9	4.0	1.5	
	40	24	72	2.3	1.7	1.2	
	45	49	49	1.5	0.7	0.4	
	50	38	58	1.6	2.4	1.6	
	55	32	58	7.1	3.2	1.6	

Table 2-7. Cation Exchange Capacities

Well Number	Depth of Sample (ft below surface)	Grain Size: Material above 2mm (%)	Grain Size: Sand (%)	Grain Size: Silt (%)	Grain Size: Clay (%)	Cation Exchange Capacity (meq/100g)	Lithology (from driller's log)
Wells Within 100-KR-2 Operable Unit							
K-18 (questionable location)	5	20	75	2.4	1.7	2.5	Sand backfill
	11	19	76	2.8	1.8	2.0	Sand backfill
	15	61	36	1.9	0.9	0.5	Coarse gravel and coarse sand
	20	23	71	4.4	2.1	0.1	Gravel and fine sand
	25	63	35	0.9	0.4	0.5	Gravel and fine sand
	30	17	79	2.8	0.9	1.2	Gravel and fine sand
	35	0	94	4.5	1.6	1.2	Fine sand
	40	49	48	2.0	1.2	1.0	Coarse gravel and fine sand
	45	47	50	2.1	0.7	1.6	Coarse gravel, cobbles, fine sand
	50	37	56	5.4	2.1	1.7	Gravel and fine sand
	55	61	37	1.0	0.7	1.1	Gravel and fine sand
	60	34	62	2.6	1.5	2.1	Coarse gravel and fine sand
Wells in the 600 Area Near the 100-K Area							
6-70-68	5	38	42	14.2	5.2	3.3	Boulders, sand and silt
	10	40	40	14.4	5.7	3.2	Boulders, sand and silt
	15	43	43	9.7	4.3	3.0	Boulders and gravel
	20	51	39	6.8	2.7	2.4	Cobbles and gravel
	25	71	23	4.3	1.7	1.5	Coarse gravel
	30	10	84	4.0	1.8	3.9	Fine and coarse sand
	35	28	64	5.5	2.1	3.8	Sand and gravel
	40	5	90	4.0	1.4	5.1	Sand
	45	10	84	4.2	1.8	6.8	Fine sand
	50	57	41	0.9	0.6	1.6	Sand and gravel
	55	37	50	10.8	1.5	3.1	Sand and gravel
	60	25	69	3.6	1.6	2.8	Sand and gravel
	65	16	62	20.6	1.8	3.1	Sand and gravel
	70	19	60	19.9	1.7	3.0	Sand and gravel
	75	65	31	2.7	1.3	1.6	Gravel and sand
	80	75	22	1.8	1.2	1.7	Gravel and sand
	85	7	89	2.8	0.7	3.0	Gravel and sand
	90	40	57	2.1	0.8	2.9	Gravel and sand
	95	17	79	3.3	1.1	4.1	Gravel and sand
	100	5	88	5.7	1.7	4.9	Sand
	105	49	45	4.9	1.7	2.8	Gravel and sand
	110	59	33	6.1	1.9	2.6	Gravel and sand

Table 2-7. Cation Exchange Capacities

Well Number	Depth of Sample (ft below surface)	Grain Size: Material above 2mm (%)	Grain Size: Sand (%)	Grain Size: Silt (%)	Grain Size: Clay (%)	Cation Exchange Capacity (meq/100g)	Lithology (from driller's log)
6-70-68 (contd.)	115	27	68	3.7	2.0	2.6	Gravel and sand
	120	11	85	3.2	1.1	2.6	Gravel and sand
	125	62	36	1.4	0.9	1.2	Gravel and sand
	130	45	51	2.6	1.0	1.2	Gravel and sand
699-78-62	5	28	49	16.5	6.2	4.9	Cemented gravel
	10	25	61	8.5	6.1	5.6	Cemented gravel
	15	19	54	21.0	5.5	5.2	Boulders
	20	32	47	16.3	4.7	4.7	Cemented gravel
	25	21	58	16.1	5.0	5.0	Gravel
	30	29	52	14.8	4.7	4.6	Gravel
	35	28	49	17.2	6.4	4.9	Gravel
	40	32	47	15.4	5.3	4.6	Gravel
	45	25	50	17.0	7.3	4.1	Cemented gravel
	50	25	52	16.0	7.0	3.4	Cemented gravel
	55	14	61	17.6	8.1	3.2	Cemented gravel
	60	21	60	14.1	5.4	2.2	Cemented gravel
	65	16	61	16.7	6.6	2.3	Cemented gravel
	70	12	68	14.8	5.1	2.0	Gravel and clay
Wells in the B/C Area							
199-B3-2	10	39.9	71.6	22.4	6.0	10.4	Boulders, gravel and silt
	25	23.6	72.7	22.1	5.2	8.5	Boulders, gravel and silt
	45	43.1	85.8	12.3	1.9	4.3	Coarse gravel, little sand and silt
	65	29.0	70.4	25	4.6	4.5	Coarse gravel, little sand and silt
	80	9.1	92.7	7.3	0	3.1	Sandy gravel and gravelly sand
	100	49.3	95.8	3.4	0.93	5.1	Sandy gravel and gravelly sand
	115	38.2	85.9	11.0	3.1	5.7	Sandy gravel and gravelly sand
	135	39.5	92.6	6.7	0.7	4.8	Sandy gravel and gravelly sand
	155	11.5	65.7	23.8	10.5	20.1	Sand and silt with some gravel, clay and caliche
	175	0	17.6	29.8	52.6	48.9	Sand and silt with some gravel, clay and caliche
	190	29.7	80.3	13.3	6.4	14.1	Sand and silt with some gravel, clay and caliche

Table 2-7. Cation Exchange Capacities

Well Number	Depth of Sample (ft below surface)	Grain Size: Material above 2mm (%)	Grain Size: Sand (%)	Grain Size: Silt (%)	Grain Size: Clay (%)	Cation Exchange Capacity (meq/100g)	Lithology (from driller's log)
199-B3-2 (contd.)	210	0	58.6	29.3	12.1	23.9	Sand and silt with some gravel, clay and caliche
	230	0	63.3	30.9	5.8	12.8	Sand and silt with some gravel, clay and caliche
	250	0	57.7	33.2	9	17.9	Sand and silt with some gravel, clay and caliche
	270	55.1	85.3	12.2	2.5	6.2	Sandy gravel
	290	57.4	83.1	12.9	4.0	6.2	Sandy gravel
	310	0	68.0	27.9	4.1	14.1	Layers of sand, silt and clay with some gravel
	325	71.0	86.2	11.9	1.9	6.8	Sandy gravel
	340	68.5	92.2	5.6	2.2	5.4	Sandy gravel
	370	11.7	93.0	6.8	0.2	4.4	Sand, silt and clay with some gravel and caliche
	380	2.1	66.4	8.2	8.5	10.0	Sand, silt and clay with some gravel and caliche
	395	0	12.5	57.5	30.0	35.8	Sand, silt and clay with some gravel and caliche
	415	0	8.8	62.0	28.8	24.2	Sand, silt and clay with some gravel and caliche
	435	0	6.7	62.5	30.8	35.2	Sand, silt and clay with some gravel and caliche
	450	0	39.8	21.8	18.4	22.3	Sand, silt and clay with some gravel and caliche
	470	11.6	12.4	58.5	29.1	38.2	Blue clay
	495	0	15.7	57.9	26.4	21.2	Blue clay
	515	0	11.0	62.5	26.5	25.8	Blue clay
	535	0	1.8	65.8	32.4	23.7	Blue clay
	560	0	17.6	63.1	19.3	32.1	Blue clay
	580	0	11.2	52.8	36.0	39.5	Blue clay
	600	38.0	69.5	20.2	10.3	19.0	Clay, sand and gravel
	620	0	71.0	19.7	9.3	19.0	Clay, sand and gravel
	640	19.4	59.6	21.6	18.8	32.9	Clay, sand and gravel
	655	0	4.0	29.5	66.5	21.2	Clay, sand and gravel
	505(?)	0	12.0	65.3	22.7	-	Clay, sand and gravel

Sources: Bensen et al 1963 and McHenry, 1957.

Reference is also made on drillers' notes to testing of other wells, e.g., Well 6-72-73; however, specific information from these tests has not yet been located.

Reported hydraulic conductivity ranges for these units for the Hanford Site include: 100 to 7,000 ft/d (4×10^{-4} to 2.5×10^{-2} m/s) for undifferentiated Hanford/Middle Ringold sediments; 0.1 to 7,000 ft/d (4×10^{-7} to 2.5×10^{-2} m/s) for the Ringold Formation; and 20 to 6,000 ft/d (1 to 210 m/s) for the Middle Ringold Unit. The reported range in storage coefficients for the overall Ringold Formation is 0.0002 to 0.05 (DOE 1988 and Schalla et al. 1988).

2.2.3.2.2.6 Confining Layer 'D' (Middle Ringold Sequence). The lowermost portion of the middle Ringold sequence, which was logged as blue clay at Well 199-B3-2 and as green or dark grey to black and medium-siltstone and claystone at Well 6-81-62, is the confining layer above the lower Ringold sequence. The thicknesses of this unit at Wells 199-B3-2 and 6-81-62 are about 140 ft (43 m) and 105 ft (32 m), respectively. It is assumed that a similar layer exists beneath the 100-K Area.

The reported range in hydraulic conductivity values for this unit, 0.11 to 10 ft/d (4×10^{-7} to 4×10^{-5} m/s) (DOE 1988), is significantly less than the ranges for the other Ringold units, as would be expected for a confining layer. The reported storage coefficient range, 0.0002 to 0.05, is for the overall Ringold Formation (DOE 1988), but the values for the "blue clay" may be even less because it is a confining layer. The vertical hydraulic conductivity of this zone, as measured at the 100-H Area, was at 10^{-1} ft/d (4×10^{-3} m/s) (Liikala et al. 1988).

2.2.3.2.2.7 Confined Aquifer 'D' (Lower Ringold Sequence). The thickness of this unit is approximately 60 ft (20 m) at Well 199-B3-2 and about 25 ft (8 m) at Well 6-81-62. In Well 199-B3-2, it was logged as clay, sand, and gravel and in Well 6-81-62, it was logged as sandstone and conglomerate. As with confining layer 'D', it is assumed that a layer similar to the lower Ringold sequence exists beneath the 100-K Area.

The hydraulic conductivities for this unit reportedly range from 0.01 to 1,000 ft/d (4×10^{-8} to 4×10^{-3} m/s) (DOE 1988 and Schalla et al. 1988). Because this unit is confined, the lower values e.g., 0.001 or less, in the reported range of storage coefficients for the overall Ringold Formation, 0.0002 to 0.05, would probably be representative.

2.2.3.2.2.8 Basalt Aquitard (Elephant Mountain Basalt). Detailed information about the uppermost basalt encountered in Wells 199-B3-2 and 6-81-62 is currently not available. The occurrence of flow tops, flow interiors, vesicular zones or other features has not yet been determined. However, in both Wells 199-B3-2 and 6-81-62, the thickness of the uppermost basalt layer is at least 100 ft (30 m); therefore, it is expected to impede vertical ground water movement beneath the 100-K Area.

Although the uppermost portion of this basalt may be a more permeable flow top, it is assumed that a less permeable flow interior is also present in this section. Reported hydraulic conductivities for flow tops in the Saddle Mountains Basalt range from 10^{-2} to 10^{-6} ft/d (10^{-7} to 10^{-11} m/s), and the reported effective porosity for flow tops in general is 5%. No data are available for review for flow interiors in Saddle Mountains Basalt, but for column zones (which may make up flow interiors) in the Wanapum and Grande Ronde Basalts, the hydraulic conductivities range from 10^{-6} to 10^{-8} ft/d (10^{-11} to 10^{-13} m/s. The reported effective porosity for the flow interior is <1% (DOE 1982). Only one hydraulic conductivity value is reported specifically for the Elephant Mountain Basalt (2,040 ft/d [7 x 10^{-3} m/s]); however, this is probably representative of a more permeable zone in the basalt (Gephart et al. 1979).

2.2.3.2.2.9 Basalt Interbed Aquifer (Rattlesnake Ridge Interbed). The uppermost interbed encountered in Wells 199-B3-2 and 6-81-62 was logged as clay/sand/ash and welded tuff/siltstone/sandstone/conglomerate, respectively. It was apparently not completely penetrated in Well 199-B3-2 but was about 40 ft (12 m) thick in Well 6-81-62.

Reported hydraulic conductivities for the interbeds in the Saddle Mountains Basalt range from 10^{-7} to 10^{-2} ft/d (10^{-13} to 10^{-8} m/s) with a storativity of 10^{-3} to 10^{-4}. The reported effective porosity for interbeds in general is <10% (DOE 1982). Reported mean hydraulic conductivities specifically for the Rattlesnake Ridge Interbed range from 0.1 to 100 ft/d (4 x 10^{-3} to 4 m/s) (Gephart et al. 1979).

2.2.3.2.3 Ground Water Flow. The water table elevation varies from about 385 to 400 ft (117 to 122 m) above mean sea level based on 1989 measurements in and around the 100-KR-1 operable unit. A contour map of the ground water elevations is shown on Figure 2-17, along with the individual well measurements. The gradient is relatively flat, on the order of 0.0009 to 0.0033, and is steeper near the river, due to either lithologic variations affecting transmissivity or the influence of the river elevation with time. The overall gradient is toward the river, as would be expected from regional conditions, but also shows a "downriver" influence. The

THIS PAGE INTENTIONALLY
LEFT BLANK

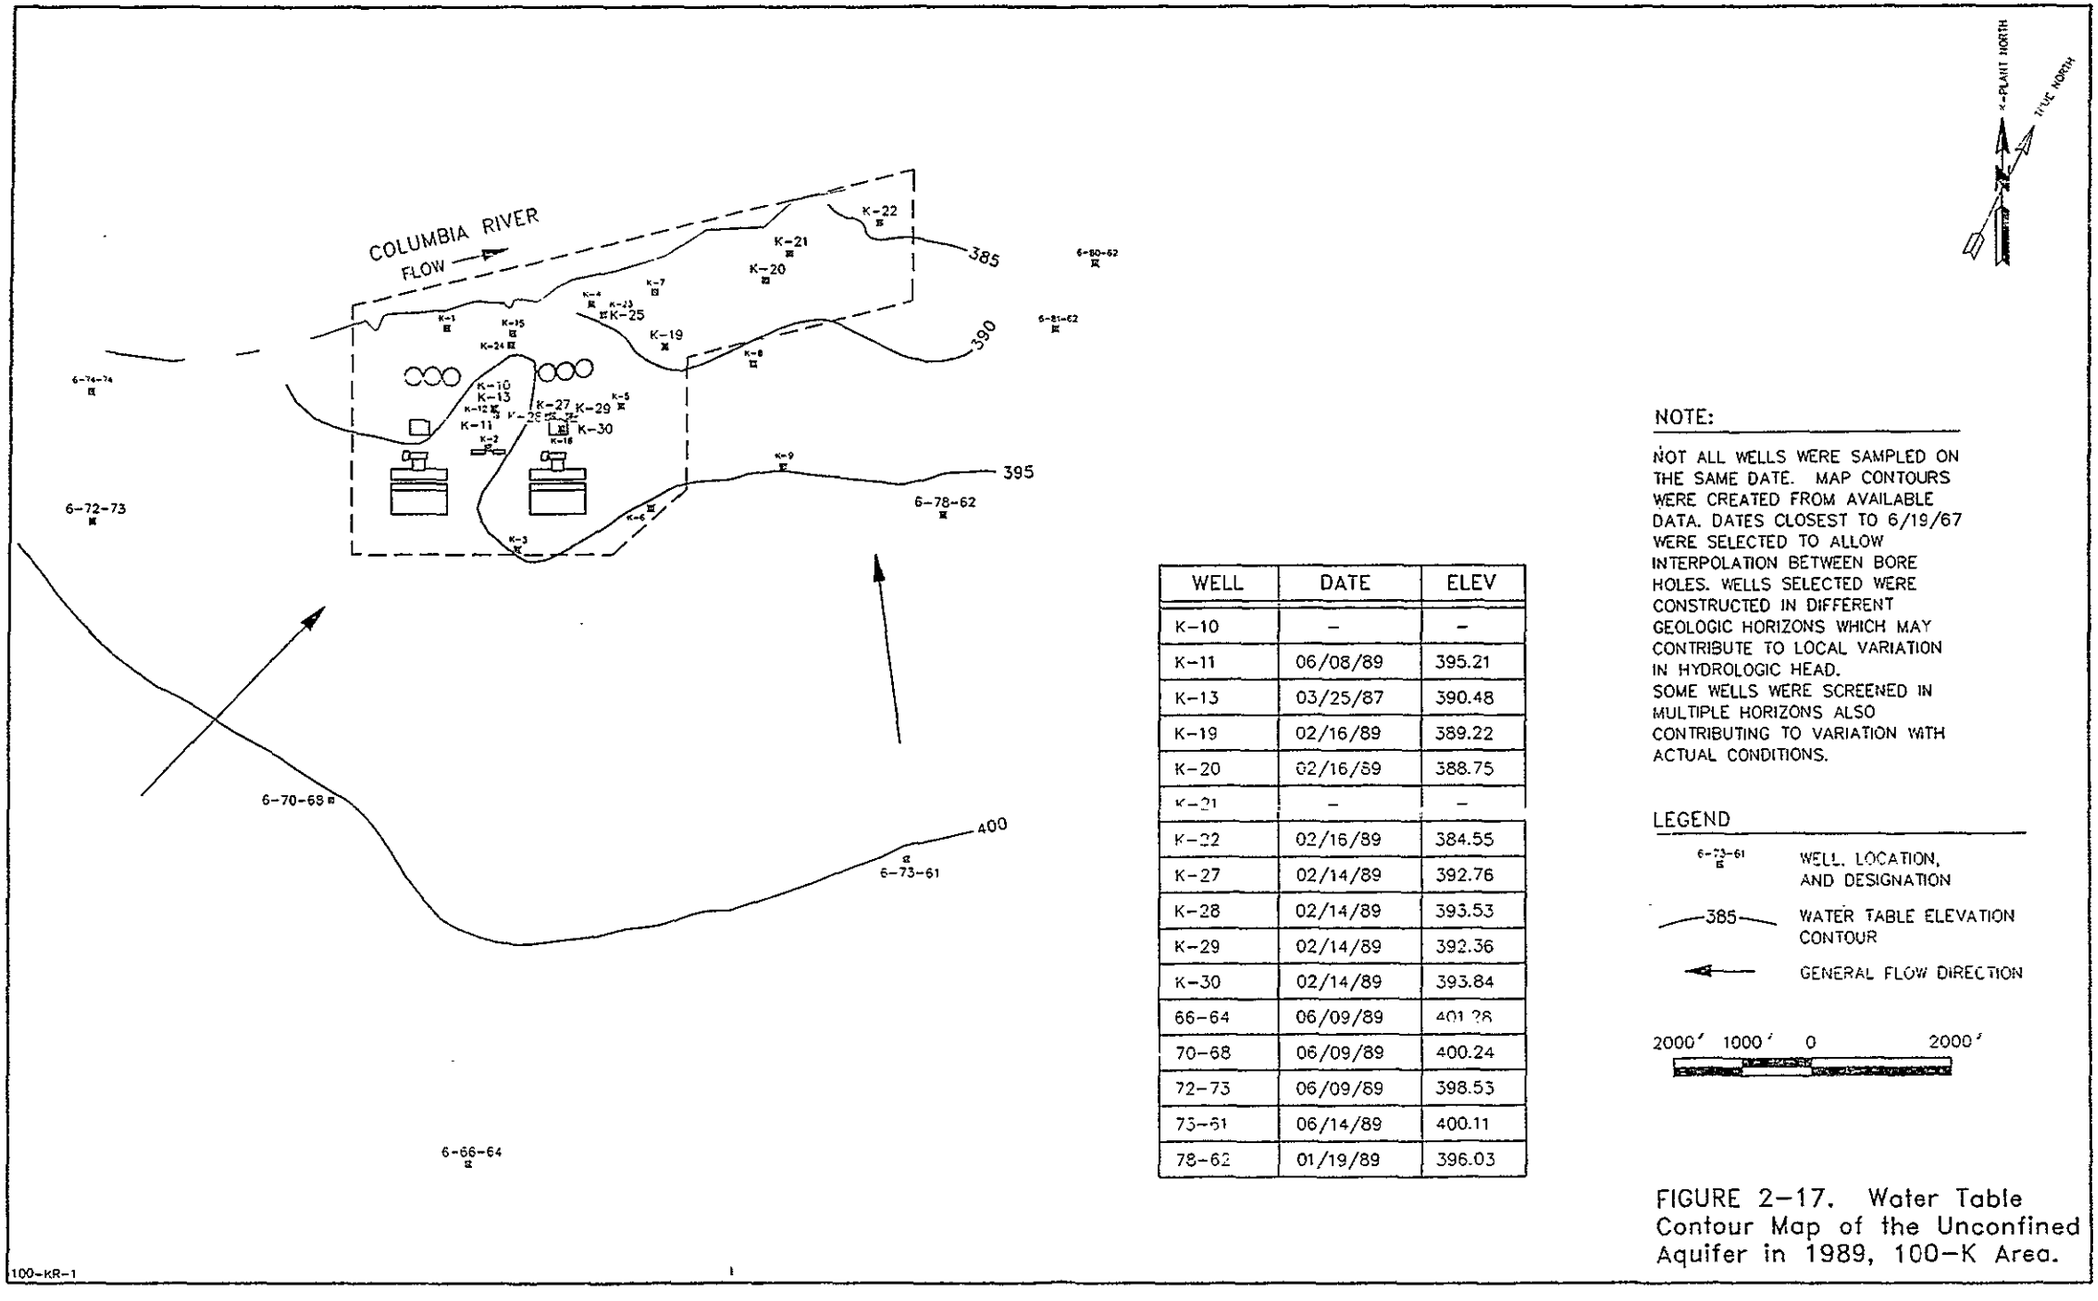

WELL	DATE	ELEV
K-10	–	–
K-11	06/08/89	395.21
K-13	03/25/87	390.48
K-19	02/16/89	389.22
K-20	02/16/89	388.75
K-21	–	–
K-22	02/16/89	384.55
K-27	02/14/89	392.76
K-28	02/14/89	393.53
K-29	02/14/89	392.36
K-30	02/14/89	393.84
66-64	06/09/89	401.28
70-68	06/09/89	400.24
72-73	06/09/89	398.53
73-61	06/14/89	400.11
78-62	01/19/89	396.03

FIGURE 2-17. Water Table Contour Map of the Unconfined Aquifer in 1989, 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

cause of higher ground water elevation in Well K11, and the relatively low elevation in Well K13 is not known. The ground water elevation difference could be explained by the following: different measurement dates; survey error; different well depths and multiple screened intervals; lithologic variations; and/or continued use of onsite facilities such as septic systems. (Known lithologic variations within the Ringold Formation are discussed in Section 2.2.2.1. Impacts of previous usage of onsite facilities are discussed in Section 2.2.3.2.6.)

It is expected that the water levels in the wells closest to the river fluctuate on the order of several feet in conjunction with fluctuations in river levels near the 100-K Area. Changes in the river level near the 100 Areas can be attributed to fluctuation in flow through the upriver Priest Rapids Dam. In the 100-H Area, fluctuations of about 10 ft (3.0 m) in the river level result in fluctuations of about 2 ft (0.6 m) in the water level in a well about 1,000 ft (300 m) from the river, as shown on Figure 2-18. A similar condition is assumed to exist in the 100-K Area. The flow gradient will change in response to river levels and may periodically reverse near the river. The river effect may even be greater in the 100-K Area, as compared to the 100-H Area,based on the relative orientations of the areas with respect to the river system, local lithology, and width of the river channel.

The changes in the ground water levels as a function of time may have affected ground water quality in the 100-K Area and in surrounding areas. For example, at the eastern end of the 116-K-2 trench, which is near the 100-N Area, ground water may periodically flow toward the 100-N Area (and vice versa), depending on the relative sizes of ground water mounds beneath the 100-K and 100-N Areas. When the mound beneath the 100-K Area was large, it may have driven contaminants toward the east and northeast.

Ground water flow directions and rates in the deeper, confined aquifers may be different than in the unconfined aquifer. For example, in the uppermost basalt aquifer, the flow direction may be to the south-southeast (Gephart et al. 1979, Graham et al. 1984).

2.2.3.2.4 Ground Water Recharge and Discharge. Recharge and other inflow to the shallow ground water system beneath the 100 Areas may include: the fluctuating water level of the Columbia River; percolation of precipitation; upward leakage of ground water from the deeper confined aquifers; lateral flow of unconfined ground water; and locally by recharge resulting from discharge of production water. The system discharges through similar mechanisms, e.g., discharge to the river and evaporation.

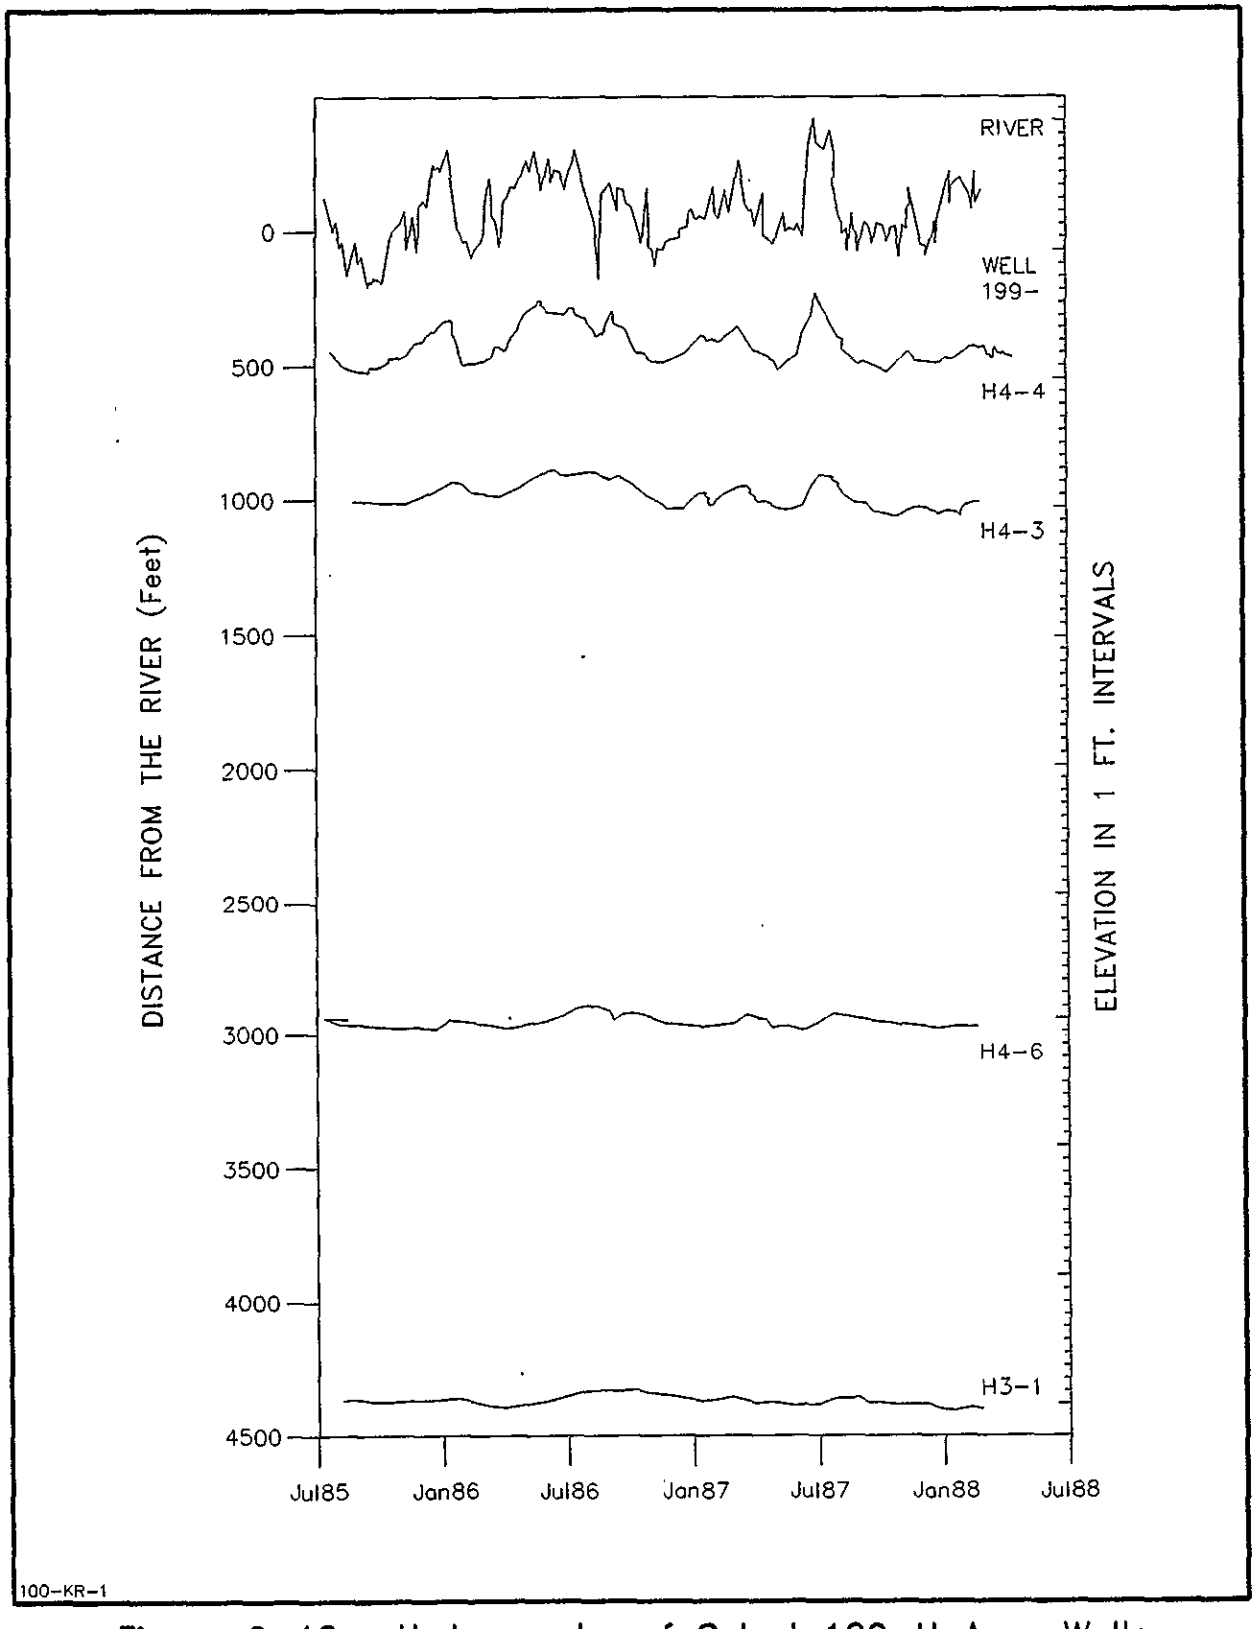

Figure 2-18. Hydrographs of Select 100-H Area Wells.

2.2.3.2.4.1 Ground Water/Surface Water Exchange. Ground water in the upper portion of the unconfined aquifer is known to discharge to the Columbia River along the river bank north of the 100 Areas. The discharges have apparently decreased since production operations ceased. Review of photographs indicate the occurrence of warm water seepage below the 100-K Area, implying a relatively shallow source for the seepage, e.g., lateral migration of water from cribs and trenches in the production areas. Shallow ground water that is not discharged directly to the river may flow downstream as subchannel flow. Deeper in the hydrostratigraphic section, e.g., producing layer 'C' and deeper, the river probably does not interact directly with ground water.

2.2.3.2.4.2 Precipitation. The amount of recharge from precipitation varies at different locations on the Hanford Site, depending on rainfall intensity and distribution, vegetative cover, soil texture, subsurface layering, and depth to ground water. Kirkham and Gee (1984) estimate that recharge is 1 to 3 in/yr (0.025 to 0.076 m/yr) for grass-covered soils. In areas covered with deep-rooted plants, little or no recharge occurs (Gee et al. 1989; Routson et al. 1988).

2.2.3.2.4.3 Upward Leakage. The potential for upward leakage of ground water from deeper confined aquifers exists, due to the fact that the potentiometric surface elevation is generally higher than the water table elevation (Gephart et al. 1979). However, the quantity of such leakage, if any, has apparently not yet been determined in the 100 areas, and its impact is poorly understood.

2.2.3.2.4.4 Lateral Flow and Site Discharges. Lateral ground water flow is from the south under natural conditions. However, the presence of a ground water mound underneath the 100-K Area during reactor operation may have locally overridden the natural gradient. Intentional and unintentional release of production water to facilities including septic tanks, cribs, ditches, ponds and leaking retention basins apparently created mounding beneath the site.

2.2.3.2.5 Historic Effects of 100-K Area Operations. Comparison between the water table elevations in 1967 and 1989 provides a partial understanding of the differences in ground water conditions before and after reactor operations. During the operation, a ground water mound existed as shown by the 1967 data (Figure 2-19). This mound locally elevated the water table as much as 25 ft (8 m) above the 1989 conditions. This increased elevation probably had several effects including reducing water table fluctuation due to river elevation changes. Of greater concern is the increased potential for downward contaminant migration, due to the opportunity for contaminated water recharging the water table coupled with increased hydraulic heads,

THIS PAGE INTENTIONALLY
LEFT BLANK

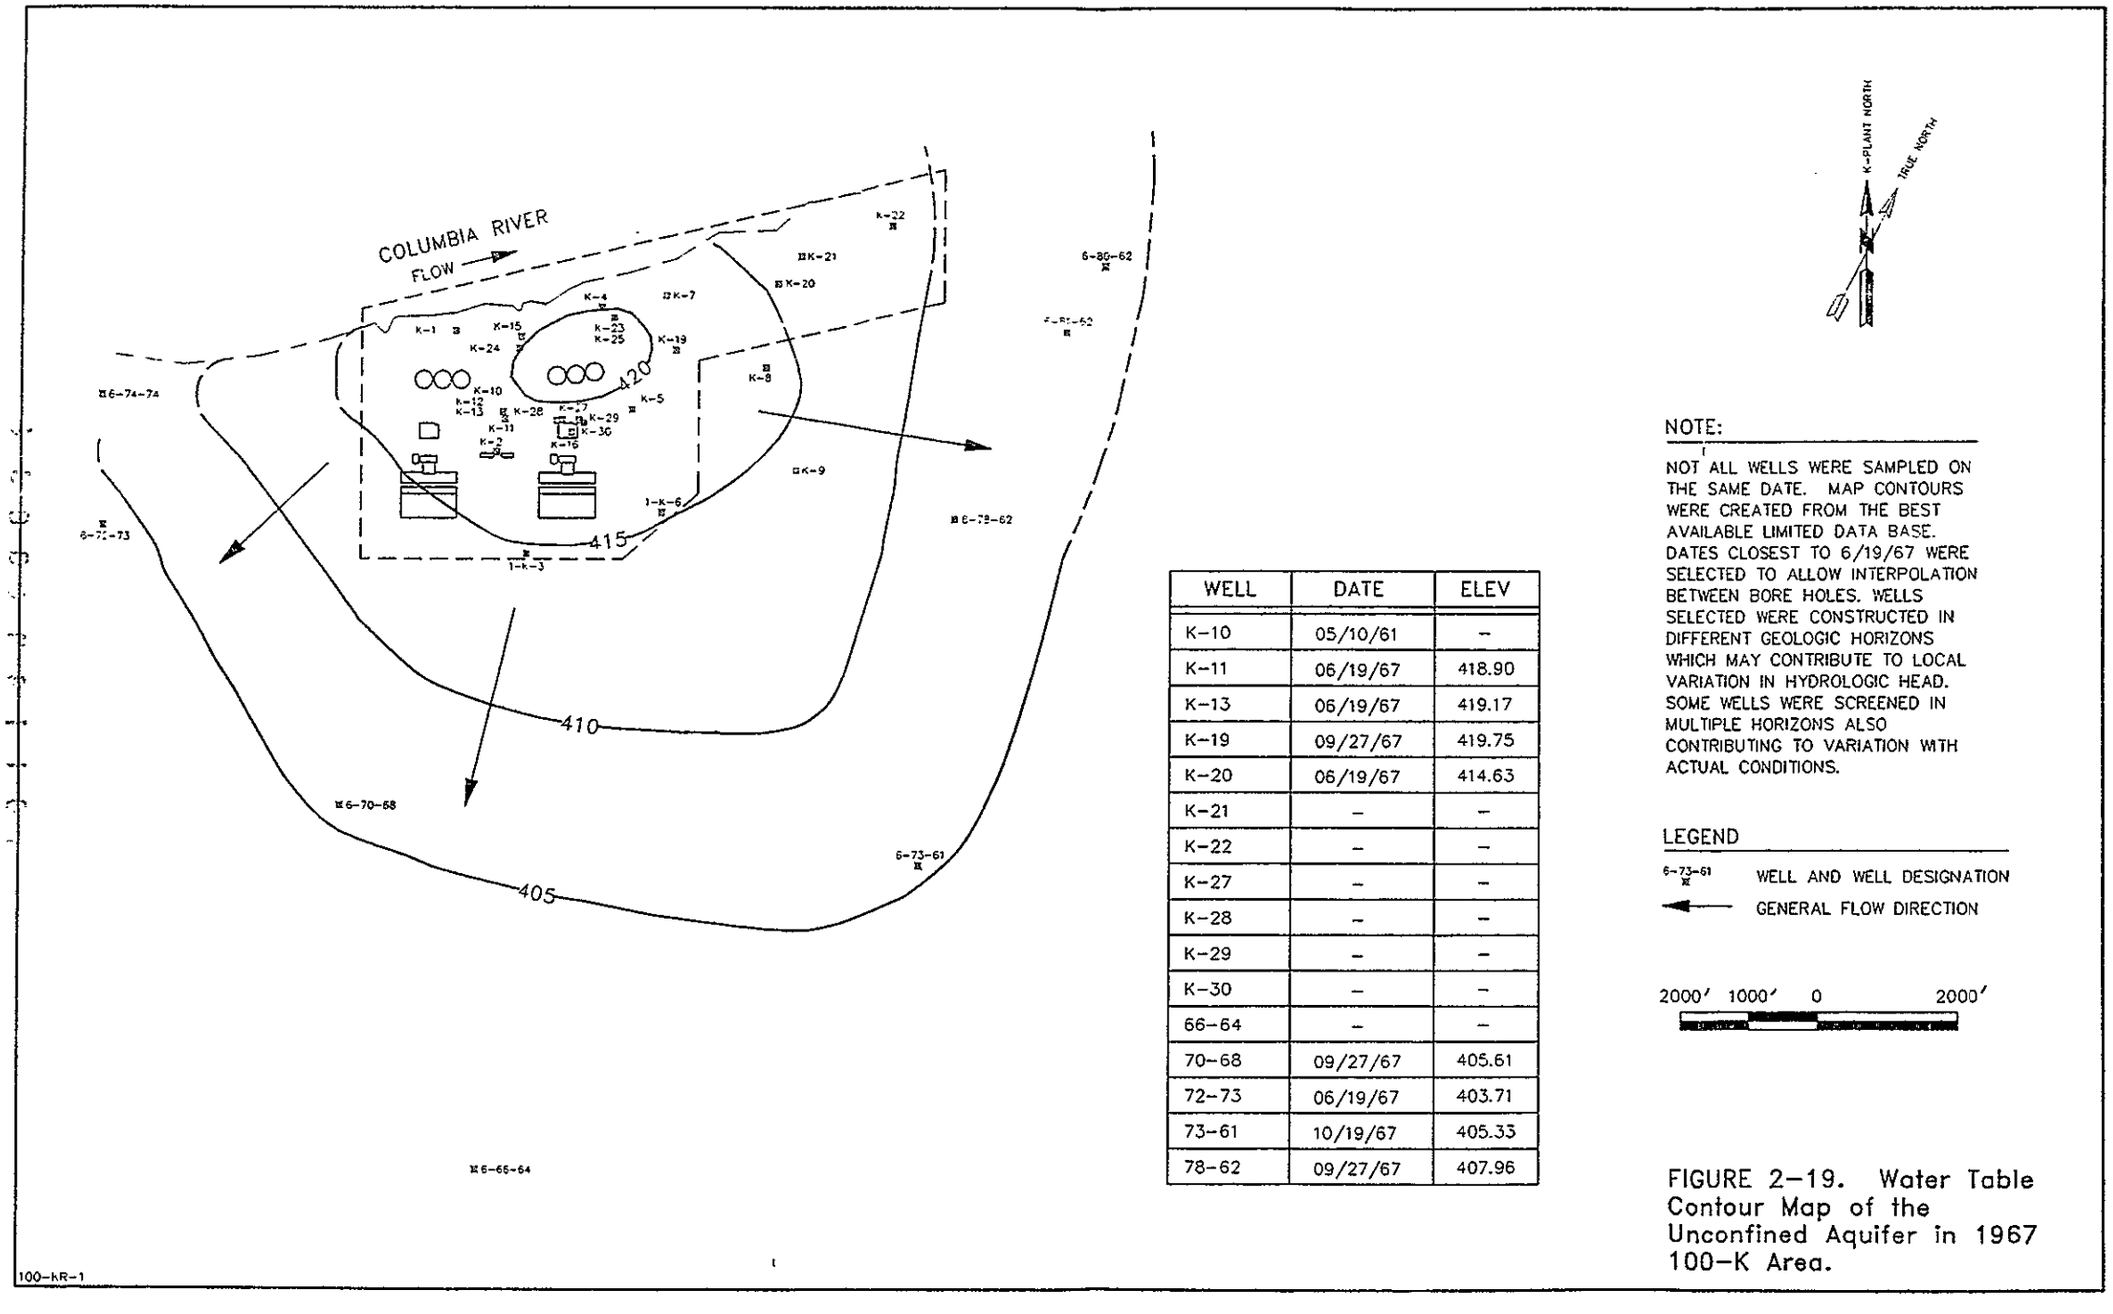

WELL	DATE	ELEV
K-10	05/10/61	–
K-11	06/19/67	418.90
K-13	06/19/67	419.17
K-19	09/27/67	419.75
K-20	06/19/67	414.63
K-21	–	–
K-22	–	–
K-27	–	–
K-28	–	–
K-29	–	–
K-30	–	–
66-64	–	–
70-68	09/27/67	405.61
72-73	06/19/67	403.71
73-61	10/19/67	405.33
78-62	09/27/67	407.96

NOTE:

NOT ALL WELLS WERE SAMPLED ON THE SAME DATE. MAP CONTOURS WERE CREATED FROM THE BEST AVAILABLE LIMITED DATA BASE. DATES CLOSEST TO 6/19/67 WERE SELECTED TO ALLOW INTERPOLATION BETWEEN BORE HOLES. WELLS SELECTED WERE CONSTRUCTED IN DIFFERENT GEOLOGIC HORIZONS WHICH MAY CONTRIBUTE TO LOCAL VARIATION IN HYDROLOGIC HEAD. SOME WELLS WERE SCREENED IN MULTIPLE HORIZONS ALSO CONTRIBUTING TO VARIATION WITH ACTUAL CONDITIONS.

LEGEND

6-73-61 WELL AND WELL DESIGNATION

GENERAL FLOW DIRECTION

2000′ 1000′ 0 2000′

FIGURE 2-19. Water Table Contour Map of the Unconfined Aquifer in 1967 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

and lateral migration in almost all directions away from the site. Once production ceased, the ground water elevations reverted to "natural" conditions. Contaminants which had been transported to the south could then migrate back toward the site and the river, perhaps at greater depth.

Figure 2-20, which shows water level measurements in three representative wells as a function of time, illustrates the rapid reduction in the water table elevation once production ceased. These data are also summarized on Table 2-8. Well 6-72-73, which is farther from the 100-K Area reactors and the associated cooling tanks (about 1 mi [1.6 km] southwest) showed the least change. Well K11, within the 100-K Area but slightly upgradient of the reactors, showed greater change. However, the greatest changes were in Well K20, which is downgradient of the reactors and along the 116-K-2 trench through which cooling water was discharged.

2.2.4 Surface Hydrology

The following section provides information on 100-K Area drainage patterns and also discusses streamflow and flooding potential of the adjacent Columbia River.

2.2.4.1 Site Drainage Patterns. No well-defined drainage channels exist within the 100-K Area because of the relatively flat topographic surface and highly permeable surficial deposits in the area. There is evidence of erosion between the north fence of the 100-K Area and the Columbia River. Surface runoff from the site could reach the river during significant storm events.

2.2.4.2 Seeps and Springs. During times of low water, various ground water seeps have been observed along the stretch of the Columbia River adjacent to the 100-K Area (McCormack and Carlile 1984) (Figure 2-16). The seepage consists primarily of bank storage draining back into the river. The volume of seep discharges at the 100-K Area has not been quantified.

2.2.4.3 Streamflow Characteristics. The Columbia River flows through the northern edge of the Hanford Site and forms part of the site's eastern boundary. The Columbia River is regulated by 11 dams within the United States, 7 upstream and 4 downstream of the Hanford Site as shown in Figure 2-21. The nearest upstream impoundment is Priest Rapids Dam and the nearest downstream impoundment is McNary Dam.

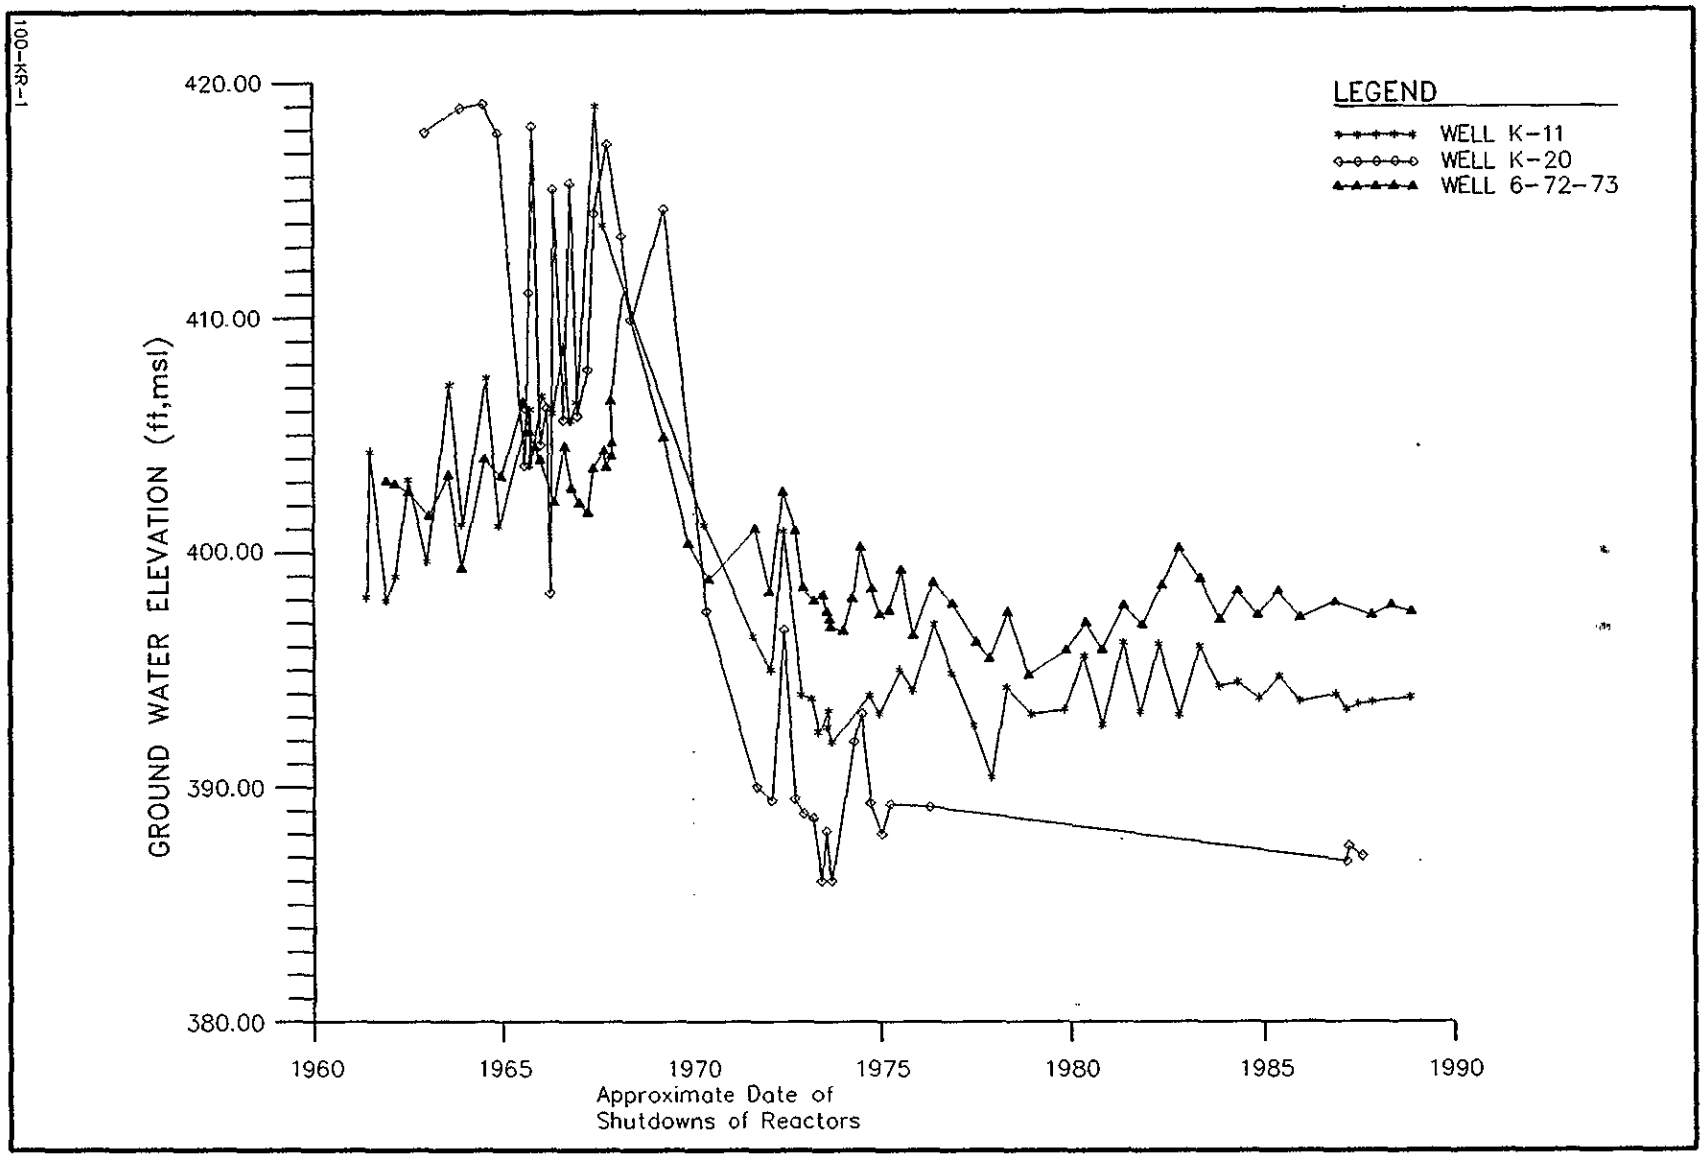

Figure 2-20. Ground Water Elevation vs. Time, 100-K Area.

Table 2-8. Ground Water Elevations in Select 100-K Area Monitoring Wells.

	Casing Elevation (ft msl)	Date Measured	Ground Water Elevation (ft, msl)
K-11	467.66	5/11/61	398.06
		6/17/61	404.21
		12/12/61	398.13
		2/22/62	398.86
		7/6/62	402.96
		12/28/62	399.72
		7/20/63	406.96
		12/11/63	401.04
		7/22/64	407.29
		12/19/64	400.99
		8/18/65	407.22
		9/22/65	404.74
		10/20/65	403.71
		12/28/65	407.22
		3/4/66	406.38
		4/14/66	404.05
		5/19/66	405.89
		7/28/66	408.82
		10/21/66	405.62
		12/30/66	406.68
		4/8/67	410.49
		6/20/67	418.90
		10/13/67	413.94
		4/24/69	407.12
		5/7/70	401.14
		9/11/71	396.27
		3/11/72	394.92
		7/14/72	400.79
		10/3/72	396.72
		1/5/73	393.83
		4/12/73	393.51
		7/7/73	392.24
		8/14/73	392.90
		8/28/73	392.32
		9/13/73	392.04
		9/29/73	391.70
		10/12/73	391.78
		10/19/74	393.79
		1/9/75	393.04
		4/15/75	393.88
		7/8/75	394.72
		12/4/75	394.06
		6/16/76	396.76
		12/9/76	394.60
		7/2/77	392.38

Table 2-8. Ground Water Elevations in Select 100-K Area Monitoring Wells.

	Casing Elevation (ft msl)	Date Measured	Ground Water Elevation (ft, msl)
		12/8/77	390.45
		6/2/78	394.10
		12/2/78	392.89
		12/2/79	393.18
		6/2/80	395.48
		12/2/80	392.64
		6/2/81	396.10
		12/2/81	393.08
		6/2/82	396.02
		12/2/82	393.01
		6/2/83	395.90
		12/2/83	394.22
		6/2/84	394.45
		12/2/84	393.75
		6/22/85	394.65
		1/4/86	393.57
		12/17/86	393.92
		3/26/87	393.20
		4/24/87	393.39
		7/29/87	393.38
		12/18/87	393.53
		12/7/88	393.80
		2/17/89	394.44
		6/9/89	395.21
K-20	422.57	12/31/57	415.17
		12/28/62	417.87
		12/11/63	418.96
		7/23/64	418.90
		12/19/64	417.84
		7/17/65	403.83
		8/18/65	406.44
		9/22/65	411.06
		10/20/65	418.02
		12/28/65	404.64
		3/4/66	406.49
		4/14/66	398.35
		5/19/66	415.51
		7/28/66	405.63
		10/20/66	415.77
		12/30/66	405.99
		4/7/67	407.79
		6/20/67	414.63
		10/13/67	417.48
		10/20/67	416.87

9 0 1 1 3 3 7 0 0 9 3

Table 2-8. Ground Water Elevations in Select 100-K Area Monitoring Wells.

	Casing Elevation (ft msl)	Date Measured	Ground Water Elevation (ft, msl)
		3/6/68	413.50
		6/5/68	409.94
		4/24/69	414.69
		5/7/70	397.37
		9/11/71	389.83
		3/11/72	389.22
		7/14/72	396.59
		10/3/72	389.34
		1/5/73	388.59
		4/12/73	388.45
		7/7/73	385.98
		8/14/73	387.91
		8/28/73	386.93
		9/13/73	386.67
		9/29/73	386.17
		10/12/73	386.62
		5/7/74	391.76
		7/24/74	392.86
		10/19/74	389.10
		1/9/75	387.90
		4/15/75	389.03
		4/19/76	389.03
		3/19/87	386.75
		3/26/87	386.91
		4/24/87	387.37
		7/29/87	386.99
		2/17/89	388.75
6-72-73	482.57	12/5/61	403.00
		12/12/61	402.97
		2/22/62	402.89
		7/3/62	402.61
		12/28/62	401.43
		7/23/63	403.21
		12/7/63	399.24
		7/15/64	403.92
		12/30/64	403.26
		7/17/65	406.57
		8/18/65	406.09
		9/22/65	405.13
		10/20/65	404.52
		12/28/65	404.09
		3/4/66	403.35
		4/14/66	402.28
		5/19/66	402.26

Table 2-8. Ground Water Elevations in Select 100-K Area Monitoring Wells.

Casing Elevation (ft msl)	Date Measured	Ground Water Elevation (ft, msl)
	7/28/66	404.49
	10/21/66	402.75
	12/30/66	402.14
	4/8/67	401.66
	6/20/67	403.71
	9/26/67	404.39
	9/28/67	404.35
	10/13/67	404.09
	10/20/67	404.02
	10/28/67	403.94
	11/10/67	404.04
	11/21/67	404.38
	11/28/67	404.27
	12/5/67	404.81
	12/12/67	406.54
	3/12/68	410.83
	3/19/68	411.12
	4/24/69	404.95
	11/13/69	400.38
	5/7/70	398.66
	9/15/71	400.86
	3/11/72	398.24
	7/14/72	402.63
	10/3/72	400.79
	1/5/73	398.52
	4/12/73	397.90
	7/7/73	398.14
	8/14/73	397.30
	8/28/73	397.15
	9/13/73	397.03
	9/29/73	396.87
	10/12/73	396.75
	1/18/74	396.72
	4/22/74	398.09
	7/23/74	400.21
	10/19/74	398.47
	1/9/75	397.34
	4/15/75	397.58
	7/8/75	399.19
	12/4/75	396.51
	6/16/76	398.67
	12/16/76	397.78
	7/2/77	396.16
	12/8/77	395.53
	6/2/78	397.39

9 0 1 1 3 3 1 3 0 9 0

Table 2-8. Ground Water Elevations in Select 100-K Area Monitoring Wells.

Casing Elevation (ft msl)	Date Measured	Ground Water Elevation (ft, msl)
	12/2/78	394.68
	12/2/79	395.78
	6/2/80	396.90
	12/2/80	395.82
	6/2/81	397.72
	12/2/81	396.87
	6/2/82	398.57
	12/2/82	400.23
	6/2/83	398.82
	12/2/83	397.14
	6/2/84	398.39
	12/2/84	397.32
	6/14/85	398.34
	1/4/86	397.33
	12/11/86	397.93
	12/12/87	397.44
	6/25/88	397.75
	12/7/88	397.52
	5/23/89	398.23
	6/10/89	398.53

100-KR-1

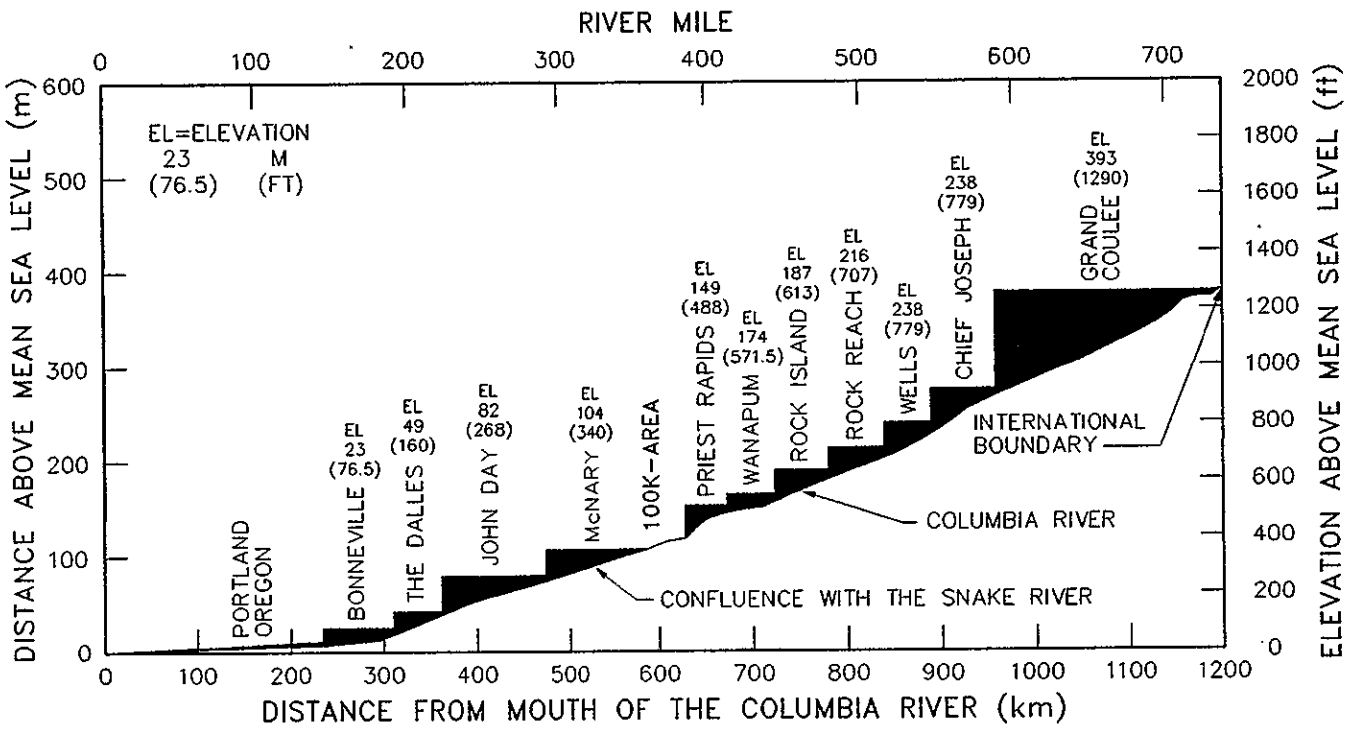

SOURCE: DOE 1982.

Figure 2-21. Profile of the Columbia River.

The Hanford Reach of the Columbia River is a free flowing stretch of river extending from the Priest Rapids Dam to the head of Lake Wallula, which is created by McNary Dam. Flows typically range from 36,000 to 250,000 ft^3/s (1,000 to 7,000 m^3/s) and during peak spring runoff, flows up to 450,000 ft^3/s (12,7000 m^3/s) have been recorded (McGavock et al. 1987). Monthly mean flows typically peak from April through June and are lowest from September through October. Maximum river depths range from 10 to 40 ft (3 to 12 m) at normal flow rates in the vicinity of the 100-K Area. Daily river elevations may fluctuate up to 5 ft (1.5 m) because of hourly water releases from Priest Rapids Dam (ERDA 1975). The monthly average river temperatures range from approximately 3° C in February to 19° C in August. There are numerous bends and several islands throughout the Hanford Reach.

There are three important time scales with regard to flow volumes in the Columbia River. There are daily variations associated with power production at Priest Rapids Dam and weekly variations associated with power production that reflect business cycle needs. In addition, there are seasonal variations associated with highly regulated discharges of the upper Columbia River to meet irrigation, flood control, and fishery conservation goals.

2.2.4.4 Flooding Potential. Historical records note that the maximum Columbia River floods occurred in June 1894 and June 1948 with maximum flows of approximately 740,000 and 690,000 ft^3/s (21,000 and 19,500 m^3/s), respectively (McGavock et al. 1987). The likelihood of floods with recurring magnitude has been significantly reduced since 1948 by construction of several flood control, water storage and electric power-generation dams upstream of the Hanford Site. The probable maximum flood, a theoretical maximum flood resulting from the most severe combination of meteorologic and hydrologic conditions possible in the region, would produce an approximate peak flow of 1,400,000 ft^3/s (39,600 m^3/s). A flood of this magnitude would be expected to inundate much of the 100-K Area (Cushing 1988), as shown in Figure 2-22. The 100- and 500-yr floods would have a lower flow magnitude than the probable maximum flood and are not expected to significantly affect the area.

The potential impact resulting from a hypothetical 50% breach of the Grand Coulee Dam has also been evaluated by the Army Corps of Engineers. The discharge resulting from the breach at the outfall of the dam was determined to be 8,000,000 ft^3/s (226,500 m^3/s) (Cushing 1988), which would flood the 100 Areas, 300 Areas, and most of Richland, Washington, as shown in Figure 2-23.

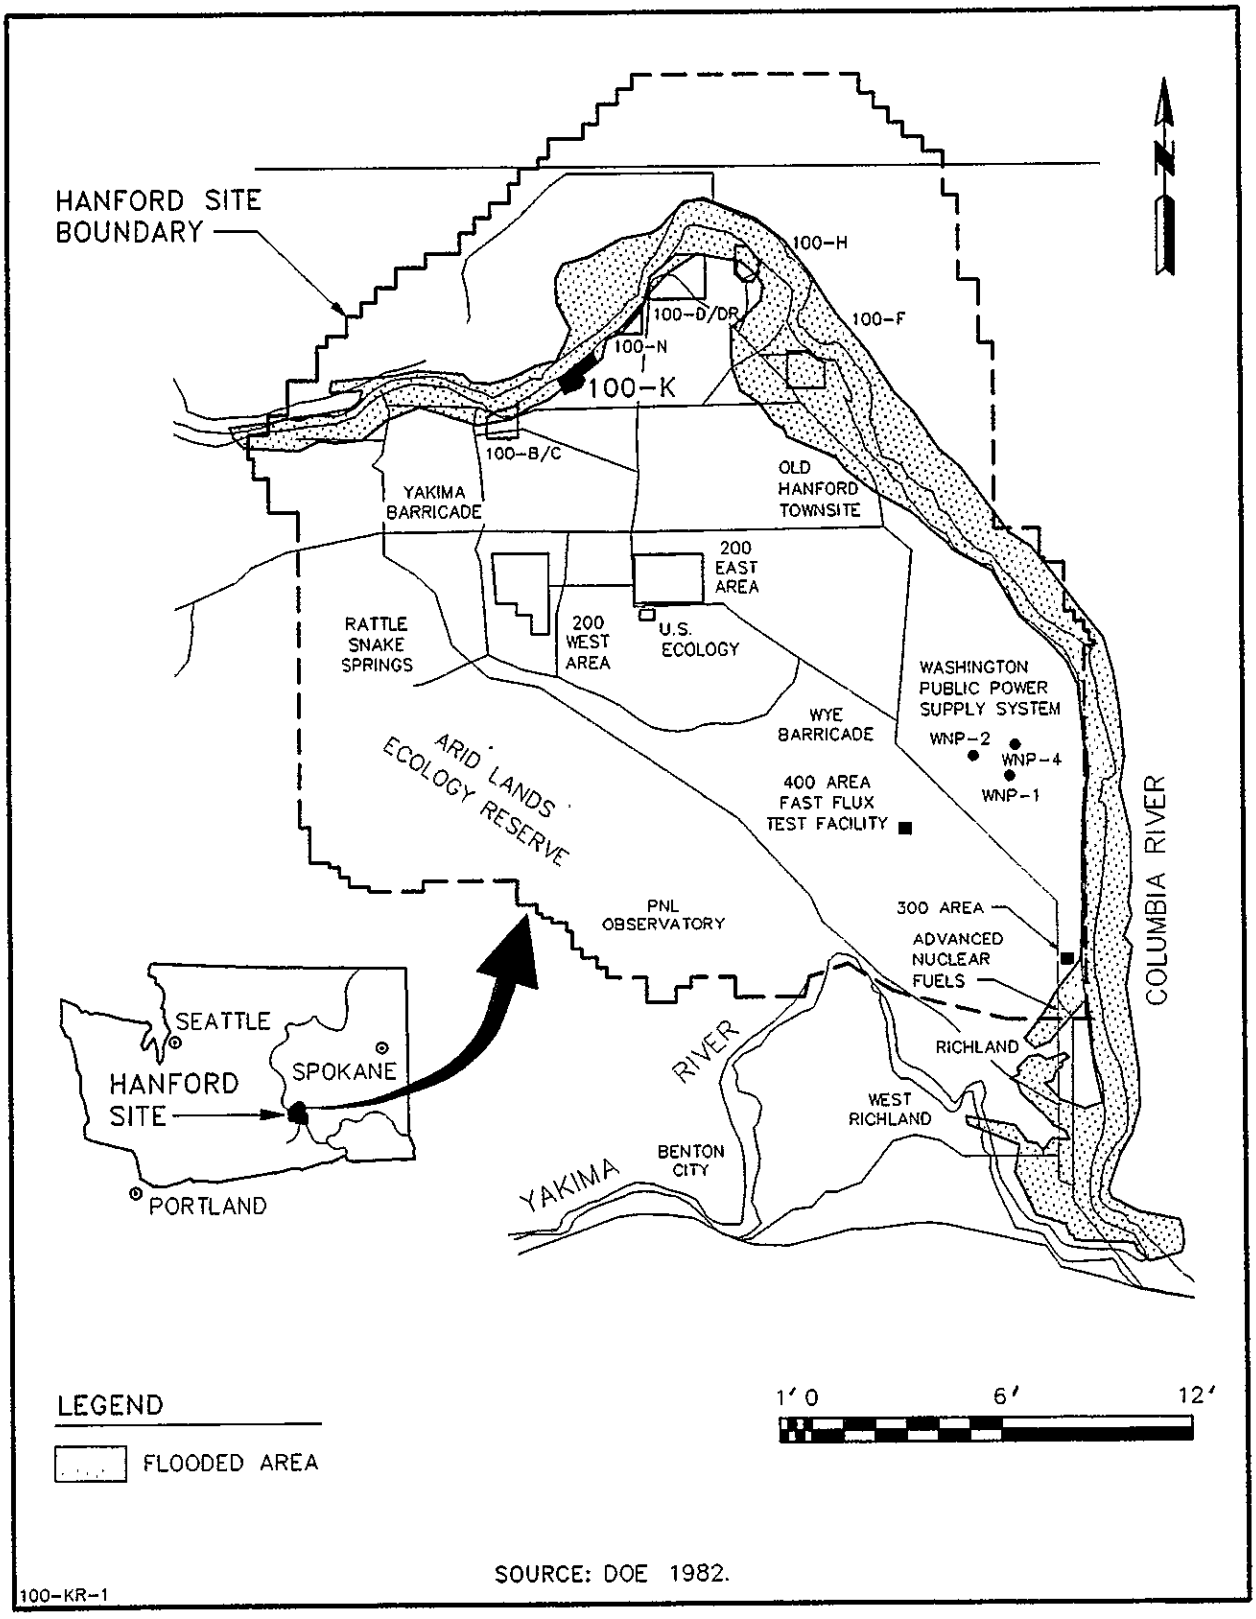

Figure 2-22. Flooded Area at the Hanford Site for the Probable Maximum Flood.

9 0 1 1 8 3 7 0 0 9 4

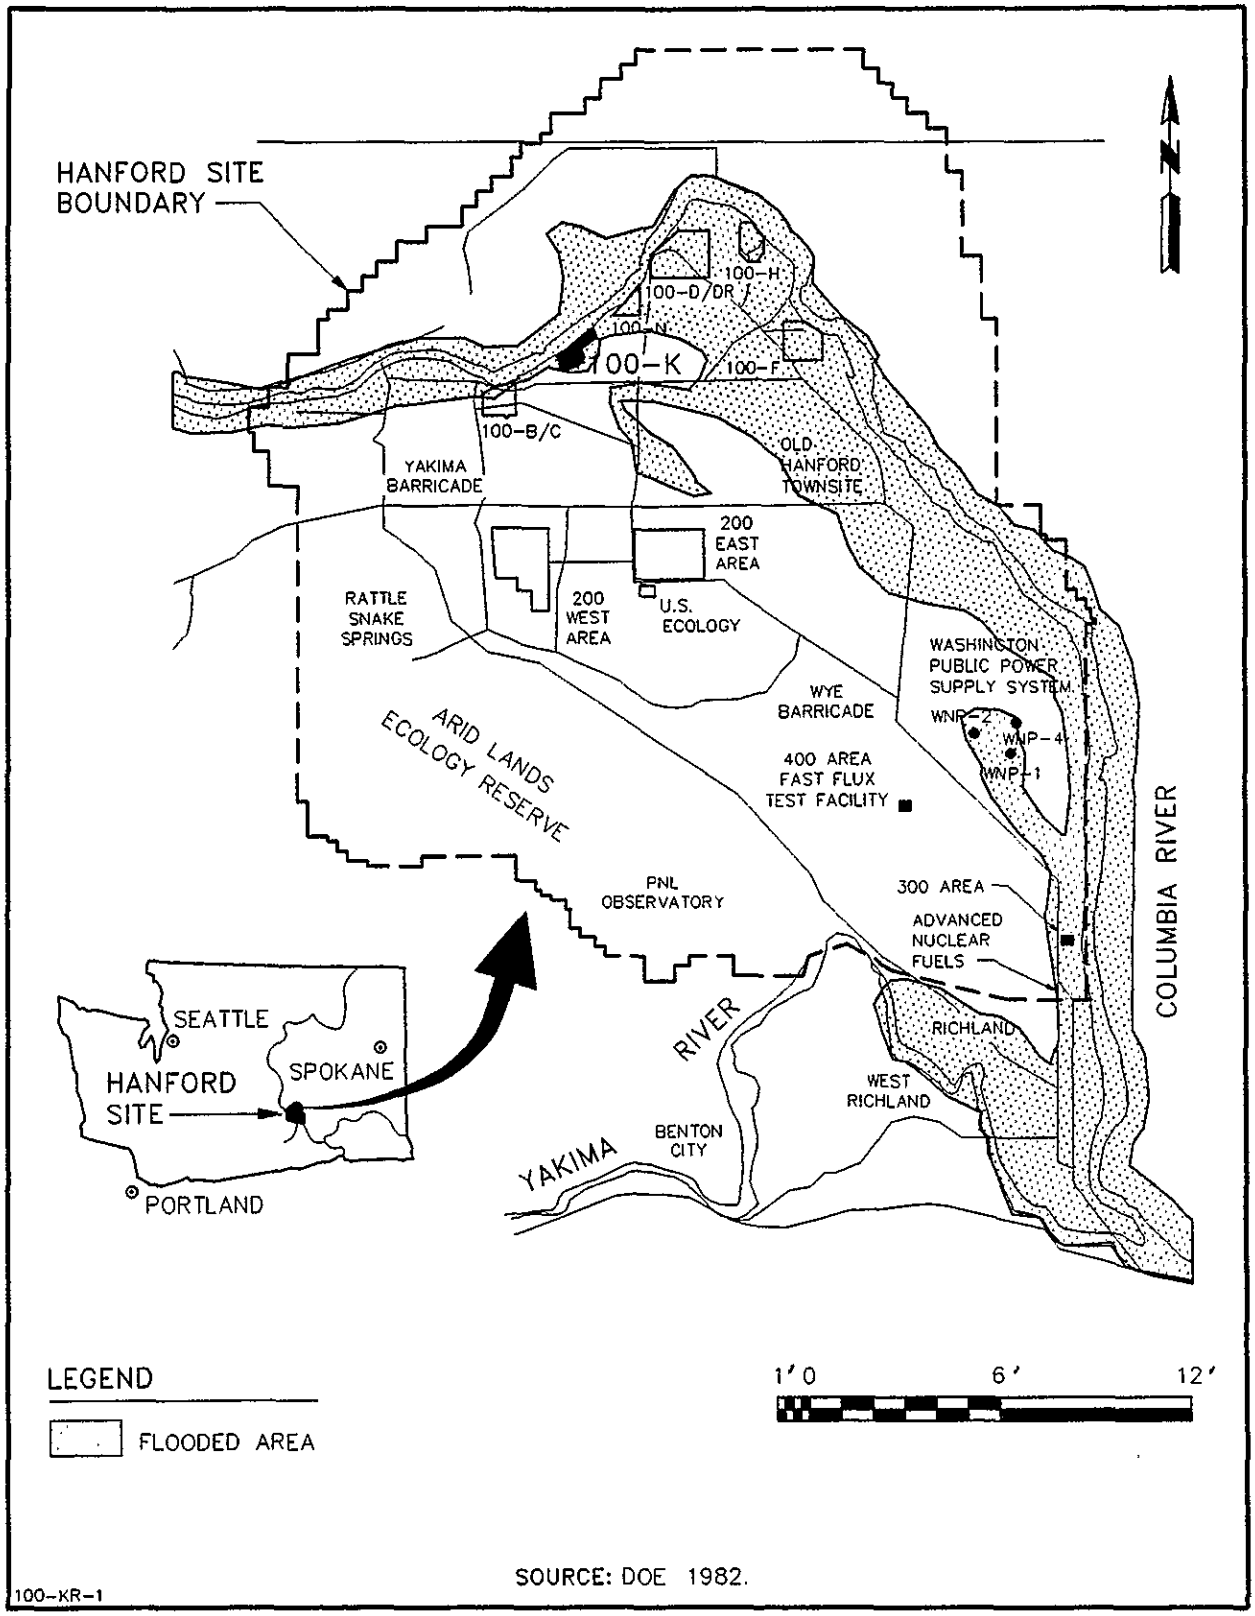

Figure 2-23. Flooded Area at the Hanford Site Resulting from a Hypothetical 50 Percent Breach of Grand Coulee Dam.

2.2.5 Meteorology

Climatological data are available from the Hanford Meteorological Station (HMS) located between the 200-East and 200-West Areas in the central portion of the Hanford Site. Since 1945 data have been collected at the HMS, located approximately 7 mi (11 km) south of the 100-K Area. Climatological data from the HMS are assumed to be representative of conditions at the 100-K Area. Additionally, wind data have been collected at 13 other sites on the Hanford Telemetry Network. The precipitation, temperature, wind, and evapotranspiration summaries presented in the following sections were largely extracted from DOE (1987).

2.2.5.1 Precipitation. The Hanford Site is located within a rain shadow formed by the Cascade Mountains 80 mi (130 km) to the west. The area is considered a desert, with an average annual precipitation of 6.3 in. (16 cm). Most of the precipitation falls during the winter, with nearly half of the annual amount occurring from November through February. Average winter monthly snowfall ranges from 0.3 in. (0.8 cm) in March to 5.3 in. (13.5 cm) in January. The record snowfall of 24 in. (62 cm) occurred in February 1916, but the second highest recorded snowfall was less than half this amount.

Days with precipitation greater than 0.5 in. (1.3 cm) occur with a frequency of less than 1% during the year. Rainfall intensities of 0.5 in/h (1.3 cm/h) persisting for 1 hr are expected once every 10 yr. Rainfall intensities of 1.0 in/hr (2.5 cm/hr) for 1 hr are expected only once every 500 yr.

The average annual relative humidity is 54%. Humidity is higher in winter than in summer, averaging about 75% and 35%, respectively.

2.2.5.2 Temperature. Average monthly temperatures at the Hanford Site range from 29° F (-1.5° C) in January to 76° F (24.7° C) in July. The lowest recorded monthly average winter temperature was 21° F (-5.9° C), and the highest recorded monthly average winter temperature was 44° F (6.9° C); both of these records were set during February. The highest recorded monthly average summer temperature was 82° F (27.7° C), which occurred during July. The coolest summer month on record was in June at 63° F (17.2° C).

2.2.5.3 Wind. Wind roses for 14 locations on the Hanford Site are displayed in Figure 2-24. The 100-K Area lies approximately equidistant from Hanford Telemetry Network Stations 13 and the HMS. The wind roses show prevailing winds from the northwest, with a secondary maximum for southwesterly winds.

9 0 1 1 9 3 0 0 9 5

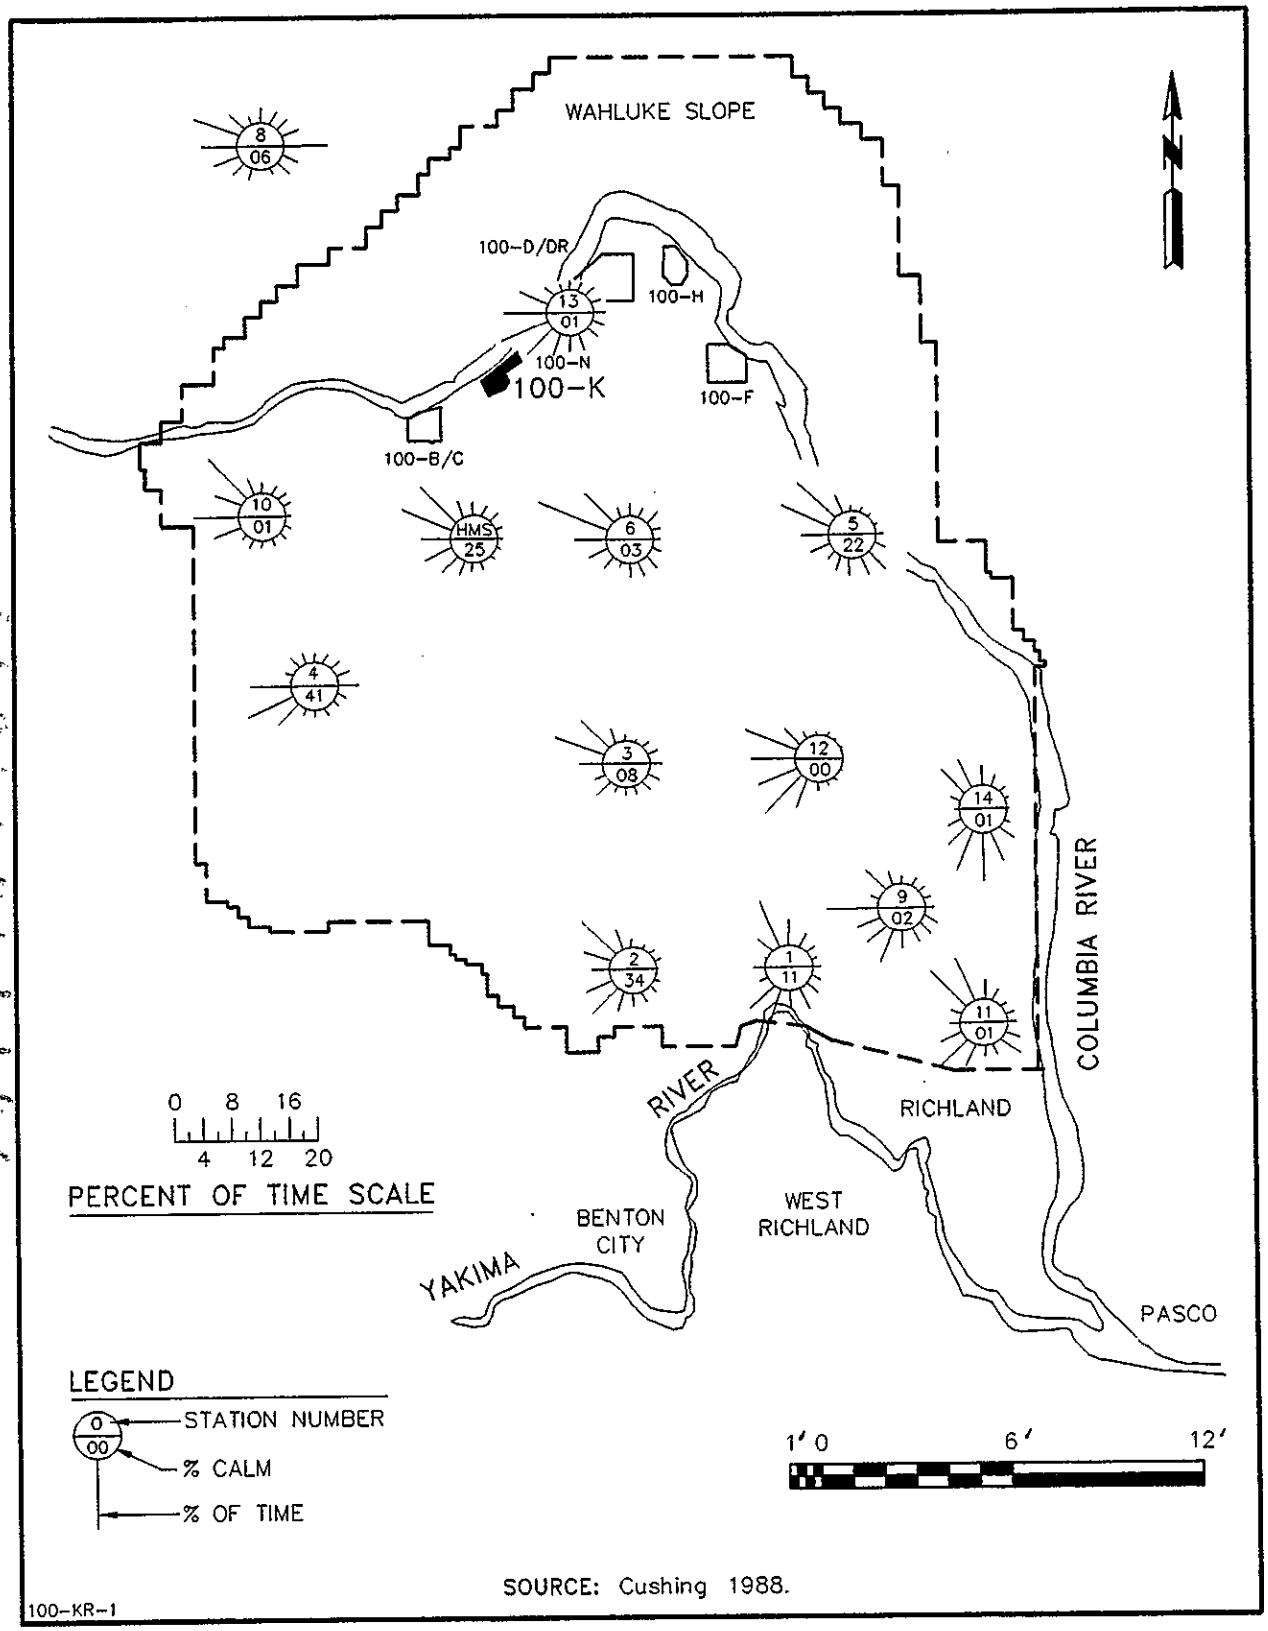

Figure 2-24. Hanford Site Wind Roses.

Winds from the northwest quadrant occur most often during the winter and summer. During the spring and fall, the frequency of southwesterly winds increase whereas winds blowing from other directions display minimal seasonal variation.

Monthly low average wind speeds are 6.2-6.8 mi/hr (10 to 11 km/hr). Monthly peak wind speeds average 8.7 to 9.9 mi/hr (14 to 16 km/hr) in the summer. Winds are usually southwesterly and in the summer, the high-speed southwest winds are responsible for most of the region's dust storms. In addition, high-speed winds are associated with afternoon winds and thunderstorms. The summertime drainage winds are normally northwesterly with average wind speeds up to 31 mi/hr (50 km/hr). An average of 10 thunderstorms occur yearly, but the winds do not display a directional preference.

2.2.5.4 Evapotranspiration. Mean annual evapotranspiration for the area immediately southeast of the Hanford Site has been estimated to be about 29 in. (74 cm).

2.2.6 Environmental Resources.

The flora, fauna, critical habitats, land use, water use, and sensitive environments for the area in and around the 100-K Area are summarized in the following sections.

2.2.6.1 Flora. The Hanford 100-K Area consists of undeveloped semiarid land with clusters of industrial buildings connected by a surface network of roadways, railroads, and electrical transmission lines. A significant amount of the active flora in the 100-K Area has been disturbed as a result of construction, reactor operation, and deactivation activities. Vegetation is controlled in contamination zones using nonselective herbicides. The natural vegetation consists mostly of a sparse covering of desert shrubs and drought-resistant grasses. The predominant vegetation type is the sagebrush/cheatgrass/bluegrass community, and bitterbrush and rabbitbrush are also common shrubs (DOE 1987; Jacquish and Mitchell 1988). A narrow riparian zone, consisting of grasses and herbs interspersed with a few scattered deciduous shrubs and trees, exists along the banks of the Columbia River.

Table 2-9 includes state-designated endangered and threatened flora that could potentially exist at the Hanford Site. State designations are as strict as or stricter than federal designations. The endangered persistent sepal yellowcress, generally found in moist to marshy places, is known to inhabit the Hanford Reach shoreline of the

Table 2-9. Washington State List of Endangered Flora Species Having the Potential to be Found on the Hanford Site.

Endangered Vascular Plants

Persistant sepal yellowcress (*Rorippa columbiae*): Known to have a scattered distribution because of specialized habitat requirements or habitat loss; generally occurs in moist to marshy places and is known to inhabit the wetted shoreline of the Hanford reach of the Columbia River in Benton County.

Threatened Vascular Plants

Columbia milk-vetch (*Astragalus columbianus*): Locally endemic to the area in the immediate vicinity of Priest Rapids Dam, including a portion of Benton County; could potentially occur along the Columbia River in the northwestern portion of the Hanford Site.

Eatonella (*Eatonella nivea*): Known to occur along the Columbia River in Grant County; could potentially occur along the river in the northern portion of the Hanford Site.

Hoover's desert parsley (*Lomatium tuberosum*): Locally endemic to southcentral Washington, including Benton County; known to inhabit rocky hillsides.

Sources: DOE 1987; Hitchcock and Crunquist 1978; Department of Natural Resources 1987; Department of Wildlife 1987.

Columbia River. Therefore, this endangered species could potentially occur along the river shoreline of the 100-K Area.

Several threatened plant species are located within or near the Hanford Site. Eatonella is known to occur along the Columbia River in nearby Grant County and could, therefore, potentially occur along the Columbia River in or near the 100-K Area. The Columbia River milk-vetch is locally endemic near the vicinity of Priest Rapids Dam. It is unlikely that this species would be encountered near the 100-K Area. Hoover's desert parsley is known to exist in Benton County, but appears to inhabit only rocky hillsides and is thus unlikely to occur at the 100-K Area.

2.2.6.2 Fauna. Predominant fauna of the sagebrush/grass community that could potentially reside in or near the 100-K Area are the cottontail rabbit, jackrabbit, Great Basin pocket mouse, horned lark, and the western meadowlark. Mule deer, elk, coyotes, and various species of raptors forage in this habitat type, and grasshoppers are the most conspicuous insects in the community (DOE 1987).

Dominant fauna along the Columbia River include muskrat, porcupine, raccoon, quail, pheasant, and waterfowl (ducks and geese) (DOE 1987). The long-billed curlew is also known to nest within the cheatgrass habitat in the 100-K Area (Allen 1980). A spit on the south side of the island at the tip of the peninsula between the 100-D/DR and 100-H Areas and about 5 mi (8 km) downstream from the 100-K Area serves as the primary loafing and staging area for curlews from the Hanford Site and the Wahluke Slope (Allen 1980). Peak waterfowl use occurs from late December through mid-January. Great Basin Canada geese have historically nested on the sparsely vegetated islands in the Hanford Reach of the Columbia River. A resident flock of Canada geese nests on islands in the Columbia River near 100-D/DR Area about 5 mi (8 km) downstream from the 100-K Area (Fitzner and Rickard 1983). Goose nests established on these islands have been counted each year since 1953 during the nesting season. The results have varied each year with a general upward trend occurring in recent years as shown in Figure 2-25. The shift may be attributable to the increase in coyote population in the upstream islands (Jacquish and Bryce 1989).

The Columbia River itself provides habitat for a wide variety of fish. Important game species are chinook salmon, steelhead, coho salmon, sockeye salmon, smallmouth bass, largemouth bass, sturgeon, walleye, yellow perch, and channel catfish. The Hanford Reach provides the most important area in the main stem of the Columbia River for fall spawning Chinook salmon. Increases in this population over the years are responsible for attracting numerous bald eagles to the area in the fall and

9011031 0010

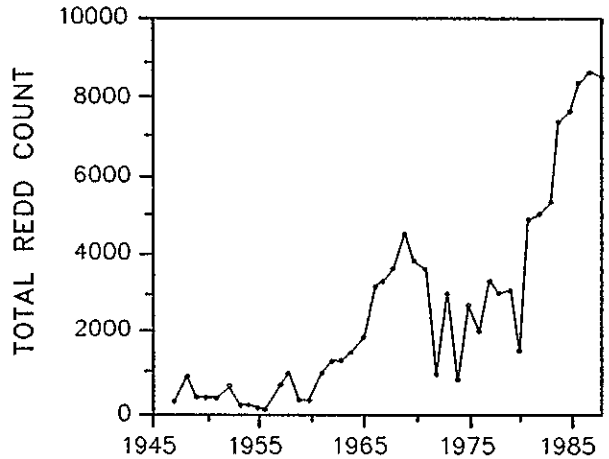

COUNTS OF CHINOOK SALMON SPAWNING REDDS IN THE HANFORD REACH OF THE COLUMBIA RIVER, 1947 THROUGH 1988.

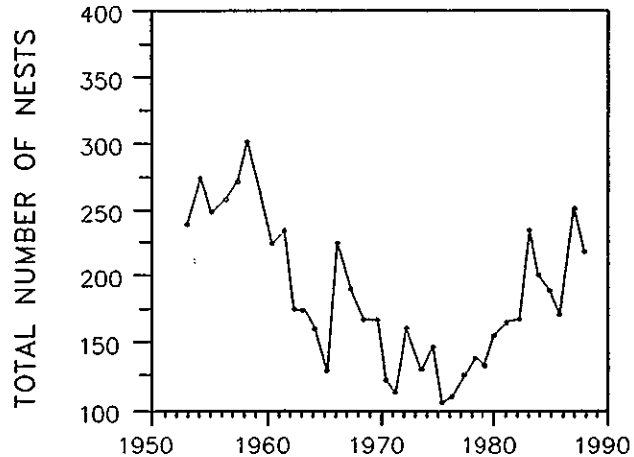

NUMBER OF CANADA GOOSE NESTS ESTABLISHED ON ISLANDS IN THE HANFORD REACH OF THE COLUMBIA RIVER, 1953 THROUGH 1988.

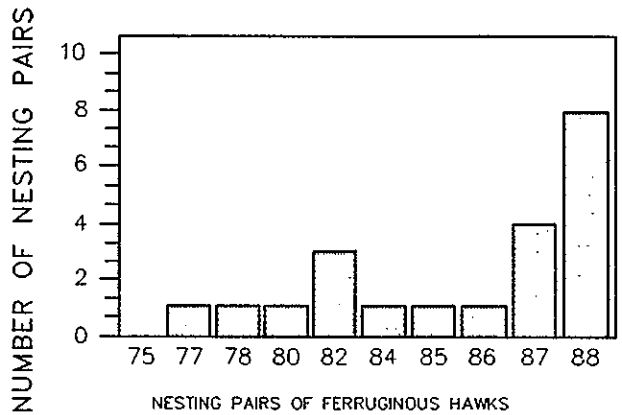

NESTING PAIRS OF FERRUGINOUS HAWKS

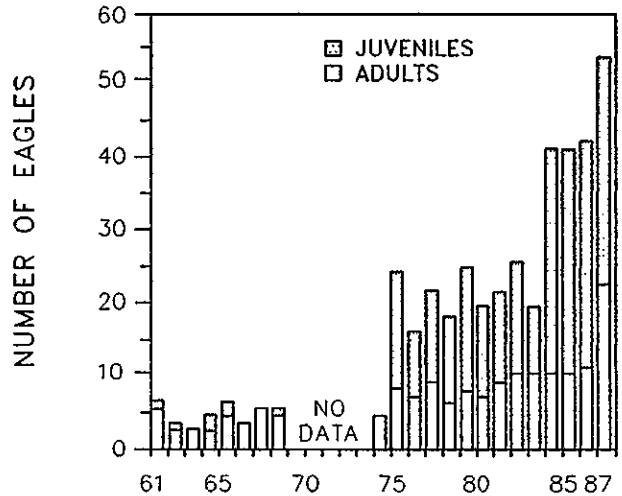

MAXIMUM NUMBERS OF BALD EAGLES SEEN ALONG THE HANFORD REACH OF THE COLUMBIA RIVER DURING AERIAL FLIGHTS IN FALL AND WINTER MONTHS, 1961 THROUGH 1987.

100-KR-1

SOURCE: Jacquish and Bryce 1989.

Figure 2-25. Wildlife, Fish and Bird Statistics at the Hanford Site.

winter to feed on the spawned-out salmon carcasses (Jacquish and Bryce 1989) as shown in Figure 2-25. Table 2-10 also lists the state endangered and threatened fauna that could potentially occur at the Hanford Site. The American white pelican and the Aleutian Canada goose are endangered animal species which occasionally occur on and along the Columbia River near the 100-K Area. During 1989, the population of white pelicans along the Hanford Reach of the river increased from a transient population of only 7 to 12 birds to a population of more than 50 birds.

The bald eagle and ferruginous hawk, both threatened species, are frequent visitors to the Hanford Site. Bald eagles spend the winter months along the Hanford Reach of the Columbia River and use groves of tall trees along the river as a roosting site. Ferruginous hawks nesting pairs have been counted on the Hanford Site since 1977 (Figure 2-25). The trend toward population increases is attributed to the hawks' attraction to recently constructed electrical transmission line towers as nesting sites (Jacquish and Bryce 1989).

2.2.6.3 Critical Habitats. The roost trees and foraging areas of the bald eagle and ferruginous hawks are regarded as critical habitats and must, therefore, be protected (Washington Department of Wildlife 1987). Since the other endangered and threatened animal species that use the 100-K Area environment are transient by nature, no other critical animal habitats have been declared in that area.

If the endangered persistent sepal yellowcress or the threatened eatonella are found to exist within or near the operable unit, the area of their occurrence would constitute a critical habitat for such plants. No specific information to the occurrence of these species within the project boundaries is currently available.

2.2.6.4 Land Use. Access to Hanford Site is administratively controlled and is expected to remain this way for the foreseeable future to ensure public health and safety and for reasons of national security (DOE 1987). The site is currently zoned as an unclassified use district by Benton County. Under the county's comprehensive land-use plan, the Hanford Site may be used for nuclear related activities. Non-nuclear activities are authorized only on approval from DOE (DOE-RL 1988).

Immediately north and across the river from the 100 Areas are the 32,100-acre Saddle Mountain National Wildlife Refuge and the 55,600-acres Washington Department of Wildlife Reserve (Figure 1-1). These lands provide a buffer zone around the reactor complexes (DOE 1987).

Table 2-10. Washington State List of Endangered and Threatened Fauna Species Having the Potential to be Found on the Hanford Site.

Page -1

Endangered Birds

Aleutian Canada goose (*Branta canadensis leucopareia*): Nests in the Aleutian Islands of Alaska and winters in California; has been occasionally sighted, as a migrant, in Benton, County; a potential seasonal user of the Columbia River valley, feeding on grasses, sedges, and berries.

American white pelican (*Pelecanus erythrorhynchus*): Winters along the southern Pacific Coast and the Gulf Coast and nests in northern prairie and intermountain lakes; no longer nests in Washington; migrates through eastern Washington; flocks are common in the Columbia Basin during the summer; known to occasionally winter on the Columbia River, foraging on fish, amphibians, and crustaceans and roosting on islands.

Peregrine falcon (*Falco peregrinus*): Breeds and winters in eastern Washington, inhabiting open marshes, river shorelines, wide meadows and farmlands; nests on undisturbed cliff faces; an erratic visitor at the Hanford Site, feeding on songbirds, shorebirds, and waterfowl.

Sandhill crane (*Grus canadensis*): Inhabits open prairies, grainfields, shallow lakes, marshes, and ponds, nesting in drier grassy and marshy areas; common migrant during the spring and fall in Washington; some known and suspected nesting sites in eastern Washington; unlikely visitor at the Hanford Site.

Upland sandpiper (*Bartramia longicauda*): Inhabits ungrazed and lightly grazed prairies, upland meadows, and fields that are usually located near lakes or rivers; breeds in the northern and central portions of North America and winters in South America; uncommon in eastern Washington; a potential migratory visitor at the Hanford Site, feeding on insects, worms, and some vegetation.

Western snowy plover (*Charadrius alexandrus*): A coastal species rarely observed in eastern Washington.

Table 2-10. Washington State List of Endangered and Threatened Fauna Species Having the Potential to be Found on the Hanford Site.

Page -2

Threatened Birds

Bald eagle (*Haliaeetus leucocephalus*): A regular winter visitor to the Columbia River, feeding on spawning salmon and perhaps waterfowl and small mammals; roosting areas are known to exist in the 100 Areas of the Hanford Site (roost sites and winter feeding areas constitute critical habitats for this species).

Ferruginous hawk (*Buteo regalis*): Inhabits open prairies and sagebrush plains, usually with rocky outcrops or scattered trees, located well away from human disturbance; known to nest in Benton and Franklin counties, with Franklin County possessing the majority of the nests within Washington; known to nest in the Hanford Site on the Arid Lands Ecology Reserve; rarely winters in Washington; known to occasionally forage on small mammals, birds, and reptiles on sagebrush plains in the Hanford Site.

Threatened Mammals

Pygmy rabbit (*Sylvilagus idahoensis*): Inhabits undisturbed areas of sagebrush with soils soft enough in which to dig burrows; once known to exist on the Hanford Site near springs in the Snively Basin west of the 200 Area plateau in the Rattlesnake Hills.

Sources: DOE 1987; Hitchcock and Crunquist 1978; Department of Natural Resources 1987; Department of Wildlife 1987.

Land use in the area surrounding the Hanford Site consists primarily of irrigated and dry-land farming, livestock grazing, and urban and industrial development. Agricultural lands are found north and east of the Columbia River and south of the Yakima River. Principal agricultural crops include hay, wheat, potatoes, corn, apples, soft fruit, hops, grapes, and vegetables. Most industrial activities in the area are associated with either agriculture or energy production (DOE 1987).

2.2.6.5 Water Use. The 100-K Area has two National Pollutant Discharge Elimination System (NPDES) discharges (outfalls) under Permit No. WA-000374-3. These outfalls are designated 003, which is the 181-KE inlet screen backwash, and 004, which is the 1908-K effluent discharge outfall. This permit is being renegotiated with EPA. The following measurements are required for the nonradioactive 100-K discharges: flow rate, suspended solids, temperature, pH, and chlorine.

2.2.6.5.2 Ground Water. The nearest known domestic use ground water well is located about 6 mi (10 km) upstream at the Vernita Bridge rest area. Because of the surrounding land use, the nearest that a private well could be located to the 100-K Area would be approximately 4 mi (6 km) to the north across the Columbia River.

2.2.6.6 Sensitive Environments. The Columbia River's importance as a recreational resource and a regional source of drinking and irrigation water, as well as being a productive habitat for waterfowl, economically important fish species, and transitory endangered and threatened wildlife, could merit special concern for the environment during implementation of remedial activities at the 100-K Area. Because of the presence of critical bald eagle habitat (Section 2.2.6.3), the 100-K Area and vicinity could be regarded as a sensitive environment, as defined in 40 CFR Part 300, Appendix A.

The Columbia River is regarded as an important environment with respect to the 100-K Area. The Hanford Reach has been designated a class A (excellent) surface water by the state of Washington (WAC 173-201-080[2]). This designation requires that water quality be maintained for the following uses (WAC 173-201-045[2][b]):

- Domestic, industrial, and agricultural water supply
- Stock watering
- Fish and shellfish migration, rearing, spawning, and harvesting
- Wildlife habitat

- Recreation (including primary contact recreation)
- Commerce and navigation.

The Hanford Reach is also being considered for status as a national wild and scenic river (Jacquish and Bryce 1989).

2.2.7 Human Resources

2.2.7.1 Demography. No one resides on the Hanford Site. Land use, in the area precludes any residential unit being closer than 5 mi (8 km) to the 100-K Area. The working population for the entire 100 Area numbers approximately 760 (EPA 1988b).

2.2.7.2 Archaeological Resources. Archaeological sites are found in various locations on the Hanford Site, several along the Hanford Reach of the Columbia River. Many of the Hanford historic sites are listed in the National Register of Historic Places in Archaeological Districts. The Ryegrass Archaeological District overlaps the 100-K Area and includes three archaeological sites. Two of the sites (45BN149 and 45BN151) are camp sites; the third is a cemetery used from prehistory into recent times (Rice 1980). Site 45BN150 is located inside the 100-KR-1 operable unit. In addition to its National Register listing, this site is considered to be sacred by the Wanapum and Yakima Indian people. Upstream of the 100-K Area is the proposed Coyote Rapids Archaeological District. Consisting of sites 45GR312, 45GR313, 45GR314, and 45BN152, this district was nominated to the National Register, but rejected for lack of information (Cushing 1988). Additional archaeological resources may exist along the Columbia River immediately adjacent to the 100-K Area, in areas that have not been surveyed for cultural resources.

2.2.7.3 Historical Resources. The Coyote Rapids, located immediately upstream of the 100-K Area, is the site of two historically important properties. During the 1850s, events took place at a camp on the Columbia River's south bank near Coyote Rapids that were of great significance to the Northwest Indian people. It was here that Smohalla, prophet of the Wanapum people, held the first *washat* or dance ceremony of what is now referred to as the Dreamer or Seven Drums religion (Relander 1956). As a result of Smohala's personal abilities, the religion spread to many neighboring tribes, and is now practiced by members of the Colville, Nez Perce, Umatilla, Warm Springs, and Yakima tribes. The place where this event is thought to have occurred is archaeological site 45BN152.

The second event was the development of irrigation in the Hanford area. In the early twentieth century, a business consortium from Seattle constructed an electrical plant at Priest Rapids and a pumping station just above Coyote Rapids to supply water to the Hanford Ditch. Without this development, the towns of White Bluffs and Hanford would not have prospered. The irrigation system is now represented by the pumping plant, known as the Allard Pumping Plant, and segments of the Hanford Ditch.

2.2.7.4 Community Involvement. The involvement of the potentially affected community with respect to the RI/FS for the 100-KR-1 operable unit is described in the Community Relations Plan (CRP) that has been developed for the Hanford Site Environmental Restoration Program. The CRP includes a discussion and analysis of key community concerns and perceptions regarding the project, along with a list of all interested parties.

THIS PAGE INTENTIONALLY
LEFT BLANK

3.0 INITIAL EVALUATION

This chapter begins with a discussion of the known and suspected contamination sources in the environmental media in the 100-KR-1 operable unit. An evaluation of these data is presented and, together with other information, is used to develop a site conceptual model for contaminant transport. Potential ARARs are presented for comparison with existing contaminant levels and evaluated. Finally, preliminary remedial action objectives, general response actions, remedial technologies, and remedial alternatives are presented. The preliminary remedial action alternatives are based on the currently available site and contaminant information, site conceptual model, preliminary risk assessment, and potential ARARs.

3.1 KNOWN AND SUSPECTED CONTAMINATION

The following sections present the known and suspected contaminant sources and current knowledge about the extent of environmental contamination in 100-KR-1 operable unit. Previous sampling in the 100-K Area focused on locating and quantifying radioactive species. Some historical data are available on the use of inorganic chemicals, but characterization efforts have generally not included analyses for nonradioactive inorganic species. Virtually no historical information or sampling and analytical data are available on the use of, or contamination by, organic species. A goal of this remedial investigation will be to develop data on the distribution and concentration of nonradioactive inorganic and organic species.

The 100 Area soils and sludges were studied during 1975 and 1976 when Dorian and Richards attempted to quantify residual radionuclide contamination. Their results were published in a 1978 report which is used as the primary reference for this work plan. The data generated for this report were used for the hazard ranking system (HRS) evaluation of the Hanford Site, the Waste Information Data System (WIDS) database maintained by Westinghouse Hanford, and this work plan.

Dorian and Richards (1978) did not evaluate all radionuclides of concern. In particular, ^{63}Ni, which is generally present at activity levels on the same order of magnitude as ^{60}Co, was reported for only some samples, and daughter product radionuclides of ^{90}Sr and ^{137}Cs, which have approximately the same activity level as the parents, were not reported at all.

3.1.1 Sources

The *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989) lists five waste sites in 100-KR-1. Figure 3-1 and Table 3-1 locate and profile the waste sites within the 100-KR-1 operable unit. The five waste sites are:

- 116-K-1 Effluent Crib
- 116-K-2 Effluent Trench
- 116-K-3 Outfall Structure
- 116-KE-4 Water Retention Basins (107-KE Basins)
- 116-KW-3 Water Retention Basins (107-KW Basins).

The major sources of contamination within the boundaries of 100-KR-1 are associated with the cooling water effluent system. A discussion of the cooling water circuit appears in Section 2.1.4.1. During normal operations, cooling water flowed in underground pipes from the reactors to the 107-K retention basins, then discharged to the Columbia River. The cooling water was contaminated with relatively low concentrations of radionuclides and hazardous chemical species, including chromium. Cooling water with elevated concentrations of radionuclides (a result of a fuel cladding failure) was generally diverted to the 116-K-2 trench and disposed of to the soil column.

During reactor operations, contaminated sludge accumulated in the bottom of the retention basins. Sludge was removed from the basins on at least one occasion and reportedly transferred to a burial ground located adjacent to the 107-KE retention basins. This burial ground was not designated as a waste site in the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989). The site has been numbered as site 118-K-2 for reference throughout this work plan. The following subsections discuss the known and potential contaminant sources associated with the water effluent system.

3.1.1.1 Waste Sites 116-KE-4 and 116-KW-3 (Retention Basins). These waste sites include the six 107-K retention basins. The 107-K retention basins are significant waste sites for the 100-K Area. Each basin was constructed of welded carbon steel

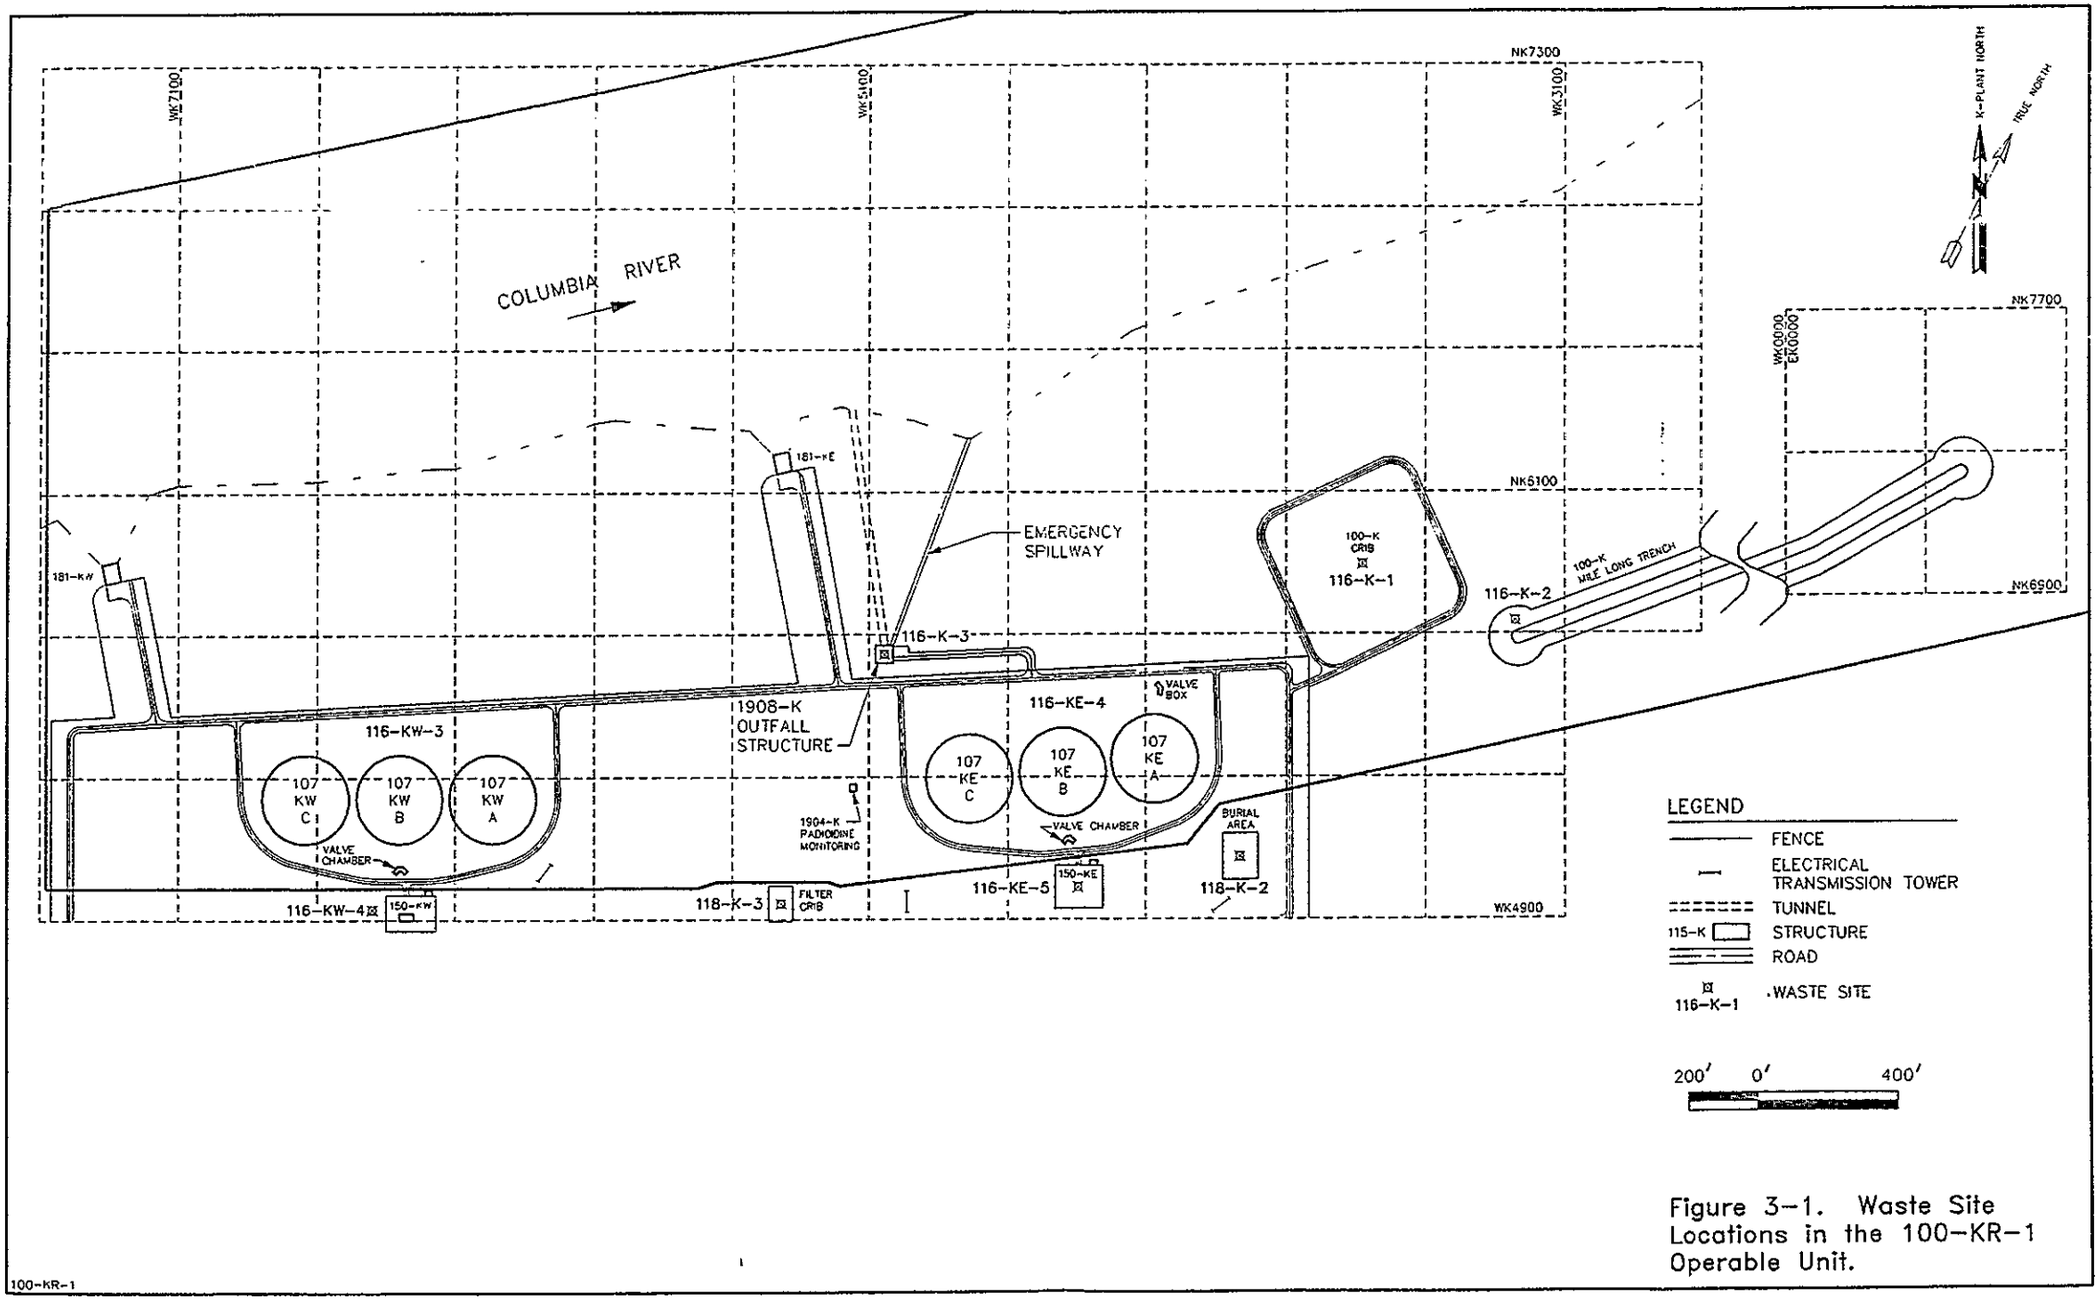

Figure 3-1. Waste Site Locations in the 100-KR-1 Operable Unit.

THIS PAGE INTENTIONALLY
LEFT BLANK

Table 3-1. Profiles of Waste Sites Within the 100-KR-1 Operable Unit.
100-KR-1

Waste site/ waste source designation number	Associated facilities	Description	Years in service	Process stream received or handled	Waste characteristics
116-K-1	100-K crib	Effluent crib	1955-1955	Effluent from 107-KE and 107-KW - retention basins on one or two occurrences of high activity due to fuel element failure	46 Ci 10,000 counts per minute 40-kg sodium dichromate
116-K-2	100-K trench	Effluent trench	1955-1971	Effluent from 107-KE and 107-KW retention basins at times of high activity due to fuel element failure	2100 Ci 1,000-12,000 counts per minute misc water treatment chemical additives
116-K-3	1908-K	Outfall structure NPDES Permit No. WA-00374-3	1955-Present	Cooling water; discharge to river	No reported data
116-KE-4	107-KE	Three cooling water retention basins & adjacent area near tanks	1955-1971	Cooling water from 105-KE reactor	6.2 Ci soil/fill 2,000 counts per minute - culvert area
116-KW-3	107-KW	Three cooling water retention basins & adjacent area near tanks	1955-1970	Cooling water from 105-KW reactor	3.9 Ci soil 2,000 counts per minute - culvert area

plate, and is 250 ft (83 m) in diameter and 20 ft (7 m) high, mounted on reinforced concrete foundations. Each inlet structure consists of a 72 in. (183 cm) pipe leading to an outlet chute that discharges at the bottom of the basin. The basins were used from 1955 to 1971 to retain effluent cooling water from the 105-KE and 105-KW reactors. The basins allowed for thermal cooling of circulated water and decay of short-lived isotopes before release to the Columbia River. In 1971 the basins were deactivated, pipe entrances were covered for wildlife control, walls were washed down, and approximately 2 ft (0.7 m) of dirt was placed at the bottom of each basin.

During operation, basins frequently developed leaks. Leakage rates were estimated at 10,000 to 20,000 gal/min. The first indications of large leaks occurred prior to 1965 when extensive ponding reportedly developed between the basins and the road directly to the north. Two to 3 ft (0.7 to 1.0 m) of fill was placed in this area to prevent ponding. Cooling water that leaked from the basins flowed overland and under the road by way of a culvert. Since the basins were less than 1000 ft (330 m) from the shoreline, it was common occurrence for leaked effluent to reach the Columbia River. Predominant radionuclides present in the soil column as a result of cooling water leaks and waste disposal are ^{3}H, ^{60}Co, ^{63}Ni, ^{90}Sr, ^{137}Cs, ^{152}Eu, ^{154}Eu, and ^{155}Eu (Dorian and Richards 1978).

Twenty-four samples from 12 locations were collected inside the 107-KE and 107-KW basins. The locations of these samples are shown in Figure 3-2. The average Geiger-Muller tube (GM) reading was 2,000 counts per minute for soil samples taken along the bottom of the basin fill material. A summary of the retention basin radioactive inventories is given in Table 3-2 (Dorian and Richards 1978). Specific radionuclide concentrations for the 24 samples are given in Table 3-3.

Table 3-2. Summary of Radionuclide Inventories in the 107-K Retention Basins in 1976 (Dorian and Richards 1978).

Samples	107-KE (3 tanks)	107-KW (3 tanks)
Sludge	0.35 Ci	0.51 Ci
Soil fill (less sludge)	0.15 Ci	0.48 Ci

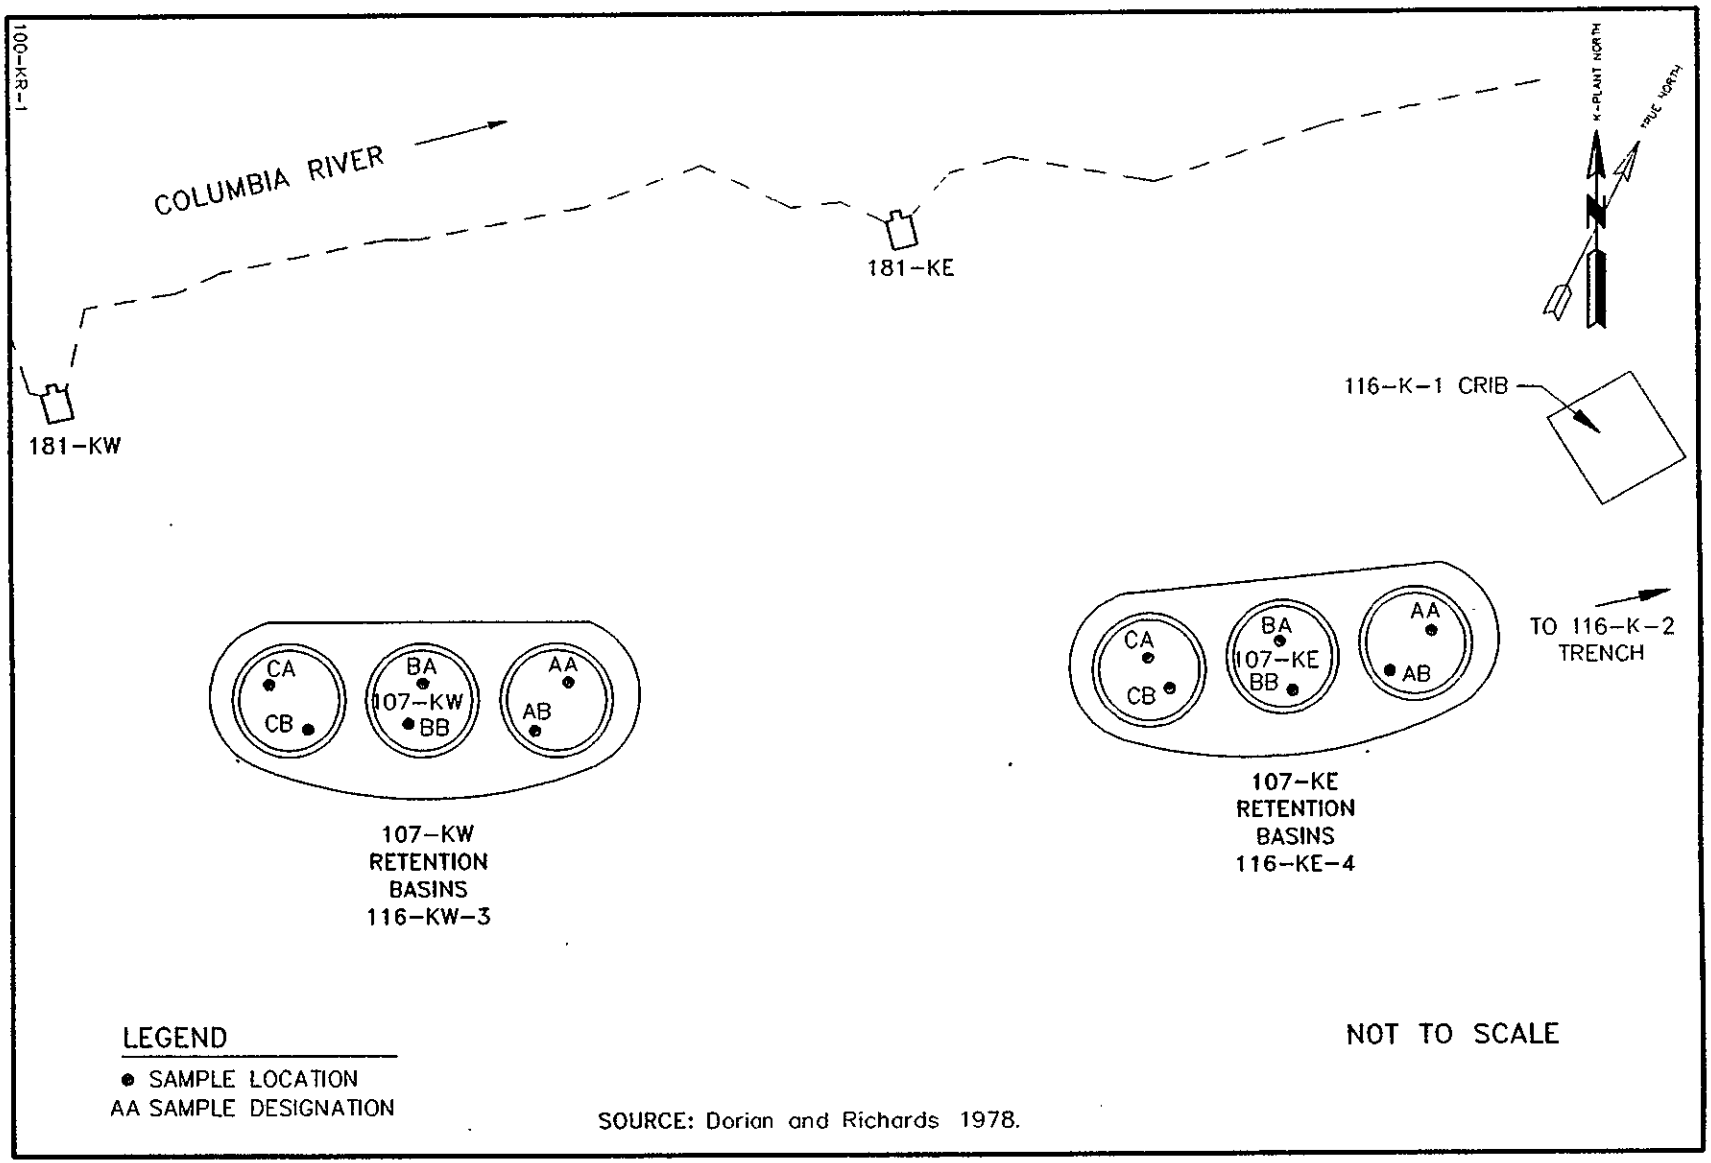

Figure 3-2. Sample Locations Inside the 107-K Retention Basins.

Table 3-3. Radionuclide Concentrations in Soil Samples Inside the 107-K Retention Basins (Dorian and Richards 1978).

107-KE Basins

Concentration (pCi/g)

Sample number/ depth (ft.)	^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	^{11}P/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu	U	^{63}Ni
AA 0	*	*	6.7×10^{-2}		<200/40	6.9×10^{-1}	1.1×10^{0}	4.9×10^{-1}	9.7×10^{-2}	1.6×10^{-1}	1.6×10^{0}		
3	*	1.9×10^{-1}	6.0×10^{0}	2.1×10^{0}	<200/160	6.6×10^{1}	2.0×10^{1}	2.4×10^{1}	*	1.6×10^{0}	5.3×10^{0}		
AB 0			7.6×10^{-2}		<200/20	4.2×10^{0}	1.8×10^{-1}	1.3×10^{0}	3.1×10^{-2}	1.3×10^{-1}	3.4×10^{-1}		
2	*	1.8×10^{-1}	6.9×10^{-1}	7.6×10^{-1}	<200/200	1.0×10^{2}	8.4×10^{0}	3.7×10^{1}	*	1.9×10^{-1}	4.4×10^{0}		
BA 1			1.6×10^{-1}		<200/30	3.4×10^{-1}	1.2×10^{-1}	*	8.8×10^{-2}	1.4×10^{-1}	1.7×10^{0}		
1-1/2	6.2×10^{-1}	4.6×10^{0}	1.6×10^{-1}	*	<200/150	6.5×10^{1}	8.0×10^{0}	3.2×10^{1}	7.3×10^{-1}	1.7×10^{0}	1.5×10^{1}		
BB 1-1/2	*	*	1.9×10^{-1}	*	<200/150	6.4×10^{1}	5.2×10^{0}	2.5×10^{1}	*	3.3×10^{-1}	3.9×10^{0}		
CA 0	*	*	3.7×10^{-2}		<200/20	1.6×10^{0}	1.4×10^{-1}	8.5×10^{-1}	*	1.4×10^{-1}	1.6×10^{0}		
2	*	9.8×10^{-1}	1.3×10^{1}	6.0×10^{0}	800	1.8×10^{2}	1.8×10^{2}	7.7×10^{1}	*	6.2×10^{0}	1.1×10^{1}		
CB 0			3.6×10^{-2}		400	1.2×10^{1}	3.9×10^{-1}	4.8×10^{0}	*	9.4×10^{-2}	1.5×10^{0}		
1	*	*	3.2×10^{-1}		400	3.5×10^{0}	2.6×10^{0}	2.3×10^{0}	*	7.8×10^{-2}	6.3×10^{-1}		
2			9.2×10^{-2}		<200/20	3.8×10^{0}	3.8×10^{0}	2.7×10^{0}	*	1.5×10^{-1}	2.7×10^{0}		
2-1/2	*	1.1×10^{0}	7.9×10^{0}	1.7×10^{1}	5,000	6.4×10^{2}	1.2×10^{3}	5.8×10^{2}	1.3×10^{1}	2.7×10^{1}	2.7×10^{2}	4.2×10^{-2}	6.1×10^{2}
Scale from bottom of inlet chute 107-KE	9.4×10^{-1}	1.2×10^{1}	4.8×10^{0}	1.1×10^{2}		5.0×10^{4}	7.7×10^{3}	1.7×10^{4}	1.8×10^{2}	7.9×10^{3}		1.6×10^{0}	

107-KW Basins

Concentration (pCi/g)

Sample number/ depth (ft.)	^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	P-11/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu	U	^{63}Ni
AA 1-1/2	*	*	1.8×10^{-2}	5.7×10^{0}	200	1.1×10^{1}	2.3×10^{1}	6.1×10^{0}	1.3×10^{-1}	3.0×10^{-1}	2.1×10^{0}		
2	*	2.1×10^{-1}	2.9×10^{-1}	5.5×10^{-1}	5,000	5.6×10^{2}	1.3×10^{3}	3.4×10^{2}	8.2×10^{0}	8.8×10^{0}	5.0×10^{1}	8.8×10^{2}	
AB 1			*		<200/40	2.7×10^{0}	1.8×10^{0}	1.4×10^{0}	4.6×10^{-2}	7.0×10^{-2}	5.4×10^{-1}		
2	*	4.3×10^{-1}	1.8×10^{-1}	1.5×10^{0}	1,000	2.1×10^{2}	1.9×10^{2}	3.9×10^{1}	*	9.7×10^{-1}	3.5×10^{2}		
BA 1-1/2	*	*	9.2×10^{-1}		<200/60	5.4×10^{0}	1.4×10^{1}	7.2×10^{-1}	*	1.9×10^{-1}	4.0×10^{-1}		
2	*	8.3×10^{0}	7.9×10^{1}	1.7×10^{0}	3,000	6.7×10^{2}	5.3×10^{2}	2.0×10^{2}	*	3.0×10^{1}	1.6×10^{1}		
BB 1-1/2			*		<200/40	1.5×10^{0}	1.1×10^{0}	5.5×10^{-1}	*	1.5×10^{-1}	*		
2	*	1.2×10^{0}	3.3×10^{0}	1.3×10^{0}	3,000	5.3×10^{2}	9.0×10^{2}	3.1×10^{2}	*	4.1×10^{0}	2.8×10^{1}		
CA 1-1/2	*	6.7×10^{-1}	1.2×10^{0}	6.0×10^{-1}	600	1.3×10^{2}	9.9×10^{1}	1.3×10^{2}	*	7.3×10^{-1}	*		
CB 2	*	1.1×10^{0}	1.2×10^{1}			1.1×10^{2}	1.0×10^{2}	6.6×10^{2}	5.3×10^{0}	1.8×10^{1}	3.6×10^{2}		

* Less than analytical detection limits
Blank denotes that data are not available

3.1.1.2 Waste Site 116-K-1 (Effluent Crib). The 116-K-1 effluent crib is an excavated rectangular percolation basin 200 x 200 ft (70 x 70 m) at the bottom, 400 x 400 ft (140 x 140 m) at the surface and 22 ft (7 m) deep. The basin failed to percolate adequately and was replaced by a 4,000 x 50 ft (1,300 x 15 m) gravel lined percolation trench (116-K-2). At least once, effluent overflowed one side of the crib resulting in direct discharge to the river. There is conflicting information concerning the number of times cooling water effluent was discharged to this basin.

The 116-K-1 percolation basin and surrounding area was investigated by collecting 16 samples from 5 locations identified as A' through E' in Figure 3-3 (Dorian and Richards 1978). Radiation along the bottom of the crib averages approximately 1,000 counts per minute with localized contamination present up to 10,000 counts per minute. Specific radionuclide concentrations for the 16 samples are presented in Table 3-4. In addition, approximately 40 kg (88 lb) of sodium dichromate were disposed of in the crib (Stenner et al. 1988). Sodium dichromate was added to the cooling water process to inhibit corrosion of the circulation system.

The sides and bottom of the crib were covered with dirt and gravel in the early 1960s. A visual site inspection in 1990 showed the crib is enclosed by a cyclone fence and posted with radiation signs.

3.1.1.3 Waste Site 116-K-2 (Effluent Trench). The 116-K-2 trench was excavated to percolate cooling water effluent into the soil column. The trench dimensions are about 4,000 x 50 ft (1,300 x 15 m) and 20 ft (7 m) deep. The trench was constructed in 1955 to replace the 116-K-1 effluent crib. In 1971, the sides and bottom of the trench were covered (except the influent end) with a layer of dirt and later back filled to grade.

The area inside the 116-K-2 trench was investigated by collecting 46 samples from 14 locations in the mid-1970s (Dorian and Richards 1978) (Figure 3-3). Radionuclide activity levels measured in sample holes ranged from less than 200 to 12,000 counts per minute with a GM probe. Specific radionuclide concentrations for the 46 samples are presented in Table 3-5. Chemical compounds disposed of in the trench include 300,000 kg (661,000 lb) of sodium dichromate, 500 kg (1,100 lb) of copper sulfate, 10,000 kg (22,000 lb) of sulfuric acid, and 10,000 kg (22,000 lb) of sulfamic acid (Stenner et al. 1988).

THIS PAGE INTENTIONALLY
LEFT BLANK

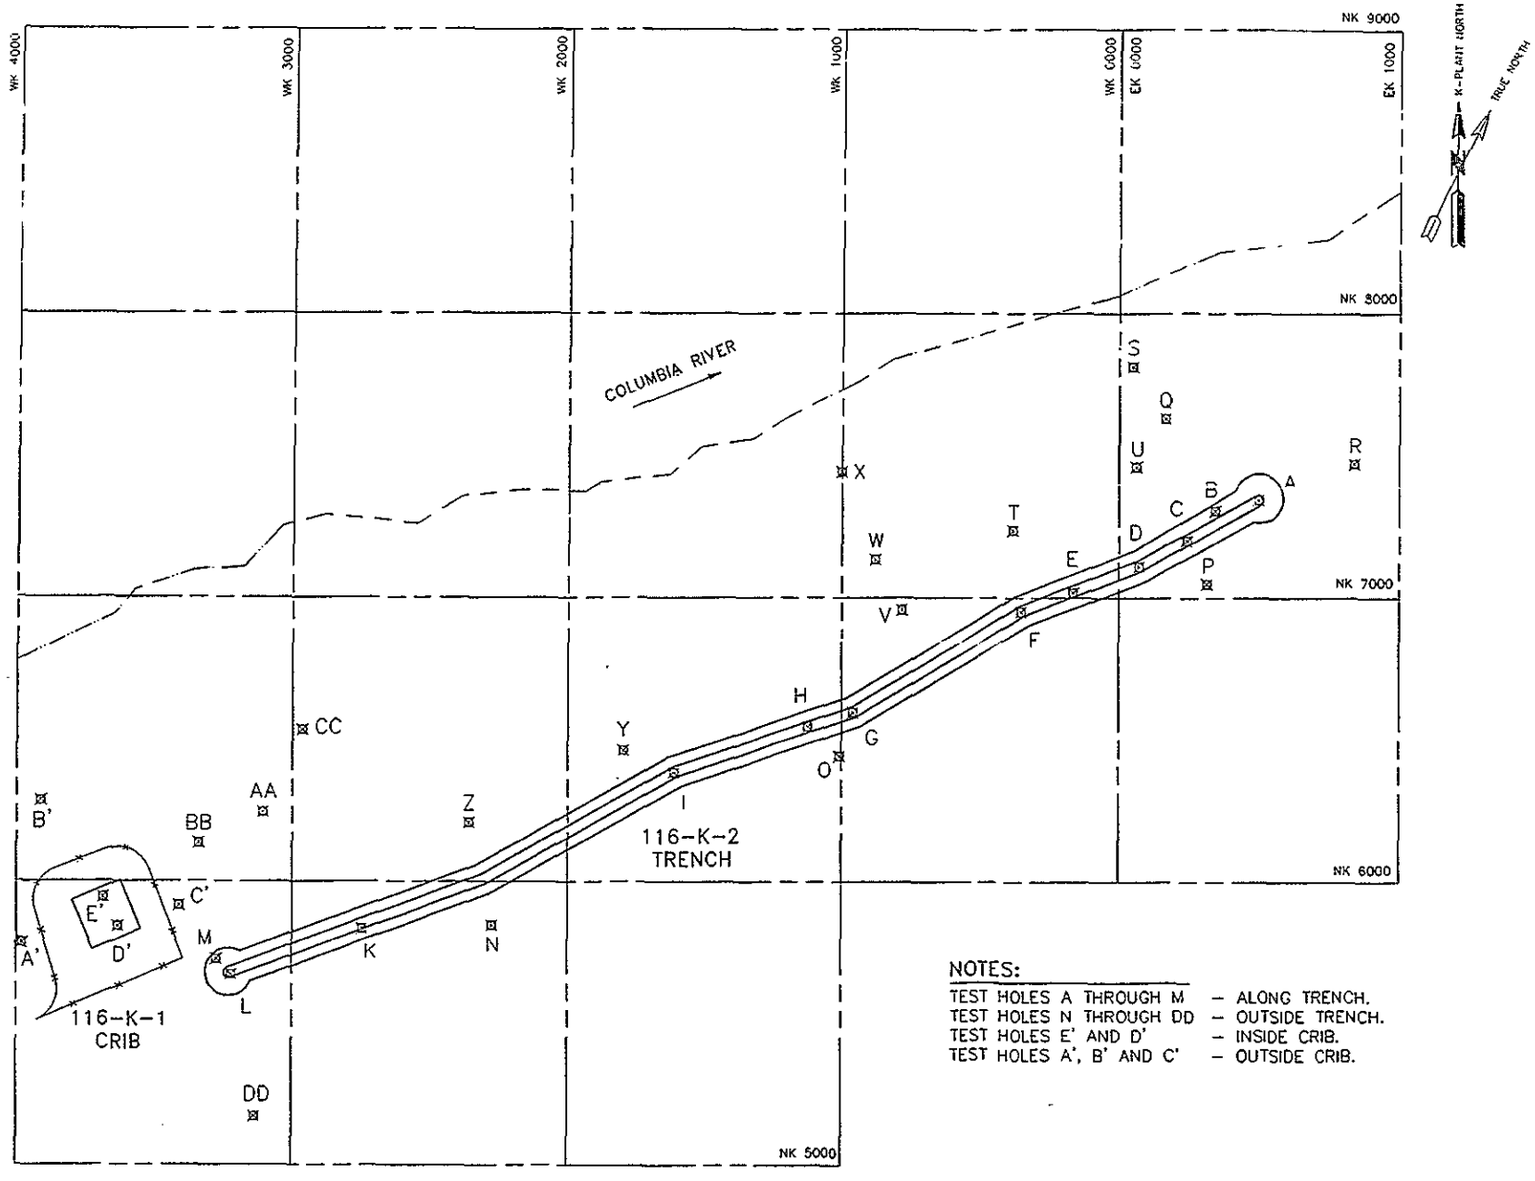

TRENCH AND CRIB SAMPLE HOLE DATA			
TRENCH POINTS			
HOLE	NORTH	WEST	ELEV
A	7314.07	493.73	427.15
B	7306.35	342.20	0.00
C	7200.94	241.08	428.11
D	7109.82	72.57	428.19
E	7017.50	-163.87	432.51
F	6950.14	-350.98	441.27
G	6596.24	-961.02	426.89
H	6544.75	-1122.38	427.59
I	6383.03	-1615.15	429.14
J	6007.33	-2313.53	434.30
K	5831.20	-2748.11	433.29
L	5670.02	-3221.84	433.40
M	5724.76	-3274.07	442.90
N	5845.30	-2275.39	442.25
O	6441.98	-1006.84	435.60
P	7049.12	313.20	434.71
Q	7632.32	165.32	411.90
R	7471.93	842.79	437.15
S	7813.41	48.70	405.61
T	7236.49	-381.24	416.17
U	7461.27	61.72	405.81
V	6957.16	-785.22	420.75
W	7133.90	-879.42	419.83
X	7443.60	-1001.93	414.46
Y	6460.41	-1799.47	426.48
Z	6204.70	-2359.54	423.84
AA	6242.68	-3108.48	404.53
BB	6133.12	-3342.05	409.00
CC	6532.98	-2965.27	398.18
DD	5170.29	-3137.24	450.98
CRIB POINTS			
HOLE	NORTH	WEST	ELEV
A'	5782.15	-3978.20	421.77
B'	6283.34	-3912.69	404.50
C'	5914.15	-3411.34	430.05
D'	5837.86	-3635.41	430.17
E'	5941.70	-3687.14	420.88

NOTES:

TEST HOLES A THROUGH M – ALONG TRENCH.
TEST HOLES N THROUGH DD – OUTSIDE TRENCH.
TEST HOLES E' AND D' – INSIDE CRIB.
TEST HOLES A', B' AND C' – OUTSIDE CRIB.

LEGEND

H SAMPLE HOLE

FENCE

500' 0' 500'

SOURCE: Dorian and Richards 1978.

Figure 3-3. Location of Soil Samples from the 116-K-1 Crib and 116-K-2 Trench.

100-KR-1

Table 3-4. Radionuclide Concentrations in Soil Samples Inside and Adjacent to the 116-K-1 Effluent Crib (Dorian and Richards 1978).

Sample number/ depth (ft.)	^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	^{11}P/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu	U	^{63}Ni
	Concentration (pCi/g)												
116-K-1 100-K CRIB													
A' 0			*		<200/5	*	*	*	*	*	*		
5			9.1×10^{-2}		<200/20	*	1.5×10^{-1}	*	*	1.7×10^{-1}	*	2.2×10^{-1}	
15			5.6×10^{-1}		<200/8kg	9.7x10-1	6.4×10^{-1}	6.4×10^{-1}	4.5×10^{-2}	*	*		
B' 5			3.7×10^{-2}		<200/30	*	5.8×10^{-2}	*	*	3.9×10^{-2}	*		
15			2.5×10^{-2}		<200/10	*	*	*	*	*	*		
25	*	3.2×10^{-3}	*		<200/30	*	5.4×10^{-2}	*	*	4.5×10^{-2}	*	1.4×10^{-1}	
C' 0	*	*	1.3×10^{-1}		<200/25	4.3x10-1	9.1×10^{-1}	2.4×10^{-1}	*	6.5×10^{-1}	1.6×10^{-1}	1.1×10^{-1}	
15			2.9×10^{-2}		<200/20	*	*	*	*	4.6×10^{-2}	1.7×10^{-1}		
25			2.6×10^{-2}		<200/5	*	*	*	3.3×10^{-2}	5.2×10^{-2}	*		
D' 0	4.8x10-1	4.4×10^{0}	1.0×10^{1}		2,500	4.2×10^{2}	3.1×10^{2}	1.7×10^{2}	6.4×10^{0}	7.7×10^{2}	1.4×10^{1}		
5			6.3×10^{0}		1,000	1.3×10^{2}	1.5×10^{2}	5.2×10^{1}	4.0×10^{0}	4.4×10^{2}	4.4×10^{0}		
10			7.2×10^{0}		<200/90	3.0×10^{-1}	3.6×10^{-1}	*	*	6.6×10^{-1}	1.5×10^{-1}		
16			7.9×10^{0}		<200/30	*	*	*	*	*	1.8×10^{-1}		
E' 0	*	2.5×10^{-1}	2.8×10^{0}		300	3.7×10^{1}	3.0×10^{1}	1.3×10^{1}	2.3×10^{-1}	3.4×10^{1}	5.7×10^{-1}		
2-1/2	*	1.8×10^{-1}	5.9×10^{0}		<200/40	1.1×10^{0}	9.7×10^{-1}	4.1×10^{-1}	*	5.9×10^{-1}	*		
24	*	*	1.0×10^{0}		<200/8kg	*	*	*	*	3.8×10^{-2}	*		

* Less than analytical detection limits

Blank denotes that data are not available

Table 3-5. Radionuclide Concentrations in Soil Samples Along the 116-K-2 Trench (Dorian and Richards, 1978).

Sample number/ depth (ft.)		Concentration (pCi/g)													
		^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	^{11}P/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu	U	^{63}Ni	
A	5	3.1×10^{-1}	7.6×10^{0}	2.5×10^{1}		1,500	*	*	*	*	*				
2A	5	*	*			<200/30	9.7×10^{-1}	2.4×10^{-1}	2.5×10^{-1}	*	1.1×10^{-1}		*		
	15	2.4×10^{-1}	2.1×10^{0}	1.8×10^{1}	1.5×10^{1}	1,000	5.8×10^{2}	1.8×10^{2}	1.7×10^{2}	1.3×10^{0}	1.1×10^{2}		9.3×10^{0}	2.5×10^{-1}	
	20	*	3.0×10^{-1}	5.7×10^{0}		<200/100	4.9×10^{0}	8.6×10^{-1}	9.3×10^{-1}	*	2.6×10^{1}		5.2×10^{-1}		
B	0	1.9×10^{-1}	2.5×10^{0}	6.2×10^{0}	2.7×10^{2}	1,500	6.0×10^{2}	2.7×10^{2}	2.5×10^{2}	5.6×10^{0}	1.2×10^{2}		6.5×10^{1}	3.1×10^{-1}	
	5	*	*	1.6×10^{0}		<200/15	2.2×10^{-1}	1.0×10^{-1}	*	*	*		*		
	10	*	*	2.7×10^{-1}		<200/25	3.4×10^{0}	1.5×10^{0}	1.1×10^{0}	*	5.9×10^{-1}		1.4×10^{-1}	2.4×10^{-1}	
C	15	4.0×10^{0}	1.3×10^{2}	2.3×10^{2}	1.4×10^{1}	12,000	4.4×10^{4}	1.3×10^{3}	1.7×10^{4}	5.3×10^{2}	4.8×10^{2}	5.1×10^{3}	9.5×10^{2}	2.1×10^{0}	3.2×10^{1}
	17-1/2	2.8×10^{-1}	1.1×10^{1}	4.4×10^{1}		2,000	5.8×10^{2}	3.1×10^{2}	1.4×10^{2}	2.8×10^{0}	4.5×10^{2}		3.7×10^{0}		
	20	*	1.6×10^{0}	1.4×10^{1}		400	1.6×10^{2}	9.9×10^{1}	6.1×10^{1}	9.7×10^{-1}	5.7×10^{1}		1.3×10^{1}		
	25	3.0×10^{-1}	4.9×10^{0}	3.7×10^{1}		2,500	1.2×10^{3}	2.7×10^{2}	4.5×10^{2}	2.3×10^{0}	2.3×10^{2}		5.7×10^{1}		
	28	*	5.4×10^{-1}	1.4×10^{1}		600	1.4×10^{2}	5.0×10^{1}	4.7×10^{1}	5.5×10^{-1}	6.5×10^{1}		2.1×10^{1}		
D	5	1.4×10^{-2}	1.2×10^{-1}	6.8×10^{-1}		<200/10	6.6×10^{0}	4.6×10^{0}	2.8×10^{0}	6.7×10^{-2}	2.8×10^{0}		3.8×10^{-1}		
	15	4.3×10^{-1}	1.3×10^{1}	5.7×10^{1}	2.7×10^{1}	2,000	1.6×10^{3}	7.3×10^{2}	6.6×10^{2}	2.1×10^{1}	3.9×10^{2}		1.8×10^{2}	4.1×10^{-1}	
	20	*	8.1×10^{0}	1.1×10^{1}		300	1.5×10^{1}	4.1×10^{0}	7.7×10^{-1}	8.6×10^{-2}	7.2×10^{0}		9.3×10^{-1}		
	28	*	*	6.3×10^{0}		<200/10	9.0×10^{-1}	3.3×10^{-1}	*	*	2.5×10^{-1}		*		
E	0	*	*	4.8×10^{-1}		<200/40	2.9×10^{0}	2.2×10^{2}	1.5×10^{0}	*	1.2×10^{0}		2.8×10^{-1}		
	12	1.2×10^{0}	2.1×10^{1}	3.0×10^{1}	8.1×10^{1}	5,000	2.2×10^{3}	7.4×10^{2}	7.4×10^{2}	2.8×10^{1}	9.2×10^{2}		2.3×10^{2}	5.5×10^{-1}	
	16	3.0×10^{-1}	4.0×10^{0}	6.7×10^{0}		900	3.5×10^{2}	1.1×10^{2}	1.2×10^{2}	1.1×10^{0}	1.9×10^{2}		4.0×10^{0}		
	20	*	3.7×10^{-1}	4.4×10^{0}		250	2.9×10^{1}	3.8×10^{1}	1.1×10^{1}	6.5×10^{-1}	6.9×10^{1}		*		
	25	*	2.6×10^{-1}	6.2×10^{0}		<200/50	6.9×10^{0}	4.6×10^{0}	2.0×10^{0}	1.3×10^{-1}	1.3×10^{1}		9.6×10^{-1}		
F	0	*	2.0×10^{-1}	2.3×10^{-1}		<200/80	4.7×10^{0}	2.5×10^{0}	*	*	1.6×10^{0}		*		
	12	*	2.0×10^{0}	4.7×10^{0}	2.2×10^{0}	800	2.8×10^{2}	1.8×10^{2}	8.2×10^{1}	9.0×10^{-1}	3.4×10^{2}		5.6×10^{0}	2.6×10^{-1}	
	20	*	6.1×10^{-1}	7.4×10^{0}		<200/100	5.8×10^{1}	4.1×10^{1}	1.8×10^{1}	5.3×10^{-1}	1.7×10^{2}		8.2×10^{-1}		
G	0	1.6×10^{-2}	*	7.6×10^{-2}		<200/55	*	1.5×10^{-1}	*	6.2×10^{-2}	6.4×10^{-1}		2.7×10^{-1}		
3G	19	3.7×10^{-1}	7.1×10^{0}	1.5×10^{1}	5.5×10^{1}	1,500	1.1×10^{3}	5.0×10^{2}	3.4×10^{2}	3.4×10^{0}	7.1×10^{2}		2.6×10^{1}	5.8×10^{-1}	
	25	*	2.4×10^{0}	4.8×10^{0}		650	2.8×10^{2}	1.3×10^{2}	1.1×10^{2}	9.0×10^{0}	6.2×10^{2}		2.9×10^{1}		
	29	*	7.8×10^{-1}	4.2×10^{0}		500	9.3×10^{1}	7.2×10^{1}	3.2×10^{1}	1.1×10^{0}	1.0×10^{0}		5.5×10^{0}		
H	0	*	*	3.3×10^{-1}		<200/85	7.8×10^{0}	5.1×10^{0}	4.0×10^{0}	1.7×10^{-1}	3.1×10^{0}		1.0×10^{0}		
	13	2.1×10^{0}	2.8×10^{1}	2.0×10^{1}	2.5×10^{1}	2,000	1.7×10^{3}	5.4×10^{2}	5.3×10^{2}	1.7×10^{1}	7.2×10^{2}		1.9×10^{2}	7.1×10^{-1}	
	15	*	4.2×10^{0}	7.6×10^{0}		500	8.7×10^{1}	4.8×10^{1}	2.9×10^{1}	2.9×10^{-1}	9.3×10^{1}		1.1×10^{0}		
	18	*	9.4×10^{-1}	1.6×10^{0}		400	1.2×10^{2}	1.2×10^{2}	3.9×10^{1}	1.6×10^{0}	1.2×10^{2}		6.3×10^{0}		
	21	*	*	1.9×10^{0}		<200/15	5.8×10^{-1}	7.8×10^{-1}	4.4×10^{-1}	*	8.2×10^{0}		3.1×10^{-1}		
I	15	*	*	3.5×10^{-2}		<200/20	2.7×10^{-1}	9.0×10^{-2}	*	*	1.5×10^{-1}		8.8×10^{-2}		
	17	8.7×10^{-1}	2.0×10^{1}	3.3×10^{1}	1.3×10^{2}	3,000	3.0×10^{3}	8.4×10^{2}	9.9×10^{2}	1.1×10^{1}	9.5×10^{2}		3.8×10^{1}	1.2×10^{-1}	
	19	*	*	3.0×10^{0}		500	2.9×10^{1}	2.1×10^{2}	1.1×10^{1}	*	*		3.6×10^{-1}		
	23	*	*	3.4×10^{0}		<200/20	3.3×10^{0}	2.0×10^{0}	1.4×10^{0}	4.2×10^{-2}	1.7×10^{0}		3.1×10^{-1}		
K	0	*	*	3.5×10^{-2}		<200/40	*	*	*	*	7.1×10^{-2}		2.0×10^{-1}		
	22	6.4×10^{-1}	1.3×10^{1}	1.9×10^{1}	9.1×10^{1}	3,000	3.8×10^{3}	2.2×10^{3}	1.4×10^{3}	1.5×10^{1}	3.0×10^{3}		1.4×10^{4}	4.5×10^{-1}	
	27	9.0×10^{-2}	1.4×10^{0}	2.6×10^{0}		1,000	2.2×10^{2}	1.7×10^{2}	8.3×10^{1}	1.0×10^{0}	1.0×10^{2}		1.1×10^{1}		
	30	*	1.9×10^{-1}	2.0×10^{0}		<200	6.1×10^{0}	4.4×10^{1}	*	*	2.6×10^{0}		*		
L	0	*	*	2.1×10^{-1}		<200/30	*	*	3.1×10^{-1}	4.9×10^{-2}	*		1.2×10^{-1}		
	17	*	1.1×10^{0}	3.5×10^{0}	2.2×10^{1}	<200/130	2.3×10^{1}	1.1×10^{2}	1.2×10^{1}	1.7×10^{-1}	2.4×10^{1}		3.7×10^{0}	4.2×10^{-1}	
M	0	*	3.6×10^{-1}	5.5×10^{-2}		<200/40	*	1.4×10^{-1}	5.6×10^{-1}	*	1.3×10^{-1}		*		
	17	*	*	1.3×10^{0}	2.8×10^{0}	<200/150	4.0×10^{-1}	1.1×10^{-1}	*	4.7×10^{-2}	5.7×10^{-2}		1.8×10^{-1}	1.9×10^{-1}	
	20	*	6.3×10^{-1}	9.3×10^{-1}		<200/25	3.7×10^{-1}	9.3×10^{-2}	4.4×10^{-1}	*	2.9×10^{-2}		*		

* Less than analytical detection limits
Blank denotes that data are not available

THIS PAGE INTENTIONALLY
LEFT BLANK

3.1.1.4 Waste Site 116-K-3 (Outfall Structure). The 116-K-3 outfall structure consists of a reinforced concrete building, approximately 30 x 30 ft (10 x 10 m) and 15 ft (5 m) high, two 84 in. (213 cm) steel effluent lines and a concrete-lined emergency overflow spillway. The outfall structure collected discharge from the 107-KE basins via a 66 in. (168 cm) steel pipeline, the 107-KW basins via a 72 in. (183 cm) steel pipeline, and via a concrete sewer from the water treatment plant. Waste from the outfall structure was discharged to the center of the Columbia River through two 84 in. (213 cm) steel pipes. The emergency overflow spillway conveyed water from the outfall structure directly to the edge of the river. The concrete in the channel has been removed and disposed. Radiological surveys are reportedly routinely performed. These data will be compiled and reviewed during the source data compilation task.

3.1.1.5 Effluent Discharge Pipelines and Valves. The discharge system includes effluent lines from the 105-K reactors to the 107-K retention basins and from the retention basins to the outfall structure, 116-K-1 crib, and 116-K-2 trench. The approximate location of the major effluent lines is shown in Figure 2-2. Exact locations are not known for several line segments.

3.1.2 Soil

The following discussion includes the soils surrounding waste sites in the 100-KR-1 operable unit. Radionuclide levels in soil outside, but associated with engineered waste units in the 100-KR-1 operable unit, were reported by Dorian and Richards in 1978. This section discusses the results of this and other studies.

3.1.2.1 Soil Sampling in Waste Sites 116-KE-4 and 116-KW-3 (Retention Basins). Soils outside the 107-K retention basins, but encompassed by waste sites 116-KE-4 and 116-KW-3, were sampled from November through December 1975. Soils were investigated by collecting 41 discrete samples from 29 test holes shown in Figure 3-4. Samples were generally collected at the surface and from 5 to 25 ft (1.7 to 8 m) below the surface. Soil contamination in the area surrounding the retention basins has direct GM readings from 500 to 1,500 counts per minute. Specific radionuclide concentrations for the 41 soil samples are given in Table 3-6. The 107-KE and 107-KW basin vicinities have total radionuclide inventories of 6.2 and 3.9 Ci, respectively. Over 80% of the radionuclide inventory of the 107-KE and 107-KW basin areas is contained in contaminated soils adjacent to the basins. The highest radionuclide concentrations in the area are in the sludges in the 107-K basins. The area inside the basin is discussed in Section 3.1.1.1. (Dorian and Richards 1978).

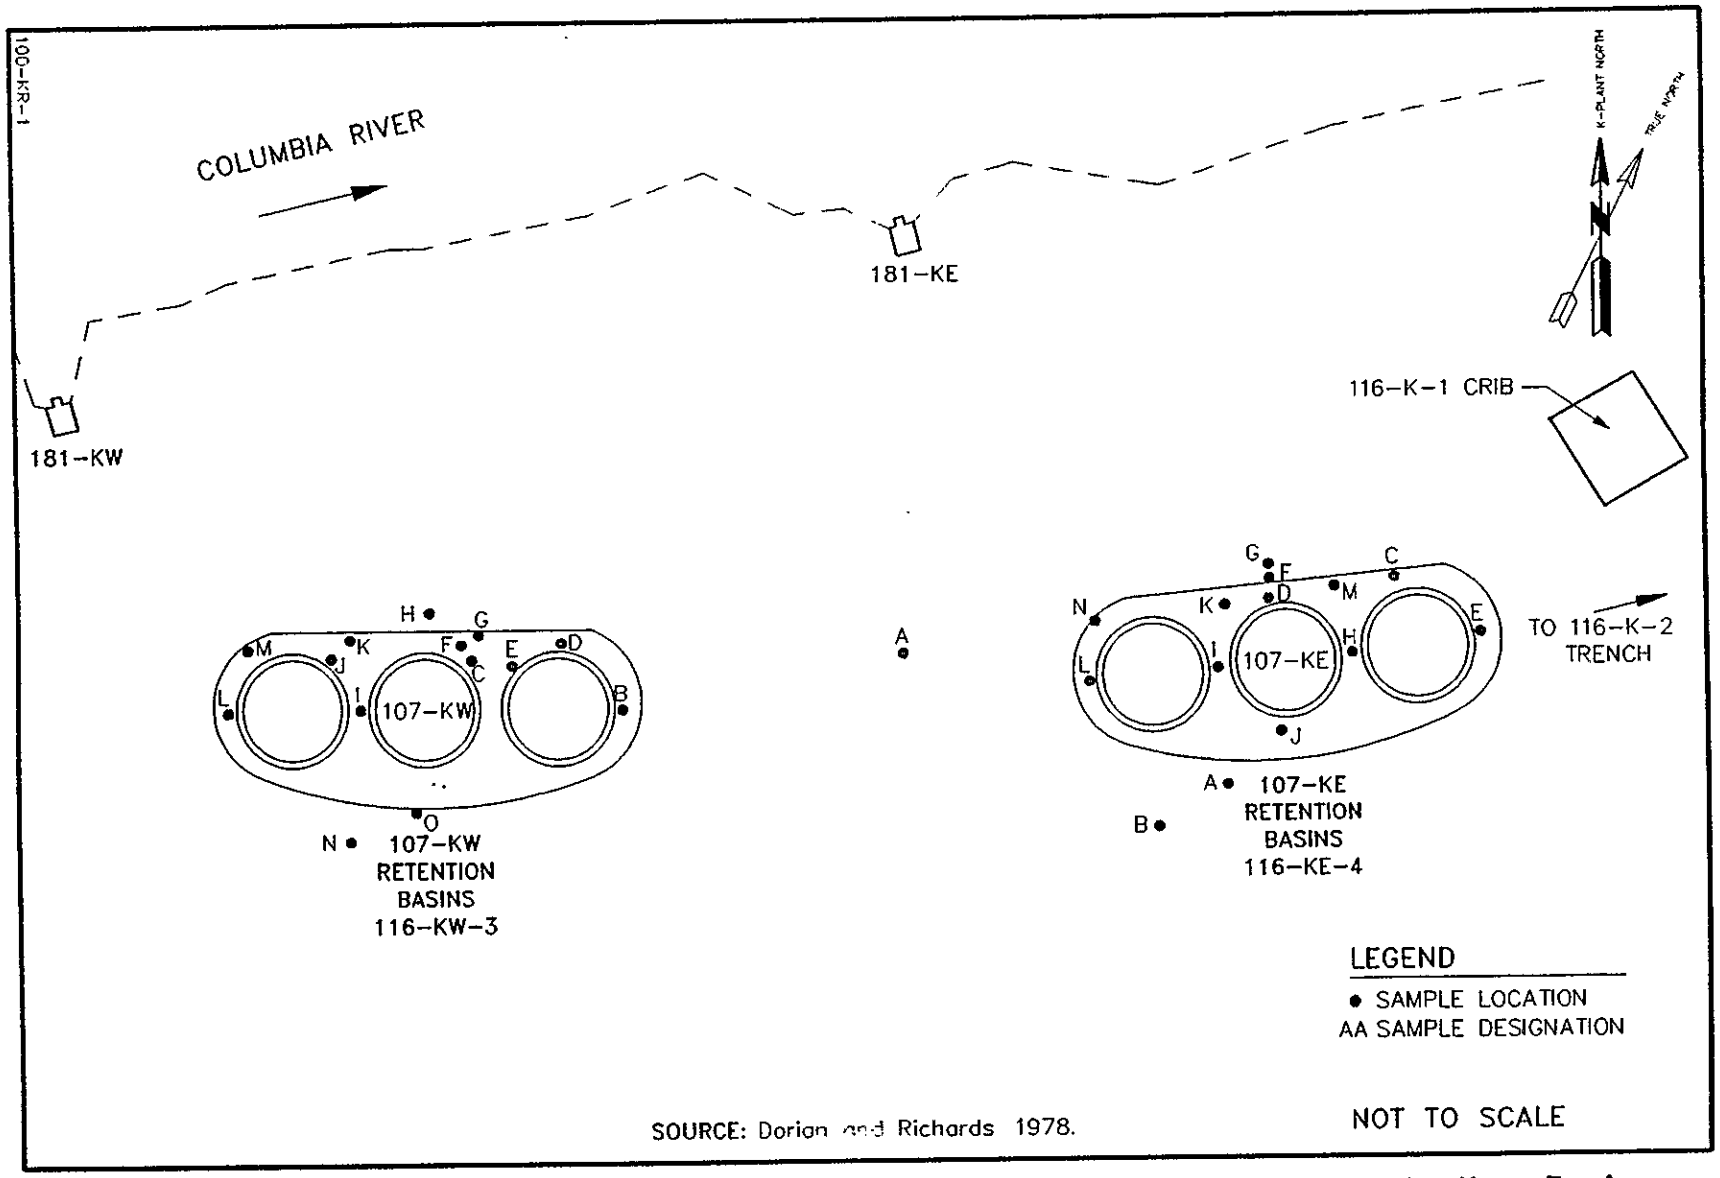

Figure 3-4. Test Hole Locations for Soil Samples Outside the 107-K Retention Basins.

TABLE 3-6. Radionuclide Concentrations In Soils Outside the 107-K Retention Basins.

Page 1

Sample Number /Depth (ft.)		Concentration (pCi/g)										
		^{238}Pu	$^{238/240}Pu$	^{90}Sr	^{3}H	P-11/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu
107-KE BASIN												
C	0	*	*	3.9×10^{-1}		<200/70	1.2×10^{1}	5.5×10^{0}	5.2×10^{0}	*	5.2×10^{-1}	4.7×10^{-1}
D	0	*	*	1.2×10^{0}		<200/80	1.4×10^{1}	8.8×10^{0}	5.2×10^{0}	*	2.4×10^{1}	1.3×10^{0}
E	5	*	*	3.0×10^{-1}		<200/50	2.3×10^{1}	1.2×10^{1}	7.8×10^{0}	2.0×10^{-1}	1.3×10^{0}	2.7×10^{0}
F	0	*	*	8.8×10^{-1}		<200/40	9.4×10^{0}	7.9×10^{0}	4.3×10^{0}	*	3.9×10^{0}	6.0×10^{-1}
	5	*	*	4.5×10^{-1}		<200/30	3.5×10^{0}	3.3×10^{0}	1.3×10^{0}	*	2.3×10^{0}	1.4×10^{-1}
G	15			1.2×10^{-1}		<200/25	3.6×10^{-1}	1.4×10^{-1}	*	*	3.7×10^{-2}	2.0×10^{-1}
H	0	*	*	4.4×10^{-1}	*	<200/50	2.5×10^{1}	8.4×10^{0}	8.3×10^{0}	*	1.4×10^{0}	2.1×10^{0}
	5			4.3×10^{-1}		<200/25	1.9×10^{0}	8.6×10^{-1}	8.1×10^{-1}	*	4.1×10^{-1}	2.7×10^{-1}
I	0	*	*	2.8×10^{-1}	5.3×10^{-1}	<200/30	5.5×10^{0}	6.5×10^{-1}	2.0×10^{0}	8.2×10^{-2}	1.9×10^{-1}	4.6×10^{-1}
J	0	*	*	1.6×10^{0}	1.3×10^{0}	<200/100	2.9×10^{1}	1.7×10^{1}	1.2×10^{1}	*	3.6×10^{0}	6.8×10^{-1}
	15			1.8×10^{-1}		<200/15	1.1×10^{-1}	1.0×10^{-1}	*	*	3.4×10^{-2}	1.1×10^{-1}
K	0	*	*	7.4×10^{-1}		<200/25	5.9×10^{0}	2.7×10^{0}	2.4×10^{0}	6.9×10^{-2}	7.4×10^{-1}	1.5×10^{0}
L	0	*	*	3.2×10^{-1}	*	<200/30	2.2×10^{0}	3.7×10^{-1}	9.6×10^{-1}	6.8×10^{-2}	3.4×10^{-1}	2.8×10^{-1}
M	1	*	*	4.3×10^{-1}		400	2.8×10^{1}	3.3×10^{1}	1.1×10^{1}	*	9.2×10^{0}	1.1×10^{1}
	0	*	2.1×10^{-1}	2.3×10^{0}	*	400	6.2×10^{1}	4.1×10^{1}	2.5×10^{1}	5.2×10^{-2}	4.0×10^{1}	1.3×10^{0}
	20	*	*	1.1×10^{0}		<200/50	1.3×10^{0}	6.6×10^{-1}	1.1×10^{0}	1.0×10^{-1}	2.3×10^{1}	7.5×10^{-1}
N	0	*	1.2×10^{-1}	1.9×10^{0}	*	<200/60	3.8×10^{1}	1.3×10^{1}	1.3×10^{1}	*	1.2×10^{1}	2.2×10^{0}
	15			1.8×10^{-2}		<200/30	5.6×10^{-1}	2.3×10^{-1}	2.0×10^{-1}	*	1.5×10^{-1}	1.0×10^{0}
107-KW BASIN												
B	0	*	*	6.9×10^{-1}	4.9×10^{-1}	<200/50	2.0×10^{1}	1.1×10^{1}	1.0×10^{1}	5.0×10^{-1}	2.0×10^{0}	4.3×10^{0}
	25	*	*	2.6×10^{-1}		<200/25	*	*	*	*	4.3×10^{-2}	*
C	0	*	*	2.1×10^{-1}	*	<200/50	1.5×10^{1}	2.4×10^{0}	4.3×10^{0}	*	5.3×10^{-1}	9.6×10^{-1}
	20			*		<200/30	*	*	*	*	*	*
D	0	*	*	6.9×10^{-1}	*	<200/80	2.2×10^{1}	1.2×10^{1}	1.1×10^{1}	2.1×10^{-1}	3.8×10^{0}	4.5×10^{0}
	10			1.8×10^{-1}		<200/25	2.2×10^{0}	1.0×10^{0}	5.1×10^{-1}	4.1×10^{-2}	7.6×10^{-1}	2.8×10^{-1}
E	0	*	3.5×10^{-1}	1.4×10^{-1}	4.3×10^{-1}	<200/40	6.8×10^{0}	3.6×10^{0}	3.2×10^{0}	5.9×10^{-2}	2.0×10^{0}	1.3×10^{0}
	20			*		<200/20	4.8×10^{-1}	4.1×10^{-2}	*	*	*	*
F	0	*	*	3.0×10^{-2}		<200/40	3.5×10^{0}	2.6×10^{0}	4.3×10^{0}	5.9×10^{-2}	3.7×10^{-1}	1.5×10^{0}
	15			*		<200/15	*	3.7×10^{-2}	*	*	*	1.7×10^{-1}
G	0	*	*	4.0×10^{-1}	*	<200/50	1.1×10^{1}	6.0×10^{0}	4.9×10^{0}	*	1.1×10^{0}	1.8×10^{0}
	8			5.4×10^{-2}		<200/30	1.1×10^{0}	4.8×10^{-1}	7.0×10^{-1}	*	1.6×10^{-1}	2.9×10^{-1}
H	0	*	*	9.8×10^{-1}	*	<200/50	6.3×10^{0}	1.1×10^{1}	1.3×10^{1}	1.5×10^{-1}	2.8×10^{0}	6.9×10^{0}

TABLE 3-6. Radionuclide Concentrations In Soils Outside the 107-K Retention Basins.

Page 2

Sample Number /Depth (ft.)	^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	P-11/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu
	Concentration (pCi/g)										
20			3.9×10^{-2}		<200/25	*	4.4×10^{-2}	*	4.3×10^{-2}	*	1.0×10^{-1}
I 0	*	*	1.3×10^{-1}		<200/25	3.4×10^{0}	1.2×10^{0}	1.3×10^{0}	*	7.3×10^{-1}	2.8×10^{-1}
J 0	*	1.4×10^{-1}	1.5×10^{0}	*	<200/60	2.1×10^{1}	8.9×10^{0}	6.4×10^{0}	*	3.1×10^{0}	2.7×10^{-1}
K 01	*	*	1.8×10^{0}		5,000	8.1×10^{2}	1.0×10^{1}	1.8×10^{2}	1.9×10^{0}	6.9×10^{0}	5.7×10^{2}
0	*	1.0×10^{-1}	1.9×10^{0}	*	<200/50	1.6×10^{1}	7.6×10^{0}	7.1×10^{0}	2.5×10^{-1}	5.3×10^{0}	2.3×10^{0}
L 01	*	5.2×10^{-1}	7.8×10^{0}	4.3×10^{-1}	600	1.3×10^{2}	5.0×10^{1}	3.3×10^{1}	*	2.8×10^{1}	2.6×10^{2}
0	*	2.3×10^{-1}	2.7×10^{0}	1.1×10^{0}	<200/140	5.4×10^{1}	2.2×10^{1}	1.8×10^{1}	*	1.5×10^{1}	1.2×10^{0}
M 0	*	3.2×10^{0}	3.8×10^{1}	7.8×10^{0}	800	5.6×10^{2}	2.6×10^{2}	2.4×10^{2}	3.9×10^{0}	2.4×10^{2}	2.4×10^{1}
N 0			1.1×10^{0}		<200/15	1.3×10^{0}	3.6×10^{-1}	3.0×10^{-1}	*	2.6×10^{0}	1.2×10^{-1}
15	*	*	1.1×10^{0}	3.2×10^{1}	<200/25	9.4×10^{-1}	2.1×10^{-1}	2.1×10^{-1}	*	4.3×10^{0}	1.7×10^{-1}

From Dorian and Richards 1978.

* Less than analytical detection limits
Blank space denotes that no data are available.

The highest soil contaminant concentrations are at sample points K, L and M adjacent to tank 107-KW-C and in 116-KE-4 at sample point M. The five samples at these four points were collected at or near the surface (0 to 1 ft [0 to 0.3 m]) and approximately 50 ft (15 m) from the nearest tank. The remaining soil samples in 116-KW-3 and 116-KE-4 showed contaminant concentrations generally below background.

3.1.2.2 Soil Sampling near Waste Sites 116-K-1 (Crib) and 116-K-2 (Trench). The soils affected by 116-K-1 crib and 116-K-2 trench were sampled from June through August 1975. The waste sites were investigated by collecting 91 discrete samples from 35 locations as shown in Figure 3-3. The crib and trench sampling was divided into the following areas: the crib, the trench, outside the crib and outside the trench. The crib and area along the trench are discussed in Section 3.1.1. A summary of the distribution of radionuclide inventories in and near the crib and trench appears in Table 3-7 (Dorian and Richards 1978).

Table 3-7. Summary of Radionuclide Inventory In and Near 116-K-1 (Crib) and 116-K-2 (Trench) (Dorian and Richards 1978).

Source	Inventory Ci
116-K-1 Crib	46
116-K-2 Trench	2,100
Adjacent to 116-K-1 Crib	0.43

The area outside the effluent trench was investigated with 29 samples from 17 locations, as shown on Figure 3-3. Data are not available for sample locations O, W and X. Surface contamination (0 to 2 ft [0 - 0.7 m]) was identified approximately 150 ft (50 m) north of the trench at sample point V in a former washout area. Surface contamination in these washout areas had direct GM readings from 500 to 3,000 counts per minute. In 1977, this contamination was covered with a few feet of soil and gravel. Specific radionuclide concentrations for the 29 samples are presented in Table 3-8 (Dorian and Richards 1978).

Samples of surface soil were collected in the 100-K Area for the 1987 Environmental Surveillance Annual Report prepared by Westinghouse Hanford. The 116-K-1 crib and 116-K-2 trench areas were investigated with five soil samples. The sample locations are shown in Figure 3-5. Concentrations of radionuclides in the five soil samples are given in Table 3-9. Very low concentrations were found at the five sample sites for all the measured contaminants.

Table 3-8. Radionuclide Concentrations in Soils Samples Outside the 116-K-1 Crib and 116-K-2 Trench

Sample No./ depth (ft.)	Concentration (pCi/g)											
	^{238}Pu	$^{239/240}Pu$	^{90}Sr	^{3}H	P-11/Scaler c/m	^{152}Eu	^{60}Co	^{154}Eu	^{134}Cs	^{137}Cs	^{155}Eu	U
N 10	*	*	*	5.7×10^{-1}	<200/10	4.0×10^{-1}	8.2×10^{-2}	*	*	7.3×10^{-2}	*	1.9×10^{-1}
O												
P 5	*	*	5.5×10^{-2}	2.9×10^{0}	<200/20	7.9×10^{-1}	2.9×10^{-1}	*	7.5×10^{-2}	1.8×10^{-1}	3.6×10^{-1}	2.6×10^{-1}
15	*	*	2.2×10^{-2}		<200/10	*	*	*	*	4.0×10^{-2}	2.5×10^{-1}	
30	*	*	5.8×10^{-1}		<200/10	*	*	1.9×10^{-1}	*	*	5.8×10^{-2}	
Q 0	*	*	3.1×10^{-1}		<200/25	5.1×10^{0}	1.9×10^{0}	1.9×10^{0}	*	8.8×10^{-1}	3.5×10^{-1}	
20	*	*	*	1.0×10^{0}	<200/10	1.7×10^{-1}	7.8×10^{-2}	*	7.0×10^{-2}	5.6×10^{-2}	*	3.0×10^{-1}
R 5	*	*	2.5×10^{-1}	9.1×10^{-1}	<200/25	5.6×10^{-1}	1.0×10^{-1}	*	4.9×10^{-2}	7.8×10^{-1}	*	3.6×10^{-1}
15	*	*	*		<200/10	2.3×10^{-1}	7.2×10^{-2}	*	*	3.9×10^{-2}	*	
S 0	*	*	4.6×10^{-1}	1.0×10^{0}	<200/25	2.1×10^{-1}	5.1×10^{-2}	*	*	*	2.0×10^{-1}	2.2×10^{-1}
18	*	*	1.6×10^{-1}		<200/10	*	*	*	4.0×10^{-2}	3.6×10^{-2}	1.8×10^{-1}	
T 15	*	1.9×10^{-1}	1.6×10^{-1}	1.7×10^{0}	<200/10	5.7×10^{-1}	*	*	5.3×10^{-2}	*	*	1.6×10^{-1}
U 0	*	*	9.7×10^{-3}	5.5×10^{-1}	<200/20	*	5.1×10^{-2}	*	*	6.9×10^{-2}	*	2.7×10^{-1}
V 0-1	*	*	2.0×10^{0}	2.7×10^{-1}	250	1.6×10^{1}	3.5×10^{0}	5.9×10^{0}	5.1×10^{-2}	2.8×10^{0}	4.9×10^{-1}	1.7×10^{-1}
0-2	*	*	2.2×10^{0}	2.3×10^{0}	600	1.3×10^{2}	6.1×10^{1}	5.3×10^{1}	2.1×10^{0}	9.7×10^{1}	1.5×10^{1}	2.8×10^{-1}
5	*	*	1.9×10^{0}		<200/15	4.7×10^{-1}	1.4×10^{-1}	*	*	3.5×10^{-2}	1.5×10^{-1}	
15	*	*	6.7×10^{-1}		<200/20	3.1×10^{-1}	5.8×10^{-2}	*	*	*	*	
W												
X												
Y 0	*	*	2.1×10^{-1}	1.9×10^{0}	<200/25	*	1.2×10^{-1}	*	3.3×10^{-2}	5.4×10^{-1}	*	2.1×10^{-1}
15	*	*	1.9×10^{0}		<200/20	*	*	*	*	*	*	
25	*	*	2.8×10^{0}		<200/10	3.1×10^{-1}	1.1×10^{-1}	*	*	1.1×10^{0}	2.2×10^{-1}	
Z 0	*	*	7.0×10^{-1}		<200/20	1.3×10^{0}	1.3×10^{0}	1.2×10^{0}	5.0×10^{-2}	6.5×10^{-1}	*	
20	*	*	4.5×10^{0}		<200/30	*	4.3×10^{-2}	*	*	*	3.4×10^{-1}	1.3×10^{-1}
25	*	*	4.2×10^{0}		<200/15	*	*	*	*	*	2.8×10^{-1}	
AA 18	*	*	5.1×10^{-1}	*	<200/20	*	*	*	*	*	*	1.2×10^{-1}
BB 20	*	*	2.2×10^{-2}	2.4×10^{0}	<200/10	*	*	*	*	*	*	1.5×10^{-1}
CC 15	*	*	3.1×10^{-1}	3.9×10^{0}	<200/10	*	*	*	*	6.8×10^{-2}	*	1.8×10^{-1}
20	*	*	2.6×10^{-2}	1.4×10^{1}	<200/15	7.2×10^{-1}	*	*	*	8.4×10^{-2}	*	1.2×10^{-1}
DD 0	*	*	2.7×10^{-1}	8.5×10^{-1}	<200/20	1.5×10^{0}	1.6×10^{0}	3.3×10^{-1}	*	9.3×10^{-1}	*	3.1×10^{-1}
10	*	*	*		<200/15	*	*	*	*	5.8×10^{-2}	3.3×10^{-1}	
20	*	*	2.8×10^{-2}		<200/5	*	3.5×10^{-2}	*	*	2.7×10^{-2}	*	

From Dorian and Richards 1978
Less than analytical detection limits
Blank denotes that data are not available

Table 3-9. Concentrations of Radionuclides Detected in 116-K-1 and 116-K-2 Waste Site Surface Soils for the 1987 Environmental Surveillance Report (WHC 1987)

Sample location	Type	^{60}Co	^{90}Sr	^{137}Cs	^{238}Pu	$^{239/240}Pu$
K-1	Soil	4.5E+O	6.5E-1	2.7E+O	9.4E-3	2.2E-1
K-2	Soil	5.5E-1	1.4E-1	8.0E-1	<5.4E-4	9.2E-3
K-3	Soil	3.5E-1	2.8E-1	9.8E-1	<4.7E-4	6.7E-3
K-4	Soil	2.0E-1	1.0E-1	5.2E-1	<1.1E-4	1.0E-2
K-5	Soil	3.7E-1	9.8E-1	1.3E-0	2.9E-3	3.0E-2

3.1.3 Ground Water

The background ground water quality and the nature and extent of ground water contamination for the entire 100-K Area are discussed in the 100-KR-4 work plan. However, there are three items that are closely related to the work in the 100-KR-1 operable unit. One, there is apparently ground water contamination originating from at least one source within the overlying 100-KR-1 operable unit. Possible sources in the 100-KR-1 operable unit include contaminants from the 116-K-1 basin, the 116-K-2 trench, and the 116-KE and KW retention basins. Two, it may be difficult to differentiate the source operable unit (i.e., 100-KR-1, -2, and -3) in which soil contamination originated due to contaminant dispersion. Therefore, it may be difficult to trace ground water contamination to a particular operable unit source. Three, the ground water table currently fluctuates several feet in response to Columbia River levels and was substantially higher during site operations due to process water infiltration.

3.1.4 Surface Water and River Sediment

Routine monitoring of Columbia River water and sediment began in 1945, soon after the startup of production operations, and continues today as part of the surface environmental monitoring project. The monitoring programs have undergone several changes over the years in response to changing operational conditions and improved techniques. Throughout the years, sample locations have been maintained upstream of the Hanford Site, away from the influence of site operations to provide information on

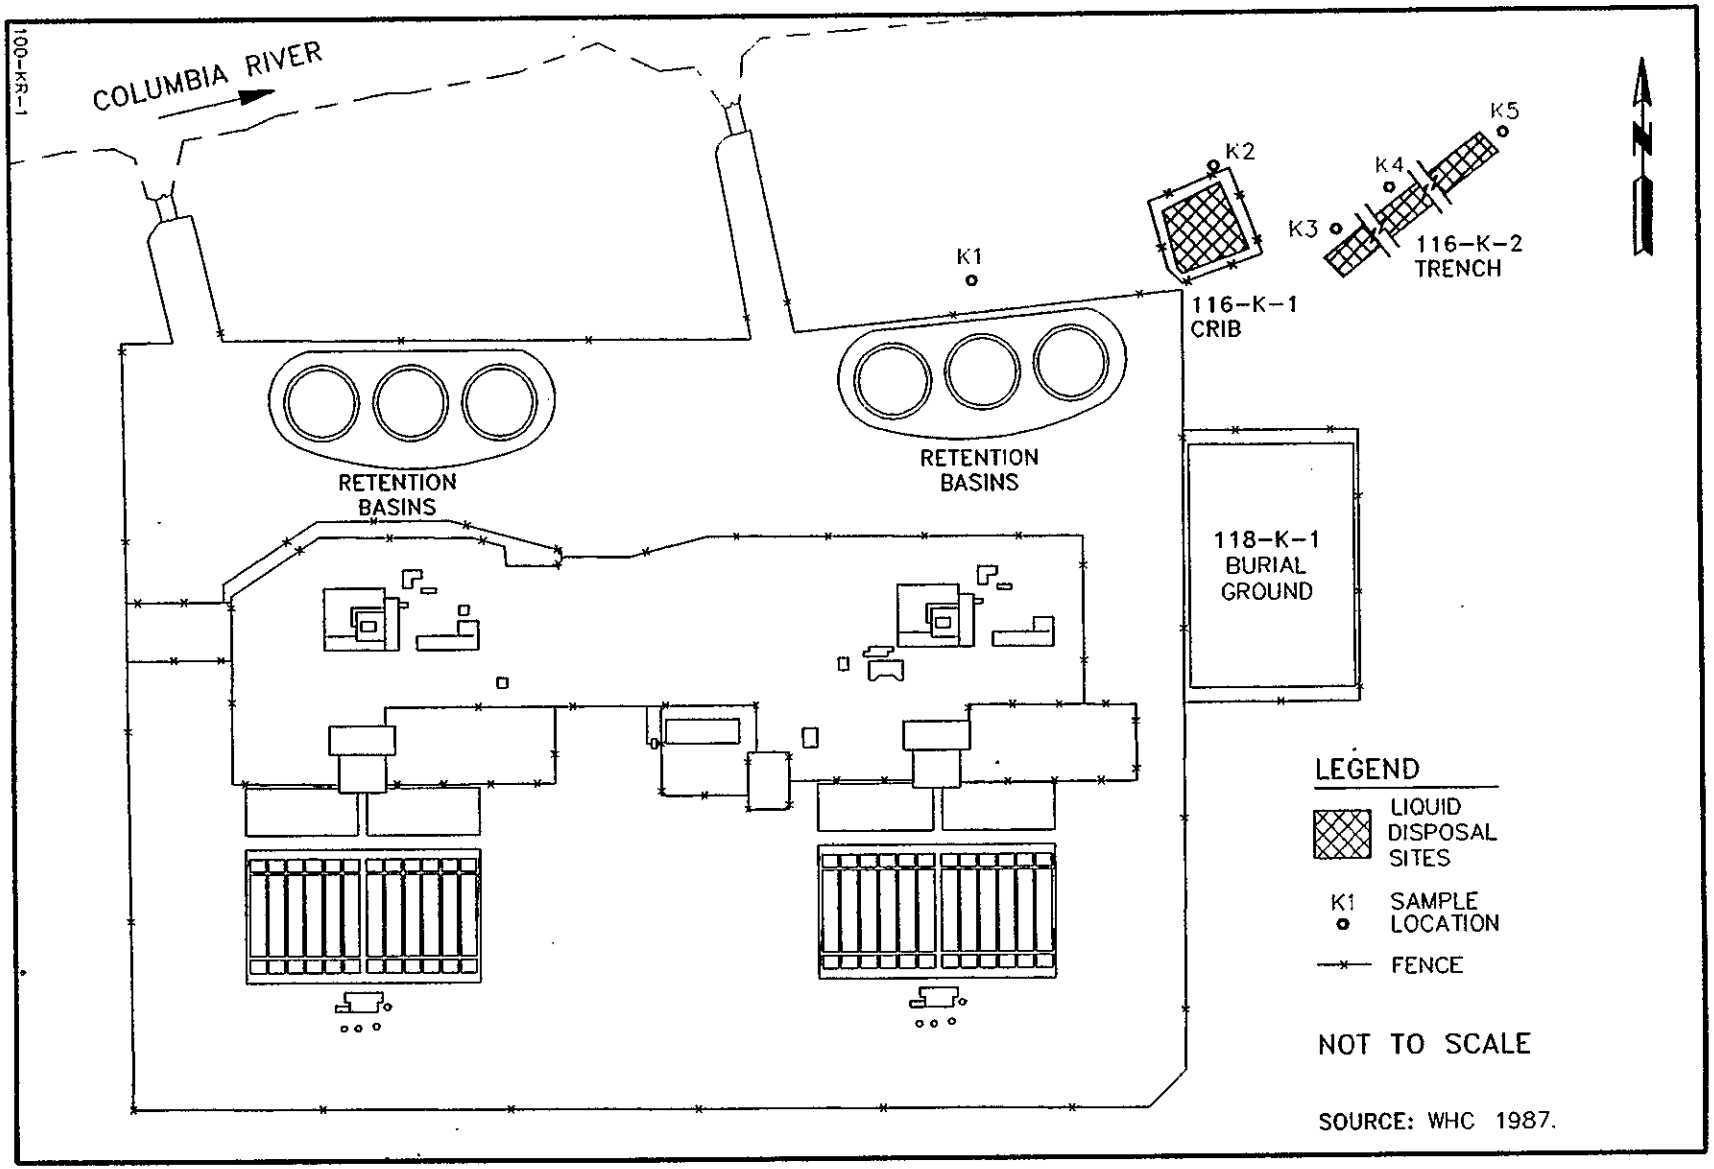

Figure 3-5. Soil Sample Locations from the 116-K-1 and 116-K-2 Area for the 1987 Environmental Surveillance Report.

the background conditions in the Columbia River. Other sample locations downstream of all site facilities identify impacts from Hanford operations. The purpose of the monitoring programs has been to determine the overall impact of Hanford operations. Therefore, increases in contaminant concentrations observed downstream of Hanford usually cannot be attributed to any one facility or operation. Results of the monitoring programs are published annually in the Hanford environmental monitoring reports. For a more detailed discussion of surface water and river sediments, see Chapters 2 and 3 in the 100-KR-4 work plan.

3.1.5 Air

3.1.5.1 Air Quality. Monitoring of airborne radionuclides has been conducted at several surrounding communities in eastern Washington. The locations are shown in Figure 3-6. The 1988 average concentrations for radioactive airborne emissions from the 100 Area and for these surrounding communities are shown in Table 3-10.

3.1.5.2 Air Emissions. Emissions from 100-K Area facilities in 1986 are provided in Table 3-11. Data provided include curies of activity released and average concentration for several radionuclides from the point sources. Emission data show stack concentrations well below DOE Derived Concentration Guides (DCG) for ^{54}Mn, ^{60}Co, and ^{137}Cs. The DCGs are not readily available for ^{90}Sr, ^{238}Pu, $^{239/240}$Pu.

In general, biweekly particulate effluent samples from active 100-K Area facility effluents are collected and analyzed individually for gross beta and alpha. Monthly composite samples undergo a gamma scan, and quarterly composite samples are analyzed for ^{89}Sr, ^{90}Sr, and isotopic uranium and plutonium. Gas samples are collected monthly and/or biweekly and analyzed for various radionuclides including ^{131}I, ^{129}I, ^{3}H, ^{14}C and ^{85}Kr (Bisping 1989).

3.1.6 Biota

3.1.6.1 Terrestrial Biota.

3.1.6.1.1 Terrestrial Flora. Terrestrial flora sampling stations in the 100-KR-1 operable unit are shown in Figure 3-7. The analytical results of onsite versus offsite for 1983 through 1988 are shown in Figure 3-8. Terrestrial vegetation radionuclide data from the 100-K Area, obtained in 1986, are summarized in Tables 3-12 and 3-13. Levels of $^{239/240}$Pu, ^{137}Cs, and ^{90}Sr are, in general, slightly higher onsite when compared to offsite sampling locations.

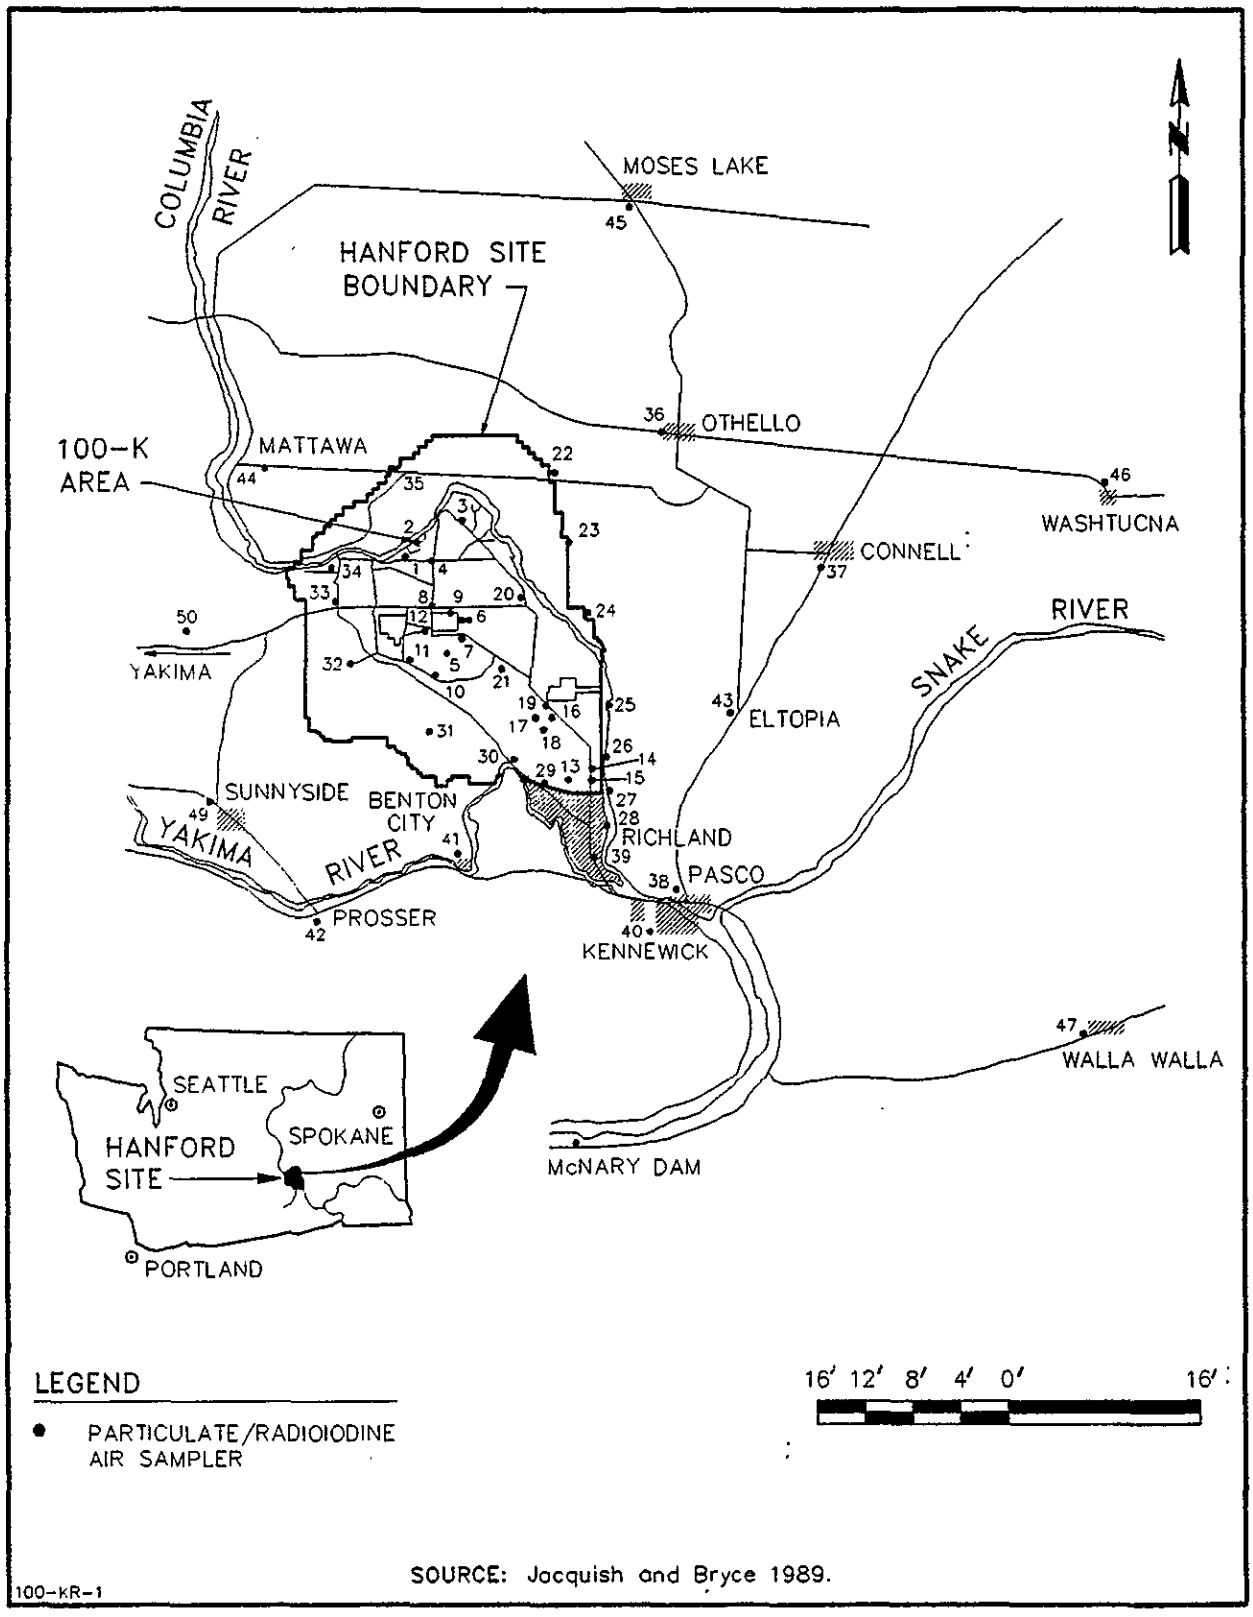

SOURCE: Jacquish and Bryce 1989.

Figure 3-6. Hanford Site and Surrounding Community Air Sampling Locations.

Table 3-10. Air Quality Data for Eastern Washington and the Hanford Site, 1988. (Jacquish and Bryce 1988)

	Near 100 Areas	On site (General)	Site Perimeter	Nearby Communities	Distant Communities
Gross beta	0.0200 ± 0.0032	0.0200 ± 0.0010	0.0190 ± 0.0013	0.0200 ± 0.0017	0.0190 ± 0.0020
Gross alpha	0.00030 ± 0.00014	0.00037 ± 0.00003	0.00042 ± 0.00004	0.00044 ± 0.00010	0.00028 ± 0.00008
^{3}H	1.4 ± 0.4	2.0 ± 0.5	1.2 ± 0.3	1.4 ± 0.9	0.8 ± 0.9
^{14}C	1.40 ± 0.20	1.40 ± 0.10	NA	NA	1.30 ± 0.10
^{90}Sr	0.00019 ± 0.00025	0.00008 ± 0.00004	0.00006 ± 0.00002	0.00006 ± 0.00002	0.00005 ± 0.00002
^{131}I	0.0001 ± 0.0006	0.0001 ± 0.0003	0.0001 ± 0.0004	-0.0013 ± 0.0012	0.0004 ± 0.0005
^{137}Cs	0.0001 ± 0.0002	0.0001 ± 0.0001	0.0001 ± 0.0001	0.0000 ± 0.0002	0.0000 ± 0.0001

* Average values ± standard error of the calculated mean.
NA = Not available.

Table 3-11. Radioactive Airborne Emissions From 100-K Area Facilities (UNC 1986).

Radio-nuclide	105-KW Ci Released	105-KW Avg. conc. pCi/L	105-KE Ci Released	105-KE Avg. conc. pCi/L	1706-KEL Ci Released	1706-KEL Avg. conc. pCi/L
^{54}Mn	2.6 E-5	6.4 E-5	2.4 E-5	6.0 E-5	—	—
^{60}Co	3.7 E-5	9.2 E-5	5.3 E-5	1.3 E-4	4.0 E-6	22 E-5
^{90}Sr	1.3 E-6	3.2 E-6	6.9 E-5	1.7 E-4	1.7 E-6	9.3 E-6
^{137}Cs	3.2 E-5	8.0 E-5	1.1 E-4	2.6 E-4	4.6 E-6	2.6 E-5
^{238}Pu	1.8 E-8	4.6 E-8	2.6 E-5	6.6 E-5	3.2 E-8	1.8 E-8
$^{239/240}Pu$	3.4 E-8	8.4 E-8	2.8 E-6	6.8 E-6	4.8 E-8	27 E-8

Table 3-12. Radionuclide Concentrations Detected in 100-K Area Vegetation (pCi/g, dry weight) (WHC 1987).

Sample location*	^{60}Co	^{90}Sr	^{137}Cs	^{238}Pu	$^{239/240}Pu$
K-1	2.0E-1	3.0E-1	1.4E-1	<7.0E-5	3.4E-4
K-2	1.8E-1	2.9E+0	8.1E-2	<8.8E-5	<1.6E.4
K-3	1.9E-1	9.9E-1	6.2E-2	<1.7E-4	<3.6E-4
K-4	1.5E-1	8.2E-1	1.2E-1	<5.1E-4	<1.2E-4
K-5	4.3E-1	1.6E+0	<1.4E-1	<1.1E-4	<9.5E-5
Average	2.3E-1	1.3E+0	1.1E-1	<1.9E-4	2.2E-4
Std. Dev.	1.0E-1	8.9E-1	3.2E-1	1.6E-4	1.1E-4
Hanford Site**	NR	1.1E+0	7.1E-2	NR	1.4E-3
Offsite**	NR	8.0E-2	6.4E-1	NR	4.7E-4

* Locations identified in Figure 3-7
** Average values obtained from (PNL 1987)
NR Not reported

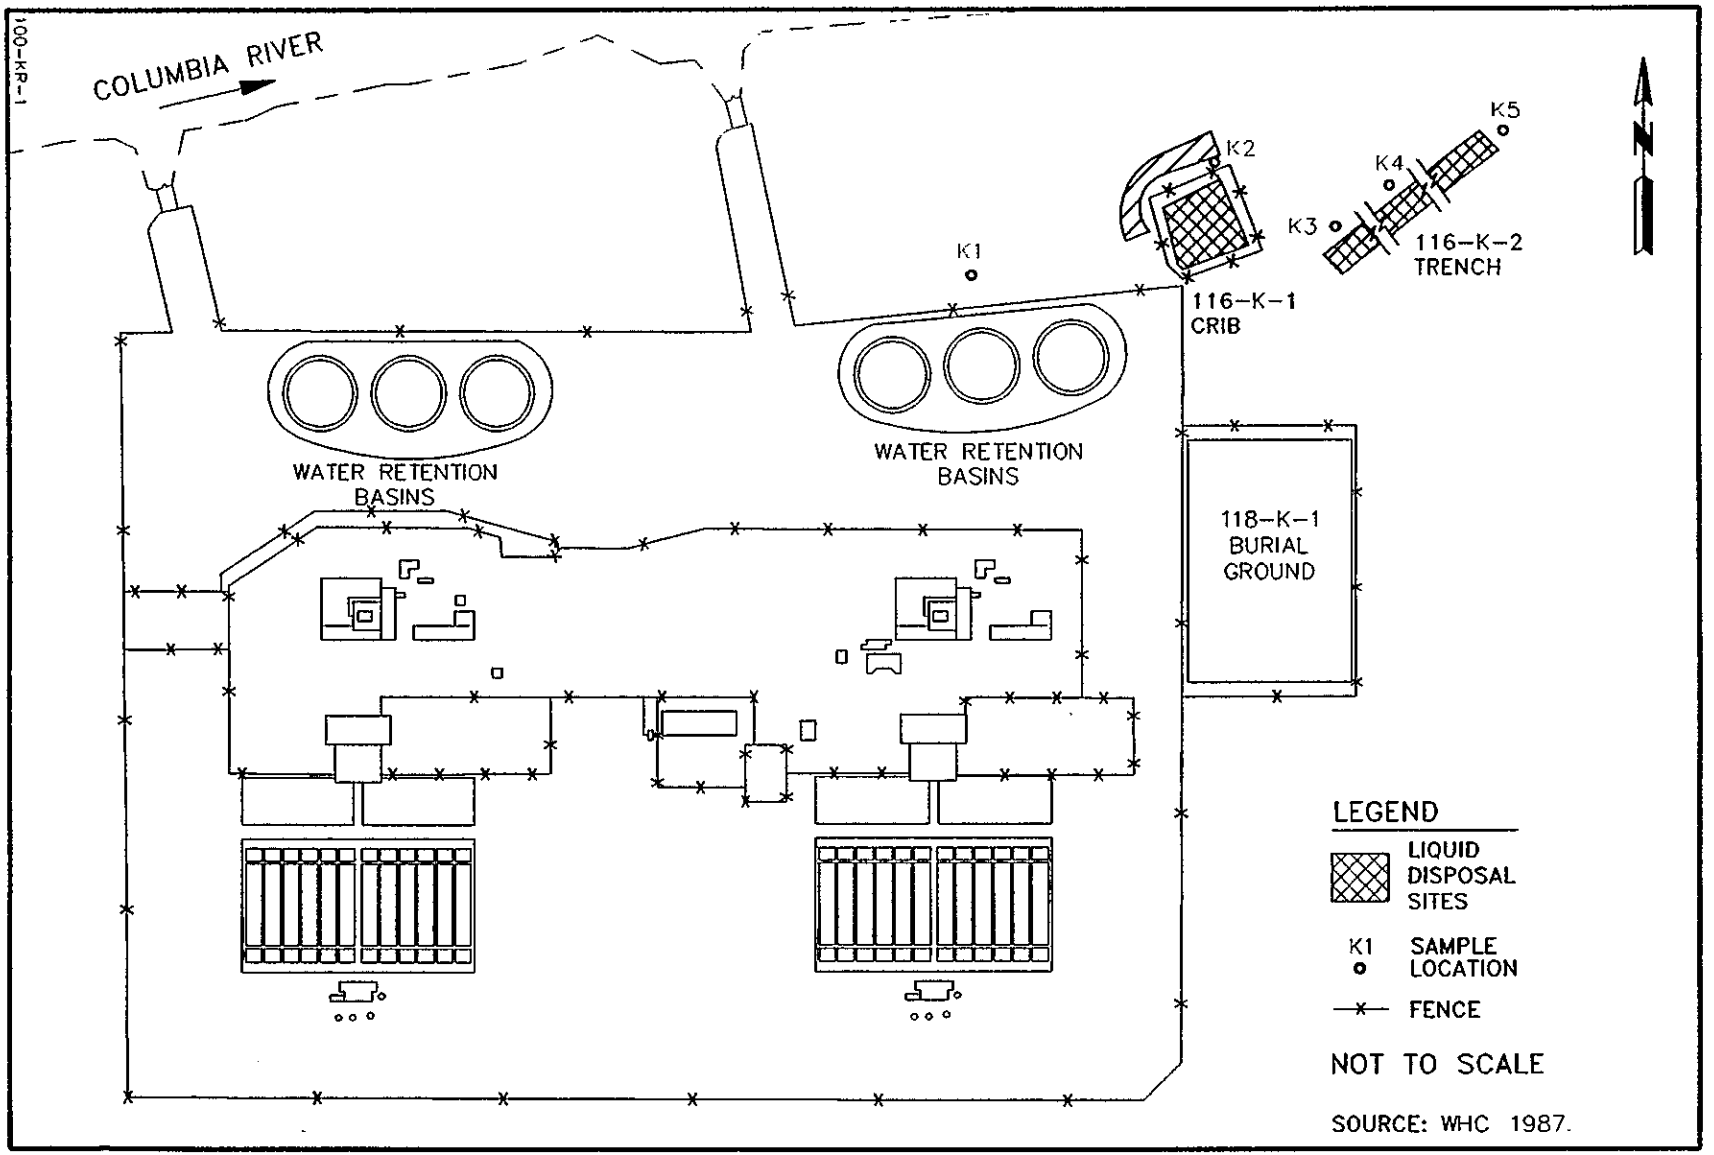

Figure 3-7. Terrestrial Flora Site Sampling Locations, 100-KR-1 Operable Unit.

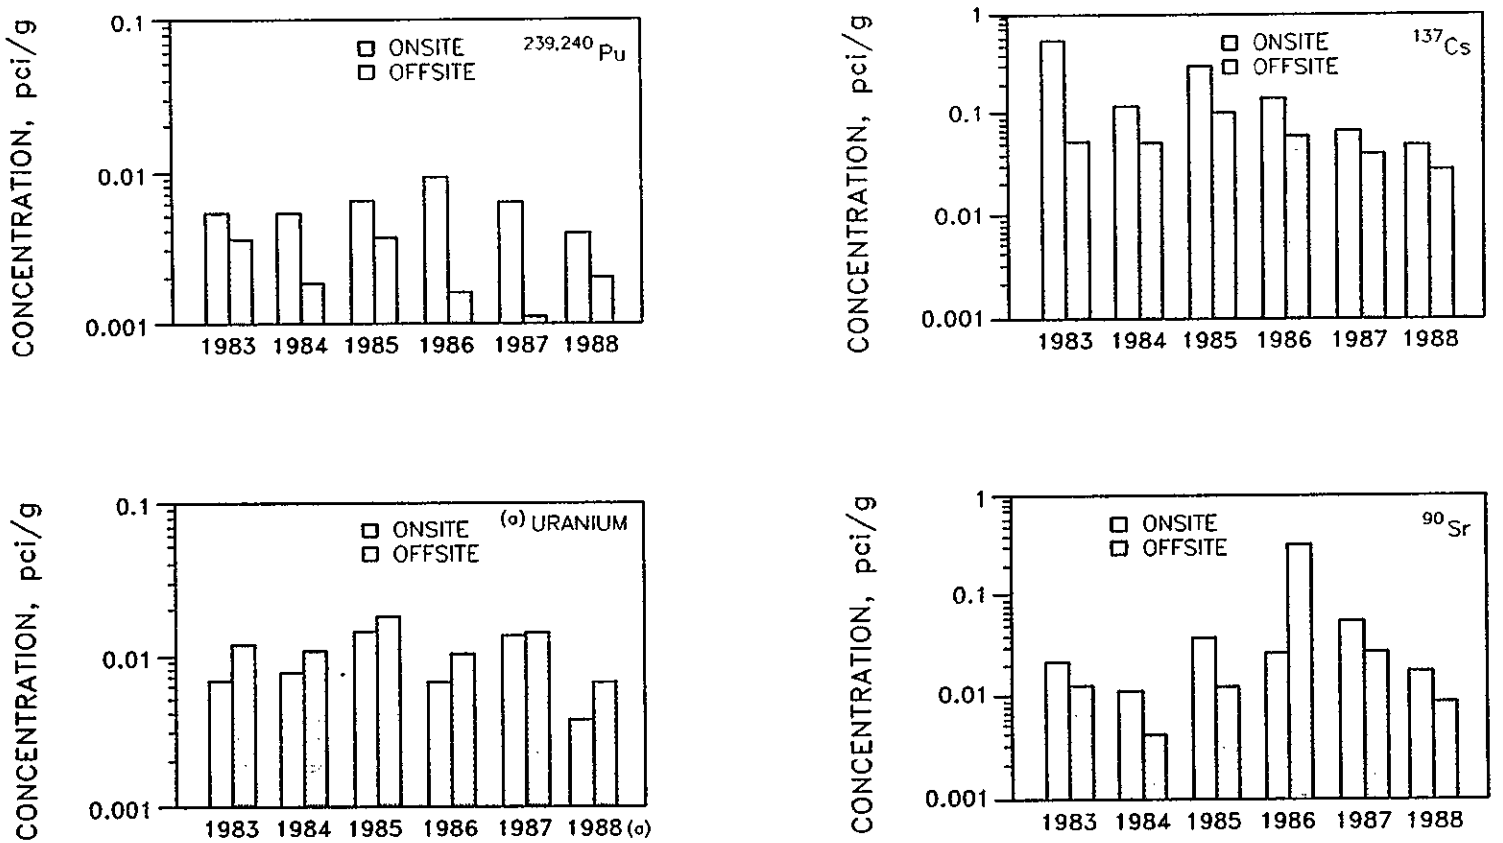

(a) 238 U BEGINNING IN 1988.

SOURCE: Jacquish and Bryce 1989.

Figure 3-8. Median (3 Standard Deviations) ^{90}SR, ^{137}Cs, ^{239,240}Pu, and U Concentrations in Vegetation at Onsite and Offsite Locations.

Table 3-13. Average Radionuclide Concentrations (pCi/g) Detected in 100-K Area Vegetation 1981 Through 1987 (WHC 1987).

Year	^{60}Co	^{90}Sr	^{137}Cs	^{238}Pu	$^{239/240}Pu$
1981	1.2E+00	NR	1.0E-01	NR	NR
1982	2.4E-01	NR	9.7E-01	NR	NR
1983	1.5E-01	NR	2.5E-01	NR	NR
1984	1.8E-01	1.3E+00	1.3E-01	2.9E-04	6.9E-04
1985	4.6E-01	3.9E-01	1.3E-01	1.9E-04	7.1E-04
1986	2.8E-01	4.0E-01	1.5E+00	2.5E-04	7.9E-0
1987	2.3E-01	1.3E+00	1.1E-01	1.9E-04	2.2E-04

NR = Not reported

3.1.6.1.2 Terrestrial Fauna. Pheasant and rabbits were monitored during 1988 in the 100 Areas and results are summarized in Table 3-14. Sample locations are shown on Figure 3-9. Median concentrations of ^{137}Cs in pheasants are within the ranges observed during previous years. Median values of ^{90}Sr (in bone) and ^{137}Cs (in muscle) from rabbits measured since 1982 are shown in Figure 3-10. The levels of ^{90}Sr in bone samples indicated that the rabbits had at some time consumed food or water contaminated with ^{90}Sr.

Table 3-14. Terrestrial Fauna Radionuclide Concentrations 100 Areas (Jacquish and Bryce 1988)

Sample description	Number of samples	Average concentration (pCi/g)	Two standard deviations (pCi/g)
Pheasant--muscle			
^{60}Co	5	0.003	0.016
^{137}Cs	5	0.016	0.018
Cottontail rabbit--bone			
^{90}Sr	2	110	200
Cottontail rabbit--muscle			
^{137}Cs	2	0.072	0.053
Cottontail rabbit--liver			
$^{239,240}Pu$	2	3.4	8.4

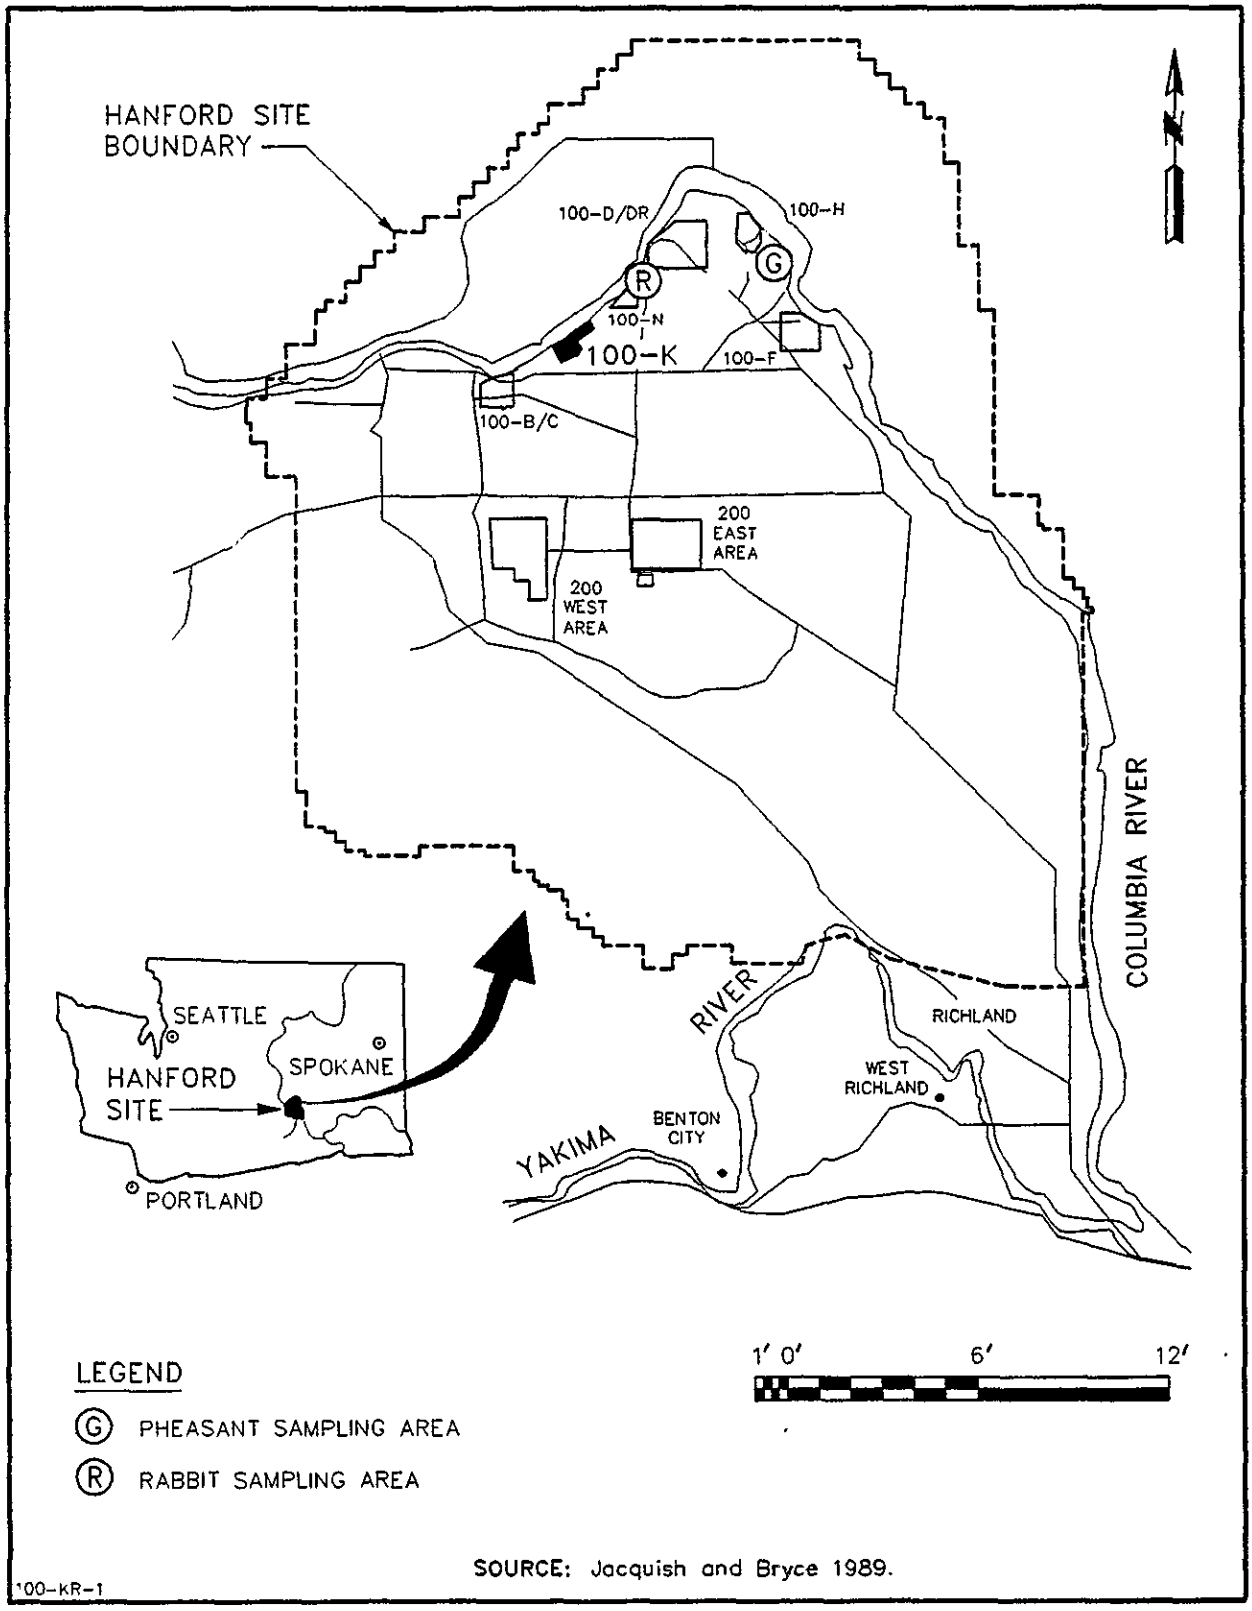

SOURCE: Jacquish and Bryce 1989.

Figure 3-9. Terrestrial Fauna Sampling Locations Near 100-K Area.

9011310134

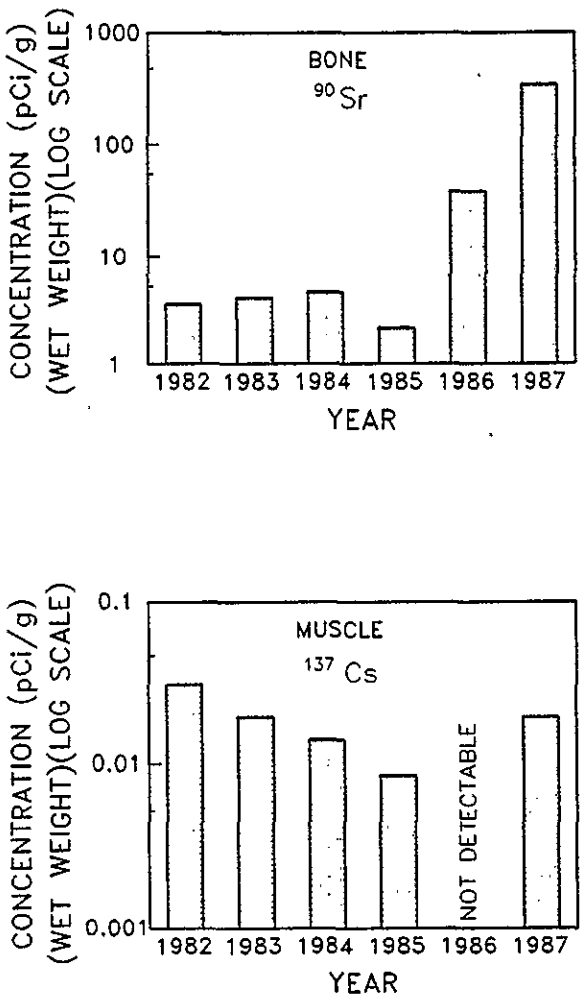

SOURCE: Jaquish and Bryce, 1989.

100-KR-1

Figure 3-10. Median Concentration of ^{90}Sr in Bone and ^{137}Cs in Muscle of Cottontail Rabbits in the 100-K Area.

3.1.7 Site Conceptual Model

The data and evaluations discussed previously are integrated and summarized in the form of a preliminary site conceptual model in this section.

The two-fold purpose of the site conceptual model is to focus the RI/FS process and provide a basis for the initial risk assessment. Many data are available, but, as stated previously, they have limited use. These data were generally collected for other purposes and, therefore, may not be suitable for the RI/FS process. The site conceptual model is shown schematically in Figure 3-11. The contaminant sources, mechanisms for these contaminants to be released into other environmental media, and potential pathways and receptors are summarized in this schematic. This schematic, together with estimates of key parameters such as contaminant concentrations, is part of the basis for modeling the initial human risks associated with the various contaminants, pathways, and receptors. The conceptual model is used to express qualitatively the best estimates or understandings of the following:

- The spatial distribution of contaminants in the vadose zone. Available data are for radionuclides only and are limited to approximately the upper 20 ft (7 m) of the vadose zone.

- Pathways that contaminants may follow to potential receptors. This is based on the integration of contaminant, hydrodynamic, hydrogeologic, and geologic data. Inferences are made on relatively sparse and unevenly distributed data.

- Contaminant sources. Most of the available data for source locations pertain to the upper 20 ft (7 m) of the vadose zone. However, inference is made to the presence of contaminants near the unconfined water table based on ground water contamination, historic records of water levels, and ground water temperature data.

- The geochemical, geologic, and physical nature of the vadose zone. Few data are available. Inferences are made based on the general geology of the Hanford Site and some 100-K Area geologic data.

- Effects on biota. Much work has been done on the Hanford Site in general, but little at the 100-KR-1 operable unit.

Key aspects of the site conceptual model are summarized and illustrated as follows.

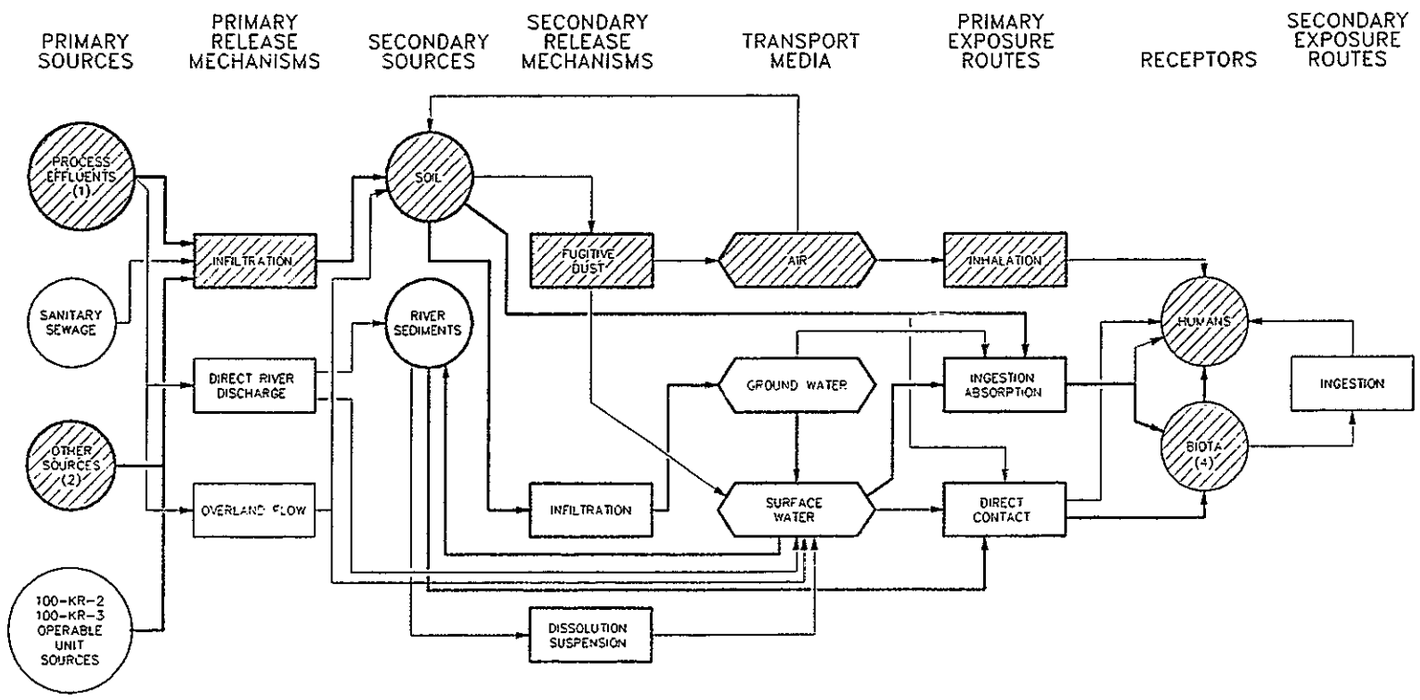

NOTES:

1. INCLUDES ALL FACILITIES THAT RECEIVED PROCESS EFFLUENTS, INCLUDING PIPELINES, BASINS, CRIBS, TRENCHES, FRENCH DRAINS AND OUTFALL STRUCTURES.
2. INCLUDES TANKS, TRANSFORMERS, SOLID WASTE LANDFILL, LEAKS AND OTHER SOURCES.
3. SHADED AREAS INDICATE SUBJECTS THAT ARE PERTINENT TO THE 100-KR-1 OPERABLE UNIT.
4. TERRESTRIAL BIOTA INVESTIGATED IN 100-KR-1 OPERABLE UNIT.

LEGEND

POTENTIAL EXPOSURE PATHWAY

POTENTIAL PRIMARY EXPOSURE PATHWAY

PRIMARY CONTAMINANT SOURCES AND KNOWN CONTAMINATED MEDIA

Figure 3-11. Site Conceptual Model - Contaminant Sources, Release Mechanisms, Environmental Transport Pathways, and Potential Receptors for 100-KR-1.

100-KR-1

THIS PAGE INTENTIONALLY
LEFT BLANK

3.1.7.1 Sources. The major known sources of vadose zone contamination in the 100-KR-1 operable unit that affected ground water quality are listed below:

- The cooling water retention basins and associated pipelines.
- The liquid waste disposal crib and trench.

Other potential sources of contamination considered less significant, based on current knowledge of the site, are the sludge that remains in the retention basins, and the radiological contamination that remains in the ground at the effluent crib and trench. The highest concentrations of beta-gamma radiation at the 100-KR-1 operable unit occur in the retention basin sludge, the retention basin fill dirt, the soil beneath the basins, and the scale and sludge that remain in the cooling water effluent pipelines. Radiological contamination has been shown to extend to a depth of at least 20 ft (7 m) beneath most of the waste disposal sources sampled. The 100-KR-1 operable unit is the largest source operable unit in the 100-K Area on the basis of surface area. Practices in the 100-KR-1 operable unit are believed to have led to much of the ground water contamination in the 100-K Area. Additional source information will be required to effectively screen remedial alternatives in the feasibility stage of the RI/FS.

Little information on nonradiological contamination at the site is available and is limited primarily to information on the chemicals used at the site and limited ground water sampling data. Large volumes of sodium dichromate were added to the cooling water to inhibit corrosion of the cooling water system in the reactor. Also, chromic acid was used as a decontamination solution in the reactor. It is assumed the main sources of chromium at the site are associated with the cooling water effluent facilities, particularly the sludge in the basins and pipelines. The source of nitrate, which has been detected in ground water in the 100-K Area and vicinity, is probably from the nitric acid used for decontamination procedures.

Few data are available on the use of organic chemicals onsite. PCB-containing transformers and hydraulic machinery were used in the 100-K Area. The use of organic solvents has been mentioned in hearsay evidence, and solvent storage tanks have been noted in review of building plans. There are no sampling or analysis data concerning organic wastes or contamination in the source areas or the vadose zone soils.

3.1.7.2 Vadose Zone. The vadose zone consists primarily of sand and gravels from ground surface to the water table. A conceptual model sketch of the vadose zone is shown in Figure 3-12. The following are key elements of the vadose zone:

- The lithology of the vadose zone is variable but consists primarily of very permeable sandy gravel, gravelly sand, cobbles, and boulders of the Hanford formation. A veneer of fill overlies the Hanford formation. In addition, less permeable, dense, cemented gravels of the Ringold Formation lie above the water table.

- The vadose zone has been contaminated with various radionuclides, nitrates, and chromium by the disposal of liquid and solid wastes within the 100-KR-1, -2, -3, and -4 operable units.

- The vadose zone is generally very permeable. However, low permeability silt lenses and the cemented gravels in this vadose zone may cause lateral spreading of infiltrating liquid wastes.

- Channeling within the vadose zone may enhance lateral contaminant movement.

- Contaminants in the portions of the vadose zone, which are in contact with the top of the water table, will be released to the ground water through a combination of infiltration and water table fluctuations.

- Distribution of contaminants in portions of the vadose is widespread as a result of the presence of a relatively thin, but extensive, ground water mound, which existed during facility operations.

- Perched water and contaminants may be localized along the top of the cemented gravels.

Most of the contaminants found in the ground water in the 100-KR-4 operable unit beneath the 100-K Area are believed to have been transported into and through the vadose zone to the ground water table in the large volumes of liquid generated by the various process and cooling water streams active during reactor operation. Natural infiltration is believed to be low, on the order of tenths of an inch per year,

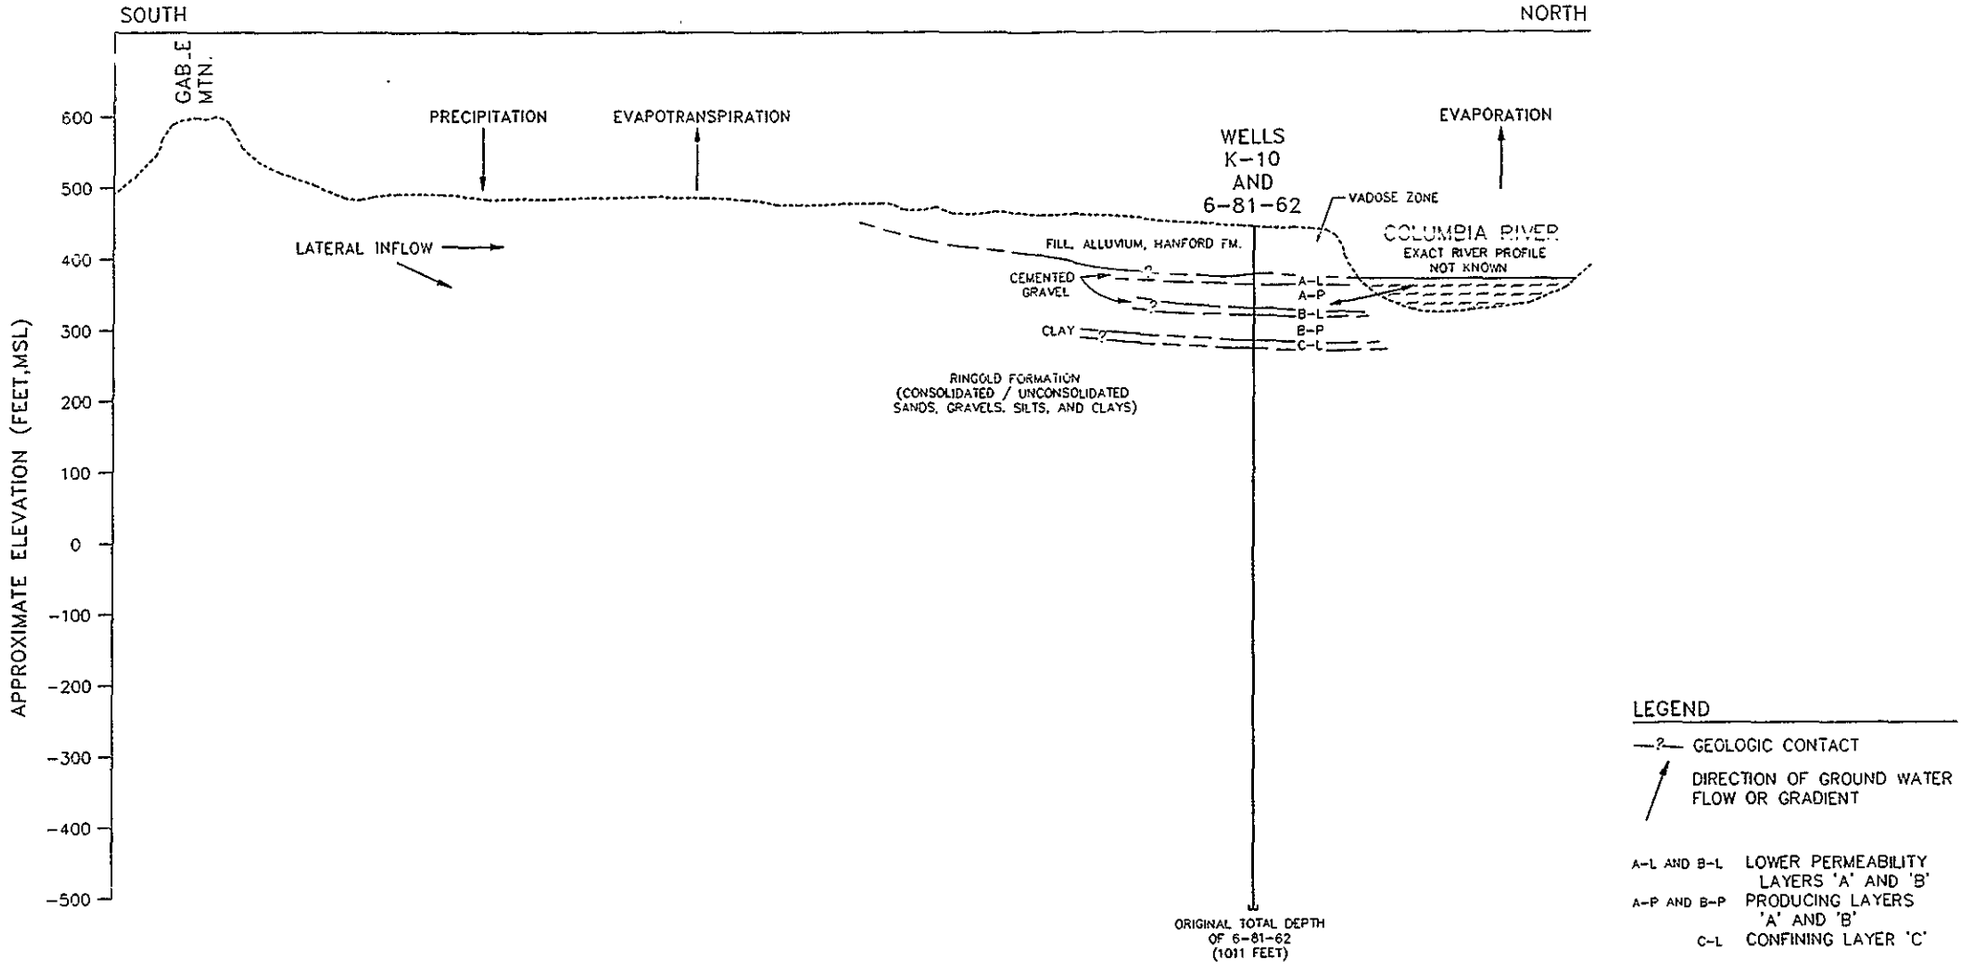

Figure 3-12. Conceptual Model of Vadose System at the 100-K Area.

THIS PAGE INTENTIONALLY
LEFT BLANK

and may not occur in some years. Contaminants are believed to be present in the unsaturated zone at all elevations. Most of the contaminants remaining in the saturated zone are believed to be relatively immobile without the driving force of the cooling water and other liquid discharges characteristic of the period in which the reactors operated. One major exception is the zone immediately above the water table. Contaminants near the water table may represent an intermittent source of ground water contamination; rising ground water may dissolve or leach out contaminants that otherwise would only reach the ground water via infiltrating precipitation or applied surface water.

3.1.7.3 Ground Water System. The conceptual model of the ground water system is discussed in greater detail in the work plan for the 100-KR-4 operable unit. However, there are three elements of the ground water system which impact the potential contaminant pathways from the 100-KR-1 operable unit. First, as mentioned in the previous section, the zone above the water table contributes to the potential for contaminant migration. The ground water level is thought to fluctuate significantly (e.g., 5 ft [1.5 m] or more) in response to similar fluctuations in the Columbia River level within a relatively short time frame (e.g., days). Plus it was higher during site operations due to process water infiltration. Second, the thickness of the vadose zone varies considerably, e.g., from 60 to 0 feet (20 to 0 m), from south to north across the 100-KR-1 operable unit due to topographic variations, some of which were man-made (i.e., filled areas). Therefore, the potential for recharge by infiltration of precipitation is greater closer to the river and in areas of more permeable soil (such as fill). Third, as mentioned in Section 3.1.3., there is apparently at least one area of ground water contamination in the 100-KR-4 operable unit where it underlies the 100-KR-1 operable unit. This area is near the west end of the 116-K-2 trench, i.e., it is in an area where soil contamination has been detected. There are seeps of unknown origin along the riverbank near this area; therefore the interaction of the 100-KR-1 and -4 operable units may need particular attention in this area.

3.1.7.4 Surface Water and Sediments. The conceptual model for surface water and sediments is discussed in the 100-KR-4 work plan. Ground water from the unconfined aquifer discharges to the Columbia River through springs near river level and as baseflow through the sands and gravels of the Hanford formation, according to our conceptual model. This ground water contains radionuclides, nitrate, and metal contaminants that exceed drinking water standards. However, because of dilution, drinking water standards are not believed to be exceeded in the Columbia River. Recreational users at a point of ground water discharge (e.g., springs) would be endangered if the water were ingested prior to being received and diluted by the river, or by direct contact with exposed sediments contaminated by the spring.

Near-shore sediments are assumed to have very low levels of contamination because of the scouring action of the river. Any threats to the environment or public health from contaminated sediments is probably through the food chain where aquatic plants would uptake contaminants from the sediments.

3.1.7.5 Terrestrial Biota. Although there are some site-specific data on biota in the 100-KR-1 operable unit, studies at other 100 Areas and the ongoing Hanford environmental monitoring provide sufficient information for a general understanding of the biota at the 100-KR-1 operable unit. Potential pathways that would affect biota or create human health risk begin with plant uptake of contaminants from surface or shallow subsurface soils. Other potential pathways include resident and visiting wildlife ingestion of vegetation.

3.1.7.6 Air. The transport of contaminants via the air pathway does not appear to be significant. Known sources of contamination in the vadose zone are generally located under several feet of clean soil. However, during the field RI, drilling may disturb some contaminated materials, bringing contaminants to the surface. This, in conjunction with strong, persistent winds at the site, will require strict adherence to health and safety procedures and dust control measures during activities such as drilling.

3.2 POTENTIAL APPLICABLE OR RELEVANT AND APPROPRIATE REQUIREMENTS

Remedial action at the 100-KR-1 operable unit is generally required to comply with federal and state environmental laws and promulgated standards, requirements, criteria, and limitations that are legally applicable or relevant and appropriate where there is release or threatened release of hazardous substances, pollutants, or contaminants. This is referred to as compliance with ARARs.

Three categories of potential ARARs will be evaluated. These are chemical-specific ARARs, location-specific ARARs, and action-specific ARARs. When the requirements in each of these categories are identified, a determination must be made whether those requirements are applicable or relevant and appropriate. A requirement is applicable if the specific terms (or "jurisdictional prerequisites") of the law or regulations directly address the circumstances at a site. If not applicable, a requirement may be relevant and appropriate if circumstances at the site are, based on best professional judgment, sufficiently similar to the problems or situations regulated by the requirements.

To-be-considered materials (TBCs) are nonpromulgated advisories or guidance issued by federal or state governments that are not legally binding and do not have the status of potential ARARs. However, in some circumstances TBCs will be considered along with ARARs in determining the necessary level of remediation for protection of human health and the environment.

The EPA has developed a two-volume guidance document for preparing ARARs in *CERCLA Compliance with Other Laws Manual, Draft Guidance*, 1988d. This guidance document defines the three categories of potential ARARs as follows:

- Ambient or chemical-specific requirements are usually health or risk-based numerical values or methodologies that, when applied to site-specific conditions, result in establishment of numerical values. These values establish the acceptable amount or concentration of a chemical that may be found in, or discharged to, the environment.

- Location-specific requirements are restrictions placed on the concentration of hazardous substances or the conduct of activities solely because they occur in special locations.

- Performance, design, or other action-specific requirements are usually technology or activity-based requirements or limitations of remedial actions.

Potential chemical- and location-specific ARARs are identified based on the compilation and evaluation of existing site data. These ARARs need to be refined during the FS process by EPA, Ecology, and DOE. Potential action-specific ARARs are discussed in this section and will be identified during development of alternatives in the RI/FS tasks.

3.2.1 Chemical-Specific Requirements

A chemical-specific requirement sets concentration limits in various environmental media for specific hazardous substances, pollutants, or contaminants. These are numerical values derived from specific standards or are health based values derived from the risk assessment. Based on existing data, contaminants that may be present in the 100-KR-1 operable unit are included in Table 3-15. Contaminant exposure pathways include ingestion of soils and biota, inhalation of particulates, and dermal contact with soils and building rubble. There are federal and state standards

for air and water quality; however, there are no soil remediation standards except for PCBs and uranium mill tailings. Typically, radiation standards and health-related values are used to back-calculate acceptable remediation levels for soil contaminants. The identified potential federal and state ARARs are summarized in the following sections.

Table 3-15. Contaminants of Concern in the 100-KR-1 Operable Unit.

Radionuclides	Inorganics	General Chemicals
Gross alpha	Arsenic	Ammonia
Gross beta	Chromium	Fluoride
Americium-241	Copper	Chloride
Carbon-14	Mercury	Nitrate
Calcium-41	Potassium	Sulfate
Cobalt-60	Zinc	Sulfamate
Cesium-134		Oxalate
Cesium-137		
Chromium-51		Organics
Europium-152		Herbicides
Europium-154		Polychlorinated Biphenyls
Europium-155		
Hydrogen-3		
Iodine-129		
Nickel-63		
Plutonium-238		
Plutonium-239		
Plutonium-240		
Strontium-90		
Technetium-99		
Uranium-152		
Uranium-154		
Uranium-155		
Zinc-65		

3.2.1.1 Federal Requirements. Federal chemical-specific requirements come from five main citations in the Code of Federal Regulations (CFR).

3.2.1.1.1 Environmental Protection Agency Rules for Controlling Polychlorinated Biphenyls under the Toxic Substances Control Act (40 CFR 761). These regulations control the manufacture, processing, storage, disposal and cleanup of PCBs. Generally, PCBs are only regulated if the source of the spill contained greater than 50 ppm PCBs. Spills that occurred before May 4, 1987 must be cleaned up in accordance with the spill policy in 40 CFR 761.120. These regulations set forth requirements based on specific circumstances.

3.2.1.1.2 Nuclear Regulatory Commission Standards for Protection Against Radiation (10 CFR 20). These regulations apply to activities licensed by the Nuclear Regulatory Commission and specify radiation dose standards for individuals in restricted and unrestricted areas. The standard for emissions to air in unrestricted areas are potential ARARs both for ambient conditions and during any remedial action that could affect the air pathway.

3.2.1.1.3 National Emission Standards for Radionuclide Emissions From DOE Facilities (40 CFR 61.90). The standards for radioactive emissions from DOE facilities apply to facilities owned or operated by the DOE except for any facilities regulated under 40 CFR 190, 191, and 192. These standards could be either chemical-specific or action-specific (such as a removal action) ARARs for the air pathway. The standards mandate that emissions of radionuclides to air from DOE facilities shall not exceed those amounts that cause any member of the public to receive in any year an effective dose equivalent of 10 mrem/yr.

3.2.1.1.4 Environmental Protection Agency (EPA) Safe Drinking Water Act (SDWA) Regulation (40 CFR 141). The SDWA provides for the establishment of drinking water quality standards for public water systems. These standards presented in Table 3-16 are of notable interest for the Hanford Site.

The annual average concentration limits for manmade radionuclides of interest are listed in Table 3-17. These radionuclides are assumed to yield an annual dose of 4 mrem to the indicated organ.

Table 3-16. Radiological Drinking Water Standards (EPA 1976).

Contaminants	Limit
Gross alpha (excluding uranium)	15 pCi/L
Combined ^{226}Ra and ^{228}Ra	5 pCi/L
$^{226}Radium$ (State of Washington only)	3 pCi/L
Gross beta and gamma radioactivity from manmade radionuclides	Annual average concentration shall not produce an annual dose from manmade radionuclides equivalent to the total body or any internal organ dose greater than 4 mrem/yr. If two or more radionuclides are present, the sum of their annual dose equivalent shall not exceed 25 mrem/yr. Compliance may be assumed if annual average concentrations for gross beta activity, ^{3}H, and ^{90}Sr are less than 50, 20, and 8 pCi/L, respectively.

Table 3-17. Annual Average Standard for Manmade Radionuclides in Drinking Water (EPA 1976).

Radionuclide	Critical Organ	Concentration, pCi/L
^{3}H	Whole body	20,000
^{60}Co	GI (LLi)[a]	100
^{89}Sr	Bone	20
^{89}Sr	Bone marrow	80
^{90}Sr	Bone marrow	8
^{95}Zr	GI (LLi)[a]	200
^{95}Nb	GI (LLi)[a]	300
^{106}Ru	GI (LLi)[a]	30
^{129}I	Thyroid	1
^{131}I	Thyroid	3
^{134}Cs	GI(s)[a]	20,000
^{137}Cs	Whole body	200
^{14}C	Fatty tissue	2,000
^{99}Tc	GI (LLi)[a]	900
^{103}Ru	GI (LLi)[a]	200
^{125}Sb	GI (LLi)[a]	300

[a] Gastrointestinal tract (lower large intestine)

3.2.1.1.5 EPA Radiation Protection Standards for Managing and Disposing of Spent Nuclear Fuel, High-Level and Transuranic Radioactive Wastes (40 CFR 191). These standards apply to radiation doses received by members of the public as a result of the management and storage of spent nuclear fuel or high-level or transuranic wastes at any disposal facility that is operated by DOE. The standards mandate that the combined annual dose equivalent to any member of the public in the general environment resulting from discharges of radioactive material and direct radiation shall not exceed 25 mrem to the whole body and 75 mrem to any critical organ.

3.2.1.1.6 Clean Air Act (40 CFR Part 50). This act establishes national Primary and Secondary Ambient Air Quality Standards.

3.2.1.1.7 U.S. Nuclear Regulatory Commission (NRC) (10 CFR Part 20). These regulations cover decontamination and decommissioning of NRC licensed facilities and is applicable to the Hanford Site.

3.2.1.1.8 Solid Waste Disposal Act (40 CFR Part 261). This act establishes standards for the management of solid waste.

3.2.1.1.9 Occupational Health and Safety Act (40 CFR Part 1910). This act establishes standards governing the safety and health of individuals in the workplace.

3.2.1.2 State of Washington Requirements. State of Washington chemical-specific requirements are listed in five regulations and are discussed individually below.

3.2.1.2.1 Washington Standards for Protection Against Radiation (WAC 402-24). These regulations specify radiation dose standards for permissible levels of radiation in unrestricted areas. Table II of Appendix A of 10 CFR 20 itemizes the allowable concentrations in air above natural background.

3.2.1.2.2 Washington Ambient Air Quality Standards and Emission Limits for Radionuclides (WAC 173-480). Ecology ambient air quality standards and radionuclide emission limits mandate that radionuclides in the air must not cause a maximum accumulated dose equivalent of more than 25 mrem/yr to the whole body or 75 mrem/yr to a critical organ of any member of the public (excluding doses from radon and radon decay products).

3.2.1.2.3 Washington Air Quality and Emission Standards for Radionuclides (WAC 402-80-050). The Washington State Department of Social and Health Services Air Quality and Emission Standards for Radionuclides adopt the Ecology standards (WAC 173-480) by reference.

3.2.1.2.4 Washington State Drinking Water Standards (Rules and Regulations of the State Board of Health, Chapter 248054). These regulations are identical to those promulgated under the Safe Drinking Water Act for the contaminant of concern.

3.2.2 Action-Specific Requirements

Action-specific ARARs are requirements that are triggered by specific remedial actions at the site. These remedial actions are not fully defined until the FS phase. However, the universe of action-specific ARARs defined by a preliminary screening of potential remedial action alternatives will help focus the FS alternatives. Potential action specific ARARs for the 100-KR-1 operable unit are listed in Table 3-18.

3.2.3 Location-Specific Requirements

Location specific ARARs identify requirements for site activities that are triggered by site location. These can include sensitive habitats, floodplains, fault locations, historical and prehistorical resources, and wetlands. These ARARs for the 100-KR-1 operable unit are listed in Table 3-19.

3.2.4 Other Criteria and Guidance

In addition to the listed ARARs, there are other federal and state criteria, advisories, and guidance that can be considered in determining the appropriate degree of remediation for the 100-KR-1 operable unit. These additional items are summarized in the sections that follow.

3.2.4.1 Health Effects Assessment. Some contaminants detected at the 100-KR-1 operable unit may not have MCLs, state water quality criteria, or radiation criteria. For individual carcinogens that do not have federal or state standards, but have a carcinogenic potency factor, ground water and soil concentrations can be calculated

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.

Action	Requirements	Prerequisites for Applicability	Citation
CHAPTER 1 - CLEAN AIR ACT			
New Source Performance Standards			
Storage of Petroleum Liquids	Floating roof, vapor recovery system, or their equivalents	Storage vessel constructed after 6/11/73 and prior to 5/19/78 having storage capacity greater than 40,000 gallons, storing petroleum liquids with vapor pressure equal to or greater than 1.5 psia	40 CFR section 60.112 (CAA)
	Floating roof or vapor recovery system	Storage vessels constructed after 5/18/78 having storage capacity greater than 40,000 gallons, storing petroleum liquids with vapor pressure equal to or greater than 1.5 psia	40 CFR section 60.112(a) (CAA)
CHAPTER 2 - TOXICS/PESTICIDES			
PCB storage prior to disposal	All storage areas[a] Storage facilities must be constructed: ■ With an adequate roof and walls ■ With a floor and curb of impervious materials ■ Without drain valves, floor-drains, expansion joints, sewer lines or other openings ■ Above the 100-year flood water level	Storage of PCBs at concentrations of 50 ppm or greater and PCB items with PCB concentrations of 50 ppm or greater	Toxic Substances Control Act (TSCA) 40 CFR section 761.65
	Temporary storage (30 days or less) Temporary storage (up to 30 days from the date of initial storage) need not comply with above storage regulations for the following items: ■ PCB articles and equipment that are nonleaking ■ Leaking articles and equipment placed in non-leaking containers		40 CFR section 761.65 (TSCA)

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.
Page 2

Action	Requirements	Prerequisites for Applicability	Citation
	■ PCB containers containing non-liquid PCBs, such as contaminated soil, rags, debris		
	■ Liquid PCB containers containing PCBs between 50-500 ppm if covered by a spill prevention, control, and countermeasure plan		
	<u>All Storage Areas</u>		40 CFR section 761.65 (TSCA)
	Storage area must be properly marked		
	No item of movable equipment used to handle PCBs that comes into contact with PCBs shall be moved from the storage area unless it has been decontaminated under section 761.79		40 CFR section 761.65 (TSCA)
	All stored articles must be checked for leaks every 30 days		40 CFR section 761.65 (TSCA)
PCB Storage Prior to Disposal	Containers must be dated when they are placed in storage		40 CFR section 761.65 (TSCA)
	All PCB articles or containers must be removed and disposed of within 1 year of storage		40 CFR section 761.65 (TSCA)
Marking of PCBs	The following must be marked as designated in 40 CFR section 761.45:		40 CFR section 761.65 and 761.180 (TSCA)
	■ PCB containers containing greater than 50 ppm PCBs, PCB transformers, PCB Large High-Voltage Capacitors, equipment containing a PCB transformer or a PCB Large High-Voltage Capacitor, PCB Large Low-Voltage Capacitor, PCB Large Low-Voltage Capacitor at time of removal, electric motors using PCB coolants, hydraulic systems using PCB hydraulic fluid, heat transfer systems using PCBS, PCB article containers containing any of the above, storage areas used to store PCBs and PCB items for disposal		

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.

Action	Requirements	Prerequisites for Applicability	Citation
	All marks must be on exterior of PCB container and must be clearly visible		40 CFR section 761.40 (TSCA)
Disposal of pesticides	Unacceptable disposal methods: ■ Those inconsistent with label ■ Open dumping ■ Open burning ■ Disposal into any body of water ■ Those inconsistent with applicable law		Federal Insecticide Fungicide and Rodenticide Act (FIFRA) 40 CFR section 165.7
	Chemically deactivate pesticide and recover the heavy metals. If chemical deactivation facilities are not available, encapsulate the pesticide and bury it	Treatment recommended for organic mercury, lead, cadmium, arsenic, and all inorganic pesticides	40 CFR section 165.8(c)
Disposal of pesticide containers and residue	Incinerate or bury in a designated landfill	Combustible containers that formerly held organic or metallo-organic pesticides, except organic mercury, lead, arsenic, and cadmium	40 CFR section 165.9 (A) (FIFRA)
	Non-combustible containers must be: ■ Triple-rinsed ■ Returned to the pesticide manufacturer for reuse if in good condition ■ Returned to a facility for recycling as scrap metal if in poor condition	Non-combustible containers that formerly held organic or metallo-organic pesticides (with exceptions noted above)	40 CFR section 165.9(b) (FIFRA)
	Triple puncture containers to facilitate drainage, and dispose of in a sanitary landfill	Combustible and non-combustible containers that formerly held organic, mercury, lead, cadmium, or arsenic, or inorganic pesticides	40 CFR section 165.9(c) (FIFRA)

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.
Page 4

Action	Requirements	Prerequisites for Applicability	Citation
Labeling of pesticides	Label pesticides legibly, and prominently, to show: ■ Ingredients; ■ Warnings and precautionary statements; ■ Toxicity; ■ Directions for use, including storage and disposal methods	Labeling requirements may apply when pesticides are considered products, and not RCRA hazardous wastes	40 CFR section 162.10 (FIFRA)
Handling of pesticides	Individuals handling certain pesticides must be State- or Federally-approved applicators		40 CFR section 171.4 (FIFRA)
CHAPTER 4 - MANAGEMENT OF RADIOACTIVE WASTES			
Discharge of radioactive pollutants to air	Airborne emissions shall not cause members of the public to receive doses greater than: ■ 25 mrem/yr to the whole body; or ■ 75 mrem/yr to the critical organ[b]	Applicable to airborne emissions from DOE, NRC-licensed, and non-DOE Federal facilities during their operational period. Not applicable to: doses caused by radon-220, radon-222, and their respective decay products; facilities regulated under 40 CFR Parts 190, 191 or 192; and low-energy accelerators and users of sealed radiation sources	Clean Air Act (CAA) 40 CFR Part 61, Subparts H and I[e]
Discharge of radionuclides to unrestricted areas (air and water)	Airborne and liquid discharges to unrestricted areas shall meet radionuclide-specific concentration limits in 10 CFR Part 20, Appendix B, Table II. These concentrations are designed to limit radiation exposure to members of the public to 0.5 rem/year to the whole body, blood-forming organs, and gonads; 3 rems/year to the bone and thyroid; and 1.5 rems/year to other organs[d]	Applicable to all categories of Nuclear Regulatory Commission (NRC) licensees; also applicable to Agreement State licensees Applicable to releases of source, byproduct, and special nuclear material, as well as to naturally occurring and accelerator-produced radioactive material (NARM) released from facilities licensed to possess source, byproduct, and special nuclear material[e]	Atomic Energy Act[f] (AEA) 10 CFR section 20.106

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.

Action	Requirements	Prerequisites for Applicability	Citation
Radioactive waste treatment and disposal	A variety of waste disposal requirements are set, including those specifying how licensees may dispose of licensed material (see Section 4.2.1.1 of Chapter 4 of Part II), as well as concentration limits for disposal of radioactive waste into sanitary sewerage systems, requirements for treatment and disposal by incineration, and specific requirements for the disposal of radioactively contaminated animal tissue and liquid scintillation media	Applicable to all categories of NRC licensees; also applicable to Agreement State licensees. Applicable to releases of source, byproduct, and special nuclear material	10 CFR sections 20.301 through 20.311 (AEA)
		Certain requirements also apply to other radioactive materials, i.e., NARM released from facilities licensed to possess source, byproduct, and special nuclear material	10 CFR sections 20.302(a) and 20.302(b) (AEA)
Closure and post-closure observation and maintenance of a low-level radioactive waste disposal site	Closure designs must assure that long-term performance objectives of 10 CFR sections 61.41-61.44 (see below) are met, taking into account site-specific geologic, hydrologic, and other conditions	Applicable to NRC-licensed land disposal facilities that receive low-level wastes from other (i.e., commercial disposal facilities)	10 CFR section 61.28 (AEA, LLWPA, and LLRWPAA)
	Following completion of closure, the disposal site must be monitored and maintained for 5 years (longer or shorter periods may be allowed) and then responsibility is transferred to a Federal or State government agency, which will implement institutional care requirements in 10 CFR section 61.23(g)	Not applicable to disposal of: ■ High-level waste and spent fuel (addressed in 10 CFR Part 60 and 40 CFR Part 191); ■ Transuranic waste (addressed in 40 CFR Part 191); ■ Uranium and thorium mill tailings (addressed in 10 CFR Part 40 and 40 CFR Part 192); and ■ Radioactive waste by an individual licensee, as provided for in 10 CFR Part 20	10 CFR sections 61.29 and 61.30 (AEA, LLWPA, and LLRWPAA)
Siting, designing, operation, closure, and control of a low-level radioactive waste disposal site	A variety of performance objectives are established, including standards that set limits on radiation exposures by members of the public, protect people from inadvertently intruding onto a radioactive waste site, and stabilize the site after closure. The public exposure limits are the same dose limits as in 40 CFR Part 190	Same prerequisites as specified above for 10 CFR Part 61	10 CFR sections 61.41 through 61.44 (Subpart C of Part 61) (AEA, LLWPA, and LLRWPAA)

Table 3-18. Selected Action-Specific Potential Applicable or Relevant and Appropriate Requirements.
Page 6

Action	Requirements	Prerequisites for Applicability	Citation
	A variety of technical requirements are established, i.e., minimum characteristics a disposal site must have to be acceptable	Same prerequisites as specified above for 10 CFR Part 61, except that existing technical requirements are applicable only to the near-surface disposal of radioactive waste. A near surface disposal facility is defined as one that disposes of waste in or within the upper 30 meters of the earth's crust	10 CFR sections 61.50 through 61.59 (Subpart D of Part 61) (AEA, LLWPA, and LLRWPAA)

a Bulk storage requires the preparation and implementation of an SPCC Plan (see 40 CFR section 761.65(c)(7)(iii) for specifications of container sizes that are considered "bulk" storage containers). Substantive requirements may be ARARs if bulk storage is performed on-site.

b A millirem (mrem) = 0.001 rem, where a rem is a measure of dose equivalence for the biological effect of radiation of different types and energies on people.

c Lead agencies are cautioned that the radionuclide NESHAPs are being reexamined subject to a voluntary remand and that they may be revised in the future.

d These dose limits are considered high relative to recent EPA standards (see discussion in Section 4.2.1.1 of Chapter 4 of Part II).

e Section 104(a)(3)(A) of CERCLA as amended by SARA prohibits response to releases "of a naturally occurring substance in its unaltered form or altered solely through naturally occurring processes or phenomena, from a location where it is naturally found." NARM possessed and used by a nuclear material licensee, in almost all cases, would not qualify as a naturally occurring substance as it is defined in this section.

f These standards are potentially applicable only for CERCLA actions at sites licensed by the NRC, but may be relevant and appropriate to radioactively contaminated sites not licensed by the NRC.

g Part 61 was promulgated primarily under the authority of the Atomic Energy Act, but two other statutes from which authority was derived are the Low-Level Waste Policy Act of 1980 (LLWPA) and the Low-Level Radioactive Waste Policy Amendments Act of 1985 (LLRWPAA).

H:\1842\TABLES\KH1\3\175

Table 3-19. Selected Location-Specific Potential Applicable or Relevant and Appropriate Requirements.
Page 1

Action	Requirements	Prerequisites for Applicability	Citation
315CHAPTER 1 - CLEAN AIR ACT			
NAAQs attainment areas	New major stationary sources shall apply best available control technology for each pollutant, subject to regulation under the Act, that the source would have potential to emit in significant amounts Owner or operator of proposed source of modification shall demonstrate that allowable emissions increases or reductions (including secondary emissions) will not cause or contribute to a violation of the NAAQS or applicable maximum allowable increase over baseline concentrations	Major stationary sources as identified in 40 CFR section 52.21(b)(1)(i)(a) that emits, or has the potential to emit, 100 tons per year or more of any regulated pollutant; any other stationary source that emits, or has the potential to emit, 250 tons per year or more of any regulated pollutant.40 CFR section 52.21(j) (CAA)	
NAAQS nonattainment areas	Source must obtain emission offsets in air quality control region of greater than one-to-one Source subject to "lowest achievable emission rate (LAER)" as defined in 40 CFR section 51.18(j)(xiii) All major stationary sources owned or operated by the person in the State are in compliance, or on a schedule for compliance, with all applicable emission standards	Any stationary facility or source of air pollutants that directly emits, or has the potential to emit, 100 tons per year or more of any air pollutant (including any major emitting facility or source of fugitive emissions of any such pollutants) [CAA section 302(j)]	CAA Part D. section 173(1) CAA Part D, section 173(2) CAA Part D, section 173(3)
Other Resource Protection Statutes			
Historic district, site, building, structure, or object	Avoid impacts on cultural resources. Where impacts are unavoidable, mitigate through design and data recovery	Properties listed in the National Register of Historic Places, or eligible for such listing	National Historic Preservation Act (NHPA) 16 CFR Part 470, et. seq.
Critical habitat of/or an endangered or threatened species	Identify activities that may affect listed species Actions must not threaten the continued existence of a listed species Actions must not destroy critical habitat	Species or habitat listed as endangered or threatened	Endangered Species Act (ESA) 50 CFR section 402.04 50 CFR section 402.01 50 CFR section 402.01

Table 3-19. Selected Location-Specific Potential Applicable or Relevant and Appropriate Requirements.
Page 2

Action	Requirements	Prerequisites for Applicability	Citation
Wild and scenic rivers	Determine if project will affect the free-flowing characteristics, scenic, or natural values of a designated river; Not authorize any water resources project or any other project that would directly or indirectly impact any designated river without notifying DOE or Forest Service	Any river, and the bordering or adjacent land, designated as "wild and scenic or recreational"	Wild and Scenic Rivers Act (WSRA) 36 CFR section 297.4
Coastal zone or an area that will affect the coastal zone	Federal activities must be consistent with, to the maximum extent practicable, State coastal zone management programs Federal agencies must supply the State with a consistency determination	Wetland, flood plain, estuary, beach, dune, barrier island, coral reef, and fish and wildlife habitat, within the coastal zone	Coastal Zone Management Act (CZMA) 15 CFR section 930.30 15 CFR section 930.34 (CZMA)
Wilderness area	The following are not allowed in a Wilderness area: ■ commercial enterprises ■ permanent, roads, except as necessary to administer the area ■ motor vehicles ■ motorized equipment ■ motorboats ■ aircraft ■ mechanized transport ■ structures or buildings	Any unit of the National Wildlife Refuge System	Wilderness Act (WA) 50 CFR section 35.5

H:\1842\TABLES\KR4\3\175A

that would result in a 10^{-4} to 10^{-6} excess lifetime cancer risk by inhalation or ingestion. Excess lifetime cancer risk is defined as the incremental increase in the probability of developing cancer compared to the background probability. For noncarcinogenic compounds, reference doses (RFD) or acceptable chronic intakes can be used to estimate concentrations that would result in no observable adverse health effects by ingestion or inhalation.

3.2.4.2 Federal Health Advisories. Federal health advisories issued by the EPA Office of Drinking Water cite the current assessment of contaminant concentrations in drinking water at which adverse health effects would not be anticipated to occur. A margin of safety (typically between 100 and 1,000, depending upon the contaminant and the extent of its toxicological database) is included to protect sensitive members of the human population. The health advisories are developed for noncarcinogenic end points of toxicity. They can be specified for 1-day, 10-day, long-term (90 days to 1 year), and lifetime exposure periods.

3.2.4.3 Maximum Contaminant Level Goals. As part of the process for developing final drinking water standards, EPA develops Maximum Contaminant Level Goals (MCLGs) formerly known as Recommended Maximum Contaminant Level (RMCL). MCLGs are enforceable health goals for drinking water that are set at a level representing "no known anticipated adverse effects on the health of persons, while allowing for an adequate margin of safety." For carcinogenic compounds, MCLGs are set at zero.

3.2.4.4 ICRP/NCRP Guidance. The International Council on Radiation Protection and the National Council on Radiation Protection have a guideline standard of 100 mrem/yr whole body dose of gamma radiation.

3.2.5 Waivers

Federal law recognizes there may be instances in which ARARs cannot be met with respect to remedial actions onsite. It, therefore, identifies six circumstances under which ARARs may be waived. However, other statutory requirements, specifically, the requirement that remedies be protective of human health and the environment, cannot be waived. Waivers are appropriate if:

- The remedial action selected is an interim remedy and only part of a total remedial action that will attain ARARs when completed.

- Compliance with ARARs at the site would result in greater risk to human health and the environment than alternative options.
- Compliance with ARARs is impracticable from a technical perspective.
- The remedial actions selected will attain an equivalent standard of performance, although ARARs are not met.
- With respect to state ARARs, the State has inconsistently applied ARARs in similar circumstances at other remedial actions within the State.
- In the case of fund-financed remedial actions, financial restrictions within the superfund program require fund-balancing such that satisfaction of ARARs at the site must give way to a greater need for protection of public health and welfare and the environment at other sites.

3.2.6 Proposed Regulations

Ecology is currently developing cleanup regulations under the Model Toxic Control Act (Chapter 173-340 of WAC). These regulations, which include standards for air contaminants and for the remediation of contaminated soils, could pertain to the 100-KR-1 operable unit and are expected to be fairly stringent. The standards probably will not cover radioactive substances. Draft regulations were expected to be published in February or March 1990, but are still in draft form as of this writing.

The EPA has issued an Advanced Notice of Proposed Rulemaking for radiation regulations in 40 CFR 193 and 40 CFR 194. These potential regulations are for low-level radioactive waste and residual radioactivity from demolition and decommissioning activities, respectively. At this time, EPA has not issued any proposed regulations.

3.3 PRELIMINARY RISK ASSESSMENT

This section presents a preliminary evaluation of the current and future potential human health and environmental impacts associated with the 100-KR-1 operable unit. This initial evaluation, as part of the work planning process, serves several functions. First, it helps to focus the RI activities on those areas where current risks can be documented, or where future risks are possible. Secondly, this process can identify

areas of uncertainty related to sources, pathways, and receptors that will need to be resolved during the RI in order to perform a quantitative and definitive risk assessment. Lastly, the initial assessment of potential impacts documents and provides, in part, the technical rationale for performing the RI/FS.

This section contains a presentation and discussion of the preliminary source-pathway-receptor model of the operable unit. There is an evaluation of the environmental and toxicological characteristics of site contaminants and the preliminary identification of the contaminants of concern. It concludes by discussing the current and potential future endangerments that have been initially identified.

3.3.1 Conceptual Exposure Pathway

Based on information presented thus far, a conceptual exposure pathway model has been developed which incorporates the potentially significant contaminant exposure pathways for the 100-KR-1 operable unit. The model is shown schematically in Figure 3-11.

The purpose of the conceptual pathway model is to present the possible unit-specific contaminant exposure pathways. During the RI, the conceptual model will be tested and refined in an iterative manner until the operable unit is sufficiently understood to support decisions regarding corrective measures. Risk assessment and sensitivity analysis are two methods of testing and refining the model. When the RI is conducted in this manner, the focus is kept on unit-specific objectives.

Each exposure pathway in the conceptual model must contain the following components:

- A contaminant source.
- A contaminant release mechanism.
- An environmental transport medium.
- An exposure route.
- A receptor.

Each of these model components is discussed in the following sections.

3.3.1.1 Sources. Primary contaminant sources in the 100-KR-1 operable unit include the 116-K-1 crib, the 116-K-2 trench, and retention basins (116-KW-3 and 116-KE-4) and associated pipelines. After an initial release to the environment occurs, contaminants can be bound in soils and sediments before being slowly rereleased. These media may serve as secondary contaminant sources.

Detailed information on individual waste facilities and their associated contaminants is presented in sections 2.1 and 3.1. A summary of the known extent of soil contamination at the 100-KR-1 operable unit is contained in Section 3.1.2.

3.3.1.2 Release Mechanisms. Release mechanisms can be divided into primary and secondary categories. Reactor cooling water and process effluent at the 100-KR-1 operable unit are known to have infiltrated the soils surrounding the reactor basins and the process effluent transfer, treatment, and disposal facilities. Some of this effluent was also directly discharged to the Columbia River. Pipeline and retention basin leaks resulted in discharges to surface soils and the vadose zone. The most significant primary release mechanism at the 100-KR-1 operable unit is infiltration and the most substantial contributions are from reactor cooling water and process effluent.

The most significant release mechanism from secondary sources is infiltration and migration of contaminants from the vadose zone to the ground water. Fugitive dust generation and overland runoff are also potential secondary release mechanisms from contaminated soils.

3.3.1.3 Environmental Transport Media. Rainwater and snowmelt infiltrating from the ground surface may transport contaminants in the unsaturated zone to the ground water. Although the average annual water infiltration at the 100-KR-1 operable unit is low, unusually heavy rainfall may cause contaminant movement in the unsaturated zone. After contaminants reach the ground water, they can be discharged to the Columbia River and transported downstream. In the case of fugitive dust emissions, wind serves as the transport medium. In addition, biota may take up or ingest contaminants providing for a direct pathway to the food chain.

3.3.1.4 Exposure Routes. Individuals or biota can be exposed to contaminants in any of the following ways:

- Direct contact with contaminated sources or transport media
- Ingestion of contaminated materials or biota

9 0 1 1 8 3 7 0 1 5 0

- Absorption of soil contaminants (for plants)
- Inhalation of contaminants in the atmosphere.

Additional exposure pathways for unrestricted future use are discussed in the 100-KR-4 work plan.

3.3.1.5 Receptors. Receptors are organisms that may potentially be exposed to contaminants. The most significant point of exposure for terrestrial plants is in the root zone where contaminants can be absorbed by roots. Plants, for example, can absorb tritiated water and incorporate it in their normal water fraction. Animals, especially those that burrow, may also be exposed by direct contact and consumption of contaminated plants.

The most critical exposure point in the aquatic environment is in the river, near ground water discharge points. Exposures may occur for aquatic plants, fish, and other organisms. A further assessment of the impact of releases to the river on the aquatic environment is contained in the RI/FS work plan for 100-KR-4.

Because of institutional control of the Hanford Site, human exposure is limited at the present time. Because most of the waste areas are covered with soil, there is little risk of air transport of contaminants. The contaminated ground water within the 100-KR-1 operable unit is not considered to be part of this operable unit, but is addressed in the work plan for the 100-KR-4 operable unit. The most important exposure to humans in the near term will be to workers at the site involved in decommissioning, environmental monitoring, RI, and remedial actions.

Future human exposure inside the 100-KR-1 operable unit will be more likely if institutional control of the site is lost or abandoned. Should this happen, it is possible that future homes could be built atop a former waste disposal site. By digging into the surface soil to construct a house or drilling for a domestic water well, exposure pathways could develop. The pathways could include:

- Inhalation of contaminated dust
- Direct radiation exposure (gamma, beta, alpha)
- Ingestion of contaminated well water (evaluated as part of 100-KR-4 operable unit)

- Ingestion of contaminated food produced at the site
- Ingestion of contaminated soil by children.

During construction of a house at the site, contaminated soil could be brought to the surface. The individual could be exposed by inhaling contaminated dust during construction and after the house is completed. If radionuclides are present in the near-surface soil, the contaminated soil excavated during construction can also be the source of direct gamma exposures. It is also possible that the individual would plant edible crops or raise edible animals which would forage in the contaminated surface soil. Plant uptake of contaminants from the soil can cause human exposures through the ingestion of contaminated vegetables, meat, and milk produced at the site.

Since strict control of the 100-KR-1 operable unit cannot be assured into the indefinite future, a future residential scenario has been included to predict future impacts.

3.3.1.6 Exposure Summary. The most significant primary source of contaminant releases in the 100-KR-1 operable unit were process effluent and contaminated water from the two 100-K Area reactors. The most significant current contaminant release mechanism is water infiltration through contaminants in the unsaturated zone. Contaminants can eventually reach the ground water and be discharged to the Columbia River, where sediments and aquatic organisms may be exposed. Future human exposures may result if the area returns to private use after institutional control is lost.

3.3.2 Primary Toxicity Assessment

The known maximum concentrations of contaminants in the soil at the 100-KR-1 operable unit will be developed. Information is currently lacking concerning concentrations of nonradioactive inorganics, PCBs, herbicides or other organic chemicals in the soils.

3.3.3 Contaminant Characteristics

To evaluate the potential threat to public health and the environment from the 100-KR-1 operable unit, it is important to focus on the contaminants of greatest

concern. Generally the contaminants of greatest concern are those that are present in the largest quantities, highly mobile, toxic, or persistent in the environment. Contaminants with a strong tendency to bioaccumulate in plants and animals are also considered. The contaminants of concern in Table 3-15 will be evaluated in detail.

3.3.3.1 Toxicity. The known or potential contaminants listed in the table of maximum contaminant concentrations include organic and inorganic acids and salts that readily dissociate in water. This toxicity assessment considers the constituents that could be present in the environment after disposal. The known or potential chemical contaminants present in the environment are sulfate and chlorine ions, hexavalent chromium, copper, mercury, and PCBs.

Hexavalent chromium and mercury can both pose a threat to human health and the environment. The primary drinking water standards for these contaminants are 50 μg/L for (total) chromium and 2 μg/L for mercury. Hexavalent chromium is classified by the EPA as a Group 1 carcinogen for inhalation exposure. However, hexavalent chromium has not been shown to be carcinogenic through ingestion. Hexavalent chromium is toxic to aquatic organisms. Ambient water quality criteria for protection of freshwater organisms are 16 μg/L for acute exposure and 11 μg/L for chronic exposure. Mercury is toxic to both fish and humans when it is converted by microorganisms into highly toxic methyl mercury.

A primary drinking water standard for copper has not been established. The secondary standard for copper is 1000 μg/L. Copper is toxic to aquatic organisms. The ambient water quality criteria for copper vary with the hardness of the water, but typical values are 12 μg/L for acute exposure and 8 μg/L for chronic exposure.

PCBs, which may be present in the 100-KR-1 operable unit, are long-lived in the environment, relatively immobile in soil, and are probably human carcinogens. No direct evidence of PCB contamination at the site was identified during the development of this work plan, but PCB transformers may have been used extensively in the 100-K Area.

Potential exposure to any of the radionuclides in the table of maximum contaminant concentrations may be important from the standpoint of radiotoxicity. The dose response functions used by EPA to estimate radiation risks assume that any radionuclide exposure causes an incremental excess cancer risk. Consequently, in light of the additive effects of the various radionuclides, all of the isotopes listed in Table 3-15 will be included in the baseline risk assessment.

3.3.3.2 Persistence. The environmentally persistent contaminants include hexavalent chromium, copper, mercury, PCBs, and radionuclides. Chromium and copper persist in the environment because they are not subject to chemical decomposition or biodegradation. Mercury may be biotransformed from its elemental state to the more toxic and more mobile methyl mercury.

The environmental persistence of a radionuclide depends in part on its half-life. The half-lives of the radionuclides of interest to the 100-KR-1 operable unit are shown in Table 3-20.

Table 3-20. Half-Lives of Selected Radionuclides of Interest to the 100-KR-1 Operable Unit (Evans and Bryce 1989).

Nuclide	Half-Life (Yrs)
^{3}H	12
^{14}C	5,700
^{60}Co	5
^{63}Ni	92
^{90}Sr	28
^{134}Cs	2
^{137}Cs	33
^{152}Eu	13
^{154}Eu	8
^{155}Eu	5
^{235}U	710,000,000
^{238}U	4,400,000,000
^{238}Pu	90
^{239}Pu	24,000
^{240}Pu	6,600

3.3.3.3 Mobility. The mobility of contaminants is dependent on the chemical form of the element, which is dependent on environmental conditions. Many metals have low mobility because they bind ionically to soils or form insoluble precipitates. However, hexavalent chromium and methyl mercury tend to be quite mobile. The negative ions, such as sulfate and chloride, are also mobile.

Metallic radionuclides such as uranium, plutonium, and cobalt tend to have low mobility. Because of their chemistry, they bond tightly to soils and do not easily move through the soil column. However, if complexing agents are present, these and nonradioactive metals can form complexes that may not be retarded on soils as are the uncomplexed ionic forms. On the other hand, tritium and carbon, partly because of their involvement in the normal chemistry of life, can be highly mobile in the soil and ground water.

9 0 1 1 3 3 0 1 6 4

3.3.3.4 Bioaccumulation. Some contaminants can accumulate in plants and animals if absorbed or consumed by the organisms. Unitless bioconcentration factors for some of the contaminants found in the 100-KR-1 operable unit are given in Table 3-21.

Table 3-21. Unitless Bioconcentration Factors for Selected Contaminants of the 100-KR-1 Operable Unit.

Contaminant	Bioconcentration Factor
Carbon	4,600 to 9,100 (invertebrates, fish)
Cesium	0.3 to 16 (birds, mammals)
Cobalt	0.2 to 2 (birds, mammals)
Copper	200 (fish)
Chromium	16 (fish)
Hydrogen	0.6 to 1 (mammals)
Mercury	5,500 (fish)
Nickel	47 to 100 (invertebrates)
Sodium	100 to 200 (invertebrates, fish)
Strontium	0.2 to 8 (mammals)

3.3.3.5 Contaminants of Concern. The preliminary contaminants of concern identified for the 100-KR-1 operable unit are given in Table 3-15 and are predominantly radionuclides and selected inorganics and chemical parameters. This list is based on the types and quantities of wastes disposed at the unit and the contaminant characteristics. Specific organic contaminants may be added to the preliminary contaminants of concern upon review of the RI Phase I results.

3.3.4 Risk Quantification

Risk quantification is based on known and suspected conditions at the 100-KR-1 operable unit. As discussed in Section 3.3.1.4, humans may be exposed under both current and future use conditions. The extent and magnitude of chemical contamination at the 100-KR-1 operable unit is not currently known; therefore, a quantitative chemical risk assessment is not possible at this time. Further quantification of hazardous substances such as PCBs, mercury, chromium, and copper must be completed during the RI to allow the determination of human risks.

3.4 PRELIMINARY REMEDIAL ACTION OBJECTIVES AND REMEDIAL ACTION ALTERNATIVES

This section develops preliminary remedial action objectives, general response actions, and a list of preliminary remedial action alternatives. The evaluation is based on available site data, the preliminary risk assessment, and the conceptual site model for the 100-KR-1 operable unit. The remedial action objectives may change or be refined as additional data are gathered and evaluated during the RI, and they will be more fully developed and evaluated in the FS when additional and more specific information becomes available from the RI. This preliminary discussion of objectives and alternatives is intended to focus the RI so that the data needed for the FS are obtained.

3.4.1 Remedial Action Objectives

The primary objective of the RI/FS at the 100-KR-1 operable unit is to protect human health and the environment from harmful effects of the contaminants of concern at the site.

In order to focus the RI/FS toward specific goals, the following preliminary remedial action objectives have been identified for the 100-KR-1 operable unit:

- Reduce to acceptable levels the current and potential future release of contaminants from the source areas and the vadose zone to the unconfined aquifer

- Remediate the source areas and soils to levels that achieve ARARs, or to levels that will not present public or human health risks under assumed future use and access

The preliminary list of contaminants of concern listed in Table 3-15, the preliminary contaminant specific ARARs listed in Section 3.2.1, and the baseline risk assessment in Section 5.3.8 will serve as the basis for establishing target levels of remediation for each media.

3.4.2 General Response Action

General response actions represent broad classes of remedial measures that may be appropriate to achieve the remedial action objectives at the 100-KR-1 operable unit. Although general response actions and their associated technologies and process options can only be evaluated in general terms at this stage, their identification is useful in the development of the RI field sampling program. The following are the preliminary general response actions for the 100-KR-1 operable unit:

- No action
- Institutional controls
- Containment
- In situ treatment
- Removal
- Treatment
- Disposal
- Monitoring

A no action alternative will be included for evaluation in the FS as required by the National Contingency Plan [40 CFR 300.68(f)(1)(v)]. A no action alternative also provides a baseline for comparison with other response actions. Finally, a no action alternative may be appropriate for some sources or areas of contamination if the risk assessment determines that unacceptable public health risks are not presented by those sources or areas and that contaminant specific ARARs are not exceeded.

Institutional controls involve the use of physical barriers or access restrictions to reduce or eliminate public exposure to contamination. Considering the nature of the 100-KR-1 operable unit and the Hanford Site as a whole, institutional controls will likely be an integral part of remediation. Many access and use restrictions are already in place at the Hanford Site.

Containment of source areas and contaminated soils by using capping technologies will be considered as a means of minimizing the driving force for

downward migration of contaminants. Capping also provides a radiation exposure barrier and a limited barrier to direct exposure.

Removal of source and contaminated soils will be evaluated as a potential response action. Removed material will either be disposed of or treated.

In situ treatment, such as vitrification or stabilization, will be considered as a means of reducing the mobility and toxicity of contaminants in the source areas and soil.

Both physical and chemical treatment processes will be considered in either in situ conditions or in conjunction with soil removal. Treatment of contaminated source material and soils using the grout facility or vitrification plant (once built and operational) will likely achieve significant reductions in risk and migration potential.

Disposal will be required for any response action that involves removal and treatment. For the onsite treatment facilities, disposal will likely be onsite.

Similar to institutional controls, monitoring is not a stand-alone response action, but will likely be a component of some or all of the remedial alternatives. Monitoring will be necessary for postremediation evaluation of remedial action performance.

3.4.3 Remedial Technologies and Process Options

The next step in developing remedial action alternatives is the identification of remedial technologies and process options associated with each general response action. Figure 3-13 summarizes the technologies and process options available that may be applicable to the 100-KR-1 operable unit based on available data and present knowledge of the site. These technologies and process options will be developed and evaluated in detail as part of the FS.

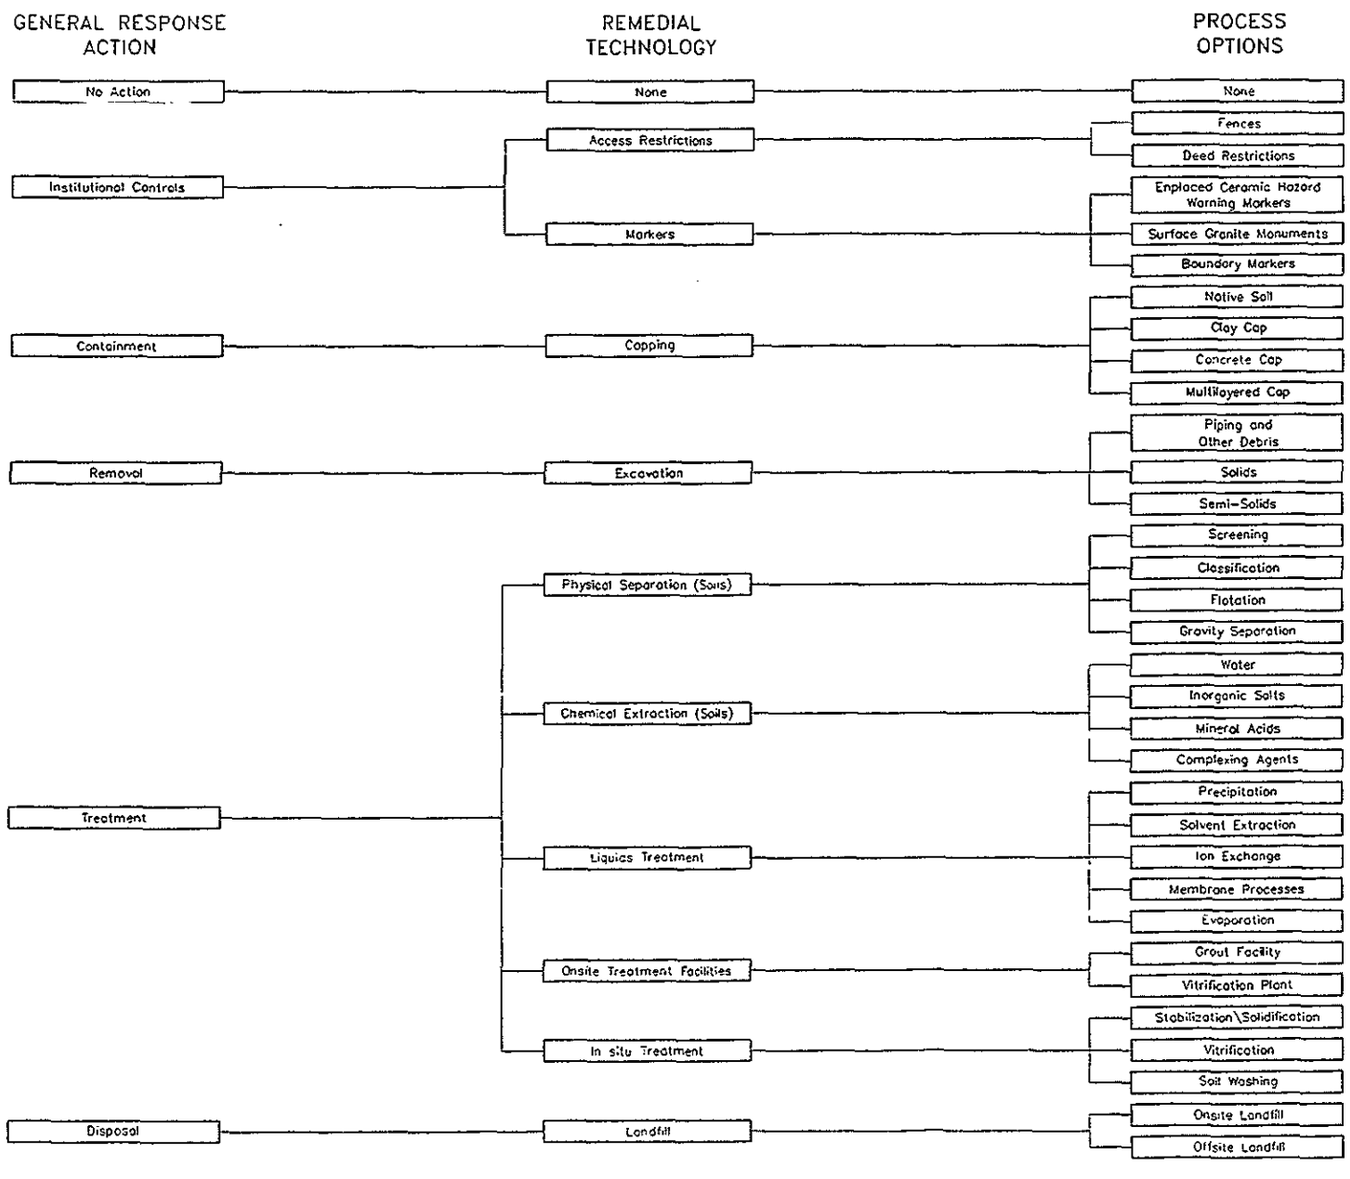

Figure 3-13. General Response Actions, Technologies and Process Options Available.

THIS PAGE INTENTIONALLY
LEFT BLANK

3.4.4 Remedial Action Alternatives

Based on available site data and the preliminary identification of general response actions and remedial technologies, the following preliminary remedial action alternatives have been defined:

- A no action alternative (assumes long-term monitoring with contingency plans if releases or exposures increase).
- An alternative that would rely heavily on institutional controls and access controls, with limited use of containment to reduce the potential for human exposure to the contaminants.
- An alternative emphasizing containment of source areas in conjunction with institutional controls to reduce release rates to the environment and the potential for human exposure to the contaminants.
- An alternative emphasizing selective removal of contaminants and site soils and either onsite or offsite redisposal to reduce rates of release to the environment and the potential for human exposure to the contaminants.
- An alternative using both selective removal with onsite treatment and selective in situ treatment of contaminants and soils to achieve ARARs and risk-based levels for unrestricted site use.
- An alternative emphasizing selective removal and onsite treatment of contaminated soils to achieve ARARs and risk-based levels for unrestricted site use.

The purpose of identifying this range of alternatives is to ensure that the remedial investigation gathers all the data necessary to develop and evaluate the full range of feasible alternatives in the FS.

9 0 1 1 3 3 0 1 7 0

THIS PAGE INTENTIONALLY
LEFT BLANK

4.0 WORK PLAN APPROACH AND RATIONALE

Section 4.0 provides the rationale and framework for conducting the Phase I RI for the 100-KR-1 operable unit. This section identifies and evaluates data needs required to complete the RI Phase I. Data uses and data users, data needs, and the data quality objectives (DQOs) for the sources, vadose, air and terrestrial biota are defined. Sections 4.1 and 4.2 summarize the essential steps in the decision-making process leading to development of the data collection program. Section 4.3 integrates these steps and discusses them in more detail. The methodology for obtaining and evaluating data is outlined to give focus to the RI Phase I and provide a preview of needed tasks.

The DQOs are specific qualitative and quantitative statements designed to ensure that data of known and appropriate quality are obtained during the remedial response process. The DQOs are developed for each data collection activity in the remedial response process (RI, FS, remedial design, remedial action). A three-stage process is used to develop DQOs:

- Stage 1 - Identify decision types
- Stage 2 - Identify data uses and needs
- Stage 3 - Design a data collection program.

For the efficient use of resources, an RI is best approached as an iterative process. After each phase of the RI, existing data will be evaluated to assess any gaps that must be addressed in the next phase of the collection effort; the DQOs will be revised accordingly. As the overall understanding of site conditions improves and the range of potential remedial alternatives is narrowed, data gaps will decrease.

Section 4.1 summarizes Stage 1 of the process used for 100-KR-1 and states the resulting DQO.

4.1 DECISION TYPES

Stage 1 of the DQO process is undertaken to identify the decision makers, the data users, and to define the types of decisions that will be made as part of the RI/FS. The major elements of Stage 1 include:

- Identifying and involving data users
- Evaluating available information
- Developing a conceptual model
- Specifying RI/FS objectives and decisions.

4.1.1 Data Users

Data users can be subdivided into primary and secondary categories. Primary data users are those individuals or organizations directly involved in ongoing RI/FS activities. Primary data users for the 100-KR-1 operable unit include:

- Managers from DOE, Westinghouse Hanford, EPA, and Ecology
- The DOE, EPA, and Ecology unit managers
- Unit manager contractor representatives
- Technical contributors
- Decision makers.

Secondary data users are those individuals or organizations who rely mainly on outputs from the RI/FS studies to support their activities. Secondary data users include the following:

- The DOE headquarters secretary
- The EPA regional administrator
- The Ecology director

- The director of the state Department of Health
- Other federal and state agencies
- The general public
- Special interest groups.

Most data needs are defined by primary data users. Secondary data users may also provide inputs to the decision makers and primary data users by communicating general or site-specific data needs or regulatory requirements, or by comment or question during the review process.

Information obtained during the RI Phase I for the 100-KR-1 operable unit will be managed in accordance with the Data Management Plan found in Attachment 4. Public participation in the RI/FS will be solicited in accordance with the Community Relations Plan found in Attachment 5. Implementation of these two plans will ensure that the data needs of both the primary and secondary data users identified for the site will be met.

4.1.2 Available Information

Available information is reviewed and evaluated as the initial step in the RI/FS process. This review provides the foundation for additional onsite activities and serves as the database for potential scoping studies. Available information for this operable unit was reviewed and evaluated by the project team to determine the adequacy of existing information so that data needs could be identified. Information on the physical setting of the operable unit is summarized in Section 2.0, and the existing data that were evaluated to guide the development of the RI Phase I is presented and summarized in Section 3.0.

4.1.3 Conceptual Models

Conceptual models describe a site and its environment and present hypotheses regarding the contaminants present, their routes of migration, and their potential impacts on sensitive receptors. The hypotheses are tested, refined and modified throughout the RI/FS process. Based upon the data reviewed by the project team, a

conceptual site model was developed for the 100-KR-1 operable unit and is presented in Chapter 3.0.

4.1.4 RI/FS Objectives and Decisions

In a broad sense, the objective of a remedial action program is to determine the nature and extent of release or threat of release of hazardous substances and to select a cost-effective remedial action to minimize or eliminate that threat. Achieving this broad objective requires that several interrelated activities be performed. Each activity must have objectives, acceptable levels of uncertainty, and attendant data quality requirements. The first step toward the development of a cost-effective data collection program is clear, precise decision statements (EPA 1987). The decision framework for developing the data collection program for the RI Phase I can be summarized in the following questions.

- Where are the contaminants located?
- What contaminants are present?
- What are the concentrations of these contaminants in the environment?
- What is the potential for the contaminants to move within the environment?
- What are the risks to people and the environment if these contaminants are not separated from the environment?
- If the risks from the contaminants are unacceptable, then how can the risks be reduced to acceptable levels?
- If the risks can be reduced, what is the most cost-effective way to reduce the risks?

The activities that provide answers to the first four questions are classified as site characterization activities. A baseline risk assessment is performed to determine the risks to people and the environment. The FS determine how risks can be reduced to acceptable levels, and the most cost-effective way to accomplish the task.

Existing data for the 100-KR-1 operable unit (as defined in Section 3.0) are insufficient to answer what contaminants are present, their exact location, and their potential to migrate in the environs. Therefore, RI Phase I activities are proposed in each media at the operable unit to answer these questions with data of appropriate quantity and quality.

Following the completion of RI Phase I data development activities, a baseline risk assessment will be performed to estimate the short-term risks to people and the environment from the contaminants that are found. The risk assessment will become one mechanism for identifying potential interim response actions that may be needed at the 100-K Area. The risk assessment will be revised and updated following Phase II data activities to estimate the long-term risks to people and the environment, and identify any additional short-term risks requiring interim action.

Questions regarding acceptable levels of contaminants and cost-effective methods of reducing risks are answered by the FS. These studies will be performed concurrently with the RI, with alternative identification and preliminary screening beginning early in the process. Alternative selection will take place once the contaminants have been identified and their locations and concentrations established.

4.2 DATA USES AND NEEDS

Stage 2 of the DQO process defines data uses and specifies the types of data needed to meet the project objectives. Although data needs are identified generally during Stage 1, it is during Stage 2 where specific data uses are defined (EPA 1987). The major elements of DQO Stage 2 include:

- Identifying data uses
- Identifying data types
- Identifying data quality/quantity needs
- Evaluating sampling/analysis options
- Reviewing data quality parameters (per Section 4.2.6).

4.2.1 Data Uses

During the RI/FS, most data uses fall into one or more of four general categories: (1) site characterization, (2) public health evaluation and risk assessment, (3) evaluation of remedial action alternatives, and (4) worker health and safety.

Site characterization refers to the determination and evaluation of the physical and chemical properties of the waste and contaminated media present at the site, and an evaluation of the nature and extent of contamination. The site characterization process involves the collection of necessary geologic, hydrologic, and meteorologic data as well as data on specific contaminants and sources.

Data collected to conduct a public health evaluation and risk assessment at the 100-KR-1 operable unit include the following: input parameters for various performance assessment models, site characteristics, and contaminant data required to evaluate the threat to public health and welfare through exposure to the various media. These needs usually overlap with site characterization needs, but higher-level quality control is often needed for risk assessment purposes and ARAR identification.

Data collected to support evaluation of the 100-KR-1 operable unit remedial alternatives include site characteristics and engineering data required for initial screening of alternatives, feasibility-level design, and preliminary cost estimates. Once an alternative is selected for implementation, much of the data collected during the RI/FS can be used for the final engineering design. Generally, collection of information during the RI for use in the final design is not cost effective. It is usually more cost effective to gather such specific information during a predesign investigation.

The worker health and safety category includes data collected to establish the level of protection for workers during various RI activities. These data are used to determine if there is concern for the personnel working in the vicinity of the operable unit.

4.2.2 Data Types

The data use categories described in Section 4.2.1 define the general purpose and intent for collecting additional data. Based upon the intended uses, a concise statement regarding the data types needed can be developed. The data types specified at this stage should not be limited to chemical parameters, but should also include

necessary physical parameters such as bulk density, porosity, etc. Since environmental media and source materials are interrelated, data types used to evaluate one media may also be useful to characterize another media. By identifying data types by media, overlapping data needs are identified. The data objectives, needs, and types to be collected for the RI Phase I are identified in Table 4-1. These are discussed in greater detail in Section 4.3 to provide focus to the RI/FS tasks discussed in Section 5.0 and the Field Sampling Plan (Attachment 1 - Part 1).

4.2.3 Data Quality Needs

The various tasks and phases of a remedial investigation may require different levels of data quality. Important factors in defining data quality include selecting appropriate analytical levels and validation and identifying contaminant levels of concern as described below. The Westinghouse Hanford document *A Proposed Data Quality Strategy for Hanford Site Characterization* will be used to help define these levels (McCain and Johnson 1990).

4.2.3.1 Analytical Levels and Validation. In general, increasing accuracy and precision are obtained with increasing cost and time. Therefore, the analytical level used to obtain data should be commensurate with the intended use. Table 4-2 defines five analytical levels based on overall data quality. The data types for the individual DQOs and the appropriate analytical levels associated with each data type are given in Table 4-3.

Before laboratory and field data can be used in the RI/FS process, it must first be validated. The activities involved in the data validation process include the following.

- Confirm that the laboratory data meet the QA/QC criteria
- Confirm the usability and quality of field data, which include geological logs, hydrologic data, and geophysical surveys
- Make sure data are documented and managed properly so they are usable

Table 4-1. Data Collection Objectives for the 100-KR-1 Operable Unit.

Data objectives	Data needs	Data types
Sources		
Refine understanding of facility characteristics	Locations of contaminant sources	- Site walkover - Topographic mapping - Source data compilation - Geophysical testing
	Integrity of waste containment structures	- Pipeline integrity testing
Determine waste characteristics and spatial distribution of contaminants	Chemical and radiological characterization of the sources	- Chemical and radiological properties - Soil gas survey
Geologic		
Identify pathways for contaminant migration	Stratigraphy, structure	- Lithology - Soil/sediment type
Determine potential migration rates, direction and dispersion of contaminants	Properties of the vadose zone	- Physical properties - Geochemical properties
Surface Water/Sediment		
See 100-KR-4 work plan.		
Vadose		
Determine presence or absence and spatial distribution of contaminants	Contaminant characterization of the soil column	- Chemical properties

Table 4-1. Data Collection Objectives for the 100-KR-1 Operable Unit.

Data objectives	Data needs	Data types
Ground Water		
See 100-KR-4 work plan		
Air		
Determine direction and dispersion of contaminants	Meteorological data	- Wind rose - Climatic information
Determine presence or absence of contaminants	Air quality	- Physical properties - Chemical properties
Terrestrial Biota		
Determine the type of ecosystem present	Identification of critical habitats Identification of ecological processes	- Literature review
Determine presence or absence of contaminants	Contaminant characterization of the biota	- Literature review - Chemical properties
Cultural Resources		
Determine presence or absence of archaeological or historical sites eligible for National Register of Historic Places	Identify archeological or historic sites	- Literature review - Field survey

H:\1842\TABLES\KR1\4\214

TABLE 4-2. Analytical Levels for Collecting Needed Data Types in 100-KR-1.

LEVEL[A]	ANALYSIS TYPE
■ LEVEL I	Field screening. This level is characterized by the use of portable instruments which can provide real-time data to assist in the optimization of sampling point locations and for health and safety support. Data can be generated regarding the presence or absence of certain contaminants (especially volatiles) at sampling locations.
■ LEVEL II	Field analysis. This level is characterized by the use of portable analytical instruments which can be used onsite, or in mobile laboratories stationed near a site (close-support laboratories). Depending on the types of contaminants, sample matrix, and personnel skills, qualitative and quantitative data can be obtained.
■ LEVEL III	Laboratory analysis using methods other than the Contract Laboratory Program Routine Analytical Services. This level is used primarily in support of engineering studies using standard EPA-approved procedures. Some procedures may be equivalent to Contract Laboratory Program Routine Analytical Services without the Contract Laboratory Program requirements for documentation.
■ LEVEL IV	Contract Laboratory Program Routine Analytical Services. This level is characterized by rigorous QA/QC protocols and documentation and provides qualitative and quantitative analytical data. Some regions have obtained similar support via their own regional laboratories, university laboratories, or other commercial laboratories.
■ LEVEL V	Nonstandard methods. Analyses which may require method modification and/or development Contract Laboratory Program Special Analytical Services are considered Level V.

[A] Per McCain and Johnson 1990, Levels I, II and III are equivalent to field or laboratory screening and Levels III, IV and V are equivalent to validated laboratory analyses.

Table 4-3. Data Collection Types, Measurements, and Required Analytical Levels for the 100-KR-1 Operable Unit.

Data types	Measurements	Analytical method	Required analytical level	Data use
Sources				
Site walkover	N/A	N/A	N/A	SC, EA, ED
Data compilation	Literature review	N/A	N/A	SC, EA, ED
Topographic mapping	1-1/2 ft (0.5-m) contours	SOP	I	SC, EA, ED
Subsurface geophysical testing	Ground penetrating radar	SOP	I	SC, EA, ED
	EMI/MAG		I	SC, EA, ED
Pipeline integrity testing	Helium concentration	SOP	I	SC, EA, ED
Chemical and radiological properties	Surface radiation survey	SOP	I/II	SC, WS
	Soil gas survey	SOP	I	SC
	Radionuclides analysis	SOP/LAP	V	SC, EA, ED, RA, WS
	Organics analysis	CLP	IV	SC, EA, ED, RA, WS
	Inorganics analysis	CLP	IV	SC, EA, ED, RA, WS
Geologic				
Lithology	Geologic log	SOP	I	SC, EA, ED
Soil/sediment type	Soil/sediment classification	SOP	I	SC, EA, ED
Physical properties	Porosity	ASTM	III	SC, EA, ED
	Bulk density	ASTM	III	SC, EA, ED
	Particle size distribution	ASTM	III	SC, EA, ED
	Moisture content	ASTM	III	SC, EA, ED
	Permeability	ASTM	III	SC, EA, ED
Geochemical properties	Cation exchange capacity	MOSA	III	SC, EA, ED
	Total organic carbon	MOSA	III	SC, EA, ED
	pH	SOP	III	SC, EA, ED
Surface Water/Sediment				
See 100-KR-4 work plan				

Table 4-3. Data Collection Types, Measurements, and Required Analytical Levels for the 100-KR-1 Operable Unit.

Data types	Measurements	Analytical method	Required analytical level	Data use
Vadose				
Chemical properties	Radionuclides	SOP/LAP	III/V	SC, EA, ED, RA
	Organics	SLM/CLP	III/IV	SC, EA, ED, RA, AA, WS
	Inorganics	SLM/CLP	III/IV	SC, EA, ED, RA, AA, WS
	Herbicides/pesticides	SLM/CLP	III/IV	SC, EA, ED, RA, AA, WS
	PCBs	SLM/CLP	III/IV	SC, EA, ED, RA, AA, WS
Ground Water				
See 100-KR-4 work plan				
Air				
Wind rose	Wind velocity and direction	SOP	I	SC, EA, ED
Climatic information	Precipitation (annual and monthly)	SOP	I	SC, EA, ED
	Temperature (annual and monthly)	SOP	I	SC, EA, ED
	Evaporation rate	SOP	I	SC, EA, ED
	Barometric pressure	SOP	I	SC, EA, ED
	Relative humidity	SOP	I	SC, EA, ED
Physical properties	Total suspended particulates	SOP	III	SC, EA, ED, AA
	PM-10	SOP	III	SC, EA, ED, AA
Chemical properties	Inorganics	SLM/CLP	III	SC, EA, ED, RA, AA
	Radionuclides	SOP/LAP	V	SC, EA, ED, RA, AA
Terrestrial Biota				
Literature review	Terrestrial vegetation & wildlife present	N/A	I	SC, EA, ED, AA
	Biota uptake of radionuclides and inorganics	N/A	I	SC, EA, ED, AA
	Presence of critical habitats	N/A	I	AA

Table 4-3. Data Collection Types, Measurements, and Required Analytical Levels for the 100-KR-1 Operable Unit.

Data types	Measurements	Analytical method	Required analytical level	Data use
Cultural Resources				
Literature search	Location of surficial archeological sites	N/A	N/A	AA
	Presence of historic or archeological sites that may be eligible for the National Register of Historic Places	N/A	N/A	AA

SOP = Standard operating procedures
CLP = Contract laboratory program
LAP = Laboratory analytical protocol
N/A = Not applicable
ASTM = American Society of Testing and Materials
SC = Site characterization
EA = Evaluation of alternatives
ED = Engineering design
RA = Risk assessment
WS = Worker safety
AA = Address ARARS
MOSA = Methods of Soil Analysis
SW846= EPA 1986b
EMI = Electromagnetic induction
MAG = Magnetometer
PM-10= Particulate monitoring (less than 10 minutes)
SLM = Standard laboratory methods

To address the first objective, all laboratory data must meet the requirements of the specific QA/QC parameters as set up in the QAPP (Part 2 of Attachment 1) before they can be considered usable. The QA/QC parameters include laboratory precision and accuracy, method blanks, field blanks, instrument calibration, and holding times.

The usability of field data must also be assessed by a trained and qualified person. The project hydrologist will review the geologic logs, hydrologic data, and geophysical surveys on a daily basis, and senior technical reviews will be conducted periodically throughout the project.

Consistent data management procedures are also necessary for validated data. Data management includes proper field activities, sample management and tracking, and document control and inventory. Specific procedures are discussed in the Data Management Plan (Attachment 4).

4.2.3.2 Contaminant Levels of Concern. In order to identify appropriate data needs, both contaminant levels of concern and action-specific requirements must be identified. This is accomplished by identifying preliminary ARARs. Because of the iterative nature of the RI/FS process, ARARs identification continues throughout the RI/FS as a better understanding is gained of site conditions, site contaminants, and remedial action alternatives.

There are three categories of ARARs. Chemical-specific ARARs define acceptable exposure levels and are used to establish preliminary remedial action objectives. Action-specific ARARs are requirements governing the implementation of remedial actions at the site. Location-specific ARARs are requirements which set restrictions on activities conducted within specific locations, such as areas identified as having historical or archeological significance. The preliminary federal and state ARARs identified for the 100-KR-1 operable unit are discussed in Section 3.2.

During RI/FS planning, an identification of chemical-specific and location-specific ARARs is made in order to develop cleanup objectives and focus data collection. Chemical-specific ARARs are expressed as numerical values and are either derived from specific standards (i.e., maximum contaminant levels [MCLs] as specified in the Safe Drinking Water Act) or are health-based (i.e. levels of contaminants which pose an excess lifetime cancer risk of 1×10^{-4} to 10^{-6}). By identifying these standards now, appropriate analytical methods and detection limits can be selected for the contaminants of concern. Analytical methods chosen will need to have a detection limit below the identified level of concern. The analytical methods

proposed in Table 4-3 were selected based upon the chemical-specific requirements identified in the preliminary ARARs analysis.

The location-specific ARARs that must be considered prior to implementation of any field activities were discussed in Section 3.2.3. The existence and potential value of any archeological resources or critical habitats need to be determined before any field investigation activities are undertaken. In order to ensure that any archaeological resources are not impacted during the RI/FS process, various Indian tribes will be afforded the opportunity to review and comment on the work plan prior to sampling.

4.2.4 Data Quantity Needs

The number of samples that need to be collected during an RI/FS can be determined by using several approaches. In instances where data are lacking or are limited, a phased sampling approach may be useful. In the absence of available data, an approach or rationale will need to be developed to justify the sampling locations selected and the number of samples collected. In situations where data are available, statistical techniques may be useful in determining the number of additional data required.

4.2.5 Sampling and Analyses Options

The resources available for performing a remedial investigation need to be evaluated during RI/FS planning. Data collection activities can then be structured to obtain the needed data in a cost-effective manner. Developing a sampling and analysis approach which ensures that appropriate levels of data quality and quantity are obtained with the resources available may be accomplished by using a phased RI approach and field screening techniques.

The RI/FS for the 100-KR-1 operable unit will take advantage of both approaches. Studies conducted either prior to or in conjunction with the RI Phase I activities, followed by a more detailed RI Phase II, will provide for a comprehensive characterization of the site in a cost-effective manner. Field screening techniques will also be used to guide and focus data collection. For example, geophysical testing will identify the locations of underground structures that may need to be investigated during RI Phase I.

Another important aspect of planning the data collection program is determining the quantity of high level analytical data required to support RI/FS objectives. In order to obtain needed data in a cost-effective manner, and still support RI/FS objectives, a combination of lower level analytical data (Levels I, II, and III) and higher level analytical data (Levels IV and V) will be collected. For instance, the samples collected from the sources will be analyzed by CLP procedures to provide litigation quality data. This will provide the certainty necessary to determine the contaminants present in the source material. Samples collected from the remaining media (i.e., soils, ground water, surface water, sediments) will be analyzed by both SW 846 and CLP procedures. Approximately 80% of the samples collected will be Level III; 20% will be Levels IV and IV. All data will be validated to qualify the accuracy and usefulness of the results regardless of the analytical method used (EPA 1986b).

4.2.6 PARCC Parameters

The precision, accuracy, representativeness, completeness, and comparability (PARCC) parameters are indicators of data quality. Ideally, the end use of the data collected should define the necessary PARCC parameters. Once the PARCC requirements have been identified, then appropriate analytical methods can be chosen to meet established goals and requirements. A complete discussion of the PARCC requirements for the RI Phase I are in the quality assurance project plan.

4.3 DATA COLLECTION PROGRAM

Conducting an RI in phases is a common method for optimizing the quantity and quality of the data collected. It would be very inefficient and overly expensive to specify beforehand all the types of samples and analyses that will yield the most complete and accurate understanding of the contamination and physical behavior of the site. Data adequate to achieve RI/FS goals and objectives are obtained at a lower cost by using the information obtained in each step to focus the investigation in succeeding steps. Phased remedial investigations are encouraged by EPA's current RI/FS guidance document (EPA 1988a).

The first phase of the RI Phase I of the 100-KR-1 work plan will complete the gathering and analysis of existing information and collect new data believed necessary to confirm and refine the conceptual model. Subsequent phases may be needed to further reduce uncertainty, to fill in remaining gaps in the data, collect more detailed

information for certain points where such information is required, and to conduct any needed treatability studies. The need for subsequent investigation phases will be assessed early in the RI Phase I investigation and as data become available.

4.3.1 General Rationale

The central rationale for undertaking an RI of the operable unit is to develop needed data that is lacking in the available information. The amount of information that has been assembled and evaluated to date is considerable. Because of the size of the operable unit, the complexity of past operations, and the number of waste management units, the amount of information that ultimately will be acquired is much greater than what is already available.

The following general rationale and corresponding technical work plan approach or strategy will be used to collect additional data for the 100-KR-1 operable unit investigation:

- Existing data will be used to the maximum extent possible. Although existing data may not be validated to current standards, the data are still useful in developing the site model and helping to focus and guide the investigations.

- Additional data will be collected to obtain the maximum amount of useful information for the amount of time and resources invested in the investigation.

- Data will be collected, as needed, to support the intended data uses identified in Section 4.2.1.

- Nonintrusive sampling (e.g. geophysical testing, surficial soil and source sampling, sampling of existing ground water monitoring wells) will be conducted early in the RI Phase I, or in a separate pre-RI process to identify necessary interim response actions. The information obtained from an early study will be evaluated and used to revise the scope of the RI Phase I, if necessary.

- Phase I data will be collected to confirm and refine the conceptual model, refine the analyte list for any subsequent investigations, and provide the information to conduct a short-term risk assessment. If the

short-term risk assessment indicates a potential risk at the site greater than 1×10^{-4} (1 in 10,000 chances of developing cancer) interim response actions will be taken.

- The RI Phase II for the 100-KR-1 and 100-KR-4 operable units will support the long-term risk assessment for final cleanup actions. If the long-term risk assessment indicates a potential risk greater than 1×10^{-5} to 1×10^{-6}, remedial action alternatives will be developed and evaluated to address these risks.

- The investigations for the 100-KR-1 and 100-KR-4 operable units will be coordinated to reduce overall costs and maximize the usefulness of the data obtained.

- Field investigation techniques will be used to minimize the amount of hazardous waste generated. However, any waste generated will be barreled in accordance with EII 4.2 "Interim Control of Unknown Suspected Hazardous and Mixed Waste" (WHC 1989c).

4.3.2 General Strategy

As stated earlier, the objective of the RI/FS is to gather additional information sufficient to support an RI/FS. The general approaches or strategies for obtaining the additional information are presented.

The following strategies will be used to collect additional data for the 100-KR-1 operable unit:

- The locations and types of sources that exist in the 100-KR-1 operable unit will be identified and evaluated as a possible contributor to ground water contamination.

- A phased approach will be used to identify the nature and extent of source and soils contamination. This will include surficial surveys followed by soil sampling at depth.

- Terrestrial biota investigations and air investigations are included in the 100-KR-1 operable unit work plan to gain an understanding of contaminant movement in these media.

The following strategies also will be used to provide additional data for the 100-KR-1 operable unit by coordinating the 100-KR-1 and 100-KR-4 operable units and using data from the 100-KR-2 and 3 operable units:

- The 100-KR-4 operable unit ground water investigation will be coordinated with the 100-KR-1 operable unit investigation. By designing the two investigations in an integrated manner, the costs of the information obtained will be reduced, and the value of the information will be increased. For example, by locating deeper boreholes and wells needed for the ground water investigation in areas adjacent to the disposal units, where near-surface samples are needed for the source investigation, the overall costs of the drilling and sampling will be reduced.

- All similar field work for the 100-KR-4 and the 100-KR-1 operable units will, to the maximum extent possible, be conducted at the same time. These and other means will be used to reduce costs or improve the value of the information obtained by coordinating the two investigations.

- All proposed ground water investigations will be conducted as part of the 100-KR-4 operable unit work plan. Ground water information relevant to the 100-KR-1 operable unit will be included in the 100-KR-1 operable unit Phase I RI report.

- The locations and types of sources that exist in the 100-KR-2 and 100-KR-3 operable units will also be identified and evaluated as a possible contributor to ground water contamination. Discussions concerning the sources in the 100-KR-2 and 100-KR-3 operable units will be included in the 100-KR-4 work plan. Impacts to 100-KR-1 from the other two source operable units will be evaluated following 100-KR-4 data generation.

- Soils and vadose zone investigations outside of the 100-KR-1 operable unit boundary will be conducted as part of the 100-KR-4 operable unit work plan and will be integrated with the equivalent data generated within the 100-KR-1 boundary.

- The aquatic biota, riverbank seeps and springs, and sediment investigations adjacent to the 100-KR-1 operable unit will be included in the 100-KR-4 operable unit work plan. Resulting information will be

evaluated to further define contaminant migration patterns from the 100-KR-1 operable unit.

4.3.3 Investigation Methodologies

The initial phase of the RI will include the following integrated tasks:

- Source investigations
- Geologic investigations
- Vadose investigations
- Surface water and sediment investigations
- Ground water investigations
- Air investigation
- Ecological investigation
- Other investigations (cultural, topography)

4.3.3.1 Source Investigations. A substantial amount of information already exists on the locations and types of sources present in the 100-K Area. However, additional data are necessary to fully characterize known sources and identify any unknown sources of potential contamination. Numerous subtasks will be conducted in a phased approach to focus the source investigation for the 100-KR-1 operable units.

Data compilation and review will provide any additional information on known or suspected sources of contamination in the 100-K Area. Available historical documents including aerial photographs, engineering plans, effluent discharge reports, and environmental release reports will be gathered and reviewed to provide additional information on waste generated and disposal, storage, and handling facilities.

Topographic base map development will be done as part of the 100-KR-4 RI or generated as part of a Hanford Site-wide effort. The base map will be used to locate all known sources and facilities and will be revised and updated if additional sources or facilities are identified. The base map will be created from a combination of aerial

photographs and ground-surveying key points and monuments, and will show elevational contours at 1.5-ft (0.5-m) intervals.

Seven field activities designed to evaluate and quantify conditions at the 100-KR-1 operable unit are discussed below.

1. A walkover of the 100-K Area will be conducted to verify the base map, identify and locate any additional contaminant sources, and provide for a better understanding of the overall site conditions. The area walkover will be coordinated with the walkover for the 100-KR-4 operable unit to avoid duplication of effort. The base map plots resulting from the area walkover for the 100-KR-1 operable unit will be focusing on the sources of contamination.

2. A surface radiation survey will be conducted to determine surface radiation levels throughout the 100-KR-1 operable unit. A map of surface radiation levels will be developed. The information obtained will help determine the level of personnel protection necessary for onsite investigations, and will help identify areas requiring further investigation.

3. A soil gas survey may be done to characterize anomalous areas identified during the site walkover. There is no current evidence to suggest that volatile organic compounds were stored, handled, or disposed of within the 100-KR-1 operable unit. This option will remain open if needed.

4. An electromagnetic induction (EMI) or magnetometer (MAG) survey of the site will locate buried facilities and screen large areas for potential disturbances, which may be related to buried contamination.

5. A ground-penetrating radar (GPR) survey may be conducted as part of the field activities subtask to identify subsurface sources not detected with the EMI/MAG surveys and to provide a better understanding of the dimensions of source units when historical information is lacking. The GPR surveys will be conducted on facilities such as cribs and trenches where no metallic objects have been disposed of, and where EMI/MAG surveys yielded inconclusive results. The GPR survey will be conducted after evaluating the results of the EMI/MAG surveys.

6. The integrity of process effluent pipelines and cooling water discharge pipelines will be assessed. The assessment will be conducted by

charging isolated pipeline sections with helium gas, then using helium detectors to locate possible leaks, or by other techniques such as remote video surveys.

7. The information obtained from the first six field activities will help to focus the waste unit source sampling. Several investigations of the retention basins, cribs, trench, and outfall structures have provided information concerning the concentrations of radionuclides present. However, very little information, if any, exists concerning the concentrations of various organic and inorganic contaminants present in the sources.

As indicated in Table 4-1, the objectives of the source investigation are to determine the radiological and chemical characteristics of the sources, the concentrations of contaminants present, and their spatial distribution. In order to achieve these objectives, a combination of surficial and vadose zone boring samples will be collected. Although the borings will provide an indication of the vertical and horizontal extent of contamination, the actual volume of the sources will be defined in the RI Phase II. A sufficient number of samples will be collected to provide an overall understanding of the sources; the locations selected for sampling will be partially based on the information obtained from the first six field activities, and the number of samples collected during the initial stages of the RI will be based on best professional judgment.

The data collected during the RI Phase I will be used to better define site characteristics, aid in the development of the risk assessment and remedial action alternatives, and will provide necessary information to ensure worker protection during subsequent RI/FS activities.

4.3.3.2 Geologic Investigations. Sufficient data are currently available on the regional geology and geologic structure of the Hanford Site. Therefore, the RI Phase I for 100-KR-1 will concentrate on obtaining specific geologic data on the vadose zone characteristics and properties.

As shown in Tables 4-1 and 4-2, information on a variety of physical parameters will be collected to determine the potential contaminant release mechanisms of the vadose zone. Information on the vadose zone geology will be obtained from samples collected during the vadose investigation as part of 100-KR-1 work and from borings drilled during the ground water investigation in the 100-KR-4 operable unit.

Any additional data available on the regional and site-specific geology will be compiled and evaluated. Geologic mapping will be conducted as part of the 100-KR-4 RI. These data will be useful in focusing subsequent soils and ground water investigations.

The information obtained during the RI Phase I will be used to better define site characteristics, aid in the development of the risk assessment and remedial action alternatives, and eventually, remedial design.

4.3.3.3 Surface Water and Sediment Investigations. The surface water and sediment investigations are discussed in the 100-KR-4 work plan.

4.3.3.4 Vadose Investigations. As indicated in Table 4-1, the objective of the vadose investigation is to determine the presence or absence and spatial distribution of contaminants in the surficial soils and vadose zone as a result of waste handling and disposal practices in the 100-KR-1 operable unit. The vadose investigation will focus on determining the general configuration of contamination related to each source or group of sources, its depth, areal extent, concentration, and potential to migrate to the surface or to the water table. Background soils data will not be collected during the RI Phase I for the 100-KR-1 operable unit since a site-wide data collection effort is being planned.

A sufficient number of samples will be collected to provide an overall understanding of site conditions. Biased sampling will be conducted to ensure needed information on known or suspected sources is obtained. Best professional judgment will be used to identify sampling locations and numbers of samples to be collected.

A substantial amount of sampling and analysis has been performed on the soils within the 100-KR-1 operable unit to determine the concentrations of radionuclides present. As is the case with the sources, insufficient information is available for determining the presence or absence of various organic and inorganic contaminants in the soils. Due to the extensive application of herbicides, potential use of pesticides, and the existence of transformers and electrical switching equipment, soil samples collected will need to be analyzed for herbicides, pesticides, and PCBs.

The data collected during the RI Phase I will be used to better define site characteristics, aid in the development of the risk assessment and remedial action alternatives, and, eventually, remedial design.

4.3.3.5 Ground Water Investigation. The ground water investigation is discussed in the 100-KR-4 work plan. The information obtained from the 100-KR-4 RI will be utilized to better define site characteristics and assist in developing remedial action alternatives for the 100-KR-1 RI.

4.3.3.6 Air Investigation. Several monitoring stations within the 100 Areas have been collecting bimonthly, monthly, and quarterly data on concentrations of airborne radionuclides. The RI Phase I sampling will not only include the collection of radiological constituents, but also the collection of nonradioactive particulates and meteorological data. Information collected will help to better define site conditions and aid in the development of the risk assessment. Based on the results of the assessment, a determination will be made if more site-specific air quality data need to be collected for the RI Phase II.

Because RI crews may be exposed to airborne contaminants, field screening will be performed at worksites. Monitoring for volatile organics will be performed with the use of field instruments. The information obtained from the field screening will help to maintain worker health and safety during RI/FS activities.

4.3.3.7 Terrestrial Biota (Ecological) Investigation. Substantial information on terrestrial biota has been collected at the Hanford Site. To better focus the RI Phase I and avoid collection of unnecessary data, a literature search will first be conducted to obtain an initial description of the ecosystem. A field survey to verify the description will also be performed. Based upon this data search and field survey, a conceptual model of the significant species and ecological processes will be constructed.

The terrestrial biota investigations at the various operable units will be coordinated and integrated to the maximum extent possible. It is expected that the biota investigations for the 100-HR-1, 100-BC-1, and 100-DR-1 operable units will provide useful data for the 100-KR-1 operable unit. The terrestrial biota investigation for 100-KR-1 will fine-tune the current understanding of site conditions. The information obtained will refine the understanding of site characteristics and aid in the development of the risk assessment.

4.3.3.8 Other Investigations. Two other investigations will be performed during the Ri for the 100-KR-1 operable unit, the cultural resource investigation and the topography investigation.

The cultural resource investigation will involve verifying the locations of known archaeological sites in the 100-K Area by reviewing data and conducting a field

survey. The focus of the investigation will be to determine whether archaeological resources are present at proposed drilling sites.

A topographic base map will be developed which will serve as a reference base for all of the RI investigations.

4.3.4 Data Evaluation and Decision Making

During the RI Phase I, data will be evaluated as soon as they become available, for use in restructuring and focusing the RI/FS, as appropriate. Data reports will be developed that summarize and interpret the collected data. The data can then be used to refine the 100-KR-1 operable unit conceptual model, further assess potential contaminant-specific ARARs, develop the baseline risk assessment, begin development of the FS, and complete the RI report.

The objectives of data evaluation are to:

- Reduce and integrate the data so that data gaps can be identified and the goals and objectives can be met for the various RI/FS objectives
- Confirm that the data are representative of the media sampled and that QA/QC criteria have been met. Data will be validated in accordance with *A Proposed Data Quality Strategy for Hanford Site Characterization* (McCain and Johnson 1990).

The decisions to be made on completion of the 100-KR-1 RI Phase I will be primarily to identify the need for additional data collection. Figures 4-1 and 4-2 illustrate the decision-making process that will be used during the RI Phase I for sources, soils, surface water and sediments, ground water, air, and biota.

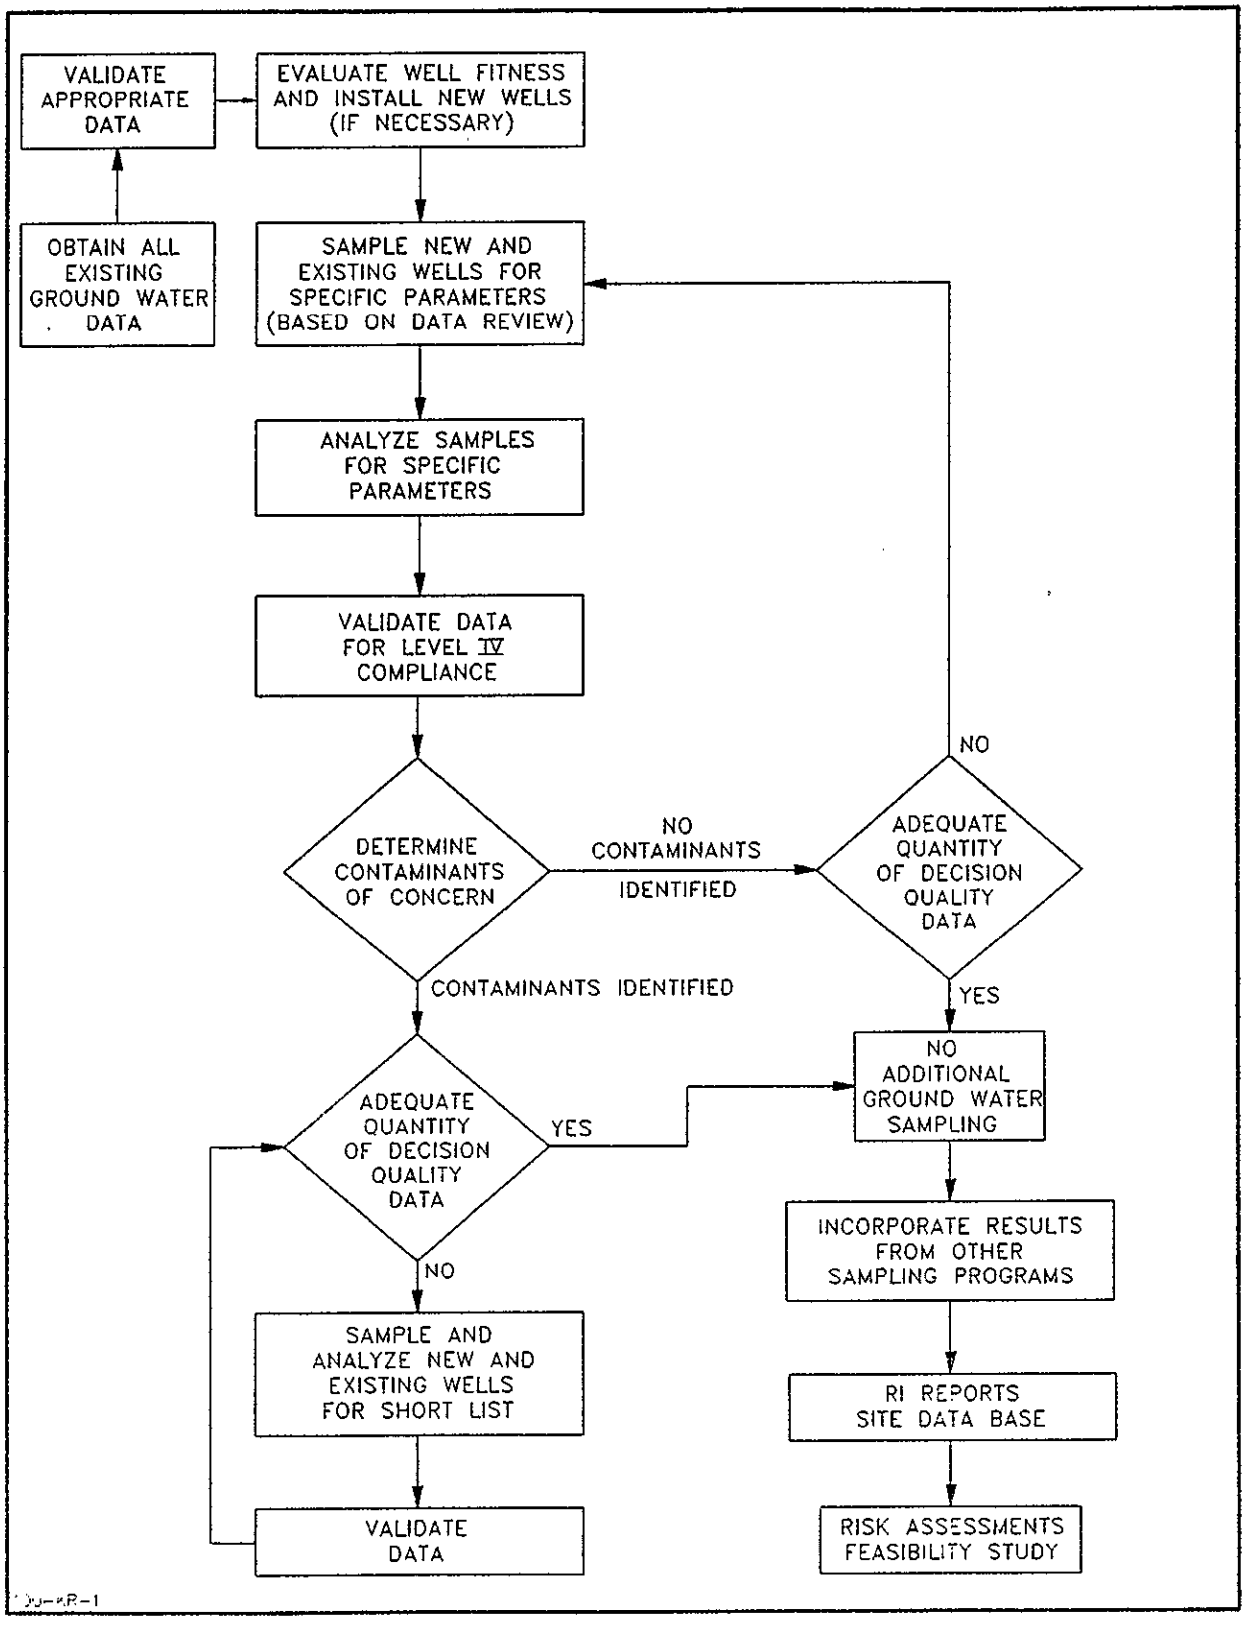

Figure 4-1. Decision Tree For RI/FS Ground Water Sampling.

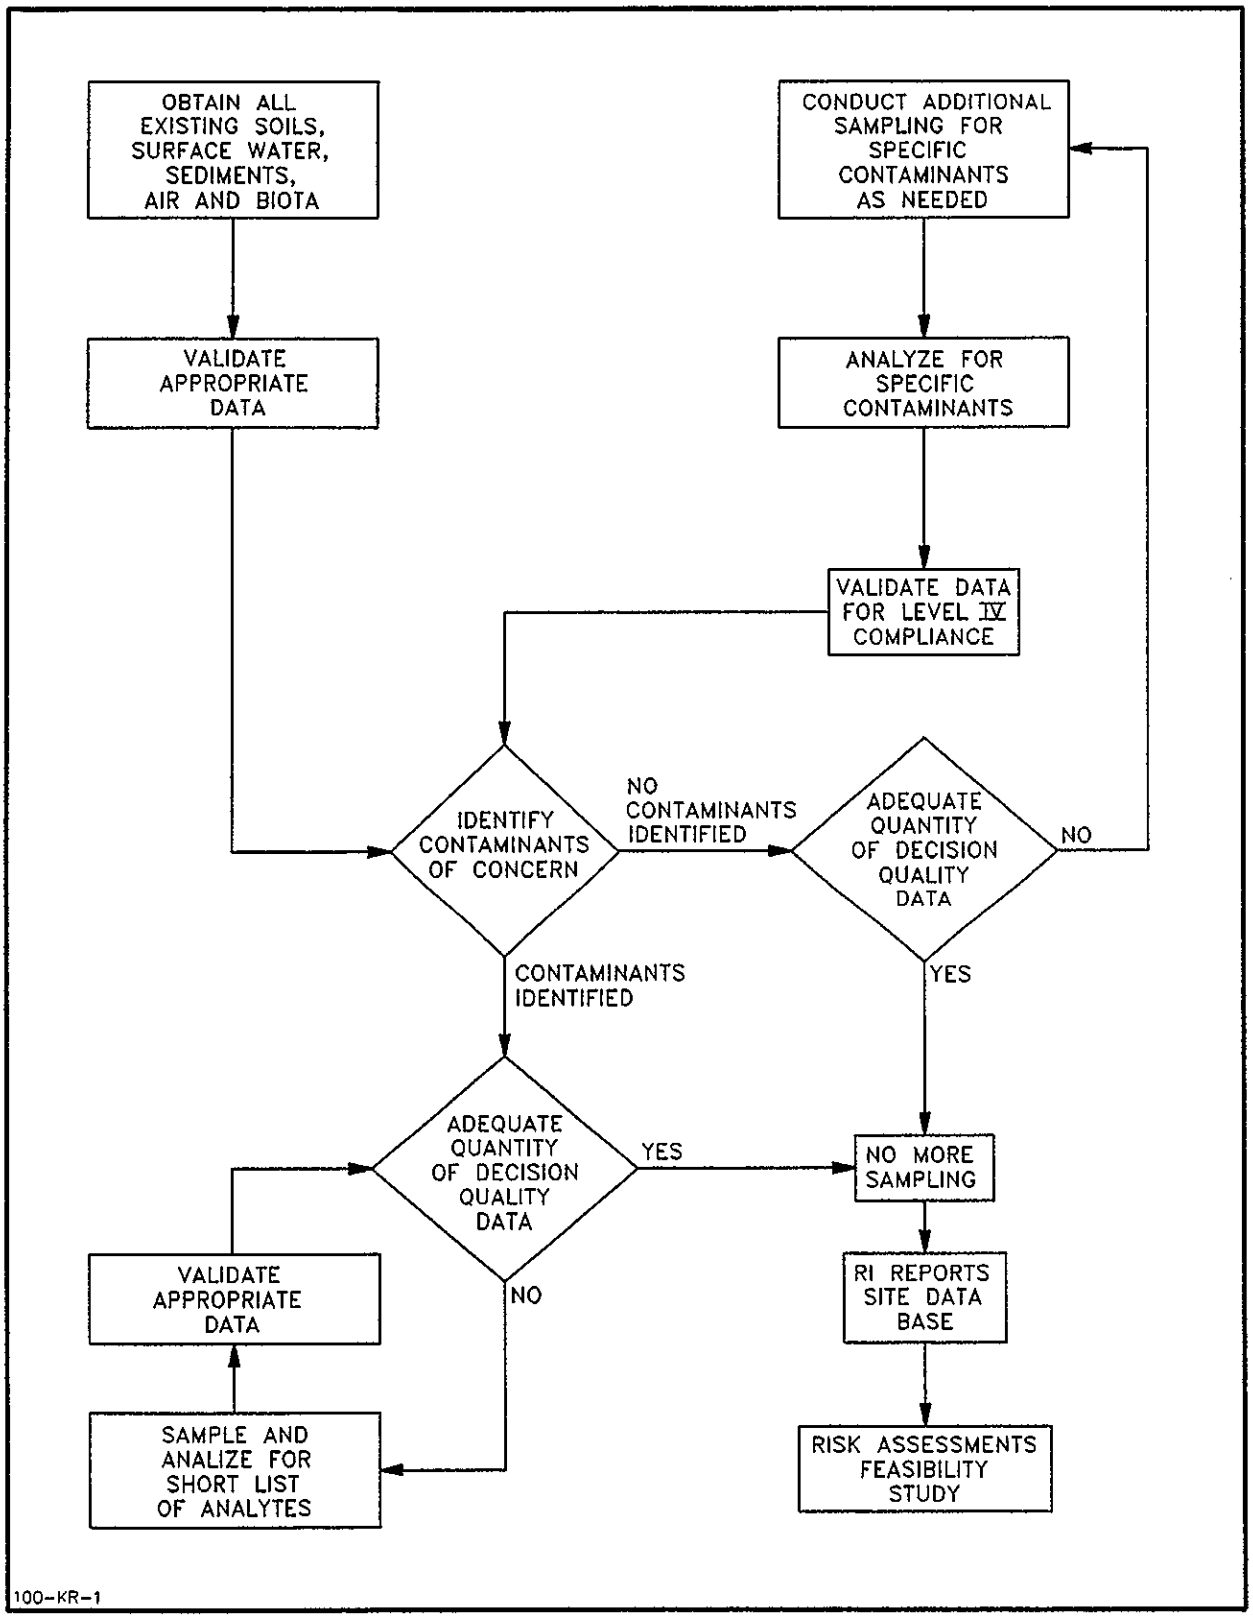

Figure 4-2. Decision Making Tree for RI/FS Soil, Surface Water, Sediment, Air, and Biota Sampling.

9011130197

THIS PA[illegible]ONALLY
LEFT BLANK

5.0 REMEDIAL INVESTIGATION/FEASIBILITY STUDY TASKS

This chapter describes the various tasks to be implemented during the course of the RI/FS process. The specified tasks are designed to provide information to meet the DQOs identified in Chapter 4.0. The following sections are included:

5.1 Project Management

5.2 Operable Unit Characterization

5.3 Feasibility Study Phase I/II - Remedial Alternatives Development

5.4 Remedial Investigation Phase II - Treatability Investigation

5.5 Feasibility Study Phase III - Detailed Analysis of Remedial Alternatives.

Detailed information on field sampling is presented in the Sampling and Analysis Plan (Attachment 1). Environmental monitoring requirements for ensuring the health and safety of onsite investigators are described in the Health and Safety Plan (Attachment 2). The Project Management Plan (Attachment 3) describes the organizational structure, responsibilities, and procedures for the overall management of the RI/FS.

It may be necessary to update this section during the course of the project as the operable unit conditions become better characterized. Depending on the results of certain tasks, other tasks may need to be created, supplemented, or deleted. As such, this portion of the work plan and the associated attachments are meant to function as a living document. Revisions will be made and distributed, as appropriate.

Preliminary Phase I RI studies may be conducted during the review period of this work plan. The primary focus of these studies will be to identify problem areas posing immediate and on-going risk of impacting human health or the environment. The secondary goal of these studies will be to supplement existing data and potentially reduce the level of effort necessary for specific investigation in the RI Phase I.

5.1 PROJECT MANAGEMENT

The objectives of project management during the performance of the 100-KR-1 RI/FS are to direct and document project activities so that the data and evaluations generated meet the goals and objectives of the work plan, and the project is kept within budget and schedule. The initial project management activity will be to assign individuals to roles established in the Project Management Plan. Specific activities that will occur throughout the RI/FS include:

- General Management
- Meetings
- Cost and Schedule Control
- Data Management
- Progress Reports.

5.1.1 General Management

General management includes the day-to-day supervision of, and communication with, project staff and subcontractors. Throughout the project, daily communications between office and field personnel will be maintained, along with periodic communications with subcontractors. This constant and continual exchange of information is necessary to assess the progress of the 100-KR-1 operable unit project and to identify potential problems quickly enough to make necessary corrections to keep the project focused on its objectives, on schedule, and within budget.

5.1.2 Meetings

Meetings will be held, as necessary, with members of the project staff, subcontractors, regulatory agencies, and other appropriate entities to communicate information, assess project status, and resolve problems.

A kickoff meeting will be held with appropriate project personnel, and project staff meetings will be held weekly. The 100-KR-1 operable unit project coordinators

for this and other operable units will meet on a weekly basis to share information and to discuss progress and problems. The frequency of other meetings will be determined based on need and on schedules published in the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989).

5.1.3 Cost and Schedule Control

Project costs, including labor, other direct costs, and subcontractor expenses, will be tracked monthly. The budget for tracking activities will be computerized and will provide the basis for invoice preparation and review and for preparation of progress reports.

Scheduled milestones will be tracked monthly for each task of each phase of the project. This will be done in conjunction with cost tracking.

5.1.4 Data Management

The project file for the 100-KR-1 operable unit will be kept organized, secured, and accessible to appropriate project personnel. All field reports, field logs, health and safety documents, QA/QC documents, laboratory data, memorandums, correspondence, and reports will be logged into the file upon receipt or transmittal. This system is also the mechanism for ensuring that data management procedures documented in the Data Management Plan (Attachment 4) are carried out appropriately.

5.1.5 Progress Reports

Quarterly progress reports will be prepared, distributed to appropriate personnel and entities (project and unit managers, coordinators, contractors, subcontractors, etc.), and entered into the 100-KR-1 operable unit project file. The reports will summarize the work completed, present data generated, and provide evaluations of the data as they become available. Progress, anticipated problems and recommended solutions, upcoming activities, key personnel changes, status of deliverables, and budget and schedule information will be included.

5.2 OPERABLE UNIT CHARACTERIZATION

As described in Chapter 4.0, the characterization of sources of contamination within 100-KR-1 operable unit will be directed toward obtaining data necessary to support site characterization, the feasibility study, risk assessment, ARAR compliance issues, and health and safety plan development. This work plan addresses currently identified source units. The operable unit source list will be expanded and additional source units will be added to the investigation as they are discovered.

To satisfy the data needs and DQOs specified in Chapter 4.0, the following tasks will be performed during the first phase of the RI:

- Task 1 - Project Management
- Task 2 - Source Investigations
- Task 3 - Geologic Investigations
- Task 4 - Surface Water and Sediment Investigations
- Task 5 - Vadose Zone Investigations
- Task 6 - Ground Water Investigations
- Task 7 - Air Investigations
- Task 8 - Ecological Investigations
- Task 9 - Cultural Resources Investigations
- Task 10 - Data Evaluation
- Task 11 - Baseline Risk Assessment
- Task 12 - RI Phase I Report: Preliminary Operable Unit Characterization Summary.

These tasks and their component subtasks and activities are outlined in the following sections. Tasks will be performed in subtask phases so that data from earlier tasks, such as historical data reviews and walkover surveys, can be used to

focus subsequent tasks. Details regarding specific sampling objectives, locations, and frequencies are provided in more detail in the FSP included as Attachment 1, Part 1. Field and laboratory analytical procedures are referenced in the QAPP included in Attachment 1, Part 2.

The data collected from the various subtasks will be provided to the operable unit manager for the 100-KR-4 operable unit. This information will also be used to focus Phase I ground water investigations on specific sources. Following the Phase I ground water investigation, the need for an interim corrective action will be determined. Subsequent source and operable unit characterization tasks may be modified based on findings from the Phase I ground water investigations and the data needs for any specific interim response action.

The lists of analyses for various sampling tasks will be evaluated following Task 2 and will be reduced, if possible, to a list of indicator species and compounds.

The ground water underlying the 100-KR-1 operable unit as well as the Columbia River sediments and surface water will be evaluated under the 100-KR-4 operable unit remedial investigation.

The general nature of contamination has the following forms:

- Surface and very-near-surface contamination resulting from spills, surface tank leaks, breaching of the crib and trench, and settlement of contaminated particular matter

- Near-surface contamination resulting from liquid disposal into the cribs, trenches, and from pipeline leaks

- Deep vadose zone contamination resulting from the infiltration of contaminated water and/or chemicals downward into the vadose zone from surface disposal, leaks, or breaches

- Ground water contamination resulting from infiltration of contaminated liquids or leaching of previously contaminated soil.

The primary sources of contamination at or near the surface must be investigated early in the characterization effort. Tasks 2 (source investigations) and 5 (vadose zone investigations) are aimed at accomplishing this by initiating sampling and

analysis work, increasing the present understanding of where the majority of contaminants are, and establishing controls over all subsequent characterization work.

Once the general location and characteristics of the contamination have been established, the extent to which contaminants may have migrated will be defined. In addition, data on general soil properties such as grain size, permeability, clay content, density adsorption/desorption characteristics, and other properties affecting contaminant transport are needed. Task 5 is aimed at both determining the distribution and nature of these deeper contaminants and at collecting basic physical and chemical soil data, and other data, which will allow for an understanding of current contaminant distribution and the potential for future migration.

5.2.1 Task 1 - Project Management

This task is necessary to meet the goals and objectives of the RI/FS and is discussed in Section 5.1 and Attachment 3, the Project Management Plan (PMP).

5.2.2 Task 2 - Source Investigation

The available information on the operation of site facilities within the 100-KR-1 operable unit is relatively complete. The location of some underground portions (e.g., pipelines) of the facilities and inventory of these sites will have to be determined and/or verified.

Site historical information generally provides good detail of facility structures and locations at the 100-KR-1 operable unit, however, the location of some facilities and engineered discharge points will need to be determined more precisely. Previous investigations provided information on some radionuclide concentrations (Dorian and Richards 1978); however, further characterization of radionuclides and other hazardous substances must be performed to understand contaminant distribution and concentrations. The source investigation will include performing the following subtasks:

- Source data compilation and review
- Topographic base map development

- Field activities
  - Site walkover survey
  - Soil gas survey
  - Surface radiation survey
  - Electromagnetic induction/magnetometer survey
  - Ground penetrating radar survey
  - Effluent pipelines integrity assessment
  - Waste unit source sampling
- Laboratory analysis and data validation
- Data evaluation.

Certain RI field studies may be conducted during the review of this work plan. The purpose of these investigations will be to identify high risk problems possibly requiring interim response actions and to supplement data deficiencies.

5.2.2.1 Subtask 2a - Data Compilation and Review. This subtask is intended to verify and evaluate the information presented in Chapters 2.0 and 3.0 of this work plan and to locate any additional waste units or contaminants information not reported herein. Additional research may provide data about source units or potential source areas in order to better focus all subsequent investigative tasks and subtasks. This subtask will consist of gathering, reviewing, evaluating, and compiling additional existing historical information on 100-KR-1 waste disposal, storage and handling practices and facilities.

Available historical documents including aerial photographs, engineering plans, effluent discharge reports, and environmental release reports will be reviewed. This task will also include interviews with individuals having personal knowledge of past activities at the 100-KR-1 operable unit site. Additional information to be gained about several units includes the exact location and construction specifications of facilities, period of operations, function or use, and inventory of radiological or hazardous material handled or disposed. Additional or confirmation information is

needed on all units described in Section 3.1. If additional information is unavailable, locations of facilities will be determined through the area walkover survey. This, combined with the geophysical methods, will determine the nature and extent of contamination by the investigations described in Subtask 2c and Subtask 5b.

Other sources of information, both historical and present day, that will be evaluated for their potential usefulness as part of the remedial investigation process include: high resolution photography, aerial gamma radiation surveys, color and false infrared photography, thermal and spectral analyses, and other multispectral remote sensing image analysis techniques as available.

5.2.2.2 Subtask 2b - Topographic Base Map Development. A topographic base map will be prepared to show the project site. Facilities and waste unit sources will be included, corrected, and supplemented as appropriate, based on an inspection of aerial photographs and field surveys of the 100-K Area. The base map will be developed as part of the planned activities in the 100-KR-4 work plan. A Hanford Site-wide base map is currently under development and will be used if available. Contour intervals will be at 1.5 ft (0.5 m) and at a 1:2,000 scale.

5.2.2.3 Subtask 2c - Field Activities. Field activities for the 100-KR-1 remedial investigation involve the following activities.

5.2.2.3.1 Site Walkover Survey. The objective of this survey is to visually identify unknown potential contaminant sources, locate areas of disturbed and/or unnatural appearance and to verify known sources with more precision.

The 100-KR-1 operable unit will be walked by a technical team and employees of Westinghouse Hanford who have a working knowledge of the 100-K Area operations and the RI tasks. Types of information gathered will include areas of disturbance and stressed vegetation, and the presence or location of monuments, old foundations, pipelines, fill and indigenous fauna. Soil types and surface geology will also be recorded and site features, such as power lines, that may induce background noise levels for the EMI/MAG survey will also be noted. Results of all surveys will be located on the base map to facilitate the correlation of diverse information.

In order to more precisely locate these and other survey information, a grid will be surveyed and staked at 100 ft (33 m) intervals across the 100-KR-1 operable unit. A more closely spaced grid system will be employed, as necessary, in areas of particular interest. The walkover will be extended outside the operable unit boundary

if it is determined that previously unidentified waste sources are present near the operable unit.

5.2.2.3.2 Surface Radiation Survey. The objective of this task is to develop a map of surface radiation levels throughout the entire 100-KR-1 operable unit. This information is needed for two purposes. First, it will be used to determine the level of personal radiation protection necessary for onsite investigations. Second, it will be used to identify areas of surface and, potentially, subsurface radioactive contamination that will require further study.

Surface radiation will be measured by using portable, laboratory-quality alpha detectors and sodium-iodide beta/gamma detectors that read in counts per minute. Radiation detection equipment will be either a manual (hand-held) system or a computer-based integrated system using vehicle-mounted or backpack-mounted detectors. The survey will help to identify any currently unknown area of surface radiation contamination. The collection of Hanford Site background soil quality data will be used to determine background surface radiation levels for comparative purposes.

If a manual radiation detection system is used, the continuous reading survey will be conducted on approximately 25 ft (8 m) spacings in all areas where no source units are known or suspected. The traverse spacing will be less than 25 ft (8 m), as necessary, if anomalous areas are noted during the survey. As a potentially cost-effective alternative to conducting the surface radiation survey entirely with portable (i.e., hand-held) radiation detectors, an integrated vehicle-mounted and backpack-mounted computer-based radiation mapping system will be evaluated. Such systems currently exist, and by the time the 100-KR-1 operable unit RI is initiated, it is expected that updated versions of these systems will be available.

An automated system that includes an onboard computer and auto-location capabilities can provide the following advantages over a manual radiation detection system.

- It provides greater coverage per unit of time. Existing vehicle-mounted units can survey an 8 ft (2 m) swath at speeds of 1 mi/h (1.6 km/h).

- It provides more detailed coverage. Vehicle-mounted detectors are spaced at approximately 2 to 3 ft (0.6 to 0.9 m) centers.

- It allows for real-time mapping of survey data. With auto-location capabilities, the survey data are displayed as a site map on a computer screen in the detection vehicle and digitized data are stored in the on-board computer.

- A constant counting geometry is maintained. All survey data are automatically entered into the computer data base; no manual entries are required.

- Having all survey data in a computer data base system provides great flexibility for studying and analyzing data.

- Computer-controlled marking of anomalies on the ground surface during the survey is possible.

Areas showing radiation above accepted background levels will be staked and flagged for more detailed investigation. Results of the radiation survey will be plotted on the base map. The survey will be performed within the 100-KR-1 operable unit and coordinated with surface radiation surveys performed as part of the ground water well siting done for the 100-KR-4 RI.

5.2.2.3.3 Soil Gas Survey. The objective of this survey is to determine if soils contain volatile organic constituents. Since there is no reason to suspect that volatile organic compounds were part of the 100-KR-1 waste inventory, soil vapor surveys will only be conducted over anomalous surface areas identified during the site walkover survey or if new information indicates a need for such a survey.

5.2.2.3.4 Electromagnetic Induction/Magnetometer Survey (EMI/MAG). The objectives of this task are to precisely locate buried facilities such as pipelines or other metallic objects. Screening surveys using EMI and MAG are cost-effective methods of reducing and refining areas for further investigation. Areas identified as potentially contaminated will be marked for further analysis in the Task 5 vadose investigation. The EMI/MAG surveys to be performed within the 100-KR-1 boundaries as part of the ground water wells siting process will be coordinated with the 100-KR-4 RI. Duplicate surveys will not be performed.

MAG surveys detect ferro-nickel metallic objects buried beneath the surface (such as steel pipelines), and will be used in conjunction with EMI surveys to further define buried objects, such as pipelines.

The EMI survey measures the electrical conductivity of subsurface materials. Variations in conductivity may be caused by changes in soil moisture content, the presence of ionic species, or the presence of metallic objects. The EMI survey will be used to screen large areas for possible contamination and to locate buried facilities. For example, areas heavily contaminated by ionic species may register anomalies on an EMI survey, but will not show up on a MAG survey.

An EMI/MAG survey will be conducted over the entire area of the 100-KR-1 operable unit with the exception of the area including and north of the 116-K-2 trench. The surveys will be conducted along approximately 25 ft (8 m) traverse lines over the operable unit. Anomalies will be marked in the field by staking the locations of occurrence. Initially, a MAG survey will be conducted to define locations of the buried pipelines. The site walkover survey will be conducted prior to the EMI survey and identify potential background noise contributors at each facility.

The facility (e.g., pipelines) boundaries as defined by the surveys will be staked and subsequently plotted on the base map. The results will be shown on a base map for each facility with data scale suitable to define dimensions of the facility. The name of the facility, and type of anomaly and its coordinates will be marked on the stakes. EMI/MAG procedures are described in the FSP.

5.2.2.3.5 Ground Penetrating Radar Survey. The objectives of this task are to identify below-ground sources not detectable, or detected but not definable with the EMI/MAG survey. Ground penetrating radar (GPR) is an effective tool for detecting subsurface irregularities such as buried objects, and soil disturbances, such as areas of loose fill. GPR is dependent on material contrasts. The technique yields good results to depths of about 15 ft (5 m), GPR surveys will be conducted on facilities, not expected to produce anomalies with the EMI/MAG survey, such as in the vicinity of cribs and trenches, where no metallic objects have been disposed of, and in areas where the EMI/MAG surveys yielded inconclusive results. The GPR survey will be conducted after evaluation and plotting of the EMI/MAG anomalies. It is expected that the GPR survey will be conducted along transects established to determine the location of the following facilities:

- Cribs and trenches where location data from historical records from Task 2a are deemed insufficient

- Buried cement or ceramic pipelines where location data from historical records are deemed insufficient in Task 2a, and where EMI/MAG surveys are expected to be ineffective.

Details on GPR survey equipment and procedures will be specified in a Westinghouse Hanford EII to be developed in accordance with EII 1.2 "Preparation and Revision of Environmental Investigation Instructions" (WHC 1989a). Continuous strip chart recording equipment will be used to generate profiles of the GPR survey. Digital signal processing equipment may be used to enhance data interpretation. A geophysicist experienced in the interpretation of GPR data will analyze the profiles to determine locations and depths of anomalies and facility boundaries. This information will be incorporated onto the base map showing locations of features identified during the survey.

Information obtained from the GPR survey will be used to identify locations for additional investigations.

5.2.2.3.6 Effluent Pipelines Integrity Assessment. The objective of this activity is to locate and analyze the severity of cracks in process effluent pipelines and above-ground portions of cooling water discharge pipelines. This investigation will identify point source leaks previously unidentified and establish source pathways. Areas that may have leaked large volumes of fluids may require specific remedial actions.

Based on reviews of existing site plans, process drawings, and EMI/MAG survey results, pipeline sections of concern will be isolated and charged with helium gas. Helium gas detectors will be used to locate major leaks and breach sites will be identified for sampling. The information gained will be used to determine additional sample locations discussed in Section 5.2.2.3.7 and Section 5.2.5, Vadose Investigation. Assuming the helium gas pipeline assessment proves to be an effective method, the entire length and interior circumference of all process effluent pipelines will be inspected for cracks or holes, where practical. The discharge pipelines will be inspected from the retention basins to the bank of the Columbia River where the outfall structures are located. Stakes marked with the name of the pipeline will be placed at the ground surface to indicate the position of the potential leak site. Locations of all large pipeline breach sites will be identified for near surface soil sampling which is conducted in Task 5 - Vadose Investigation.

Because of the large dimensions of effluent pipelines (66 to 84 inches in diameter [162 to 213 cm]) charging the pipes with helium gas may prove to be impractical. An assessment of this leak detection technique will be undertaken prior to the performance of the activity. If this assessment concludes that the technique is not feasible, an alternate method of detecting potential leak points will be undertaken (e.g., remote video survey).

5.2.2.3.7 Waste Unit Source Sampling. The objective of this task is to collect and analyze samples from the waste unit sources to determine the chemical and radiological characteristics, extent, and concentrations of the contamination. Previous radiological data will also be verified in this task. Information gained will be used in determining remedial actions in the FS and the health risks in the risk assessment. The source investigations objectives will be accomplished by collecting soil and sludge samples from waste unit sources using various methods including borings and surficial samples. Sampling and analysis will be conducted in stages; each stage will be directed by the results of the preceding stage. Additional borings may be subsequently conducted as part of Task 5 if deemed necessary to better define horizontal and/or vertical extent of contamination. A biased sampling approach is utilized in determining sample locations.

The use of test pits has been discounted as a viable option to the characterization effort at 100-KR-1 because of the waste disposal issue, potential fugitive dust problems, lack of need for bulk samples, presence of fill material, and worker safety concerns. The following is a listing of known and potential waste sources:

- 116-KE-4 and 116-KW-3 retention basins
- 116-K-1 effluent crib
- 116-K-2 effluent trench
- 116-K-3 outfall structure
- Effluent discharge pipelines and valves.

The known waste unit sources are all associated with the cooling water effluent discharges that contain radioactive species and possible chemical contamination. Section 2.1.4.1 contains a description of the cooling water cycle.

The proposed sample borehole locations are shown on Figure 5-1, and the sample designations, sampling intervals, laboratory analyses, and sampling rationale are listed in Table 5-1. The specific analytical parameters are defined in Table 5-2.

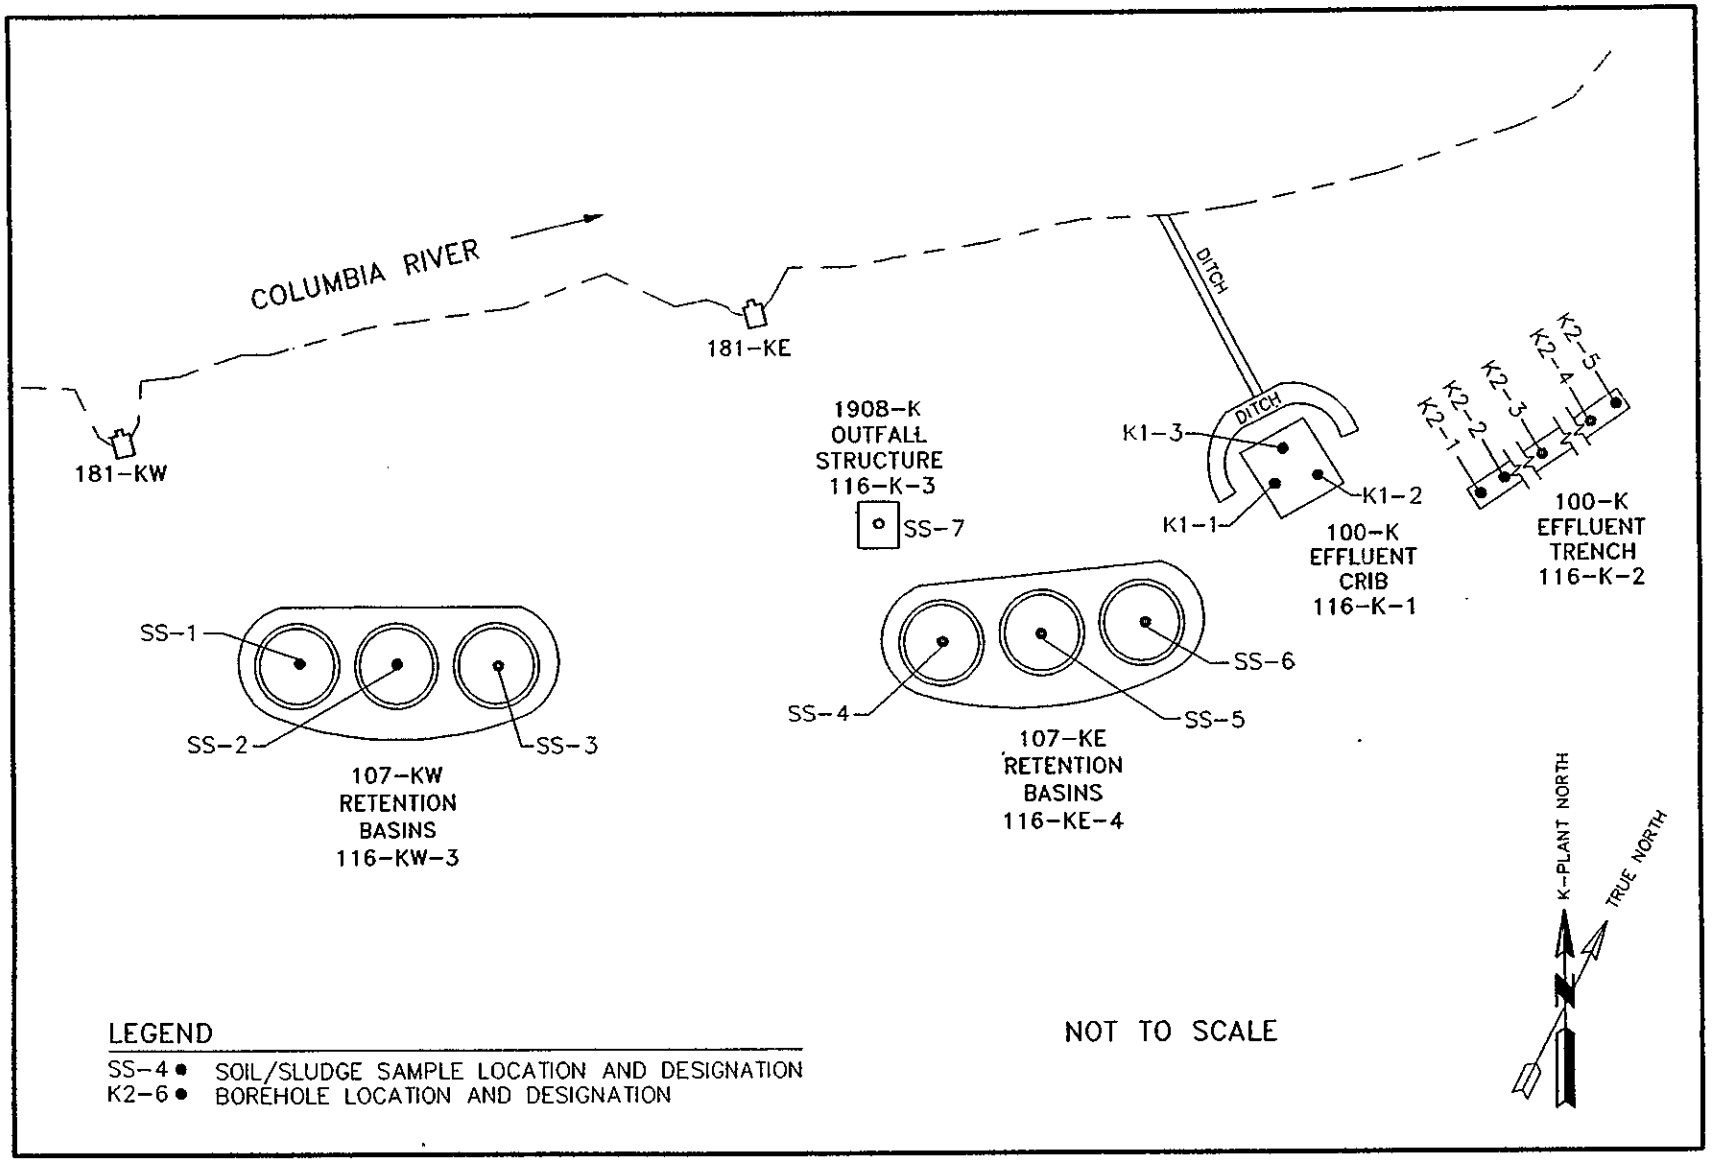

Figure 5-1. Proposed Sampling Locations For 100-KR-1 Source Investigations.

Table 5-1 Proposed Samples for the 100-KR-1 Source Investigations.

Page - 1

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list	Short chemical analyses list	Physical analyses[a]	Sampling Rationale
SS-1	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-2	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-3	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-4	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-5	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-6	Surface to sludge	X[c]			Source characterization
	Sludge interval	X[c]			
SS-7	Sludge layer	X[c]			Source characterization
K1-1	2-ft intervals (surface to 20 ft)	X[d]		X	Source and vadose characterization
	5-ft intervals (20ft to GW1)		X		
K1-2	2-ft intervals (surface to 20 ft)	X[d]		X	Source and vadose characterization
	5-ft intervals (20ft to GW1)		X		
K1-3	2-ft intervals (surface to 20 ft)	X[d]		X	Source and vadose characterization
	5-ft intervals (20ft to GW1)		X		

Table 5-1 Proposed Samples for the 100-KR-1 Source Investigations.

Page - 2

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list	Short chemical analyses list	Physical analyses[e]	Sampling Rationale
K2-1	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-2	5-ft interval (surface to 20 ft)		X	X	Source and vadose characteriztion
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-3	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-4	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
K2-5	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	

[a] Sample locations shown on Figure 5-1
[b] Analyses listed in Table 5-2
[c] Level IV and V analyses
[d] Level IV and V analyses on two sample intervals, level III on remaining intervals
[e] Physical parameters will be analyzes for in each distinct lithologic unit if field screening methods do not detect contamination
GW1 - Ground water estimated at 80 ft

Table 5-2. 100-KR-1 Operable Unit Chemical and Physical Analyses.

Physical Parameters

Moisture
Permeability
Cation exchange
Capacity
pH
Soil classification
Consolidation
Grain-size distribution
including percent clay

Long List of Chemical Analysis

General chemical parameters

Ammonia-N
Carbonate
Chloride
Fluoride
Nitrate
Phosphate
Sulfate
Sulfamate
Oxalate

Radionuclides

Americium-241
Carbon-14
Cobalt-60
Europium-152
Europium-154
Europium-155
Gamma scan
Gross alpha
Gross beta
Iodine-129
Nickel-63
Plutonium
Strontium-90
Technetium-99
Tritium
Uranium

Metals

Aluminum
Antimony
Arsenic
Barium
Beryllium
Cadmium
Chromium,
hexavalent
Chromium (total)
Cobalt
Copper
Cyanide
Iron
Lead
Magnesium
Manganese
Mercury
Nickel
Potassium
Selenium
Silver
Sodium
Thallium
Vanadium
Zinc

Herbicides, Pesticides & PCBs

2,4,5 TP silvex
2,4-D
Alpha-BHC
Beta-BHC
Delta-BHC
Gamma-BHC (Lindane)
Heptachlor
Aldrin
Heptachlor epoxide
Endosulfan I
Dieldrin
4,4'-DDE
Endrin
Endosulfan II
4,4'-DDD
Endosulfan sulfate
4,4'-DDT
Methoxychlor
Endrin ketone
Alpha-Chlordane
Gamma-Chlordane
Toxaphene
Aroclor-1016
Aroclor-1221
Aroclor-1232
Aroclor-1242
Aroclor-1248
Aroclor-1254
Aroclor-1260

Volatile organic compounds

Chloromethane
Bromomethane
Vinyl chloride
Chloroethane
Methylene chloride
Acetone
Carbon disulfide
1,1-Dichloroethene
1,1-Dichloroethane
1,2-Dichloroethene(total)
Chloroform
1,2-Dichloroethane
2-Butanone
1,1,1-Trichloromethane
Carbon tetrachloride
Vinyl acetate
Bromodichloromethane
1,2-Dichloropropane
cis-1,3-Dichloropropane
Trichloroethene
Dibromochloromethane
1,1,2-Trichloromethane
Benzene
trans-1,3-Dichloropropane
Bromoform
4-Methyl-2-pentanone
2-Hexanone
Tetrachloroethane
Toluene
1,1,2,2-Tetrachloroethane

Table 5-2. 100-KR-1 Operable Unit Chemical and Physical Analyses.

Chlorobenzene
Ethyl benzene
Styrene
Xylenes (total)

Semi-volatile organic compounds

Acenaphthene
2,4-Dinitrophenol
4-Nitrophenol
Dibenzofuran
2,4-Dinitrotoluene
2,6-Dinitrotoluene
Diethylphthalate
4-Chlorophenyl-phenylether
Fluorene
4-Nitroaniline
4,6-Dinitro-2-Methylphenol
N-Nitrosodiphenylamine
4-Bromophenyl-phenylether
Hexachlorobenzene
Pentachlorophenol
Phenanthrene
Anthracene
Di-N-Butylphthalate
Fluoranthene
Pyrene
Butylbenzylphthalate
3,3'-Dichlorobenzidine
Benzo (a) Anthracene
bis (2-Ethylhexyl) Phthalate
Chrysene
Di-N-Octyl Phthalate
Benzo (b) Fluoranthene
Benzo (k) Fluoranthene
Benzo (a) Pyrene
Indeno (i,2,3-cd) Pyrene
Dibenz (a,h) Anthracene
Benzo (g,h,i) Perylene
Phenol
bis (-2-Chloroethyl) Ether
2-Chlorophenol
1,3-Dichlorobenzene
1,4-Dichlorobenzene
Benzyl Alcohol
1,2-Dichlorobenzene
2-Methylphenol
bis (2-chloroisopropyl) Ether
4-Methylphenol
N-Nitroso-Di-Propylamine
Hexachloroethane
Nitrobenzene
Isophorone
2-Nitrophenol
2,4-Dimethylphenol
Benzoic Acid
bis (-2-Chloroethoxy) Methane
2,4-Dichlorophenol
1,2,4-Trichlorobenzene
Naphthalene
4-Chloroaniline
Hexachlorobutadiene
4-Chloro-3-Methylphenol
2-Methylnaphthalene
Hexachlorocyclopentadiene
2,4,6-Trichlorophenol
2,4,5-Trichlorophenol
2-Chloronaphthalene
2-Nitroaniline
Dimethyl Phthalate
Acenaphthylene
3-Nitroaniline

Short List of Chemical Analyses

Radionuclides

Gross alpha
Gross beta

Inorganics

Arsenic
Chromium
Copper
Mercury
Pottassium
Zinc

General Chemicals

Ammonia
Flouride
Chloride
Nitrate
Sulfate
Sulfamate
Oxalate

Organics

Herbicides
Pesticides
PCBs
Total Organic Carbon
Total Organic Halogens

5.2.2.3.7.1 116-KE-4 and 116-KW-3 Retention Basins. The retention basins contain very limited amounts of sludge from the effluent cooling water. Any remaining sludge has been covered with approximately 2 ft (0.6 m) of soil. The soil was placed there as an interim deactivation measure in 1971.

Characterization will be performed by sampling the sludge (if possible) and the soil. Because of the limited amount of sludge, one small test hole will be hand-dug within each of the six retention basins so enough sludge surface area will be exposed to collect a sample. The test holes (SS-1, 2, 3, 4, 5, and 6) will also allow for direct observation of condition as they exist. The primary purpose of this sampling effort is to define the chemical parameters of the sludge to help refine the list of contaminants of concern when testing the soils of the vadose zone.

5.2.2.3.7.2 116-K-1 Effluent Crib. The effluent crib was designed to contain cooling water effluent in the event of a fuel cladding failure. Three soil borings (K1-1, 2 and 3) will be drilled within the effluent crib, and soil samples will be collected at 2 ft (0.6 m) intervals from ground surface down to 20 ft (6 m) and at 5 ft (1.5 m) intervals from 20 ft (6 m) to ground water. The mean river level will be used as the depth to ground water (approximately 80 ft [24 m]) in order to account for seasonal variation. Soil borings will be used instead of test pits because the depth to the original surface of the crib bottom is poorly known. Reports on depth of fill within the crib conflict, varying from as little as 3 ft (1 m) to as much as 25 ft (8 m). It is believed that the crib was used on one occasion, so the contaminant inventory is expected to be relatively small. To prevent cross contamination of ground water by vadose zone contaminants, borings will not penetrate the water table (or capillary fringe) if significant levels of contamination are detected above this zone using field screening techniques.

As part of the evaluation of analytical results, the distribution of contaminants beneath the facility will be plotted and compared. If the distribution of contaminants shows a predictable pattern (e.g., evenly distributed, contained at or near surface, or located within distinct subsurface horizons), no further sampling will be undertaken during this phase. However, if no pattern of contaminant distribution can be shown to exist, a statistical based sampling effort will be initiated. The subsequent sampling effort will be performed to define lateral and vertical extent of contaminant distribution with the vertical projection of the facility boundaries.

5.2.2.3.7.3 116-K-2 Effluent Trench. The effluent trench was excavated in 1955 following failure of the effluent crib and was designed to receive cooling water effluent in the event of a fuel cladding failure. Five soil borings (K2-1, 2, 3, 4 and 5)

will be drilled within the effluent trench, and soil samples will be collected. The five borings will be approximately evenly spaced (i.e., 1,300 ft [400 m] apart) from the influent end. Three of the five soil borings (K2-1, 2 and 3) will be drilled from the surface of the ditch down to ground water. Since the approximate depth of the original ditch was 20 ft (6 m), sampling intervals will be 5 ft (1.5 m) to 20 ft (6 m), 2 ft (0.6 m) intervals from 20 ft (6 m) to 40 ft (12 m), and 5 ft (1.5 m) intervals to ground water. The three deeper holes will be located closest to the head of the trench. The remaining two soil borings (K2-4 and 5) will be sampled from 0 to 40 ft (12 m) at the same intervals described above.

As with the effluent crib sampling, a more rigorous sampling effort will be conducted on the trench to better define contaminant distribution if analyses show contaminants to be distributed unpredictably.

5.2.2.3.7.4 116-K-3 Outfall Structure. The outfall structure consists of a concrete building, which received effluent from the six retention basins and discharged effluent to the Columbia River via pipes, and a surface overflow structure. The outfall structure will be assessed for signs of visible contamination during the site walkover survey. If there is existing sludge in the outfall structure, then one composite sludge sample (SS-7) will be collected. Since this facility is still in use, an evaluation of the NPDES discharge permit requirements will be done. Samples collected will be submitted for broad spectrum analysis in order to characterize potential contaminants which may not typically be found elsewhere in the operable unit.

5.2.2.3.7.5 Effluent Discharge Pipelines and Valves. The outfall structure received effluent from the 107-KW retention basins via a 72-in. (183 cm) steel pipe and from the 107-KE retention basins via a 66-in. (168 cm) steel pipe. Two 84-in. (213 cm) pipes conveyed the effluent from the outfall structure to the center of the river. Not all piping and valves have currently been identified. Exact locations of these underground facilities will be determined based on geophysical survey results, or pipeline integrity testing results. Characterization will be performed by sampling and analyzing sludge within selected portions of the effluent pipes and valve pits.

Methods for accessing the pipeline interiors and collecting samples will be evaluated as part of this subtask. Sampling locations will include junction boxes as well as the interior of the pipes. The number of samples will be determined based on review of the survey data and the length of each pipeline. Knowledge of the presence and extent of contamination is needed to evaluate potential remedial actions for the pipelines, as well as the risk associated with leaving the lines in place.

5.2.2.3.7.6 Drilling and Sampling Procedures. Sampling equipment and procedures are described in Attachment 1, Part 1, the Field Sampling Plan and are based on procedures developed by Westinghouse Hanford.

Currently, the most effective method of drilling through the very coarse gravels encountered at the 100-K Area is cable tool. However, this does not preclude the use of another more efficient method at the time of initiation of RI activities. For purposes of drilling at the 100-K Area drive casing will be telescoped through the vadose zone. Due to the high permeability of the vadose zone sediments, grouted boreholes are not expected to act as conduits to ground water. Distinct low-permeability hydrostratigraphic units and contaminated zones will be cased off and sealed before drilling proceeds.

5.2.2.3.7.7 Borehole Logging. The principal purpose of the logging program is to provide a record of the geology and other vadose characteristics encountered in the boreholes. Both geologic and geophysical logging will be conducted during the drilling and sampling activities.

Geologic logging will be conducted on each well by a qualified site geologist. The geologic log will contain a description of the borehole lithology and observations of occurrences of perched water, moisture, lithologic changes, sample intervals as well as other pertinent observations. Detailed geologic logging will not be performed on samples with an indication of radioactive or chemical contamination as determined by field screening techniques.

Each borehole will be geophysically logged during the drilling and sampling process. Geophysical logs will include gamma-gamma, neutron, epithermal neutron, and high resolution spectral gamma. Borehole geophysical logging is helpful for the correlation of sedimentary facies by measuring physical properties such as porosity, density, and water content. High-resolution spectral gamma logging permits the identification of gamma-emitting radionuclides and should help identify strata that have trapped specific species of radionuclides.

5.2.2.3.7.8 Drill Cuttings Disposal. Soil cuttings containing low-level and mixed radioactive waste and hazardous waste will be contained and disposed of according to Westinghouse Hanford procedures.

5.2.2.3.7.9 Borehole Abandonment. All boreholes will be properly abandoned, following approved Ecology and EPA procedures. All steel casings will be removed and transferred to an appropriate controlled decontamination facility and

each boring will be pressure grouted from the bottom up, using a portland cement/bentonite slurry. Washington State Regulation WAC 173-160 requires that all boreholes not completed as a well be sealed with grout.

5.2.2.4 Subtask 2d - Laboratory Analysis and Data Validation. Table 5-1 presents the sample designation, the sampling interval, laboratory analyses, and the rationale. Specific analytical parameters are presented in Table 5-2. Samples from several sources will be analyzed for a broad suite of radionuclides as well as numerous chemical constituents and physical parameters. In most cases, no nonradioactive characterization of the waste source has ever been performed.

All samples will be field screened for volatile organics and beta/gamma radiation. Samples obtained for laboratory analysis will be placed in containers and will be properly preserved in accordance with EPA (EPA 1988c) protocols and the Field Sampling Plan, EII 5.2 "Soil and Sediment Sampling" (WHC 1989a), and Chapter 4.0 of the QAPP. All samples for laboratory analysis will be transported under chain-of-custody procedures, in accordance with EII 5.1 "Chain-of-Custody" (WHC 1989a) and Chapter 5.0 of the QAPP.

All laboratory chemical data generated during the RI will be validated. Data validation is a quantitative and qualitative review of specified QA/QC parameters: laboratory precision and accuracy, method blanks, field blanks, instrument calibration and holding times. This review will assess the usability (quality) of the data for subsequent RI data reduction, evaluation of remedial alternatives and risk assessment. Data validation will be conducted throughout the RI as data are generated.

The usability of geologic and geophysical data will be assessed in a qualitative sense via the technical review process. To help assure that the data are of acceptable quality, the field personnel responsible for data collection will be trained and qualified. The geologic logs and geophysical surveys will be reviewed daily by the project hydrogeologist for quality and consistency. Senior technical reviews will be conducted periodically throughout the project.

5.2.2.5 Subtask 2e - Data Evaluation. The objectives of source data evaluation are to confirm that the data are representative of the media sampled, and to compile and present the data in the forms most applicable to the end uses of the data.

For each source investigation task described in Task 2, the data will be compiled for each source or group of related sources so that the source units are defined and the level of understanding is sufficient for the data uses described in

Chapter 4.0. This compilation will include descriptions of each source with dimensions, estimated volumes, levels and types of contamination in the source, and a preliminary evaluation of the potential for migration from the source. The evaluation of potential for migration will be based on the waste type, depth and concentrations of contamination, and physical and chemical properties of the contaminant.

5.2.3 Task 3 - Geologic Investigations

The objectives of the 100-KR-1 site geologic investigation are to characterize the geology of the surface vadose zone sediments and to evaluate their influence on the movement or localization of contaminants. This task includes:

- Data compilation and review
- Field activities
- Laboratory analysis
- Data evaluation.

5.2.3.1 Subtask 3a - Data Compilation and Review. General geologic information on the site and surrounding area is available. Some detailed information is also available both from this site and from studies on adjoining sites. The search for additional geologic data will be an ongoing process prior to initiation of field activities. It is conjectured at this time that little additional existing geologic data, specific to the 100-K Area, will be located.

5.2.3.2 Subtask 3b - Field Activities. Geologic information will be collected from all boreholes drilled during Phase I studies for Tasks 2 - Source Investigations and 5 - Vadose Investigations. Borings will be limited to the vadose zone for the 100-KR-1 investigation. Appropriate geologic studies will also be made on any deep boreholes drilled as a part of the 100-KR-4 investigation. Site-specific data needed for the 100-KR-1 operable unit include:

- Thickness, areal extent, and continuity of geologic subunits
- Details of lithologic, mineralogic, and particle size variations
- Degrees of compaction or cementation

- Geologic parameters that can be shown to affect contaminant distribution.

A surface geologic map will be prepared under Task 3 of the 100-KR-4 operable unit investigation.

5.2.3.3 Subtask 3c - Laboratory Analysis and Data Validation. Laboratory analysis for geologic investigations will be performed to gain an understanding of the lithology, physical parameters and characteristics of the vadose zone. A list of physical analyses is shown in Table 5-2. A well-defined approach to physical testing is not presented because of potential mitigating factors such as radioactivity and chemical contamination levels of samples. In general, no samples will be sent for physical analysis if detectable levels of radioactivity or chemical contamination are noted during field screening. If necessary, physical parameters determined during drilling of ground water wells outside of source areas will be used as analogs of 100-KR-1 operable unit conditions.

The usability of geologic data will be assessed in a qualitative sense via the technical review process. To help assure that the data are of acceptable quality, the field personnel responsible for data collection will be trained and qualified. The geologic logs, hydrologic data, and geophysical surveys will be reviewed by the project hydrogeologist for quality and consistency. Senior technical reviews will be conducted periodically throughout the project.

5.2.3.4 Subtask 3d - Data Evaluation. The purpose of this subtask is to integrate geologic data obtained from several tasks and present it in a format useful to understanding the site and to fulfill data needs identified in Chapter 4.0. Additional objectives are to quantify transport mechanism through the vadose zone and subsequent interactions with ground water.

The surface geologic map and specific geologic data collected during the operable unit vadose investigation and ground water well installation will be evaluated. Data from well and borehole logs and geophysical logs will be graphically formatted and used for construction of site-specific cross-sections. Other graphics and data tables will be developed as necessary to interpret the geology underlying the site.

Soils and geologic data obtained during the vadose investigations will be integrated so that the quantities and concentrations of hazardous and radioactive constituents, as well as vadose zone characteristics that affect migration of contaminants are understood. This task will include identification of data gaps, and

will direct future soils and subsurface investigations. Physical soil characteristics obtained from drilling and sampling in the 100-KR-1 RI will be evaluated to provide physical and numerical descriptions of each of the geologic or stratigraphic units present at the operable unit to the water table. These data will be used to determine infiltration and retardation properties related to specific contaminants, to estimate flux and velocity of contaminants in the vadose zone, to develop vadose flow and transport models, and to provide information on engineering aspects of site corrective actions.

5.2.4 Task 4 - Surface Water and Sediment Investigations.

The surface water and sediment investigation will be conducted as part of and is described in the 100-KR-4 work plan.

5.2.5 Task 5 - Vadose Zone Investigation

A significant portion of the soil chemical testing will be performed as part of Task 2 - Sources Investigation. However, a background soil evaluation, further characterization of soils not in source areas, and soil physical characterization will be performed under the vadose investigation. This investigation includes the following:

- Data compilation and review
- Field activities
- Laboratory analysis and data validation
- Data evaluation.

The tasks listed above may be performed in conjunction with ground water monitoring well installation. The boreholes drilled for monitoring well installation may be suitable for soil sampling.

5.2.5.1 Subtask 5a - Data Compilation and Review. The objective of this subtask is to gain an understanding of the vadose zone at the 100-K Area as defined by existing data. A preliminary review of existing information was conducted in preparation of this work plan and the 100-KR-4 work plan. These data will be supplemented with vadose zone information collected at nearby operable units.

As discussed in Chapters 3.0 and 4.0, determination of remedial actions will be based on a combination of: (1) threat to human health and the environment, and (2) contaminant concentration levels that exceed regulatory criteria. Two important determinations are to be made for vadose zone soils.

1. Near surface contaminant concentrations: Are they or will they be a threat if surface soils are disturbed?

2. Deep vadose zone soils: If contaminants exist, will they release sufficient concentrations to ground water to pose a threat to health or the environment?

Neither of these major data needs requires a comparison to "background." However, they both require knowledge of the actual contaminant concentrations in soils beneath the site. If background soil concentrations are to be used for definition of contamination, then background data should be defined for the entire Hanford Site, especially for vadose zone soils. Some background data are available for offsite surface soils. Because of the possible need to locate background soil borings offsite, this task will be integrated with background studies performed for other operable units on the Hanford Site (e.g., 100-HR-1 operable unit). Other proposed background boring locations will be reviewed to determine their suitability for use as background data for the 100-KR-1 operable unit.

Background soil data for the 100-KR-1 operable unit will be obtained by collecting vadose zone samples from borings drilled outside of source areas as part of the 100-KR-4 operable unit investigation.

The collection of background soils data for use in statistical comparisons to determine the presence or absence of contamination is not necessary in the case of organic chemicals or man-made radionuclides, especially below depths of 1 ft (0.3 m) where natural background should be near zero. It is recognized that fallout from non-Hanford activities has resulted in contamination of surface soils by man-made radionuclides. Background ranges for concentrations or naturally occurring substances such as uranium, chrome or nitrate should be established.

5.2.5.2 Subtask 5b - Field Activities. Field activities for the vadose investigation will focus on determining quality of vadose zone soils.

5.2.5.2.1 Surface Surveys. Prior to commencing vadose zone field investigation activities, review of the data generated from the surface surveys,

described under Task 2 will be done. If the data are complete and adequate to determine borehole locations no additional surveys will be performed. However, if survey coverage is incomplete a site-specific survey(s) will be performed in conjunction with the borehole siting process.

5.2.5.2.2 Siting of Boreholes. The process of siting individual boreholes will be undertaken as part of the field activity process. After surface surveys data are reviewed, an evaluation of the general area on which boreholes are to be sited will be completed. Individual(s) cognizant of the capabilities and limitations of the drilling and sampling equipment to be used for the vadose zone investigation will conduct field observations. The primary purpose of the siting process is to evaluate access, health and safety concerns and determine the most effective routes into and out of potential sites while creating a minimal amount of surface disturbance. Subsequent to completion of survey and siting activities the borehole locations will be staked.

5.2.5.2.3 Drilling and Sampling. The objective of this task is to collect and analyze soil samples to determine chemical and physical characteristics. Soil sample collection will be performed using soil boring techniques. Areas that will be sampled as part of this soil investigation include:

- Areas of retention basin leaks
- Areas of effluent crib failure
- Areas of effluent trench overflow.

Proposed boreholes locations for the vadose zone investigation appear in Figure 5-2, and Table 5-3 presents the sample designations, sampling intervals, laboratory analyses, and rationale.

5.2.5.2.3.1 Area of Retention Basin Leaks. The retention basins leaked extensively and released cooling water to the area in and around the basins. Cooling water had been observed ponding on the ground between the basins and the road located to the north. Two to 3 ft (0.6 to 1 m) of fill was placed in this area to prevent ponding. Effluent that leaked from the basins flowed overland, under the road via a culvert, then to the Columbia River. One borehole will be drilled adjacent to each of the six 107 retention basins. The six boreholes (KW3-1, 2, 3 and KE4-1, 2, 3) will be drilled and sampled from the surface to the water table. The top 20 ft (6 m) will be continuously sampled at 2 ft (0.6 m) intervals and from 20 ft (6 m) to ground water at 5 ft (1.5 m) intervals.

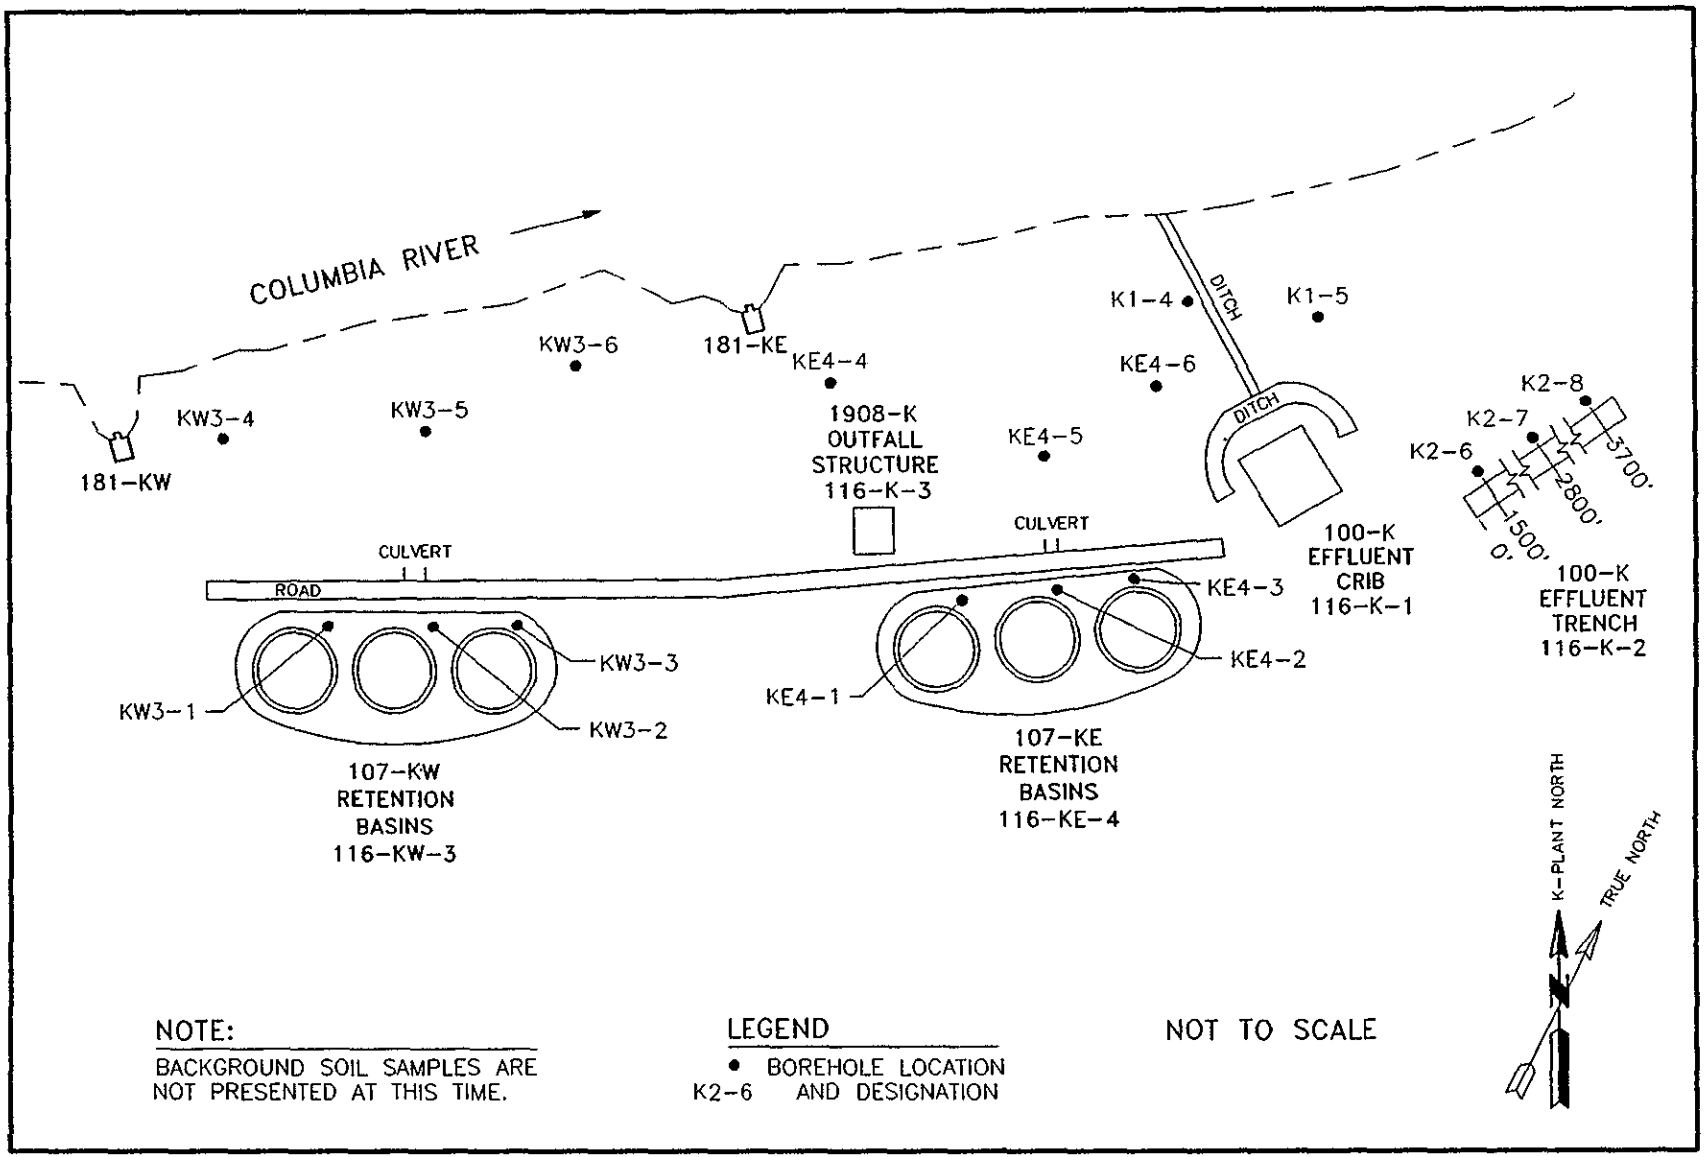

Figure 5-2. Proposed Sampling Locations for Soil Investigation.

Table 5-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list[c]	Short chemical analyses list	Physical analyses[d]	Sampling Rationale
KW3-1	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-2	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-3	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KW3-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KW3-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-1	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

Table 5-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Page - 2

Sample designation[a]	Sampling interval	Laboratory analyses[b]: Long chemical analyses list[c]	Laboratory analyses[b]: Short chemical analyses list	Laboratory analyses[b]: Physical analyses[d]	Sampling Rationale
KE4-2	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KE4-3	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KE4-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K1-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K1-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K2-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

Table 5-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Page - 3

Sample designation[a]	Sampling interval	Laboratory analyses[b]: Long chemical analyses list[c]	Laboratory analyses[b]: Short chemical analyses list	Laboratory analyses[b]: Physical analyses[d]	Sampling Rationale
K2-7	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
K2-8	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

[a] Sample locations shown on Figure 5-2
[b] Analyses listed in Table 5-2
[c] Level IV and V analyses on two sample intervals, level III on remaining intervals
[d] Physical parameters will be analyzes for in each distinct lithologic unit if field screening methods do not detect contamination
GW1 = Ground water estimated at 80 ft
GW2 = Ground water estimated at 40 ft

In addition to the six boreholes adjacent to the basins, six boreholes (KW3-4, 5, 6 and KE4-4, 5, 6) will be drilled to ground water between the road north of the retention basins and the Columbia River. Locations for the boreholes, as shown in Figure 5-2, are approximate and will be precisely located based on the surface radiation survey, walkover surveys, and accessibility. An attempt has been made to locate the boreholes in areas likely to show higher concentrations of contaminants by spotting boreholes on areas of fill or near washouts that were presumably formed during basin leak events. These boreholes will be sampled in the same manner as those near the retention basins: the top 20 ft (6 m) at 2 ft (0.6 m) intervals and the remainder at 5 ft (1.5 m) intervals. To avoid cross contamination of ground water by vadose zone contaminants, borings will not penetrate the water table (or capillary fringe) if significant levels of contamination are detected directly above this zone using field screening techniques.

This biased sampling approach is designed to characterize the chemical and radiological nature of the vadose zone impacted by retention basins leaks. Based on the results of this effort a sampling program may be initiated to further define the distribution of contaminants throughout the zone.

5.2.5.2.3.2 Area of Effluent Crib Failure. The effluent crib received cooling water effluent when fuel cladding failure occurred in the reactors. The effluent crib failed the first time it was used, and some effluent flowed overland to the Columbia River. Approximately 90 acres was contaminated with the effluent, and the top 6 in. (15 cm) of soil is reportedly the most contaminated.

Two boreholes (K1-4 and 5) will be drilled and sampled from the surface to the water table. As with other boreholes, discussed earlier, sampling will be at 2 ft (0.6 m) intervals from 0 to 20 ft (6 m) and at 5 ft (1.5 m) intervals from 20 ft (6 m) to ground water. A more extensive characterization effort may be undertaken based on the results of these analyses. Boreholes were sited in areas suspected of being most highly contaminated; one sited where effluents ran overland toward the river as a result of the crib breach, and the second sited adjacent to a ditch running from the crib to the river. As with other vadose zone borings, these drill holes will not penetrate the ground water if significant levels of contamination exist directly above the water table.

5.2.5.2.3.3 Area of Effluent Trench Overflow. Effluent water in the retention basins leaked through valves into lines, which drained to the effluent trench. The volume of leakage was sufficient enough to fill the trench causing periodic overflows. Three areas of overflow are known to exist on the north side of the trench

and are recognized by areas of graded fill. One borehole will be located on each washout area (K2-6, 7 and 8). Sampling will be done from the surface down to ground water and sampling intervals will be as stated for the other boreholes. No boreholes will be located north of the washout areas until a cultural resource assessment is completed. Any subsequent work in that area will be performed in consultation with the cognizant cultural anthropologist. Boreholes will not penetrate to ground water if significant levels of contamination are encountered directly above the water table.

5.2.5.2.3.4 Sampling Procedures. Sampling equipment and procedures are described in the Sampling and Analysis Plan and are based on procedures developed by Westinghouse Hanford.

5.2.5.2.3.5 Borehole Logging. The principal purpose of the logging program is to provide a record of the geology and other vadose characteristics encountered in the boreholes. Both geologic and geophysical logging will be conducted during the drilling and sampling activities.

Geologic logging will be conducted on each well by a qualified site geologist. The geologic log will contain a description of the borehole lithology and will contain observations of occurrences of perched water, moisture, lithologic changes, sample intervals as well as other pertinent observations. No detailed geologic logging will be performed on samples containing or suspected of containing contamination as indicated by field screening techniques.

Each borehole will be geophysically logged during the drilling and sampling process. Geophysical logs will include gamma-gamma, neutron, epithermal neutron, and high resolution spectral gamma. Borehole geophysical logging is helpful in the correlation of sedimentary facies using physical properties such as porosity, density, and water content. High-resolution spectral gamma logging permits the identification of gamma emitting radionuclides and should help identify strata that have trapped specific species of radionuclides.

5.2.5.2.3.6 Drill Cuttings Disposal. Soil cuttings containing low-level and mixed radioactive waste and hazardous waste will be contained and disposed of according to Westinghouse Hanford procedures.

5.2.5.2.3.7 Borehole Abandonment. All boreholes will be properly abandoned, following approved Ecology and EPA procedures. All steel casings will be removed and transferred to an appropriate controlled decontamination facility and

each boring will be pressure grouted from the bottom up, using a portland cement/bentonite slurry. Washington State Regulation WAC 173-160 requires that all boreholes not completed as a well be sealed with grout.

5.2.5.3 Subtask 5c - Laboratory Analysis and Data Validation. Table 5-3 describes the proposed borehole sample locations, the sample media, general analytical parameters, and the rationale and objectives. All samples will be field screened for beta/gamma radiation and volatile organics. Physical soil characteristics obtained will be evaluated to provide numerical descriptions of each of the geological units present at the operable unit.

Analytical data will be plotted to reveal areal and depth distributions of contaminants. Contaminant data determined by standard laboratory methods and laboratory screening methods will also be statistically compared to background values to determine the feasibility of using the screening methods to reduce analytical costs. Background data will be examined by probability plots and goodness of fit test, and an appropriate probability function will be selected to fit the distribution. Analytical results below detection limits will be handled in accordance with EPA methods. Contaminant and physical analysis will be performed to allow a student-t test to be conducted for each parameter result from the comparative samples obtained during drilling of ground water wells located outside of source areas.

All laboratory chemical data generated during the RI will be validated. Data validation is a quantitative and qualitative review of specified QA/QC parameters: laboratory precision and accuracy, method blanks, field blanks, instrument calibration and holding times. This review will assess the usability (quality) of the data for subsequent RI data reduction, evaluation of remedial alternatives and risk assessment. Data validation will be conducted throughout the RI as data are generated.

The usability of hydraulic, geologic, and geophysical data will be assessed in a qualitative sense via the technical review process. To help assure that the data are of acceptable quality, the field personnel responsible for data collection will be trained and qualified. The geologic logs, hydrologic data, and geophysical surveys will be reviewed by the project hydrogeologist for quality and consistency. Senior technical reviews will be conducted periodically throughout the project.

5.2.5.4 Subtask 5d - Data Evaluation. Soils and geologic data obtained during the soils investigations will be integrated so that the quantities and concentrations of hazardous and radioactive constituents, as well as vadose zone characteristics that affect migration of contaminants are understood. This task will include identification

of data gaps and will direct future soils and subsurface investigations. Surface radiation survey results will be evaluated to determine locations for additional sampling. Physical soil characteristics obtained from drilling and sampling will be evaluated to provide physical and numerical descriptions of each of the geologic or stratigraphic units present at the operable unit to the water table. These data will be used to determine infiltration and retardation properties related to specific contaminants, to estimate flux and velocity of contaminants in the vadose zone, to develop vadose zone flow and transport models, and to provide information on engineering aspects of site corrective actions.

Soil contaminant data will be evaluated to determine what contaminants are present at elevated levels. Contaminant data will be plotted to reveal areal and depth concentration distributions.

5.2.6 Task 6 - Ground Water Investigations

The ground water investigations will be conducted as part of and are described in the 100-KR-4 work plan.

5.2.7 Task 7 - Air Investigations

The objective of this task is to evaluate field worker safety when exposed to potentially contaminated soils. The investigation will include the following subtasks:

- Data Compilation
- Field Activities
- Laboratory Analysis
- Data Evaluation.

5.2.7.1 Subtask 7a - Data Compilation and Review. The air investigation will include obtaining the compilations of meteorological data from the ongoing RIs at other 100 Area operable units (e.g., 100-DR-1, 100-HR-1, 100-BC-1) and performing additional data compilation as necessary for the 100-KR-1 operable unit.

5.2.7.2 Subtask 7b - Field Activities. The proposed RI/FS field sampling activities include actions that will potentially expose waste and contaminated soil to the atmosphere. There will be minimal disturbance of contaminated materials during the field sampling activities. However, because RI field crews may be exposed to airborne contaminants during sampling activities, air sampling will be performed at work sites where invasive investigations occur. Sampling will be performed for both airborne particulates and volatile organics. The monitoring for volatile organics will be performed with the use of field instruments. Sampling for airborne particulates will be performed with high-volume air samplers. Sampling will coincide with field activities at the activity site (e.g., boring location). The number of samples collected will depend on the nature of the field activities.

5.2.7.3 Subtask 7c - Laboratory Analysis. The air sample filters will be analyzed for ^{60}Co, ^{137}Cs, gross beta, and gross alpha. If significant (as defined by site-specific applicable relevant and appropriate requirements) concentrations of gross alpha are detected, samples will be composited and analyzed for ^{239}Pu.

5.2.7.4 Subtask 7d - Data Evaluation. Data gathered during the air investigation will be evaluated by Health Physics and industrial hygiene support personnel. They will determine if sampling activities have generated airborne radioactive materials and if additional sampling is necessary.

Air samples will reflect natural radioactivity and world-wide fallout from past nuclear weapons testing. The possible presence of airborne, long half-life alpha activity as a result of sampling activities will be based on comparisons of project-related samples to natural background samples taken under the same conditions, using the same type samplers, sample duration, and analytical procedure. All samples more than 50% above the background value will be analyzed for plutonium. If there are several samples from the same general location or samples from different days at the same location, they may be composited for the plutonium analysis. Algorithms may be developed from statistical analysis of local air samples to develop other criteria. Such algorithms may include the ratio of gross alpha analyses at 5 h after collection to that at 24 or 48 h after collection.

5.2.8 Task 8 - Ecological Investigations

The initial 100-KR-1 ecological field investigations will only involve a survey of terrestrial biota; and the 100-KR-4 ecological investigations will concentrate on

aquatic and riparian biota at the 100-K Area. The objectives of the terrestrial biota investigation are:

- Establish the biological inventory at the operable unit
- Determine significant pathways and potentially affected species
- Provide information necessary to complete the risk assessment
- Provide information necessary to evaluate the potential biological effects of implementing the proposed remediation alternatives.
- Provide information necessary to verify or refine the conceptual model.

The data required from the terrestrial monitoring program include determination of significant potential pathways of contaminant movement to humans, determination of critical habitat for species of special concern, and conceptual models of human and environmental risk.

In order to provide the most efficient use of resources, the terrestrial biota studies will proceed incrementally and in conjunction with the ecological studies planned for the 100-KR-4 operable unit. This approach involves several subtasks:

- Subtask 8a - Data Compilation and Review
- Subtask 8b - Field Investigations
- Subtask 8c - Laboratory Analysis
- Subtask 8d - Data Evaluation.

5.2.8.1 Subtask 8a - Data Compilation and Review. A literature search will be performed to gather available information on contamination of terrestrial biota from site activities. Hanford Site Environmental Reports (PNL 1988, 1989) represent one source of information. Sufficient data are currently available from previous studies to provide at least qualitative descriptions of ecosystem structure, and to propose provisional estimates of pathways and potential risks.

A description of the terrestrial biota is given in Section 2.2.6. Existing area and site-specific biological data will be collected. This task will focus on work performed as part of the ongoing Hanford environmental monitoring program, on special studies conducted at the Hanford Site, and on information available from the Washington State Departments of Wildlife and Natural Resources, as well as the Washington State Natural Heritage Program. Emphasis will be placed on using data developed during investigations at other operable units in the 100 Areas.

Existing data will be used to identify terrestrial species with protected management status that occur at the site; species that are dominant in the community in terms of productivity, abundance, or biomass; and species whose removal from the ecosystem would result in a dramatic change in the characteristics of the system. Probable pathways of contaminant transfer in the environment will also be identified.

These data will be used to design a focused field monitoring program to test the applicability of the data to the 100-KR-1 operable unit, and to collect information needed for other tasks in the study. The field investigation will concentrate on areas of known contamination in the operable unit, and on species with demonstrated potential to translocate contaminants of concern.

5.2.8.2 Subtask 8b - Field Activities. This subtask will supplement the literature review described under Subtask 8a through an onsite terrestrial biological survey. This survey can be regarded as a qualitative operable unit specific verification of the body of knowledge on the 100-KR-1 terrestrial ecosystem. The biologist in charge of this task will make the decision as to when a field survey is required to support Subtask 8a. Special searches will be made to locate clumps of wild asparagus. If asparagus plants occur in the 100-KR-1 operable unit, samples will be collected and analyzed during the season when they are most likely to be harvested by people.

The survey will be conducted over the entire operable unit surface, including the riparian zone, and will be conducted as part of the site walkover survey described under Subtask 2a. Major species present will be confirmed, to the extent practicable, under this subtask. Information gained from the survey will be entered onto the base map (or overlay).

Sampling done as part of the 100-KR-4 investigation will supply contaminant concentrations in plant tissues collected in the vicinity of the operable unit riparian zone and enable comparisons of these values with "control" areas. If values are significantly elevated over the background control values, herbivorous animals will be harvested and their tissues analyzed for specific contaminants, e.g., strontium-90 in

bone tissue and cesium-137 in muscle tissue. There are a variety of contaminants that could be bioaccumulated in animal tissues (Evans et al. 1989). Biomagnification is well documented in the literature, and thus low levels of contaminants found in plants may be indicative of elevated levels in wildlife. The animals selected for harvest would likely be mice-and/or cottontail rabbits because of their restricted home ranges, they are herbivores, and are usually available in numbers sufficient for sampling and monitoring.

5.2.8.3 Subtask 8c - Laboratory Analysis. Asparagus will be analyzed for radionuclides. If animals are harvested they will be analyzed for specific contaminants identified in riparian zone plants as part of the 100-KR-4 ecological investigation.

5.2.8.4 Subtask 8d - Data Evaluation. After completion of the field studies, data will be evaluated to see if the provisional understanding developed from the existing data is supported. This will include an evaluation of the predicted significant release mechanisms on major species and the estimate of the risk to humans and the environment through terrestrial biota. In addition, any gaps in the data that remain, or that develop as a result of unexpected results from the field studies, will be identified. If data gaps exist, or if anomalous results are obtained in initial field studies, additional field studies will be developed to attempt to resolve the uncertainty. Major terrestrial species present in and near the 100-KR-1 operable unit, as determined through Tasks 8a and 8b, will be tabulated. Feeding relationships among these species will be presented graphically in the form of a generalized food web. Potential indicator species and ecological indicators will also be presented. The understanding of the biological setting of the operable unit will be updated, as appropriate.

If the site conceptual model is supported by the field data, and no data gaps are evident, no further field studies will be conducted for this portion of the RI.

5.2.9 Task 9 - Cultural Resource Investigations

A cultural resource investigation has determined the location of surficial archaeological or historical sites listed on or eligible for the National Register of Historic Places. However, additional archaeological sites may exist along the Columbia River immediately adjacent to the 100-K Area and will be part of this investigation.

The task will involve verifying the locations of known sites by reviewing available data on historic land uses by local Indian tribes as well as early 20th century

land use by pioneer farmers and settlers. The focus of the investigation will be to determine whether archaeological resources are present at proposed drilling sites. A Class 3 field survey will be conducted by a qualified archaeologist as part of the initial RI field activities. The *Hanford Cultural Resource Management Plan* (Chatters 1989) will be followed during the review process. No RI work will be performed in the area of known sites prior to completion of this task.

5.2.10 Task 10 - Data Evaluation

Data evaluation will occur after data validation or qualification has been completed. Validated or qualified data from all site investigations will be organized in a logical manner so that the relationships between investigations are apparent. This organization will allow decisions to be made regarding any necessary rescoping of the RI/FS process, such as the need for additional sampling. The data evaluation will describe (1) the quantities and concentrations of specific contaminants at the site and the ambient levels surrounding the site; (2) the number, location, and types of nearby populations and activities; and (3) the potential transport mechanism and the expected fate of the contaminant in the environment.

Data evaluations will be performed on the major and applicable 100-KR-1 field investigation tasks listed below and are discussed in the previous task descriptions.

- Source Investigations
- Geologic Investigations
- Vadose Investigations
- Air Investigations
- Ecological Investigations.

5.2.11 Task 11 - Base Line Risk Assessment

The objective of the baseline risk assessment is to determine the magnitude and probability of potential harm to human health and/or the environment by the threatened or actual release of a hazardous substance from a waste site in the absence of remedial action. Results of the risk assessment are used to determine whether

remedial action is necessary and to justify the remedial actions. The baseline risk assessment will follow the guidelines set forth in the *Human Health Evaluation Manual* (HHEM) (EPA 1989b), which discusses human health assessments, and in the *Environmental Evaluation Manual* (EEM) (EPA 1989c), which discusses ecological assessments.

To achieve the baseline risk assessment objectives, the following areas will be identified and characterized:

- Quantity and concentrations of hazardous substances present in air, soil, ground water, surface water, sediment, and biota
- Environmental fate and transport mechanisms within specified environmental media, such as physical, chemical, and biological degradation processes and hydrogeologic conditions
- Potential exposure pathways and extent of actual or expected exposure
- Extent of expected impacts and the potential for such impacts occurring (i.e., risk characterization)
- Acceptable levels of exposure based on regulatory and/or toxicological information.

The risk assessment process is composed of the following components that, collectively, address the areas identified above:

- Contaminant identification
- Exposure assessment
- Toxicity assessment
- Risk characterization.

Figure 5-3 shows how these four components interrelate.

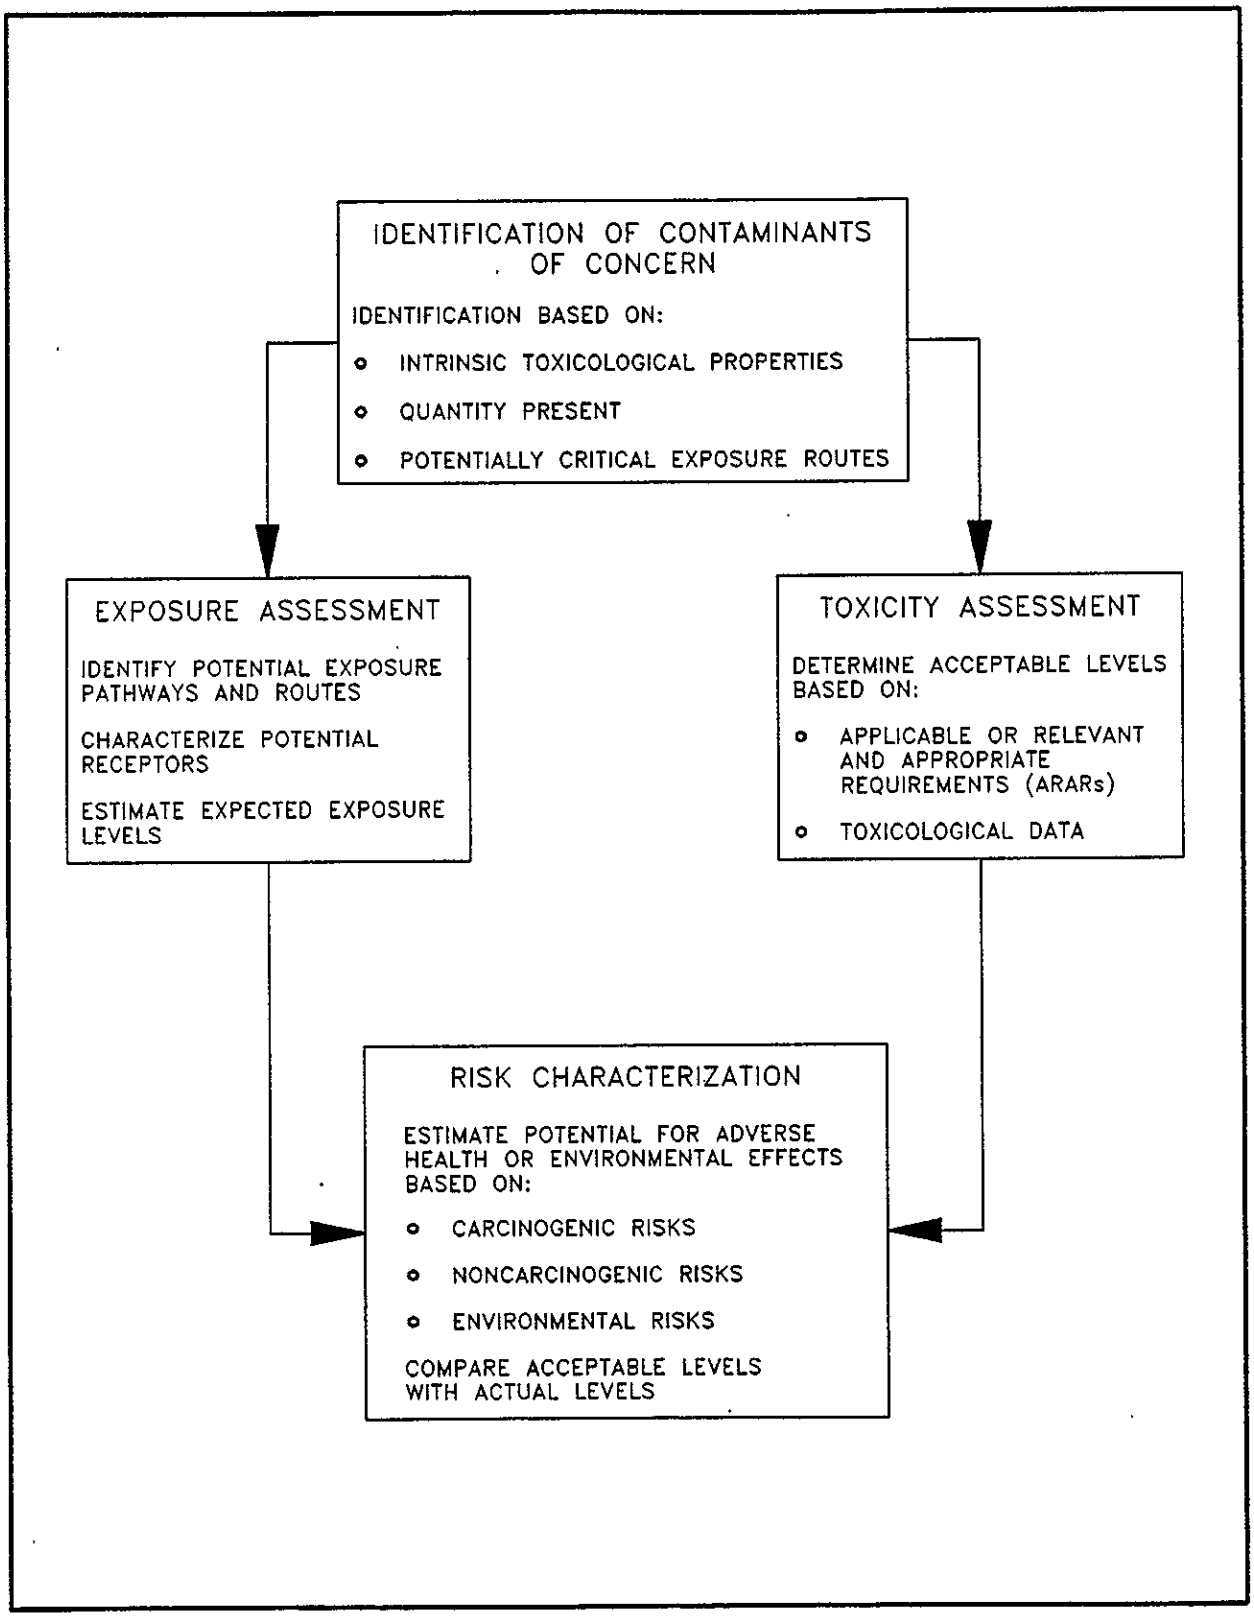

Figure 5-3. Components of the Risk Assessment Process.

5.2.11.1 Subtask 11a - Contaminant Identification. The first component of the risk assessment process is to identify contaminants of concern. The objective of this component is to screen the field of contaminants to provide a list of contaminants for which the subsequent risk assessment activities are focused. The basis for selecting contaminants of concern will include their intrinsic toxicological properties, presence in large quantities, and/or presence in media of potentially critical exposure pathways such as a source of drinking water.

5.2.11.2 Subtask 11b - Exposure Assessment. The objective of exposure assessment is to estimate the environmental concentrations of hazardous substances so that the extent and duration of human and environmental exposure can be predicted or determined. This objective will be achieved by identifying potential or actual exposure pathways, characterizing potentially exposed populations, and estimating both present and future exposure levels.

The first step of the exposure assessment involves identifying exposure pathways. Each exposure pathway consists of four elements: (1) a source and mechanism of chemical release to the environment; (2) an environmental transport medium, such as ground water; (3) a potential point for receptor contact with the contaminated medium (i.e., exposure point); and (4) an exposure route at the contact point, such as ingestion of drinking water or crop irrigation.

Data gathered during the preliminary assessment/site inspection, environmental monitoring activities, RI of the 100-KR-1 and 100-KR-4 operable units, and any other data sources will be used to identify the potential release sources and release mechanisms from the sources. As the release mechanism(s) for contaminants are identified (or postulated), the transport medium for the contaminants will also be identified.

The next element of the exposure pathway analysis is identifying the potential exposure points and exposure routes for human and environmental populations. This analysis involves identifying and characterizing maximally exposed individuals for a worst-case scenario and various populations for which an exposure potential exists. This characterization involves determining the number of individuals in a population, the demographics of each population, and the potential exposure routes to populations and individuals. The analysis will be used to identify exposure points for short- and long-term exposures. In addition to existing exposure points, credible future exposure points will be postulated. A preliminary discussion of exposure routes and receptors is found in Sectors 3.3.1.4 and 3.3.1.5.

Once this information is gathered, it will be assembled to determine the complete exposure pathways that exist for the 100-KR-1 operable unit. After potential exposure pathways are determined, environmental concentrations for each contaminant of concern or indicator chemical will be estimated at each of the identified exposure point locations. Concentrations will be estimated for each environmental medium through which potential exposures could occur as a function of time to assess short- and long-term exposures. These concentrations will be estimated by combining environmental monitoring and characterization data with numerical modeling to predict the release rates from the various waste sources. Then, the fate and transport of the contaminants in the transport medium of the exposure pathways will be determined. The fate and transport modeling will consider the environmental transport of contaminants (e.g., ground water migration), contaminant transformation (e.g., biodegradation), and mechanisms for transfer of a contaminant from one transport medium to another (e.g., sorption, volatilization). The predicted environmental concentrations and exposure route information will then be used to estimate the amount of contaminant that the various receptors potentially could intake (i.e., dosage rate).

5.2.11.3 Subtask 11c - Toxicity Assessment. The objectives of toxicity assessment are to determine the nature and extent of health and environmental hazards associated with exposure to contaminants from the 100-KR-1 operable unit. The final product of the toxicity assessment is a qualitative description of the toxic properties of each contaminant and a quantitative index of each contaminant's toxicity (i.e., acceptable exposure level).

Available contaminant-specific ARARs (e.g., maximum contaminant levels, 25 mrem/yr effective dose equivalent, all pathways) will be used as acceptable levels for human exposure unless exposure at the ARAR level results in a risk greater than 10^{-4}. Acceptable levels for other contaminants will be based on reference doses for noncarcinogens and cancer potency factors for carcinogens. These values are available in toxicity profiles such as IRIS (EPA 1989a) and HEAST (EPA 1989d).

Environmental hazard assessment will determine actual or potential effects of contaminants on plants and animals. Acceptable levels for environmental receptors (e.g., various species of fish) will be contaminant toxicity levels which are available in the literature.

5.2.11.4 Subtask 11d - Risk Characterization. The final component of the risk assessment process is characterizing the risk to various receptors from exposure to contaminants from the 100-KR-1 operable unit. This objective is attained by

integrating the information gathered during exposure and toxicity assessments to characterize the potential or actual risks resulting from contaminants released from the 100-KR-1 operable unit. These include the carcinogenic, noncarcinogenic, and environmental risks.

Potential human risks from the 100-KR-1 operable unit will be assessed by comparing acceptable contaminant exposure levels with actual or predicted levels. For noncarcinogens, the goal will be exposure, such that the sum of fractions of actual or predicted exposure versus the reference dose is less than one. The goal for exposure to carcinogens will be a lifetime risk of contracting cancer between 10^{-6} to 10^{-4}.

The environmental risk evaluation will discuss the effects of exposure on indigenous species, food chains, and habitat. All of these factors affect environmental quality in the vicinity of the 100-KR-1 operable unit and along exposure pathways.

The final assessment will include a summary of risks associated with the 100-KR-1 operable unit, data associated with each step of the risk assessment process, estimated uncertainty of various parts, assumptions made during the assessment, and distribution of risk across different segments of the population and environment.

The results of the risk assessment will be used to determine whether the 100-KR-1 operable unit poses a potential threat to human health and/or the environment. The results will be the primary means of documenting the decision for choosing the no-action alternative or performing remedial action. If the no-action alternative is not selected as the preferred alternative for addressing hazards at the 100-KR-1 operable unit, remedial alternatives will be assessed as part of the FS. The risks for each of the remedial alternatives will also be assessed, but they are beyond the scope of the current effort.

5.2.12 Task 12 - RI Phase I Report: Preliminary Operable Unit Characterization Summary

5.2.12.1 Subtask 12a - Report Preparation. An interim report will be prepared at the end of the RI Phase I. This report will consist of a preliminary summary of the results of the 100-KR-1 operable unit characterization activities. Information pertinent to the 100-KR-1 conceptual model will be refined as necessary; sources of contaminant releases will be definitively identified; the nature and extent of contamination within the operable unit sources, soils, air, and terrestrial biota will be

described; a definitive list of contaminant and location-specific ARARs will be provided; and the risks associated with the contaminant releases will be presented.

5.2.12.2 Subtask 12b - Report Review and Approval. This report will be prepared primarily for interim internal review, although EPA and Ecology have the option to comment on it. It will also provide a means for communicating 100-KR-1 operable unit findings to the project FS coordinator for use in the ongoing evaluation of potential operable unit remedial action measures.

5.3 FS PHASE I/II - REMEDIAL ALTERNATIVES DEVELOPMENT

The objective of the Feasibility Study is to develop a range of potential remedial alternatives that are protective of human health and the environment and satisfy ARARs. A range of remedial alternatives for operable unit problems will be developed to provide decision-makers with choices.

The development of alternatives for the 100-KR-1 operable unit must be coordinated with the same activity for the 100-KR-4 operable unit to ensure that overall remediation objectives can be attained. Remediation options being considered for the 100-KR-4 operable unit could affect the choice of options being considered for the 100-KR-1 operable unit.

Four tasks will be utilized to develop remedial alternatives and include:

- Task 1 - Project Management
- Task 2 - FS Phase I Alternatives Development
- Task 3 - FS Phase II Alternatives Screening
- Task 4 - FS Phase I/II Report: Remedial Alternatives Development.

5.3.1 Task 1 - Project Management

This task is necessary to meet the goals and objectives of the 100-KR-1 RI/FS and is discussed in Section 5.1 and Attachment 3, the Project Management Plan.

5.3.2 Task 2 - FS Phase I Alternatives Development

Section 3.4 presented a general identification of remedial action objectives, general response actions, remedial technologies, and a preliminary list of remedial action alternatives for the 100-KR-1 operable unit. These preliminary response actions, technologies, and alternatives will be modified, as appropriate, based on the evaluation of RI data and the risk assessment. The development of remedial alternatives will be accomplished in the following steps:

- Subtask 2a - Development of remedial action objectives
- Subtask 2b - Development of general response actions
- Subtask 2c - Identification of potential remedial technologies
- Subtask 2d - Evaluation of process options
- Subtask 2e - Assembly of remedial alternatives
- Subtask 2f - Action-specific requirement identification
- Subtask 2g - Evaluation of data needs
- Subtask 2h - Feasibility study report Phase I - remedial alternatives development.

Each subtask is summarized below. Additional details can be found in EPA's Interim Final RI/FS guidance document (1988a).

5.3.2.1 Subtask 2a - Development of Remedial Action Objectives. Remedial action objectives will be developed that state environmental medium-specific or source-specific goals for protecting human health and the environment. The environmental media of concern are unsaturated soil, air and terrestrial biota. Contaminants of concern, exposure routes, receptors, and acceptable contaminant levels or ranges of levels for each exposure route will be specified for each medium. Acceptable contaminant levels will be based upon identified chemical-specific ARARs, TBCs, or risk assessment calculations.

5.3.2.2 Subtask 2b - Development of General Response Actions. General response actions, which are broad classifications of actions or combinations of actions that will

satisfy the remedial action objectives, will be developed on a medium-specific basis. Examples of general response actions are no action, institutional controls, disposal, extraction, excavation, containment, and treatment.

The important site and waste characteristics will be defined for the 100-KR-1 operable unit as part of this task. These characteristics will include the radiological, chemical and physical conditions to which general response actions might be applied.

5.3.2.3 Subtask 2c - Identification of Potential Remedial Technologies. A list of potential remedial technologies will be developed for each identified general response action. The technologies to be considered should address the key site and waste characteristics identified in the RI report. Process options, which are the different processes within a technology type, will be identified for each technology.

The following example, using a hypothetical ground water situation, illustrates how the degree of technological specificity narrows in moving from general response action to remedial measure technology to process option categories:

- General response action for ground water treatment
- Potential remedial technologies within the ground water treatment category
  - Physical
  - Chemical
  - Biological in situ
- Potential process options within the ground water chemical treatment technology type
  - Neutralization
  - Precipitation
  - Ion exchange
  - Oxidation
  - Chemical reduction

The identified technologies and process options may not all be suitable for use at the 100-KR-1 operable unit. First, the identified options are evaluated for technical implementation. This is determined by comparing the capabilities of each process option to the physical and chemical characteristics of the operable unit. An entire

technology may be eliminated because its process options are not technically implementable at the project site. The rationale for this preliminary screening will be documented.

5.3.2.4 Subtask 2d - Evaluation of Process Options. Once identified options are evaluated for technical implementation, then the second step involves a closer evaluation of the process options associated with each remaining technology. Process options will be evaluated on the basis of effectiveness, implementability, and cost.

The effectiveness evaluation will focus on:

- The potential effectiveness of the process options in handling the estimated areas or volumes of the contaminated medium and attaining the remedial action objectives for that medium
- The effectiveness of the process options in protecting human health and the environment during remedy construction and implementation
- How proven and reliable the process option is with respect to the contaminants and conditions at the 100-KR-1 operable unit.

Both technical and institutional implementability are considered in evaluating process options. Technical implementability will eliminate those options that are clearly ineffective or unworkable at the 100-KR-1 operable unit. Institutional considerations include the ability to obtain necessary permits for any offsite actions, the ability to meet substantive requirements of relevant permits for onsite actions, the availability and capacity of appropriate treatment, storage, and disposal services, and the availability of essential equipment and skilled labor.

Cost will be an evaluation criteria. Relative capital, operations and maintenance costs, as opposed to detailed estimates, will be determined based on engineering judgement. Processes within the same technology type will be compared with respect to cost.

Innovative technologies may by applicable at the 100-KR-1 operable unit. Should an innovative technology exhibit fewer environmental impacts, better treatment, or lower costs over a conventional technology, then it could progress through the screening process.

Applicable technologies with one or more feasible process options will be used in developing remedial alternatives. Multiple process options based on one technology may be combined into a given remedial alternative. Process options that are not selected for development, generally, will not be considered later in the FS. They may, however, be reinvestigated during remedial design if the associated technology is selected for implementation at the 100-KR-1 operable unit.

5.3.2.5 Subtask 2e - Assembly of Remedial Alternatives. Preliminary remedial alternatives will be developed for each contaminated environmental medium of concern. This will involve assembling medium-specific process options or possibly remedial technologies or general response actions. The three types of environmental media are discussed in Section 5.3.1 and can be remediated using two methods: (1) develop alternatives for the entire operable unit; or (2) screen medium-specific alternatives first (see Section 5.4) to reduce the alternatives for the entire operable unit. Both methods are consistent with EPA's interim final RI/FS guidance (1988a). The chosen method will be discussed with EPA before undertaking this task.

Several waste management options are available for remediation of the site. They include:

- A no-action alternative
- Treatment alternatives related to treating waste prior to onsite storage to eliminate the need for long-term management
- Management alternatives for onsite and offsite waste containment and storage.

Section 121(b)(1) of CERCLA has a statutory preference for permanent and significant waste treatment. Containment and treatment alternatives will be developed in conjunction with the selection of treatment technologies. This is more acceptable than waste removal and offsite disposal alternatives.

5.3.2.6 Subtask 2f - Action-Specific Requirement Identification. The preliminary action-specific remedial action requirements, which were identified in Section 3.2.2, will be reexamined after the technology alternatives have been examined to eliminate options that are not desirable or feasible. Special consideration will be given to the regulations that may influence the treatment (or exemption from treatment) of water containing tritium because of the lack of treatment options.

5.3.2.7 Subtask 2g - Evaluation of Data Needs. In the process of developing remedial alternatives, additional RI data needs may be identified. An assessment will be made as to their value in the 100-KR-1 conceptual model or alternative evaluation criteria. Any uncertain data needs will be discussed in the detailed analysis of alternatives (Section 5.5) and may be evaluated in a sensitivity analysis. Other data needs may require additional characterization or treatability studies.

5.3.2.8 Subtask 2h - FS Report Phase I - Remedial Alternatives Development. The Phase I feasibility study report will document the results of the identification and screening of remedial technologies and the development of remedial alternatives. Examples of the types of information to be included in the 100-KR-1 FS report are:

- Operable unit background summary with available project scoping information and any initial RI data, to include the nature and extent of contamination and contaminant fate and transport
- Confirmation of the operable unit environmental media of concern, include the rationale for continued inclusion in the FS
- Identification of the preliminary remedial action objectives for each environmental medium of concern
- Identification of the general response actions for each environmental medium of concern
- Identification of potential remedial technology types for each medium-specific general response action category
- Documentation of the screening process for technical implementability of remedial technology types
- Identification of potential technological process options for each technology type retained
- Documentation of the process options evaluation process and the selection of representative process options for each technology type
- Documentation of the assembly of general response actions, technologies, and process options, into a range of remedial action alternatives

- Notation of those process options that have not been screened out but are being represented by the processes comprising the alternative
- Identification of action-specific ARARs potentially pertinent to each alternative
- Identification of any new data needs for the RI Phase II.

5.3.3 Task 3 - FS Phase II - Remedial Alternatives Screening

The screening of remedial alternatives follows the development of the alternatives and precedes analysis of these alternatives. The objective of screening the alternatives is to reduce the list of potential remedial actions to a manageable level. The potential remedial actions will then be evaluated in greater detail, based on effectiveness, implementability, and cost.

The major steps to be performed during the screening process are as follows:

- Remedial action objectives are refined
- Remedial alternatives are refined
- The refined alternatives are screened on a general basis to determine their effectiveness, implementability, and cost.

The alternatives that meet the remedial action objectives are then retained for detailed analysis in Phase III of the FS.

The following is a summary of the Phase II FS process. Further details can be found in the draft EPA RI/FS guidance (1988a).

5.3.3.1 Subtask 3a - Refinement of Remedial Action Objectives. The remedial action objectives developed in Phase I of the FS for each environmental medium of interest will be refined based on the information gathered during the RI. Exposures may occur through multiple pathways and may involve interactions between environmental media. Refinement of the remedial action objectives will ensure protection of human health and the environment from potential pathways of concern at the operable unit.

Evaluation of media interactions will determine if ongoing releases significantly affect contaminant levels in other media, such as soil to ground water. Media may be identified that do not pose a significant risk to human health and the environment. RI Phase I information will be used to refine remedial action objectives to better fit the project site and to allow for newly developed remedial technologies.

5.3.3.2 Subtask 3b - Definition of Remedial Action Alternatives. The remedial action alternatives developed in Phase I of the FS will be further defined to identify details of process options, process sizing requirements, remedial time frames, and the refined remedial action objectives.

RI Phase I information will more accurately identify the extent of contamination so that suitable equipment, technologies, and process options can be evaluated in more detail.

The specific types of information that will be developed under this task for the remedial technologies and process options used in each alternative will be as follows:

- Size and configuration of onsite removal and treatment systems
- Identification of contaminants that impose the most demanding treatment requirements
- Size and configuration of containment structures
- Time frame in which treatment, containment, or removal goals can be achieved
- Treatment rates or flow rates associated with treatment processes
- Special requirements for construction of treatment or containment structures, staging construction materials, or excavation
- Distances to disposal facilities
- Required permits and imposed limitations.

All information and assumptions used in generating this information will be thoroughly documented.

5.3.3.3 Subtask 3c - Screening of Remedial Alternatives. The remedial alternatives will be screened with regard to the short- and long-term aspects of effectiveness, implementability, and cost. An evaluation of innovative alternatives will also be made, and comparisons will be made among similar alternatives. The most promising alternatives will be carried forward for further analysis, and then distinctions across the entire range of alternatives will be made.

Alternatives will be retained that have the most favorable composite evaluation. The selections, to the extent practicable, will preserve the range of appropriate remedial alternatives discussed in Section 5.3.2.5. Ten or fewer alternatives that address the entire operable unit are expected to be retained. Additional alternatives may be needed if disposal, as opposed to operable, unit-specific alternatives are developed and preferred. Unselected alternatives may be reconsidered if new information shows additional advantages.

5.3.3.3.1 Effectiveness Evaluation. Each alternative will be evaluated on the basis of its protection to human health and the environment through reductions in toxicity, mobility, or waste volume. Short-term protection needed during the construction and operation period, and long-term protection required after completion of the remedial alternative, will both be evaluated. Sensitivity analyses will be made to evaluate performance.

Residual contaminant levels expected to remain after a reduction of waste toxicity, mobility, or volume will be compared to contaminant-specific ARARs, to pertinent to-be-considered (TBC) values, or to levels established through risk assessment calculations.

5.3.3.3.2 Implementability Evaluation. Implementability is the measure of both the technical and institutional feasibility of accomplishing an operable unit remedial alternative. Technical feasibility refers to the ability to construct, operate, meet action-specific ARARs, and maintain and monitor the remedial technologies or process options. Institutional feasibility refers to the ability to obtain approvals from appropriate agencies and to procure required services, equipment, and personnel.

Alternatives deemed technically unfeasible will be dropped from consideration. Lack of agency approval will be the only reason institutionally unfeasible alternatives will not be dropped. In the latter situation, the remedial alternative will be retained, if possible, with the incorporation of appropriate coordination steps needed to lessen its negative aspects.

5.3.3.3.3 Cost Evaluation. Comparative cost estimates will be made. Cost estimates will be based on cost curves, generic unit costs, vendor information, conventional cost-estimating guides, and prior similar estimates. Both capital and operating and maintenance costs will be considered where appropriate. Present worth analyses will be used to evaluate expenditures that occur over different time periods, so that costs for different remedial alternatives can be compared on the basis of a single figure for each.

5.3.3.3.4 Evaluation of Innovative Alternatives. Innovative technologies will be considered if they are fully developed but lack sufficient cost or performance data for routine use at CERCLA sites. It is unlikely that alternatives that incorporate innovative technologies will be evaluated as thoroughly as is done with available technologies. However, innovative technologies will pass through the screening phase if they offer promise of significant advantages. The need for treatability studies on retained innovative technologies will be made in conjunction with Subtask 3e.

5.3.3.4 Subtask 3d - Identification of Action-Specific ARARs. Identification of action-specific ARARs will be made easier by the new information gathered on technologies and configurations during the screening process. The ARARs previously identified will be refined by project staff with input from Ecology and EPA. Regulatory agency participation will provide project focus and direction and expedite the FS Phase I/II report review produced under Task 4.

5.3.3.5 Subtask 3e - Reevaluation of Data Needs. During the RI Phase II, treatability testing will be conducted on the remaining alternatives. Additional site characterization data needs may develop during the screening phase, which would necessitate additional field investigations. The work would then focus on a more thorough explanation of the effect of operable unit conditions on the performance of the remedial measure technologies and process options of greatest interest. The effectiveness of performance will be evaluated using sensitivity analysis. Data quality objectives will be refined or developed, as needed for any additional investigations.

5.3.4 Task 4 - FS Phase I/II Report: Remedial Alternatives Development

5.3.4.1 Subtask 4a - Report Preparation. The results of the initial screening of alternatives will be combined with the interim FS Phase I report and any significant comments will be contained in that report. This information will help develop a document summarizing both the development and screening of alternatives for the operable unit. The report will list the procedures for evaluating, defining, and

screening the alternatives. The following types of information pertinent to the screening phase will also include:

- Refined remedial action objectives associated with each alternative, including any modifications made to ensure that multiple-pathway exposures and media interactions are addressed

- Definition of each alternative, including extent of remediation, area or volume of contaminated media, sizes of major technologies, process parameters, cleanup time frames, transportation distances, and special considerations

- Notation of those process options that have not been screened out but are being represented by the processes composing the alternative

- Screening evaluation summaries of each alternative process

- A comparison of screening evaluation among alternatives.

A reevaluation of data needs for the RI Phase II will be included in this report. Details of the FS Phase I/II report will, in turn, be summarized in the final FS report Phase III.

5.3.4.2 Subtask 4b - Report Review and Approval. The FS Phase I/II report will be subject to internal peer review before being forwarded to regulatory agencies. As a primary document, the report will be reviewed and approved by EPA and Ecology.

5.4 RI PHASE II - TREATABILITY INVESTIGATION

5.4.1 Task 1 - Operable Unit Characterization

Additional data needs essential to evaluating alternatives may be identified as operable unit information is collected during the RI Phase I and FS Phase I and II. In response to these needs, additional site characterization data may need to be collected or treatability studies performed to better evaluate certain remedial action technologies.

Some of the technologies selected for detailed analysis at the 100-KR-1 operable unit may be well developed, proven, and documented. Should this be the case, then unit-specific information collected during the RI Phase I should be adequate for evaluation without conducting treatability testing. However, for untested technologies, it is impossible to predict treatment performance or to estimate the size and cost of treatment units. Some treatment processes, particularly innovative technologies, are not sufficiently understood to predict performance, even with complete waste characterization.

When treatment performance is difficult to predict, either bench-scale or pilot-scale testing may provide the most cost-effective means of obtaining the necessary process performance data. At the Hanford Site, some treatability investigations may be performed on a site-wide basis, rather than on an operable unit-specific basis. Any site-wide treatability investigation results that are relevant to the 100-KR-1 operable unit and completed in time to be applied to the operable unit will be incorporated into the project.

The primary purpose of the treatability investigation, in accordance with EPA's interim final RI/FS guidance document (EPA 1988a), is to provide sufficient technology performance information and to reduce cost and performance uncertainties to acceptable levels, so that treatment alternatives can be fully developed and evaluated during detailed analysis. Secondarily, the treatability investigation may generate useful information for conducting the detailed design of a treatment remedy, if the particular treatment technology is a component of the selected remedial action alternative. The allocation of time for a potential treatability investigation also provides a mechanism to conduct further site characterization activities.

The need for any treatability investigation or additional characterization of the 100-KR-1 operable unit will be identified once remedial alternatives are developed. If and when the need arises for a treatability investigation, the work plan will be amended to provide detailed RI Phase II activities, to provide accompanying volumes of the RI/FS project plans, and to provide guidance for the required work prior to implementation. The RI/FS Phase I report will give formal, interim evaluations of further data needs, in terms of treatability investigation. Responsibility for this task rests with the unit managers for the project.

5.4.2 Task 2 - Treatability Investigation Work Plan

5.4.2.1 Development of Treatability Investigation Work Plans. Once treatability tests have been identified, the work plan will be updated to include the treatability investigations. The plan will identify the treatability tests needed, the additional site characterization data needed, and any site samples and other test materials and equipment needed to conduct the tests. A schedule will be prepared for obtaining all necessary site characterization data, samples, test materials, equipment, analytical services, and permits.

Following approval of this plan, individual treatability investigation work plans will be prepared for each technology to be tested. The development of each plan will involve the following steps:

- Determine the scale of the test
- Identify parameters needed and evaluate the treatment viability of the technology
- Determine specifications for test samples and sample procurement
- Determine the test equipment, materials, and procedures to be used in the treatability test
- Identify where and by whom the tests and any analytical services will be conducted; identify any special procedures and permits required to transport samples and residues; conduct tests
- Identify the methods required for residue management and disposal
- Identify any special quality assurance/quality control needed for the tests
- Identify any special safety training or procedures needed for the tests.

Determining the scale of the test is the first step in developing an individual treatability investigation work plan for a specific technology because it has a major influence on the cost, schedule, and complexity of the test. Establishing the scale involves: scaling the results to the expected full-scale process; finding data to design, construct, and operate the equipment at a minimum acceptable scale; and obtaining the necessary quantities of site materials for the test. For most treatment technologies,

bench-scale tests will be sufficient to obtain the data necessary to evaluate a full-scale process. However, some technologies (e.g., in situ treatment technologies and containment or barriers technologies), may require pilot-scale tests to obtain the data needed to conduct a satisfactory evaluation of the technology. Furthermore, if insufficient data are available to design the pilot test, then bench-scale tests will have to be conducted first. The scale of the test will also be influenced by the difficulty in obtaining the sample volume necessary for conducting the test.

The range of each key parameter that will be evaluated in the tests will be specified. Some of these parameters, such as pH or temperature, will be varied over a range determined by site characteristics and the effects of any pretreatment steps. In addition, key performance criteria such as contaminant removal efficiency or leaching rate will be established in the test plan.

For example, to prepare samples for testing in a precipitation/coagulation process for removing chromium from water, it is conceivable that uncontaminated ground water could be spiked with varying quantities of hexavalent chromium and principal dissolved solids, such as calcium or sulfate, as necessary to cover the specified test range. An ion exchange process, on the other hand, may need actual wastewater for valid treatability testing.

The equipment, materials, and test procedures will be specified for each individual treatability investigation as required to obtain the necessary data. In determining what equipment and test procedures are required, particular attention will be given to those identified in a literature survey. The equipment and procedures will also be consistent with approved EPA testing methods. Particular attention will be given to the methods and accuracy required for measuring key performance variables, such as effluent contaminant concentration, to ensure that the sensitivity of the analytical methods and equipment match the sensitivity required to compare results to the test criteria.

Two important considerations in developing each individual plan are where and by whom the tests will be conducted. If the test is to be conducted offsite or at the 100-K Area, special permits may be necessary for either constructing and operating equipment or transporting wastes and residues offsite. Similarly, when the work is conducted by a subcontractor, equipment, test, and sample analyses will need to be negotiated with respect to the treatability investigation work plan.

Management and disposal requirements for residues produced during the test will be determined. The quantity, composition, and location of the waste may

influence treatability test plans. Management of the residues may be an important consideration in determining where and at what scale the tests are to be conducted.

Quality assurance/quality control plans will be reviewed to determine any special quality-related requirements necessary for each individual treatability investigation. Special consideration will be given to the ability to detect and reliably measure contaminants at the concentrations required by the criteria, as well as the potential for contamination of samples during collection, storage, and analysis.

Health and safety plans will be reviewed to determine whether any special training or procedures will be needed. Health and safety considerations will be given to both waste-handling and test operations.

5.4.2.2 Update of RI/FS Work Plans. The information gathered during the treatability investigation will be used to update this work plan. The work plan will include a description of the technology, background site information relevant to each technology requiring a treatability investigation, and documentation of missing data. The plan will contain the following information:

- Project description and site background
- Summary of individual treatability tests
- Schedule
- Cost.

The project description and site background section will summarize appropriate information on site characteristics, contaminant levels, allowable levels, and the remedial action alternatives that are relevant to the technologies being investigated in the treatability investigation. The section summarizing treatability tests will contain brief descriptions of each test, including the scale of the test (bench or pilot scale), and whether there are any special requirements for the test that could impact the overall schedule for the plan.

A separate plan will be prepared for each individual treatability investigation and will provide the detail necessary for conducting the tests. Each plan will include the following sections:

- Project description and site background
- Remediation technology description
- Test objectives
- Description of equipment and materials
- Test procedures
- Test plan for parameters to be tested
- Sampling plan
- Analytical methods
- Data management
- Data analysis and interpretation
- Reporting of results
- Health and safety
- Quality assurance
- Residuals management
- Schedule
- Test sample disposal.

Each of these sections will incorporate information developed during previous activities, as described above.

5.4.2.3 Treatability Investigation. Treatability testing can be performed by using either bench-scale or pilot-scale studies. As noted above, a literature survey will be undertaken to identify specific data needs for the treatability investigation. The objectives of such a survey will be to:

- Determine whether the performances of treatment technologies under consideration have been sufficiently documented on similar wastes, taking into consideration the scale of such documentation (e.g., bench-, pilot-, or full-scale)

- Determine the number of times the treatment technologies have been successfully used

- Gather information on relative costs, applicability, removal efficiencies, operations and maintenance requirements, and implementability of the candidate treatment technologies

- Determine specific testing requirements and appropriate scale for any required treatability tests.

Treatability studies will include the following steps:

- Preparation, review, and approval of a treatability investigation work plan for the bench-scale or pilot-scale studies

- Performance of the bench-scale or pilot-scale testing

- Evaluation of data from bench-scale or pilot-scale testing

- Incorporation of the results of the testing into the final RI report.

5.4.3 Task 3 - Treatability Investigation Implementation and Data Evaluation

This task is the implementation of the treatability investigations. This task will also include any related data evaluation activities that are needed. Specific components and goals of the data evaluation will depend upon the needs of RI Phase II.

Bench-scale (laboratory) testing may be used to provide information to determine the feasibility of waste treatment or destruction technologies, although care must be taken in extrapolating laboratory data to full-scale performance. Bench-scale tests can be used to evaluate a wide variety of operating conditions and to determine broad operating conditions to allow optimization during additional bench- or pilot-scale tests. Bench-scale testing is usually a relatively fast and low-cost process.

Potential objectives of bench-scale testing are to determine:

- Effectiveness of the treatment technology on wastes
- Differences in performance between competing manufacturers
- The differences in performance between alternative chemicals used in the treatment process
- Sizing requirements for any pilot-scale studies
- Potential technologies to be pilot tested
- Sizing of those treatment units that would affect the technology cost sufficiently to affect the detailed analysis of remedial alternatives
- Compatibility of process materials with wastes of the 100-KR-1 operable unit.

Prior to initiating bench-scale treatability tests, the following information will be collected or developed:

- A waste sampling plan
- Waste characterization information, which will be available from RI Phase I data
- Treatment goals, which will be available from remedial action objectives and action-specific ARARs

- Data requirements for estimating the technology cost within -30 to +50% accuracy
- Required test services, equipment, chemicals, and analytical services
- Method of disposal for sampled material.

For a technology that is well developed and tested, bench-scale studies are usually sufficient to evaluate performance on new wastes.

A pilot-scale test, as compared to a bench-scale test, is intended to more accurately simulate the operations of a full-scale process. However, pilot-scale tests require significant time and can be quite costly. Therefore, the need for pilot-scale testing must be determined by balancing the data need against the additional time or money for the test. Pilot-scale testing is often appropriate for innovative technologies, and such testing will be considered if it offers a potential significant savings in time or money required for an alternative to achieve remedial action objectives.

Prior to the initiation of any pilot-scale testing, the following information, in addition to the items mentioned above with regard to bench-scale testing, will be collected or developed:

- Operable unit-specific information impacting test requirements, including waste characteristics, facility characteristics, availability of services and equipment
- Waste requirements for testing; volumes needed for any pretreatment, handling, transport, and disposal
- Specific data requirements for technologies to be tested.

Recommended formats for bench-scale and pilot-scale treatability investigation work plans, along with additional details on the process, can be found in EPA's interim final RI/FS guidance document (EPA 1988a).

5.4.4 Task 4 - RI Phase II Report

The treatability investigation report will describe the testing that was performed, the results of the tests, and an interpretation of how the results will affect the evaluation of the remedial action alternatives considered for the 100-KR-1 operable unit. The report will contain a discussion of the effectiveness of the tested treatment technology for the onsite wastes and an evaluation of how test results affect treatment costs developed during the detailed analysis of alternatives. These results will be combined with the site characterization results, including the results of any further activities carried out under the RI Phase II, and will be published as the final report documenting all RI activities for the 100-KR-1 operable unit.

5.5 FS PHASE III - DETAILED ANALYSIS OF REMEDIAL ALTERNATIVES

The detailed analysis of remedial alternatives follows the development and screening of alternatives and precedes the actual selection of the remedial action to be implemented at the operable unit. The results of the detailed analysis provide the basis for identifying a preferred alternative and preparing the operable unit Proposed Plan and Record of Decision (ROD). The detailed analysis of alternatives consists of the following components:

- Further definition of each alternative, if appropriate, with respect to the volumes or areas of contaminated environmental media to be addressed, the technologies to be used, and any performance requirements associated with those technologies

- An assessment and a summary of each alternative against the nine evaluation criteria specified in EPA's interim final RI/FS guidance document (1988a)

- Comparative analysis among each of the alternatives that will facilitate the selection of an operable unit remedial action.

The brief summary of the detailed analysis process presented below is derived from EPA's interim final RI/FS guidance document (1988a).

5.5.1 Task 1 - Definition of Remedial Alternatives

The remedial alternatives that remain after initial screening may need to be defined more completely prior to the detailed analysis. During the detailed analysis, each alternative will be reviewed to determine whether additional definition is required to apply the evaluation criteria consistently and to develop order-of-magnitude cost estimates (-30 to +50%). Information developed to further define alternatives at this stage may include preliminary design calculations, process flow diagrams, sizing of key process components, preliminary layouts, and a discussion of limitations, assumptions, and uncertainties concerning each alternative. Information collected from treatability investigations, if conducted, will also be used to further define applicable alternatives.

5.5.2 Task 2 - Detailed Analysis of Alternatives

Nine evaluation criteria will serve as the basis for conducting the detailed analysis and for subsequent selection of a cost-effective and protective corrective measure. The nine evaluation criteria are:

- Overall protection of human health and the environment
- Compliance with ARARs
- Short-term effectiveness
- Long-term effectiveness and permanence
- Reduction of toxicity, mobility, or volume
- Implementability
- Cost
- Community acceptance
- Support agency acceptance.

These criteria encompass technical, cost and institutional considerations, compliance with specific promulgated requirements and environmental and health protection.

The last two criteria will be addressed in the responsiveness summary and ROD documents following the public comment period on the FS report and the Proposed Plan.

5.5.2.1 Subtask 2a - Short-Term Effectiveness Analysis. This evaluation criterion addresses the effects of the alternative during the construction and implementation prior to remedial action objectives being attained. The following factors relating to effects on human health and the environment will be addressed for each alternative:

- Protection of the community during construction and implementation
- Protection of workers during construction and implementation
- Environmental impacts during construction and implementation
- Time until remedial action objectives are achieved.

The evaluation of these factors will include a discussion of any increased risks posed by the subject remedial alternative and an evaluation of the effectiveness and reliability of protective measures that may be taken for any needed worker protection or environmental impact mitigation.

5.5.2.2 Subtask 2b - Long-Term Effectiveness Analysis. This criterion will address the results of a potential remedial action in terms of any risk that would remain at the operable unit after remedial action objectives have been met. The following components will be addressed to evaluate the extent and effectiveness of controls that may be required to manage residual or untreated wastes:

- Magnitude of remaining risk
- Adequacy of controls
- Reliability of controls.

The evaluation of these components will include an assessment of residual risk, the adequacy of containment systems, long-term environmental monitoring networks,

institutional controls, and the potential need to replace components of the remedial alternative.

5.5.2.3 Subtask 2c - Analysis of Reduction in Waste Toxicity, Mobility, and Volume. This evaluation criterion addresses the statutory preference for selecting remedies that employ treatment technologies that permanently and significantly reduce toxicity, mobility, or volume of a hazardous substance as their principal element (CERCLA 121[b][1]). The following specific factors will be addressed:

- Treatment processes, the remedies they will employ, and the materials they will treat
- Amount of hazardous materials that will be destroyed or treated
- Degree of expected reduction in toxicity, mobility, or volume as a percentage
- Degree to which treatment will be irreversible
- Type and quantity of treatment residuals that will remain.

Alternatives that treat an operable unit through destruction of toxic contaminants, reduction of the total mass of toxic contaminants, irreversible reduction in contaminant mobility, or reduction of total volumes of contaminated media will be deemed to satisfy the preference for permanent treatment.

5.5.2.4 Subtask 2d - Implementability Analysis. The implementability criterion addresses the technical and institutional feasibility of implementing an alternative, compliance with ARARs, and the availability of various services and materials required during its implementation as outlined in Section 5.3.3.3.2.

5.5.2.5 Subtask 2e - Cost Analysis. Costing procedures outlined in the *Remedial Action Costing Procedures Manual* (EPA 1985) will be used in this analysis. Both capital costs and annual operation and maintenance costs will be considered. Costs will be developed within an accuracy of -30 to +50%. In addition, a present worth analysis will be conducted so that all alternatives can be compared on the basis of a single figure in a common base year. A discount rate of 5% will be used for a period of performance of 30 yr.

5.5.2.6 Subtask 2f - Analysis of Overall Protection of Human Health and the Environment and Compliance with ARARs. This evaluation criterion provides a final check to assess whether each alternative meets the statutory requirement that it be protective of human health and the environment (CERCLA 121[d][1]). The overall assessment of protection is based on a composite of factors discussed under long-term effectiveness and permanence, short-term effectiveness, and compliance with ARARs. The analysis will address how each specific alternative achieves protection over time and how operable unit risks are reduced. A discussion will be included of how each source of contamination is to be eliminated, reduced, or controlled for each alternative.

5.5.2.7 Subtask 2g - Analysis of Community and Support Agency Acceptance. A preliminary assessment of community and support agency acceptance will be limited to formal comments made in earlier phases of the RI/FS. Agency comments on the remedial alternatives analysis and Proposed Plan will be specifically addressed in the responsiveness summary prior to the selection of the remedial action and ROD development. The potentially impacted community, special interest groups, the general public, and other interested governmental agencies will have an opportunity to review and comment on the FS report. Community concerns will also be addressed in the responsiveness summary and ROD.

5.5.3 Task 3 - Comparison of Remedial Alternatives

Once the alternatives have been individually assessed against the nine criteria, a comparative analysis will be conducted to evaluate each alternative in relation to each evaluation criterion. The key tradeoffs or concerns among alternatives will generally be based on the evaluations of short-term effectiveness; long-term effectiveness and permanence; reduction of toxicity, mobility, and volume; implementability; and cost. Overall protection and compliance with ARARs serve as a threshold determination in that they either will or will not be met.

The comparative analysis will include a narrative discussion describing the strengths and weaknesses of the alternatives relative to one another with respect to each criterion. The potential advantages in cost or performance of innovative technologies and the degree of uncertainty in their expected performance will also be discussed. The differences between all of the alternatives will be summarized in matrix form to facilitate direct comparisons. The information obtained by analyzing the alternatives individually against the nine criteria in Section 5.5.2 will be the basis for the matrix.

5.5.4 Task 4 - Feasibility Study Report

The analysis of individual alternatives against the nine criteria will be presented as a narrative discussion accompanied by the summary matrix of section 5.5.3. The alternatives discussion will include data on technology components, quantity of hazardous materials handled, time required for implementation, process sizing, implementation requirements, and assumptions. The key ARARs for each alternative will also be incorporated into those discussions. The discussion will focus on how, and to what extent, the various factors within each of the criteria are addressed.

5.5.5 Task 5 - Corrective Action Plan

Based on the results of the comparison of alternatives in the FS, the preferred remedial alternative will be selected by EPA in consultation with Ecology. The preferred alternative will be developed into a Proposed Plan to be completed in accordance with Section 117(a) of CERCLA. The Proposed Plan and FS report will be made available for public review at the same time, after regulatory approval. The Proposed Plan will consist of a very brief summary, written for the public, in terms of content and distribution, of the nature and extent of contamination at the 100-KR-1 operable unit, the overall corrective action process, the preferred alternative and its advantages and disadvantages, and the other alternatives that are fully developed and analyzed in the FS Report.

Significant comments on the Proposed Plan will be addressed in a responsiveness summary to be prepared during the selection-of-corrective measures process that immediately follows the RI/FS. The Proposed Plan will be finalized based on significant comments and published as a final corrective action plan. The corrective measure selection process will then be formally documented.

6.0 PROJECT SCHEDULE

The anticipated schedule for completing the RI/FS for the 100-KR-1 operable unit is presented in Figure 6-1. This schedule represents the best professional judgment of the Work Plan preparation team based on the assumptions stated as footnotes to Figure 6-1, and should be viewed as an initial planning effort. Many variables exist that could affect the schedule, including resource commitments, findings of the initial RI data gathering efforts, availablility of drilling rigs, and availability of suitable treatability data, and federal, state, and public dispute resolutions.

9 0 1 1 3 3 5 6 2 6 3

THIS PAGE INTENTIONALLY
LEFT BLANK

OPERABLE UNIT CHARACTERIZATION
Task 1 – Project Management
Task 2 – Source Investgations
2a – Data Compilation
2b – Maps
2c – Field Activities (1)
2d – Laboratory Analysis (2)
2e – Data Evaluation
Task 3 – Geological Investigations
3a – Data Compilation (3)
3b – Field Activities
3c – Laboratory Analysis (4)
3d – Data Evaluation
Task 4 – Surface Water and Sediments Investigations
Task 5 – Vadose Investigations
5a – Data Compilation
5b – Field Activities (5)
5c – Laboratory Analysis (2)
5d – Data Evaluation
Task 6 – Ground Water Investigations
Task 7 – Air Investigations
7a – Data Compilation
7b – Field Activities
7c – Laboratory Analysis (4)
7d – Data Evaluation
Task 8 – Ecological Investigations
8a – Data Compilation
8b – Field Activities (6)
8c – Laboratory Analysis (4)
8d – Data Evaluation
Task 9 – Cultural Resources Investigations
Task 10 – Data Evaluations (7)
Task 11 – Baseline Risk Assessment
Task 12 – Report
FS PHASE I/II REMEDIAL ALTERNATIVES DEVELOPMENT
Task 1 – Project Management
Task 2 – Alternatives Development
2a – Develop Objectives
2b – Develop General Response Actions
2c – Identify Potential Technologies
2d – Evaluate Process Options
2e – Assemble Alternatives
2f – Identify/ Action Specific ARARs
Task 3 – Alternatives Screening
3a – Refine Objectives
3b – Define Alternatives
3c – Screen Alternatives
3d – Verify/Action Specific ARARs
3e – [illegible]
Task 4 – Report
4a – Prepare [illegible]
4b – Review [illegible]

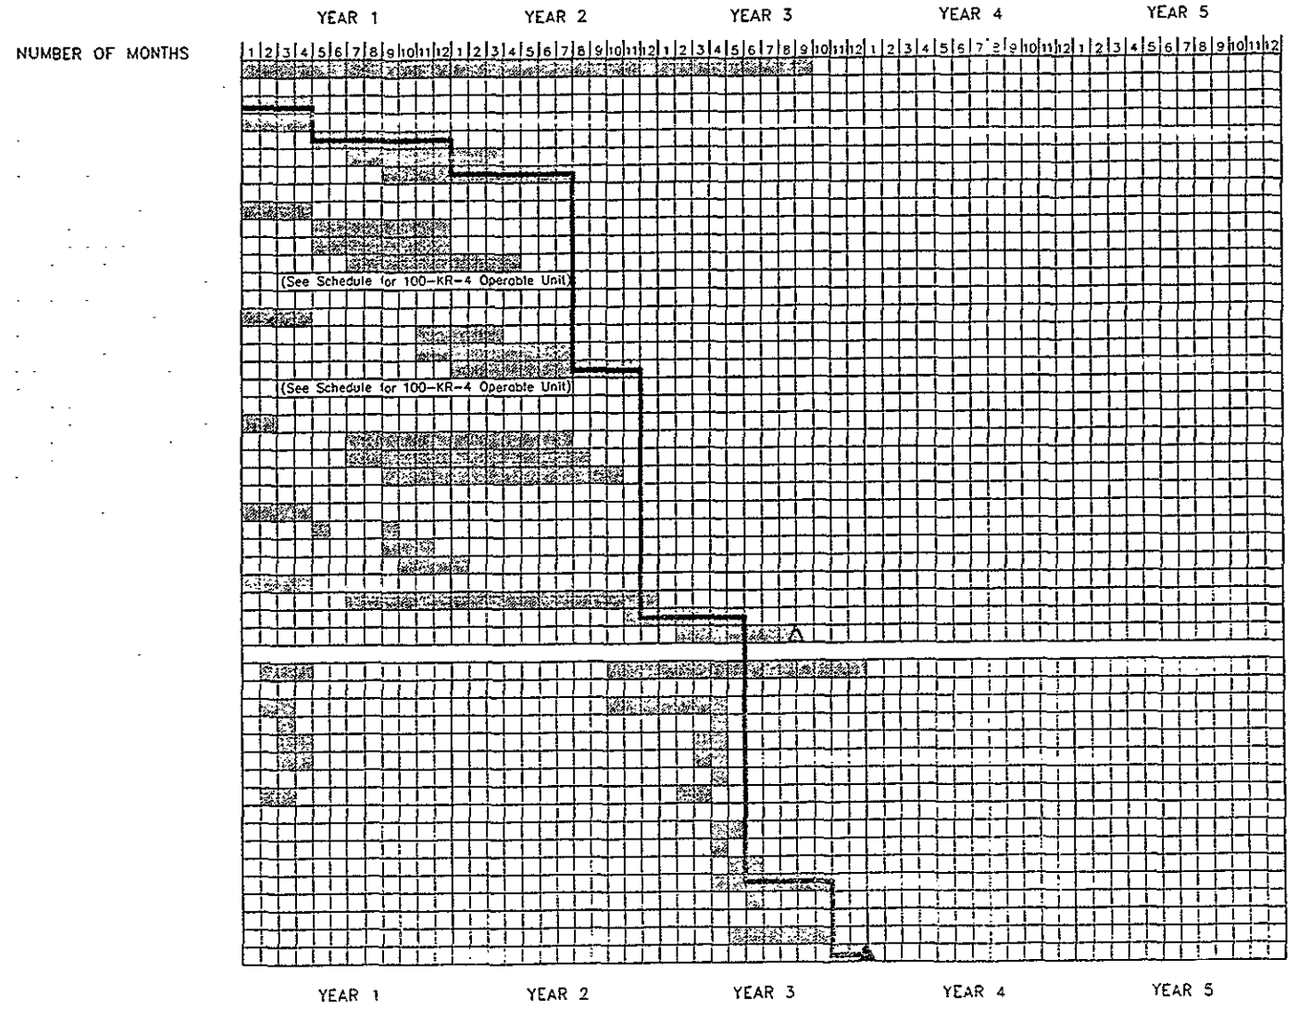

Figure 6-1. RI/FS Schedule for the 100-KR-1 Operable Unit. (Pg. 1 of 2)

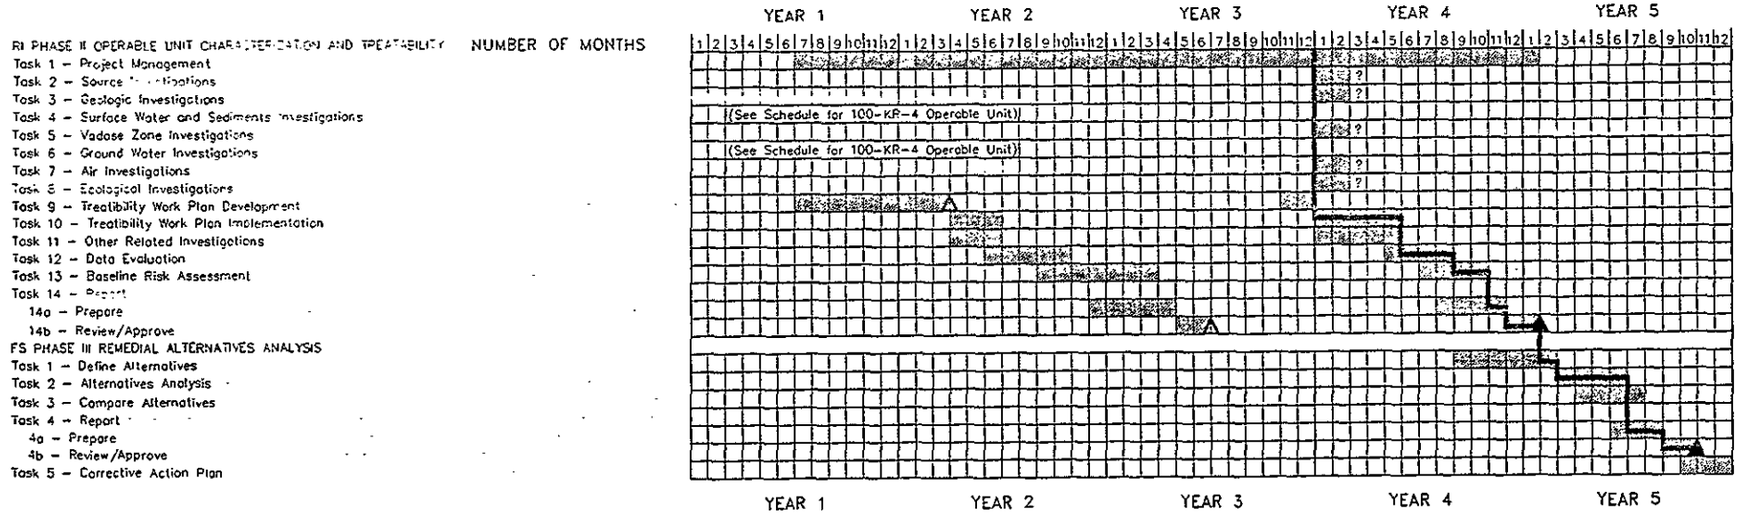

(1) ALL SURFACE SURVEYS INCLUDED; ASSUMES 80 FEET DEEP SOIL BORINGS, 2 WEEKS TO COMPLETE EACH, AND ONE DRILL RIG USED.

(2) ASSUMES 45 DAYS TURNAROUND FOR LABORATORY ANALYSIS PLUS 30 TO 60 DAYS TO COMPLETE DATA VALIDATION.

(3) ASSUMES DATA WILL BE DEVELOPED FROM PREVIOUS OPPERABLE UNIT STUDIES.

(4) ASSUMES 30 DAY TURNAROUND FOR LABORATORY ANALYSIS.

(5) ASSUMES 40 FOOT DEEP SOIL BORINGS, 1 WEEK TO COMPLETE EACH, AND ONE DRILL RIG USED

(6) ASSUMES SAMPLING WILL BE CONDUCTED AFTER DATA REVIEW FROM 100-KR-4 STUDIES.

(7) THIS TASK WILL INCLUDE EVALUATION OF DATA DEVELOPED FROM OTHER RI/FS AND RFI/CMS INVESTIGATIONS

LEGEND

- ACTIVITY DURATION
- ▲ PRIMARY REPORT ISSUED AND APPROVED
- △ SECONDARY REPORT ISSUED AND APPROVED
- CRITICAL PATH

Figure 6-1. RI/FS Schedule for the 100-KR-1 Operable Unit. (Pg. 2 Of 2)

7.0 PROJECT MANAGEMENT

Execution of the project management plan will require that all activities be performed cooperatively between subcontractor, Westinghouse Hanford, DOE, EPA, and Ecology personnel.

The progress in completing the 100-KR-1 operable unit work plan will be documented through monthly project activity reports, unit manager meetings, and technical interchanges. Project management tasks will include:

- Writing, reviewing, and commenting on documents
- Maintaining administrative record files
- Distributing documents and correspondence
- Maintaining formal change control system for modifying the work schedule in the work plan
- Determining financial and project tracking requirements
- Coordinating project activities between EPA, Ecology, DOE, Westinghouse Hanford and subcontractors
- Determining scoping study efforts (if required)
- Determining if interim remedial action is required
- Completing progress reports
- Attending technical interchange meetings.

These and other details of project management are discussed in Attachment 3 - project management plan.

9 0 1 1 8 3 0 2 7 1

THIS PAGE INTENTIONALLY
LEFT BLANK

8.0 REFERENCES

Allen, J. N. 1980, "The Ecology and Behavior of the Long-Billed Curlew, *Numenius Americanus Parvus,* in Southeastern Washington," *Wildlife Monograph,* 73:67.

American National Standards Institute/American Society of Mechanical Engineers (ANSI/ASME) 1986, *Quality Assurance Program Requirements for Nuclear Facilities,* ANSI/ASME NQA-1, New York, New York.

Atomic Energy Commission (AEC), GE Study Group for the Economic Development of Richland, 1964, *Catalogue of Hanford Buildings and Facilities,* Richland, Washington.

Beasley, T. M., L. A. Ball, J. E. Andrews III, and J. E. Halverson 1981, "Hanford-Derived Plutonium in Columbia River Sediments, *Science* Vol. 214, pp. 913-915.

Bisping, L. E. 1989, *Environmental Monitoring Master Sample Schedule,* PNL-6816, Pacific Northwest Laboratory, Richland, Washington.

Brown, D. J. 1989, *Geology Underlying Hanford Reactor Areas,* HW-69571, General Electric Company, Richland, Washington.

Chatters, J. C. (ed.), 1989, *Hanford Cultural Resources Management Plan,* PNL-6942, prepared for the U.S. Department of Energy, Pacific Northwest Laboratory, Richland, Washington.

Clough, Jr., R. G. 1971, *Reactor Plant Deactivation History 100-KE and K Plant,* DUN-7661, Douglas United Nuclear, Inc., Richland, Washington.

Cushing, C. E. 1979, "Trace Elements in a Columbia River Food Web," *Northwest Science,* Vol. 53, pp. 118-125.

Cushing, C. E. (ed.) 1988, *Hanford Site National Environmental Policy Act (NEPA) Characterization,* PNL-6415, Pacific Northwest Laboratory, Richland, Washington.

Dabrowski, T. E. 1979, *Environmental Impact of KE Basin Operation,* United Nuclear Industries, Inc., Richland, Washington.

DeMers, A. E. 1985, *KE Basin Sludge Sample,* UNC Nuclear Industries, Inc., Richland, Washington.

DOE, see U.S. Department of Energy.

DOE/RL, U.S. Department of Energy-Richland Operations Office.

Dorian, J. J. and V. R. Richards 1978, *Radiological Characterization of the Retired 100 Areas,* UNI-946, United Nuclear Industries, Inc., Richland, Washington.

Ecology, see Washington State Department of Ecology.

EPA, see U.S. Environmental Protection Agency.

ERDA, see U.S. Energy Research and Development Administration.

Evans, J. C., R. W. Bryce, and D. R. Sherwood 1989, *Hanford Site Groundwater Monitoring for January Through June 1988,* PNL-6315-3, Pacific Northwest Laboratory, Richland, Washington.

Fecht, K. R., S. P. Reidel, and A. M. Tallman 1985, *Paleodrainage of the Columbia River System on the Columbia Plateau of Washington: A Summary,* RHO-BW-SA-318P, Rockwell Hanford Operation, Richland, Washington.

Fitzner, R. E., W. H. Richard, L. L. Cadwell, and L. E. Rogers 1981, *Raptors of the Hanford Site and Nearby Areas of South-Central Washington,* PNL-3212, Pacific Northwest Laboratory, Richland, Washington.

Gee, G. Jr., 1987, *Hanford Site: Status Report,* PNL-6403, Pacific Northwest Laboratory, Richland, Washington.

Gee, G. W. and P. R. Heller 1985, *Unsaturated Water Flow at the Hanford Site: A Review of Literature and Annotated Bibliography,* PNL-5428, Pacific Northwest Laboratory, Richland, Washington.

General Electric Company 1964, *1963 Hazards Summary Report, Volumes 1, 2, and 3,* HW-74095, Hanford Atomic Products Operation, Richland, Washington.

Gephart, R. E., R. C. Arnett, R. G. Baca, L. S. Leonhart, F. A. Spane, Jr., D. A. Palumbo, and S. R. Strait 1979, *Hydrologic Studies Within the Columbia Plateau, Washington: An Integration of Current Knowledge,* RHO-BWI-ST-5, Rockwell Hanford Operation, Richland, Washington.

Graham, M. J., G. V. Last, and K. R. Fecht 1984, *An Assessment of Aquifer Intercommunication in the B Pond - Gable Mountain Pond Area of the Hanford Site,* RHO-RE-ST-12, Rockwell Hanford Operation, Richland Washington.

Hsieh, J.J.C., A. E. Reisenauer, and L. B. Brownell 1973, *A Study of Soil Matric Potential and Temperature in Hanford Soils,* BNWL-1712, Pacific Northwest Laboratory, Richland, Washington.

Jacquish, R. E., and P. J. Mitchell (eds.) 1988, *Environmental Monitoring at Hanford for 1987,* PNL-6464, Pacific Northwest Laboratory, Richland, Washington.

Jacquish, R. E. and R. W. Bryce (eds.) 1989, *Hanford Site Environmental Report for Calender Year 1988,* PNL-6825, Pacific Northwest Laboratory, Richland, Washington.

Kirkam, R. R. and G. W. Gee 1984, *Measurements of Unsaturated Flow Below the Root Zone at an Arid Site,* PNL-SA-116229, Pacific Northwest Laboratory, Richland, Washington.

Ledgerwood, R. K., C. W Meyers, and R. W. Cross 1978, *Pasco Basin Stratigraphic Nomenclature,* RHO-BWI-LD-I, Rockwell Hanford Operations, Richland, Washington.

Liikala, T. L., R. L. Aaberg, N. J. Aimo, D. J. Bates, T. J. Gilmore, E. J. Jensen, G. V. Last, P. L. Oberlander, K. B. Olsen, K. R. Oster, L. R. Roome, J. C. Simpson, S. S. Teel, and E. J. Westergard 1988, *Geohydrologic Characterization of the Area Surrounding the 183-H Solar Evaporation Basins,* PNL-6728, Pacific Northwest Laboratory, Richland, Washington.

McCain, R. G. and W. L. Johnson 1990, *A Proposed Data Quality Strategy for Hanford Site Characterization,* WHC-SD-EN-AP-023, Westinghouse Hanford Company, Richland, Washington.

McCormack, W. D. and J.M.V. Carlile 1984, *Investigation of Groundwater Seepage from the Hanford Shoreline of the Columbia River,* PNL-5289, Pacific Northwest Laboratory, Richland, Washington.

McGavock, E. H., W. D. Wiggins, R. L. Blazs, P. R. Boucher, L. L Reed, and M. L. Smith 1987, *Water Resources Data Washington, Water Year 1985,* Water-Data Report WA-85-1, U.S. Geological Survey, Tacoma, Washington.

McGhan, V. L. 1989, *Hanford Wells,* PNL-6907, Pacific Northwest Laboratory, Richland, Washington.

McGhan, V. L., P. J. Mitchell, and R. S. Argo 1985, *Hanford Wells,* ONL-5397, Pacific Northwest Laboratory, Richland, Washington.

McHenry, J. R. 1957, *Properties of Soils of the Hanford Project,* HW-53218, Hanford Atomic Products Operations, General Electric Company, Richland, Washington.

Myers, C. W., S. M. Price, J.A. Caggiano, M. P. Cochran, W. H. Czimer, N. J. Davidson, R. C. Edwards, K. R. Fecht, G. E. Holmes, M. G. Jones, J. R. Kumnk, R. D. Landon, R. K. Ledgerwood, J. T. Lillie, P. E. Long, T. H. Mitchell, E. H. Price, S. P. Reidel, and A. M. Tallman 1979, *Geologic Studies of the Columbia Plateau: A Status Report,* RHO-BWI-ST-4, Rockwell Hanford Operations, Richland, Washington.

PNL 1987, *Environmental Monitoring at Hanford for 1986,* PNL-6120, Pacific Northwest Laboratory, Richland, Washington.

Relander, C. 1956, *Drummers and Dreamers,* Caston Printers, Caldwell, Idaho.

Rice, D. G. 1980, *Overview of Cultural Resources on the Hanford Reservation in South Central Washington State,* U.S. Department of Energy-Richland Operations Office, Richland, Washington.

Rickard, W. H. and K. R. Price, 1989, *Strontium-90 in Reed Canary Grass and Canada Goose Eggshells from the Columbia River, Washington,* PNL-SA-16118, Pacific Northwest Laboratory, Richland, Washington.

Rickard, W. H., J. D. Hedlund, and R. J. Schreckhise 1978, "Rejecta Cast from Heron Nests as an Indicator of Food Chain Contamination," *Auk,* Vol. 95, pp. 425-427.

Robertson, D. E. and J. J. Fix 1977, *Association of Hanford Origin Radionuclides with Columbia River Sediment,* BNWL-2305, Pacific Northwest Laboratory, Richland, Washington.

Routson, R. C., M. R. Fuchs, and W. A. Jordon 1988, *Recharge Estimate for the Hanford Site 200 Areas Plateau,* WHC-EP-0046, Westinghouse Hanford Company, Richland, Washington.

Schalla, R., R. W. Wallace, R. L. Aaberg, S. P. Airhart, D. J. Bates, J. M. Carlile, C. S. Cline, D. I. Dennison, M. D. Freshly, P. R. Heller, E. J. Jensen, K. B. Olsen, R. G. Parkhurst, J. T. Rieger, and E. J. Westergard 1988, *Interim Characterization Report for the 300 Area Process Trenches,* PNL-6716, Pacific Northwest Laboratory, Richland, Washington.

Stenner, R. D., K. H. Cramer, K. A. Higley, S. J. Jette, D. A. Lamar, T. J. McLaughlin, D. R. Sherwood, and N. C. Van Houten 1988, *Hazard Ranking System Evaluation of CERCLA Inactive Waste Sites at Hanford,* PNL-6456, 3 vols., Pacific Northwest Laboratory, Richland, Washington.

Sula, M. J. 1980, *Radiological Survey of Exposed Shoreline and Islands of the Columbia River Between Vernita and the Snake River Confluence,* PNL-3127, Pacific Northwest Laboratory, Richland, Washington.

Swanson, D. A., T. L. Wright, P. R. Hooper, and R. D. Bently 1979, *Revisions in Stratigraphic Nomenclature of the Columbia River Basalt Group,* Bulletin 1467, U.S. Geological Survey, Washington, D.C.

Tallman, A. M., J. T. Lillie, and K. R. Fecht 1981, "Superbasalt Sediment of the Cold Creek Syncline Area," *Subsurface Geology of the Cold Creek Syncline,* C. W. Myers and S. M. Price, eds., RHO-BWI-ST-14, Rockwell Hanford Operations, Richland, Washington.

Tolan, T. L. and S. P. Reidel 1989, *Revision to Estimates of the Areal Extent and Volume of the Columbia River Basalt Group,* Special Paper 239, Geological Society of America, Boulder, Colorado.

U.S. Department of Energy 1982, *Site Characterization Report for the Basalt Waste Isolation Project,* DOE/RL-82-3, 3 vols., U.S. Department of Energy-Richland Operations Office, Richland, Washington.

U.S. Department of Energy 1987, *Final Environmental Impact Statement, Disposal of Hanford Defense High-Level, Transuranic and Tank Waste,* DOE/EIS-0113, 5 vols., U.S. Department of Energy-Richland Operations Office, Richland, Washington.

U.S. Department of Energy 1988, *Consultation Draft, Site Characterization Plan, Reference Repository Location,* DOW/RW-0164, Vol. 2 of 9, Office of Civilian Radioactive Waste Management, U.S. Department of Energy, Washington, D.C.

U.S. Department of Energy-Richland Operations Office 1988, *Hanford Site Waste Management Units Report,* DOE/RL-88-30, Richland, Washington.

U.S. Energy Research and Development Administration (ERDA) 1975, *Final Environmental Statement, Waste Management Operations,* ERDA-1538, Hanford Site, Richland, Washington.

U.S. Environmental Protection Agency (EPA) 1976, *National Interim Primary Drinking Water Regulations,* EPA-570/9-76-003, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1983, *Interim Guidelines and Specifications for Preparing Quality Assurance Project Plans,* PB83-170514, Office of Exploratory Research, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1985, *Remedial Action Closing Procedures Manual 4,* EPA/600/8-87/049, OSWER Dir. 9355.0-10, U.S. Environmental Protection Agency, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1986a, *Superfund Public Health Evaluation Manual,* EPA/540/1-86-001, Office of Emergency and Remedial Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1986b, *Test Methods for Evaluating Solid Waste,* (SW-846) 3rd Edition, Office of Solid Waste and Emergency Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1987, *Data Quality Objectives for Remedial Response Activities,* OSWER Dir. 9335.0-7B, EPA/540/G-87/003, Office of Emergency and Remedial Response and Office of Waste Program Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1988a, *Guidance for Conducting Remedial Investigations and Feasibility Studies Under CERCLA, Interim Final,* OSWER Dir. 9355.3-01, EPA/540/G-89/004, October, Office of Solid Waste and Emergency Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1988b, *Superfund Exposure Assessment Manual,* OSWER Dir. 9285.5-1, EPA/540/I-88/001, Office of Solid Waste and Emergency Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1988c, *NPL Candidate: U.S. DOE Hanford 100 Area,* Region X, Seattle, Washington.

U.S. Environmental Protection Agency (EPA) 1988d, *CERCLA Compliance with Other Laws Manual,* OSWER 9234.1-01, August 8, 1988, Office of Emergency and Remedial Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1989a, *Risk Assessment Guidance for Superfund, Volume I, Human Health Evaluation Manual,* Office of Solid Waste and Emergency Response, Washington, D.C.

U.S. Environmental Protection Agency (EPA) 1989b, *Risk Assessment Guidance for Superfund, Volume II, Environmental Evaluation Manual,* Office of Solid Waste and Emergency Response, Washington, D.C.

U.S. Geological Survey 1986a, *Vernita Bridge 7.5-Minute Topoghraphic Quadrangle,* Provisional Edition, USGS, Denver, Colorado.

U.S. Geological Survey 1986b, *Coyote Rapids 7.5-Minute Topographic Quadrangle,* Provisional Edition, USGS, Denver, Colorado.

Washington State Department of Ecology, U.S. Environmental Protection Agency, and U.S. Department of Energy 1989, *Hanford Federal Facility Agreement and Consent Order,* Richland, Washington, May 1989.

Washington Department of Natural Resources 1987, *Endangered, Threatened, and Sensitive Vascular Plants of Washington,* Washington Natural Heritage Program, Olympia, Washington.

Washington Department of Wildlife 1987, *Threatened and Endangered Wildlife in Washington,* Olympia, Washington.

Westinghouse Hanford Company 1987, *Environmental Surveillance Data Set,* WHC-EP-0160, Richland, Washington.

Westinghouse Hanford Company 1989a, *Quality Assurance,* WHC-CM-4-2, Richland, Washington.

Westinghouse Hanford Company 1989b, *Preliminary Operable Units Designation Project,* WHC-EP-0216, Richland, Washington.

Westinghouse Hanford Company 1989c, *Environmental Investigations and Site Characterization Manual,* WHC-CM-7-7, Richland, Washington.

Watson, D. G. 1970, *Fall Chinook Salmon Spawning in the Columbia River Near Hanford 1947-1967,* BNWL-1515, Pacific Northwest Laboratory, Richland, Washington.

Federal Regulations

U.S. Nuclear Regulatory Commission, *Standards for Protection Against Radiation,* Title 10, Code of Federal Regulations, Part 20, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *National Primary and Secondary Ambient Air Quality Standards,* Title 40, Code of Federal Regulations, Part 50, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *National Emission Standards for Hazardous Air Pollutants*, Title 40, Code of Federal Regulations, Part 61, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *National Primary Drinking Water Regulations*, Title 40, Code of Federal Regulations, Part 141, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *Environmental Radiation Protection Standards for Nuclear Power Operations*, Title 40, Code of Federal Regulations, Part 190, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *Environmental Radiation Protection Standards for Management and Disposal of Spent Nuclear Fuel, High-Level and Transuranic Radioactive Wastes*, Title 40, Code of Federal Regulations, Part 191, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *Health and Environmental Protection Standards for Uranium and Thorium Mill Tailings*, Title 40, Code of Federal Regulations, Part 192, as amended, Washington, D.C.

U.S. Environmental Protection Agency, *Identification and Listing of Hazardous Waste*, Title 40, Code of Federal Regulations, Part 261, Washington, D.C.

U.S. Environmental Protection Agency, *National Oil and Hazardous Substances Pollution Contingency Plan*, Title 40, Code of Federal Regulations, Part 300, Washington, D.C.

U.S. Environmental Protection Agency, *Polychlorinated Biphenyls (PCBs) Manufacturing, Processing, Distribution in Commerce, and Use Prohibitions*, Title 40, Code of Federal Regulations, Part 761, as amended, Washington, D.C.

State Regulations

Ecology, *Water Quality Standards for Waters of the State of Washington,* Chapter 173-201, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Dangerous Waste Regulations,* Chapter 173-303, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Minimum Functional Standards for Solid Waste Handling,* Chapter 173-304, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Ambient Air Quality Standards and Emission Limits for Radionuclides,* Chapter 173-480, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Health, Board and Division of Department of Social and Health Services,* Chapter 248, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Standards of Protection Against Radiation*, Chapter 402-24, as amended, Washington Administrative Code, Olympia, Washington.

Ecology, *Monitoring and Enforcement of Air Quality and Emission Standards for Radionuclides,* Chapter 402-80, as amended, Washington Administrative Code, Olympia, Washington.

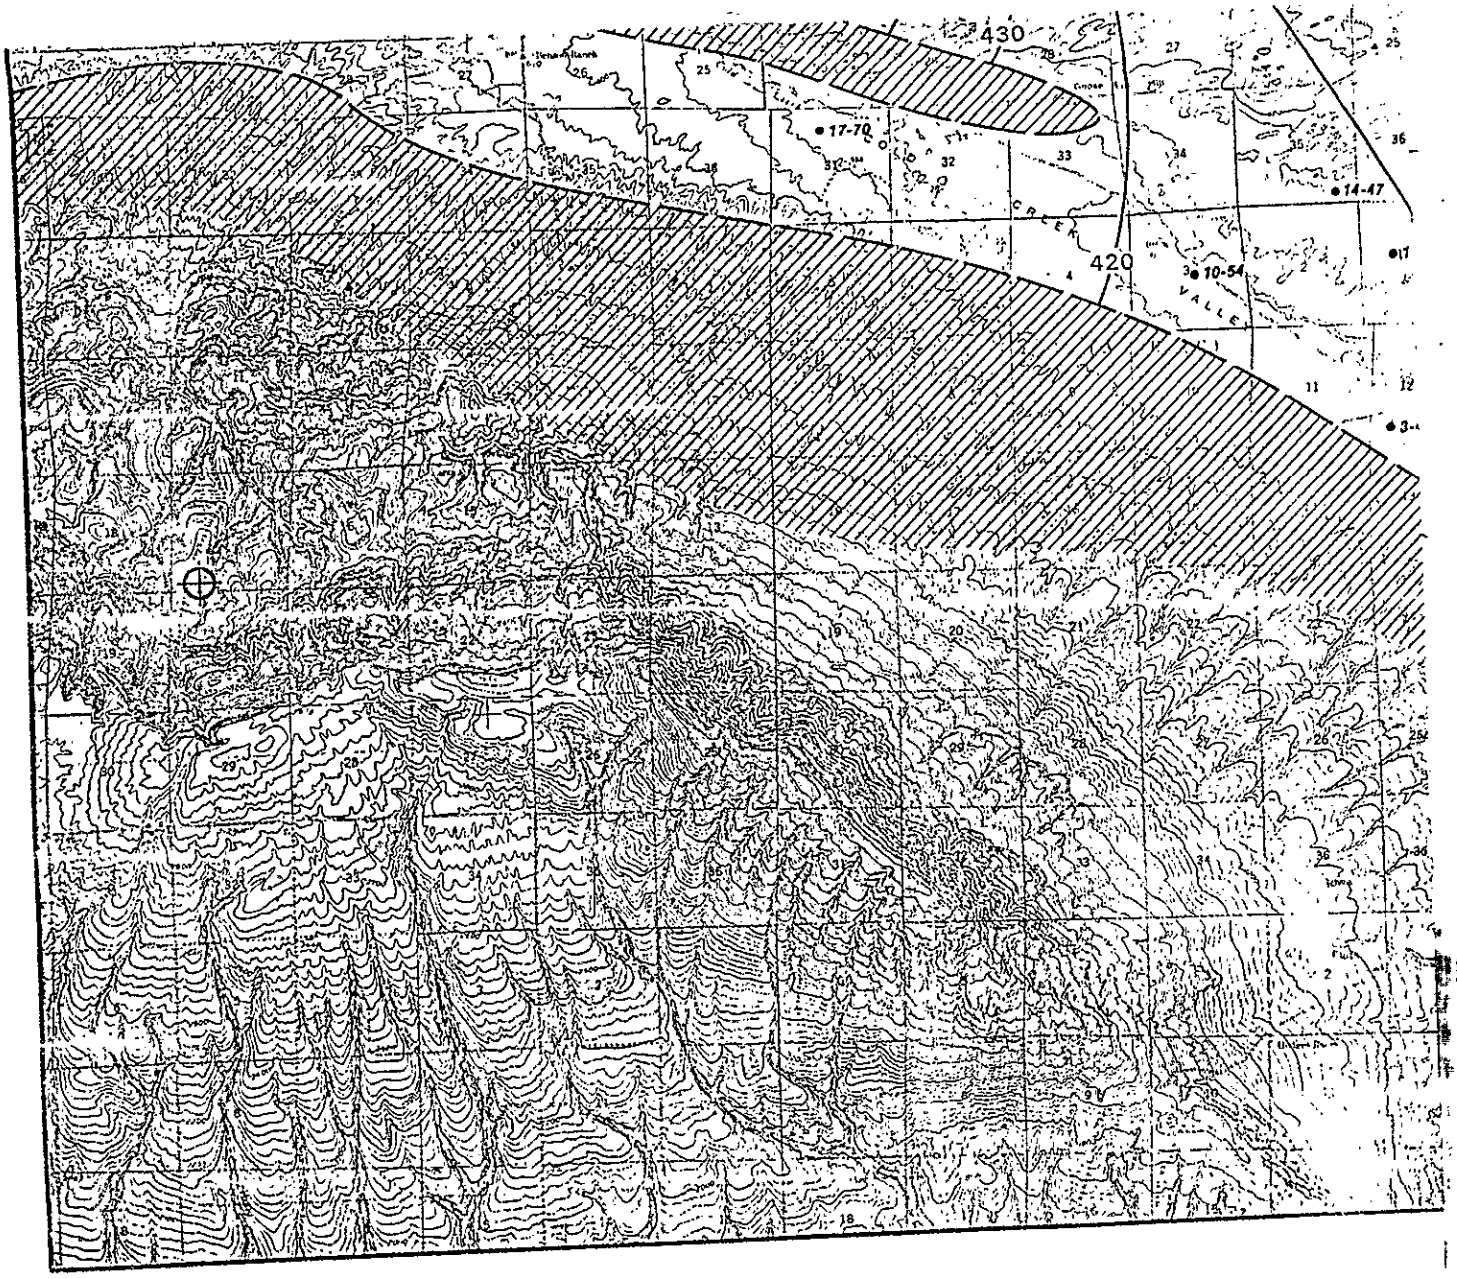

SCALE

0 1 2 3 MILES

0 1 2 3 4 KILOMETERS

GN MIN

1° 43′ / 31 MILS

21° / 373 MILS

UTM GRID AND 1951
MAGNETIC NORTH
DECLINATION AT
CENTER OF SHEET

PLATE 1. HANFORD SITE WAT

THIS PAGE INTENTIONALLY
LEFT BLANK

Attachment 1

SAMPLING AND ANALYSIS PLAN

9 0 1 1 0 3 1 3 0 2 0 1 3

THIS PAGE INTENTIONALLY
LEFT BLANK

1.0 INTRODUCTION

1.1 BACKGROUND

The U.S. Environmental Protection Agency (EPA) has included the 100 Area at the Hanford Site on the National Priorities List (NPL) under the Comprehensive Environmental Response, Compensation, and Liability Act of 1980. The 100-K Area has been divided into three source or surface operable units (100-KR-1, 100-KR-2, and 100-KR-3), and one ground water operable unit (100-KR-4), for the purpose of focusing and managing the necessary environmental investigations, studies, and actions. Air, sources, soil, and terrestrial biota are being addressed in the 100-KR-1 operable unit. Details of this operable unit are presented in the text of the work plan.

1.2 PURPOSE AND OBJECTIVES

The purpose of the sampling and analysis plan (SAP) is to describe field procedures and sample locations that will be used to meet the specific objectives for each field task described in Chapter 5.0 of the work plan. This document will not, however, include the detailed descriptions of all of the field procedures that are typically found in an SAP. Instead, wherever possible, specific procedures will be referred to the latest version of the Westinghouse Hanford environmental investigations and instructions (EII); WHC-CM-7-7 (WHC 1989). This is done to provide a level of consistency of data collection methods (and ultimately data quality and usability) employed at the 100-KR-1 operable unit and with those used at other areas within the Hanford Site. A copy of the EII must be used in conjunction with this SAP. It is important that the procedures in these documents be referenced and followed.

1.3 CONTENTS

This SAP consists of two parts:

- Part 1--Field Sampling Plan (FSP)
- Part 2--Quality Assurance Project Plan (QAPP)

The FSP and QAPP each conform with EPA guidance with respect to content and format (EPA 1988). All procedures (including participant contractor or subcontractor procedures) required for this project shall be approved as being in compliance with Westinghouse Hanford criteria.

2.0 REFERENCES

U.S. Environmental Protection Agency, 1988, *Guidance for Conducting Remedial Investigations and Feasibility Studies Under CERCLA (Interim Final)*, EPA/540/G-89/004, OSWER Directive 9335.3-01, Office of Solid Waste and Emergency Response, Washington, D.C.

Westinghouse Hanford Company, 1989, *Environmental Investigations and Site Characterization Manual*, WHC-CM-7-7, Richland, Washington.

Part 1

FIELD SAMPLING PLAN

9 0 1 1 3 9 2 0 2 9 4

THIS PAGE INTENTIONALLY
LEFT BLANK

CONTENTS

1.0 Introduction . . . . . FSP 1

2.0 Task 1 - Source Investigation . . . . . FSP 2

3.0 Task 2 - Geologic Investigation . . . . . FSP 3
3.1 Subtask 2a - Data Compilation and Review . . . . . FSP 3
3.2 Subtask 2b - Topographic Base Map Development . . . . . FSP 3
3.2.1 Survey Equipment and Procedures . . . . . FSP 4
3.3 Subtask 2c - Field Activities . . . . . FSP 4
3.3.1 Site Walkover Survey . . . . . FSP 5
3.3.2 Surface Radiation Survey . . . . . FSP 6
3.3.3 Soil Gas Survey . . . . . FSP 8
3.3.4 Electromagnetic Induction/Magnetometer (EMI/MAG) Survey . . . . . FSP 9
3.3.5 Ground Penetrating Radar (GPR) Survey . . . . . FSP 11
3.3.6 Process Effluent and Discharge Pipeline Integrity . . . . FSP 11
3.3.7 Source Sampling . . . . . FSP 12
3.4 Subtask 2d - Laboratory Analysis . . . . . FSP 21
3.5 Subtask 2e - Data Evaluation . . . . . FSP 21

4.0 Task 3 - Geologic Investigation . . . . . FSP 22
4.1 Subtask 3a - Data Compilation and Review . . . . . FSP 22
4.2 Subtask 3b - Field Activities . . . . . FSP 22
4.2.1 Surface Mapping . . . . . FSP 22
4.2.2 Geologic Logging . . . . . FSP 23
4.3 Subtask 3c - Laboratory Analysis . . . . . FSP 23
4.4 Subtask 3d - Data Evaluation . . . . . FSP 23

5.0 Task 4 - Surface Water and Sediments Investigation . . . . . FSP 23

6.0 Task 5 - Vadose Investigations . . . . . FSP 27
6.1 Subtask 5a - Data Compilation and Review . . . . . FSP 27
6.2 Subtask 5b - Field Activities . . . . . FSP 27
6.2.1 Borehole Siting . . . . . FSP 28
6.3 Subtask 5c - Laboratory Analysis . . . . . FSP 31
6.4 Subtask 5d - Data Evaluation . . . . . FSP 31

7.0 Task 6 - Ground Water Investigations . . . . . FSP 32

8.0 Task 7 - Air Investigations . . . . . FSP 32
8.1 Subtask 7a - Field Activities . . . . . FSP 32
8.2 Subtask 7b - Field Activities . . . . . FSP 32
8.3 Subtask 7c - Laboratory Analysis . . . . . FSP 33
8.4 Subtask 7d - Data Evaluation . . . . . FSP 33

9.0 Task 8 - Ecological Investigation . . . . . FSP 33
9.1 Subtask 8a - Compile and Review Existing Data . . . . . FSP 34
9.2 Subtask 8b - Field Activities . . . . . FSP 34
9.3 Subtask 8c - Laboratory Analysis . . . . . FSP 35
9.4 Subtask 8d - Data Evaluation . . . . . FSP 35

10.0 Task 9 - Cultural Resources Investigations . . . . . FSP 35

11.0 Task 10 - Data Evaluation . . . . . FSP 36

12.0 Task 11 - Baseline Risk Assessment . . . . . FSP 36

13.0 Task 12 - RI Phase Report: Preliminary Operable Unit Characterization Summary . . . . . FSP 36

14.0 Standard Field Procedures . . . . . FSP 36
14.1 Sample Designation . . . . . FSP 37
14.1.1 Facility Association . . . . . FSP 37
14.1.2 Type of Sample with Sample Number . . . . . FSP 37
14.1.3 Depth of Sample . . . . . FSP 37
14.1.4 Analysis of Samples . . . . . FSP 38
14.2 Sample Equipment and Procedures . . . . . FSP 39
14.3 Sample Handling . . . . . FSP 39

FIGURES

FSP-1 Proposed Sampling Locations for 100-KR-1 Source Investigations . . FSP 18
FSP-2 Proposed Sampling Locations for Soil Investigation . . . . . FSP 29

TABLES

FSP-1 Proposed Samples for 100-KR-1 Source Investigations . . . . . FSP 14
FSP-2 100-KR-1 Operable Unit Chemical and Physical Analyses . . . . . FSP 16
FSP-3 Proposed Samples for the 100-KR-1 Vadose Investigations . . . . . FSP 24

9 0 1 1 8 3 0 2 9 7

THIS PAGE INTENTIONALLY
LEFT [illegible]

1.0 INTRODUCTION

This field sampling plan (FSP) is Part 1 of Attachment 1, sampling and analysis plan (SAP), of the RI/FS work plan for the 100-KR-1 operable unit. This plan provides direction for obtaining field samples to implement the RI/FS and is designed for use with the 100-KR-1 operable unit work plan, attachments to that plan, and referenced procedures. This plan references many of the sampling and related procedures to the Westinghouse Hanford Company, *Environmental Investigations and Site Characterization Manual* (WHC-CM-7-7).. Sampling contractors should be familiar with WHC 1989 and the SAP and use them as ready reference for daily guidance.

The work plan contains important summaries on the background and physical setting of 100-KR-1 in the first three sections and a description of the objectives of the SAP in Chapter 5.0. The work plan also contains a list of acronyms, abbreviations and a glossary of terms used in this plan. Field personnel should be aware of the project schedule contained in Chapter 6.0 of the work plan (or the most recent update of that schedule).

The quality assurance project plan (QAPP) is an integral part of the SAP (Part 2 of the Attachment 1) and must be used concurrently with this FSP. The QAPP references the sampling equipment and procedures, and analytical procedures and quality assurance requirements that must be used to obtain valid representative field samples and measurements. Knowledge of the health and safety plan (HSP, Attachment 2) is critical during field sampling because it specifies procedures for the protection of project field personnel. The data management plan (DMP, Attachment 4) denotes the requirements for field notebooks and data procedures.

The FSP is organized by RI Phase I tasks, subtasks, and activities. For completeness, those RI/FS Phase I components not concerned with field sampling or measurements or that are part of the 100-KR-4 RI are also briefly addressed in this plan. If additional field sampling or measurement requirements are necessary in the operable unit characterization or other phases of the project, this plan will incorporate such requirements by amendment according to Chapter 3.0 of the project management plan (PMP, Attachment 3).

The RI Phase I program includes the following tasks:

- Task 1 - Project Management
- Task 2 - Source Investigations
- Task 3 - Geologic Investigations
- Task 4 - Surface Water and Sediments Investigations
- Task 5 - Vadose Investigations
- Task 6 - Ground Water Investigations
- Task 7 - Air Investigations
- Task 8 - Ecological Investigations
- Task 9 - Cultural Resources Investigations
- Task 10 - Data Evaluation
- Task 11 - Baseline Risk Assessment
- Task 12 - RI Phase I Report: Preliminary operable unit characterization summary

Standard field procedures are also summarized in this FSP. The sampling approach taken in this work plan is to phase activities, starting with source evaluation and noninvasive surveys, followed by a source sampling program and a phased boring program based on information from the preceding sampling efforts. Sampling and analysis options will be evaluated during the program to ensure that the data collected are sufficient and of adequate quality for their intended uses. The data quality objectives process will be revised, as needed, based on the results of each data collection and analysis activity.

2.0 TASK 1 - PROJECT MANAGEMENT

The project management task does not involve any field activities and is discussed in Section 5.1 of the 100-KR-1 work plan and Attachment 3, PMP.

3.0 TASK 2 - SOURCE INVESTIGATIONS

This task is designed to provide necessary information regarding the location and types of hazardous substances used, and the structure and integrity of certain facilities within the operable unit. The investigation will be conducted using the following subtasks:

- Subtask 2a - Data compilation and review
- Subtask 2b - Topographic base map development
- Subtask 2c - Field activities
- Subtask 2d - Laboratory analysis
- Subtask 2e - Data evaluation

3.1 SUBTASK 2a - DATA COMPILATION AND REVIEW

This subtask does not require field investigation, but does include conducting interviews. The results of this task may modify subsequent tasks. Details of this activity are described in Section 5.2.2.1 of the work plan.

3.2 SUBTASK 2b - TOPOGRAPHIC BASE MAP DEVELOPMENT

A topographic base map will be prepared to show the 100-K Area. The base map will be developed as part of the planned activities in the 100-KR-4 work plan or, if available, from the Hanford Site base map currently under development.

Horizontal control will be established on two points at each grid location required for the surveys. The horizontal plane survey accuracy will be 1 ft (±0.3 m). Relative coordinates for the remainder of the grids will be obtained by using a tape and compass traverse or by Global Positioning Satellite instruments and electronic distance measuring instruments tied to these reference points. Grid point locations will be staked with coordinates marked on the stakes. Adequate vertical control will be provided by the topographic base map.

Locations of soil borings and surface soil samples described in Task 3 will be surveyed for both horizontal coordinates and vertical elevations. The horizontal plane survey accuracy will be ±1 ft (±0.3 m). The vertical plane

survey must be accurate to ±0.1 ft (±0.03 m). The elevation will be obtained at the ground surface of the borehole or surface sample locations.

The locations of all surveyed facilities, areas of interest, and anomalies discovered as a result of various surveys will be plotted on the topographic base map. The base map will be developed showing contour intervals of 1.5 ft (0.5 m) and at a scale of 1:2,000. The base map will include site features observed during the site walkover survey; results and location of EMI/MAG, GPR, soil gas, surface radiation and pipeline integrity surveys; grids; biological and geological reconnaissance observations; the locations and elevations of soil borings and surface soil samples; and any other relevant information that lends itself to graphic display in plan view. Overlays will be developed for the base map to plot each separate and distinct data set.

3.2.1 Survey Equipment and Procedures

Surveys are to be completed by a surveyor who is licensed and registered in the state of Washington. Vertical control will be referenced to a United States Geological Survey (USGS) datum obtained from a permanent benchmark. Third-order plane surveys and horizontal angular measurements will be made with a 20-second or better transit. Angles will be doubled, with the mean of the double angle within 10 seconds at the first angle. Distance measurements will be made with a calibrated tape or with a calibrated electronic distance measuring instrument (EDMI). When using an EDMI, the manufacturer's parts per million (ppm) error will be applied as well as corrections for curvature and refraction. Global Positioning Satellite surveying techniques may also be used.

Additional details on the surveying equipment and procedures shall be specified in approved participant contractor procedures. Procedural approval and control are described in Chapter 4.0 of the QAPP.

3.3 SUBTASK 2c - FIELD ACTIVITIES

Field activities within the 100-KR-1 operable unit source investigation include:

- Site walkover survey
- Surface radiation survey
- Soil gas survey

- Electromagnetic induction magnetometer survey
- Ground penetrating radar survey
- Process effluent and discharge pipeline integrity assessment
- Source sampling.

Prior to initiating field survey activities, a grid system will be surveyed over the 100-KR-1 operable unit to facilitate precise orientation of subsequent field work. The grid spacing will be 100 ft (33 m) and will be oriented N-S and E-W. An alpha numeric designation will be assigned to grid lines such that E-W lines are assigned alpha identifiers (i.e., A, B, C, etc.) and N-S lines numeric (i.e., 1, 2, 3, etc.). The grid will be superimposed onto the base map and all subsequent field observations will be located using tape and compass relative to node points.

3.3.1 Site Walkover Survey

A technical team will walk the entire area with an individual having knowledge of current and previous site conditions to identify potential features of concern that have not been discovered in the record search. No samples will be collected for analysis. However, areas of interest will be staked and recorded in preparation for future data gathering.

Special attention will be given to areas where there is evidence of past disturbances, mounded or subsided areas that may indicate buried facilities, old foundations, monuments indicating the location of items, and indications of former seepage, pits or drains, etc. Areas of potential concern will be staked, noted in a field logbook, and location recorded on the base map.

Although the focus of the walkover survey will be on visual observations, the survey team will be equipped with radiation survey and field volatile organic monitoring instruments for health and safety screening. Radiation exposure rates and airborne concentrations of volatile organics will be recorded. Soil vapor measurements will be made by opening a small hole with a shovel and taking a brief measurement with the field equipment. This information will supplement current knowledge and minimize the potential for unexpected exposure during subsequent tasks. All radiation level readings will be performed by health physics personnel.

3.3.2 Surface Radiation Survey

This activity is intended to locate areas of elevated radioactivity in the surface soil within the operable unit. Background surface radiation conditions will be determined so that meaningful comparisons can be made to the data obtained in the potentially affected areas.

3.3.2.1 Surface Radiation Survey Locations. The operable unit radiation survey will be a one-time event and will include determining the natural radiation background and the associated statistical variation, as well as performing a comprehensive survey of the 100-KR-1 operable unit.

A background plot will be established for the 100-KR-1 operable unit based on the site walkover survey. An approximately 9,514 ft^2 (2,900 m^2) area will be selected outside of the 100-KR-1 source operable unit boundaries, based on the absence of radiation-related operations and an initial radiation survey. The area will be used for determining background surface radiation levels for comparison to the 100-KR-1 operable unit levels. If an appropriate area is not found, the background plot for the 100-BC-1 operable unit may be used. If a hand-held manual radiation detection system is used, measurements at the background plot will be conducted at intersecting points on approximately 25 ft (8 m) transects (in relation to the 100 ft [33 m] staked grid) to obtain discrete readings at each point. The grid measurement will be a combination of transects so that each grid node is measured twice. The grid system described above is an estimate and is subject to modification.

As a potential alternative to conducting the surface radiation survey entirely with portable (i.e., hand-held) radiation detectors, an integrated vehicle-mounted and backpack-mounted computer based radiation mapping system will be evaluated. Such systems currently exist, and by the time the 100-KR-1 operable unit RI is initiated, it is expected that updated versions of these systems will be available.

3.3.2.2 Surface Radiation Survey Methods. Grid coordinates for the background plot will be designated A, B, C, etc., along the length of the plot, and 1, 2, 3, etc., for the width of the plot. Each point measured will be designated by the combined grid coordinates (e.g., B2, C1) to allow rechecking measurements. Similar grids may also be used as secondary means of locating results for extensive surveys in an area. If the radiation survey is performed manually, field logbooks will be kept indicating the general location of the anomalies. If the radiation survey is performed by the vehicle-mounted computer based system, the locations of anomalies will be automatically entered

into the computer mapping system. The denoted locations will be precisely located as part of the survey.

The surface radiation survey will be conducted for alpha, beta, and gamma radiation using properly calibrated portable instruments (vehicle-mounted or hand-held, as appropriate). The field surveys will be primarily based on gamma surveys; however, alpha beta/gamma measurements will also be made. Because of self-absorption of alpha and beta radiation in the source material and the attenuation in moisture and dirt, alpha and beta radiation are difficult to monitor in the field. Furthermore, the thin windows required on alpha and beta instruments make them very susceptible to damage, hence the detectors are generally not placed near enough to contamination, when performing large area surveys in the field, to detect low levels of contamination. Because of these difficulties, gamma radiation will be used as the surrogate for all forms of contamination for most of the field survey. Alpha and beta measurements will be taken at 5 percent of the transect locations (and only chosen among all locations) where elevated levels of gamma radiation are detected. Furthermore, alpha measurements will specifically be taken in areas of known or suspected plutonium contamination.

The gamma survey will be performed using a sodium iodide (NaI) detector that is cross-calibrated to a tissue-equivalent detector designed to respond in rem or Sieverts per hour. The instrument will read out in counts per minute. The traverses between the measurement points will be traveled at a slow enough rate to allow continuous surveying, and actual measurements along and between the grid lines, using 25 ft (8 m) traverses, will be made using a scaler to allow accurate recording of the counts per minute at that point. Any areas with values above 25 mR/h will be staked and shown on the topographic base map.

The surveys may be performed using the USRADS (CHEMRAD Tennessee Corporation) telemetry tracking system. This system provides for accurate tracking and automatic data input of the location and numeric value of measurements.

Details on surface radiation survey equipment and procedures will be developed. These will either be Westinghouse Hanford procedures developed in accordance with EII 1.2 "Preparation and Revision of Environmental Investigation Instructions" (WHC 1989) or participant contractor or subcontractor procedures approved and controlled as specified in Chapter 4.0 of the QAPP. These procedures will include details on equipment specifications, data logging equipment, and calibration and maintenance requirements.

Continuous recording equipment will be used to generate data along the grid lines during the surface radiation survey. Records of all calibrations and procedures will be maintained in a field notebook in accordance with EII 1.5 "Field Logbooks" (WHC 1989). Anomalies identified in the survey will be staked and plotted on the base map using the relative coordinates established in the topographic map development. The anomaly designation and coordinates will be marked on the stakes.

3.3.3 Soil Gas Survey

The objective of the soil gas survey is to identify areas where petroleum products or organic solvents may have been released. No field activities are currently planned for soil gas survey field investigations. These surveys will be conducted if new information is uncovered during data compilation and review or if anomalous or suspicious areas are discovered as part of other field studies. As a contingency, field activities that may be carried out are briefly discussed below.

3.3.3.1 Soil Gas Survey Locations. A soil vapor survey will be conducted over the surface areas of known or suspected contamination. Exact locations of these surveys will be based on the initial data review and various other field activities. Probes for the soil vapor survey will be installed on an appropriate grid scale at locations of known or suspected contamination.

For all soil gas survey areas, the extent of contamination will be determined by installing additional probes until no detectable contamination is found in two adjacent probes bounding the area.

Probes will be installed to an approximate 4-ft (1.3-m) depth at all locations. Installation of additional deep probes to about 30 or 40 ft (10 or 13 m) using vibratory techniques will be evaluated prior to initiating the survey. Final depth at any individual location will depend on subsurface obstructions.

3.3.3.2 Soil Gas Survey Method. Soil gas survey techniques will proceed as per EII 5.9 "Soil Gas Sampling." (WHC 1989), which is in development. However, if the method has not been developed, the following procedures will be used.

Equipment required to conduct the soil gas survey includes: (a) stainless steel probes, (b) gas-tight fittings for the probes, (c) vacuum pump for purging and sampling, and (d) sample containers (may include gas-tight syringes, stainless steel cylinders, Tevlar bags, glass sample bulbs). Complete details on

equipment and procedures for soil gas probe installation, penetrating and sealing pavement, purge volumes, sample depths, soil gas extraction, sample collection, and sample analysis shall be specified in procedures to be developed. These procedures shall be approved and controlled as specified in Chapter 4.0 of the QAPP.

Soil gas samples will be obtained in clean gas-tight sample containers. Level II analysis for volatile organic and halogenated compounds will be conducted onsite using a field portable gas chromatograph (GC) in order to provide real-time data as the survey proceeds. Ten percent of the samples will be shipped to a laboratory for analysis by EPA Method 8240 (Level III). The field GC will be equipped with a photo-ionization detector (PID) and an electron-capture detector (ECD). The PID is suitable for detecting volatile organic compounds and the ECD is capable of detecting halogenated organic compounds at low concentrations. Additional information for sample procedures is provided in the QAPP.

3.3.4 Electromagnetic Induction/Magnetometer (EMI/MAG) Survey

The objectives of the EMI/MAG survey include screening large areas for subsurface items that may relate to potential contamination for subsequent sampling and precisely locating buried facilities. Areas identified as having potential for being contaminated will be investigated further in the Task 5 vadose investigation.

3.3.4.1 Electromagnetic Induction/Magnetometer Survey Locations. The implementation of the operable unit EMI/MAG survey will be a one-time occurrence. Electromagnetic induction (EMI) equipment measures the electrical conductivity of subsurface materials. Variations in conductivity may be caused by changes in soil moisture content, the presence of ionic species, or the presence of metallic objects. Magnetometer (MAG) equipment detects ferro-nickel metallic objects, such as pipelines, buried beneath the surface. The areas surveyed will be selected based on the operating history and the capabilities of the equipment. In general, the 100-KR-1 operable unit surveys will cover the land surface from the western edge of the 100-K Area to grid line W^k 3,100, just east of the 116-K-1 crib.

The MAG will be primarily used to look for unknown subsurface pipelines and to better define the location of the known pipelines (concrete pipelines will not be identified by this technique). General traverses of suspected areas will be made to identify subsurface pipelines, and the locations of pipelines will be defined and staked.

The EMI survey will be conducted over cribs, trenches, suspected concrete pipelines, and for facilities with uncertain locations. Prior to performing the survey for unknown facilities, several well defined systems will be surveyed to "ground truth" the EMI system for this application. Also, a general site reconnaissance will be conducted prior to field survey work to identify the background noise level at each facility.

The focus of these surveys will be cross-section traverses, rather than actual grids, to identify the locations of pipelines and the boundaries of trenches and cribs. The spacing of traverses or grids will depend on the size and relative dimensions of the item being investigated (e.g., 5 ft by 2,000 ft [1.5 m by 610 m] pipelines). For long pipelines (e.g., 1,000 ft [305 m]) traverses will be on about a 50 ft (15 m) spacing. Horizontal control will be established under Subtask 2b. The survey will continue until readings approach background levels. The EMI and MAG surveys will be conducted to precisely locate facilities in the field and confirm existing information. There is no reason to suspect the existence of undocumented facilities or structures in the 100-KR-1 operable unit; however, anomalies and boundaries for subsurface facilities will be identified.

3.3.4.2 Electromagnetic Induction/Magnetometer Survey Methods. The magnetometer survey will be conducted using a fluxgate magnetometer. At each survey location, vertical dipole (parallel and perpendicular), horizontal dipole, and in-phase conductivity readings will be recorded on an automatic data logger. Azimuthal readings will be taken where anomalous readings are encountered to attempt to define geometry of the anomaly.

Additional details on magnetometer and electromagnetic survey equipment and procedures shall be developed in accordance with EII 1.2 "Preparation and Revision of Environmental Investigation Instructions" (WHC 1989). Alternatively, the EMI/MAG survey may be conducted by approved participant contractor or subcontractor procedures as specified in Chapter 4.0 of the QAPP. These procedures will include details on equipment specifications, including sensitivities and interference, signal generator and antennae array, and data logging equipment.

Boundaries of structures found will be staked and recorded on the topographic base map. Data will be recorded in a field notebook in accordance with EII 1.5 "Field Logbooks" (WHC 1989) to supplement the staked locations and base map. In addition, an automatic data logger will be used to log EMI survey data. All field data will be handled in accordance with QAPP and DMP procedures.

Data generated during the EMI/MAG survey will be displayed graphically with profiles showing the depth and lateral extent of any anomalies detected and the boundaries of buried structures. Contour maps defining site patterns in relation to survey lines may be produced to depict the results of the EMI survey.

3.3.5 Ground Penetrating Radar (GPR) Survey

The GPR survey will be used to determine the locations and boundaries of buried features that are not adequately defined by historic records, visual identification, or the EMI/MAG survey. The usefulness of the GPR survey results will be checked against the results from the EMI/MAG survey for several locations to determine whether it provides supplemental information. If useful supplemental information may be provided, the survey will be performed. The GPR survey will focus on cribs, and trenches where no metallic objects have been disposed of and where the GPR results may be superior to those from the EMI/MAG survey.

3.3.5.1 GPR Survey Locations. The actual selection of locations will depend on the results of the EMI/MAG survey and assessment of additional information that may be provided by the GPR.

3.3.5.2 GPR Survey Method. Actual survey techniques will follow those to be developed for EII 1.2 "Preparation and Revision of Environmental Investigations Instructions" (WHC 1989b). It is proposed that initially 50 ft (15 m) grid or transect spacings will be used. For specific facilities, the transect spacing will be varied depending on the size of the facility. Final grid spacing for any given facility will be determined in the field. If the resolution of the GPR is adequate, the grid spacing will be reduced. Additional surveys will be conducted as needed.

Continuous strip chart recording equipment will be used to generate profiles of the survey. Records of all calibrations and procedures will be maintained in the field logbook. This information will be incorporated onto a location base map and will be related to the other facility information.

3.3.6 Process Effluent and Discharge Pipeline Integrity Assessment

The objective of this task is to evaluate the integrity of the pipelines and to locate places in the pipelines where leaks occurred and where the soil may have become more heavily contaminated from the leaking effluent. Areas

where large volumes of effluent leaked from the pipelines may be considered as individual contamination sources and may be evaluated independently for remedial action.

3.3.6.1 Review of Feasibility of 100-KR-1 Operable Unit Pipeline Assessment. The applicability of using helium gas and detectors to evaluate the pipelines will be tested in this program. Sludge deposits occurred in the various 107-K retention basins, and it is likely that sludge/corrosion products were deposited in the pipelines. If sludge deposits are present, they would probably cover cracks or breaks in the pipelines and may not be readily identified using alternate techniques. The primary advantage of using a technique such as the helium gas method is that it limits the need to send personnel or equipment into potentially contaminated pipelines.

If the evaluation of the technique indicates that this method of assessing pipeline integrity is not feasible due to the size of the pipelines or provides limited useful information, it may be replaced by an alternate technique. If necessary, the Task 5 vadose investigations will be modified to sample additional sites along the pipelines to determine the nature and extent of any contamination as a result of leakage.

If evaluation of the technique indicates that the method is practical but that procedural modifications are required, the procedure will be modified as necessary.

3.3.6.2 Integrity Assessment Method. The details on helium detection equipment and procedures are in development by WHC as EII 13.1 "Leak Detection Survey" (WHC 1989). This procedure will include a description of the pipe penetration, capping details, and gas detection. The procedure will describe methods on pipeline location, pipe capping, tracer gas detection, sensor calibration, operation and maintenance, status determination and methods for preventing contamination.

The leak detection survey results will be manually recorded. All readings, leak locations, and current leak flowrates will be documented in the field logbook. Leak locations will be visibly marked and identified for soil sampling.

3.3.7 Source Sampling

The objective of this task is to collect and analyze samples and determine the chemical and radiological characteristics, extent, and concentrations of the

source contamination. The source sampling investigation will involve collecting soil and sludge from borings and facility surfaces.

3.3.7.1 Sampling Locations and Methods. Sampling will be done in the 116-KE-4 and 116-KW-3 retention basins, the 116-K-1 effluent crib, the 116-K-2 effluent trench, the 116-K-3 outfall structure, and various effluent discharge pipelines and valves in the 100-KR-1 operable unit. All samples will be field screened for beta/gamma and volatile organics per EII 2.3 "Radiation Survey" and EII 3.2 "Health and Safety Monitoring Instruments" (WHC 1989), respectively.

Table FSP-1 presents the proposed sample designation, sampling intervals, laboratory analyses, and rationale for sampling; Table FSP-2 presents the specific analytes. Figure FSP-1 illustrates the proposed sample locations, and the following sections present the detailed sampling activities.

3.3.7.1.1 Waste Units 116-KE-4 and 116-KW-3 (Retention Basins). One soil boring will be hand augured or dug in each of the 116-KE-4 and 116-KE-3 retention basins totaling six locations (SS-1 through SS-6). A 2 or 3 in (5 or 8 cm) hand-held soil bucket auger or shovel will be used per EII 5.2 "Soil and Sediment Sampling" (WHC 1989). The sampling team will auger or dig through the 2 to 3 ft (0.7 to 1 m) of fill, composite the material in a stainless steel pan, and collect one sample of the fill material from the pan. When the auger encounters sludge below the fill, the sludge will be composited in a decontaminated stainless steel pan, and one composite sample of sludge material will be collected from the pan. Any soil or sludge in the pan that is not collected into a sample container will be backfilled into the borehole (sludge on the bottom and soil on the top). The sampling will proceed from one retention basin to another, and the soil bucket auger or shovel will be decontaminated between sampling efforts as specified in EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989).

3.3.7.1.2 Waste Unit 116-K-1 (Effluent Crib). Three soil borings (K1-1, 2, 3) will be drilled in the 116-K-1 effluent crib. Drilling will be performed per EII 6.7 "Ground Water Well and Borehole Drilling" (WHC 1989). Borehole locations will be staked, and the drill rig will move sequentially through the staked locations. Soil samples will be collected at 2 ft (0.7 m) intervals from ground surface to 20 ft (7 m) and at 5 ft (1.5 m) intervals from 20 ft (7 m) to ground water using a split spoon sampler in accordance with EII 5.2 "Soil and Sediment Sampling" (WHC 1989). Borings will not penetrate the water table (or capillary fringe) if significant levels of contamination are detected directly above this zone using field screening methods so that cross contamination of ground water is avoided. The drill rig

Table FSP-1 Proposed Samples for the 100-KR-1 Source Investigations.

Page - 1

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list	Short chemical analyses list	Physical analyses[a]	Sampling Rationale
SS-1	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-2	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-3	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-4	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-5	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-6	Surface to sludge Sludge interval	X[c] X[c]			Source characterization
SS-7	Sludge layer	X[c]			Source characterization
K1-1	2-ft intervals (surface to 20 ft) 5-ft intervals (20ft to GW1)	X[d]	X	X	Source and vadose characterization
K1-2	2-ft intervals (surface to 20 ft) 5-ft intervals (20ft to GW1)	X[d]	X	X	Source and vadose characterization
K1-3	2-ft intervals (surface to 20 ft) 5-ft intervals (20ft to GW1)	X[d]	X	X	Source and vadose characterization

Table FSP-1 Proposed Samples for the 100-KR-1 Source Investigations.

Page - 2

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list	Short chemical analyses list	Physical analyses[e]	Sampling Rationale
K2-1	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-2	5-ft interval (surface to 20 ft)		X	X	Source and vadose characteriztion
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-3	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
	5-ft intervals (40 ft to GW1)		X	X	
K2-4	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	
K2-5	5-ft interval (surface to 20 ft)		X	X	Source and vadose characterization
	2-ft interval (20 ft to 40 ft)	X[d]		X	

[a] Sample locations shown on Figure 5-1
[b] Analyses listed in Table 5-2
[c] Level IV and V analyses
[d] Level IV and V analyses on two sample intervals, level III on remaining intervals
[e] Physical parameters will be analyzes for in each distinct lithologic unit if field screening methods do not detect contamination
GW1 - Ground water estimated at 80 ft

Table FSP-2. 100-KR-1 Operable Unit Chemical and Physical Analyses.

Physical Parameters

Moisture
Permeability
Cation exchange
Capacity
pH
Soil classification
Consolidation
Grain-size distribution
including percent clay

Long List of Chemical Analysis

General chemical parameters

Ammonia-N
Carbonate
Chloride
Fluoride
Nitrate
Phosphate
Sulfate
Sulfamate
Oxalate

Radionuclides

Americium-241
Carbon-14
Cobalt-60
Europium-152
Europium-154
Europium-155
Gamma scan
Gross alpha
Gross beta
Iodine-129
Nickel-63
Plutonium
Strontium-90
Technetium-99
Tritium
Uranium

Metals

Aluminum
Antimony
Arsenic
Barium
Beryllium
Cadmium
Chromium, hexavalent
Chromium (total)
Cobalt
Copper
Cyanide
Iron
Lead
Magnesium
Manganese
Mercury
Nickel
Potassium
Selenium
Silver
Sodium
Thallium
Vanadium
Zinc

Herbicides, Pesticides & PCBs

2,4,5 TP silvex
2,4-D
Alpha-BHC
Beta-BHC
Delta-BHC
Gamma-BHC (Lindane)
Heptachlor
Aldrin
Heptachlor epoxide
Endosulfan I
Dieldrin
4,4'-DDE
Endrin
Endosulfan II
4,4'-DDD
Endosulfan sulfate
4,4'-DDT
Methoxychlor
Endrin ketone
Alpha-Chlordane
Gamma-Chlordane
Toxaphene
Aroclor-1016
Aroclor-1221
Aroclor-1232
Aroclor-1242
Aroclor-1248
Aroclor-1254
Aroclor-1260

Volatile organic compounds

Chloromethane
Bromomethane
Vinyl chloride
Chloroethane
Methylene chloride
Acetone
Carbon disulfide
1,1-Dichloroethene
1,1-Dichloroethane
1,2-Dichloroethene(total)
Chloroform
1,2-Dichloroethane
2-Butanone
1,1,1-Trichloromethane
Carbon tetrachloride
Vinyl acetate
Bromodichloromethane
1,2-Dichloropropane
cis-1,3-Dichloropropane
Trichloroethene
Dibromochloromethane
1,1,2-Trichloromethane
Benzene
trans-1,3-Dichloropropane
Bromoform
4-Methyl-2-pentanone
2-Hexanone
Tetrachloroethane
Toluene
1,1,2,2-Tetrachloroethane

Table FSP-2. 100-KR-1 Operable Unit Chemical and Physical Analyses.

Chlorobenzene
Ethyl benzene
Styrene
Xylenes (total)

Semi-volatile organic compounds

Acenaphthene
2,4-Dinitrophenol
4-Nitrophenol
Dibenzofuran
2,4-Dinitrotoluene
2,6-Dinitrotoluene
Diethylphthalate
4-Chlorophenyl-phenylether
Fluorene
4-Nitroaniline
4,6-Dinitro-2-Methylphenol
N-Nitrosodiphenylamine
4-Bromophenyl-phenylether
Hexachlorobenzene
Pentachlorophenol
Phenanthrene
Anthracene
Di-N-Butylphthalate
Fluoranthene
Pyrene
Butylbenzylphthalate
3,3'-Dichlorobenzidine
Benzo (a) Anthracene
bis (2-Ethylhexyl) Phthalate
Chrysene
Di-N-Octyl Phthalate
Benzo (b) Fluoranthene
Benzo (k) Fluoranthene
Benzo (a) Pyrene
Indeno (1,2,3-cd) Pyrene
Dibenz (a,h) Anthracene
Benzo (g,h,i) Perylene
Phenol
bis (-2-Chloroethyl) Ether
2-Chlorophenol
1,3-Dichlorobenzene
1,4-Dichlorobenzene
Benzyl Alcohol
1,2-Dichlorobenzene
2-Methylphenol
bis (2-chloroisopropyl) Ether
4-Methylphenol
N-Nitroso-Di-Propylamine
Hexachloroethane
Nitrobenzene
Isophorone
2-Nitrophenol
2,4-Dimethylphenol
Benzoic Acid
bis (-2-Chloroethoxy) Methane
2,4-Dichlorophenol
1,2,4-Trichlorobenzene
Naphthalene
4-Chloroaniline
Hexachlorobutadiene
4-Chloro-3-Methylphenol
2-Methylnaphthalene
Hexachlorocyclopentadiene
2,4,6-Trichlorophenol
2,4,5-Trichlorophenol
2-Chloronaphthalene
2-Nitroaniline
Dimethyl Phthalate
Acenaphthylene
3-Nitroaniline

Short List of Chemical Analyses

Radionuclides

Gross alpha
Gross beta

Inorganics

Arsenic
Chromium
Copper
Mercury
Pottassium
Zinc

General Chemicals

Ammonia
Flouride
Chloride
Nitrate
Sulfate
Sulfamate
Oxalate

Organics

Herbicides
Pesticides
PCBs
Total Organic Carbon
Total Organic Halogens

H:\1842\TABLES\KR1\FSP\180A

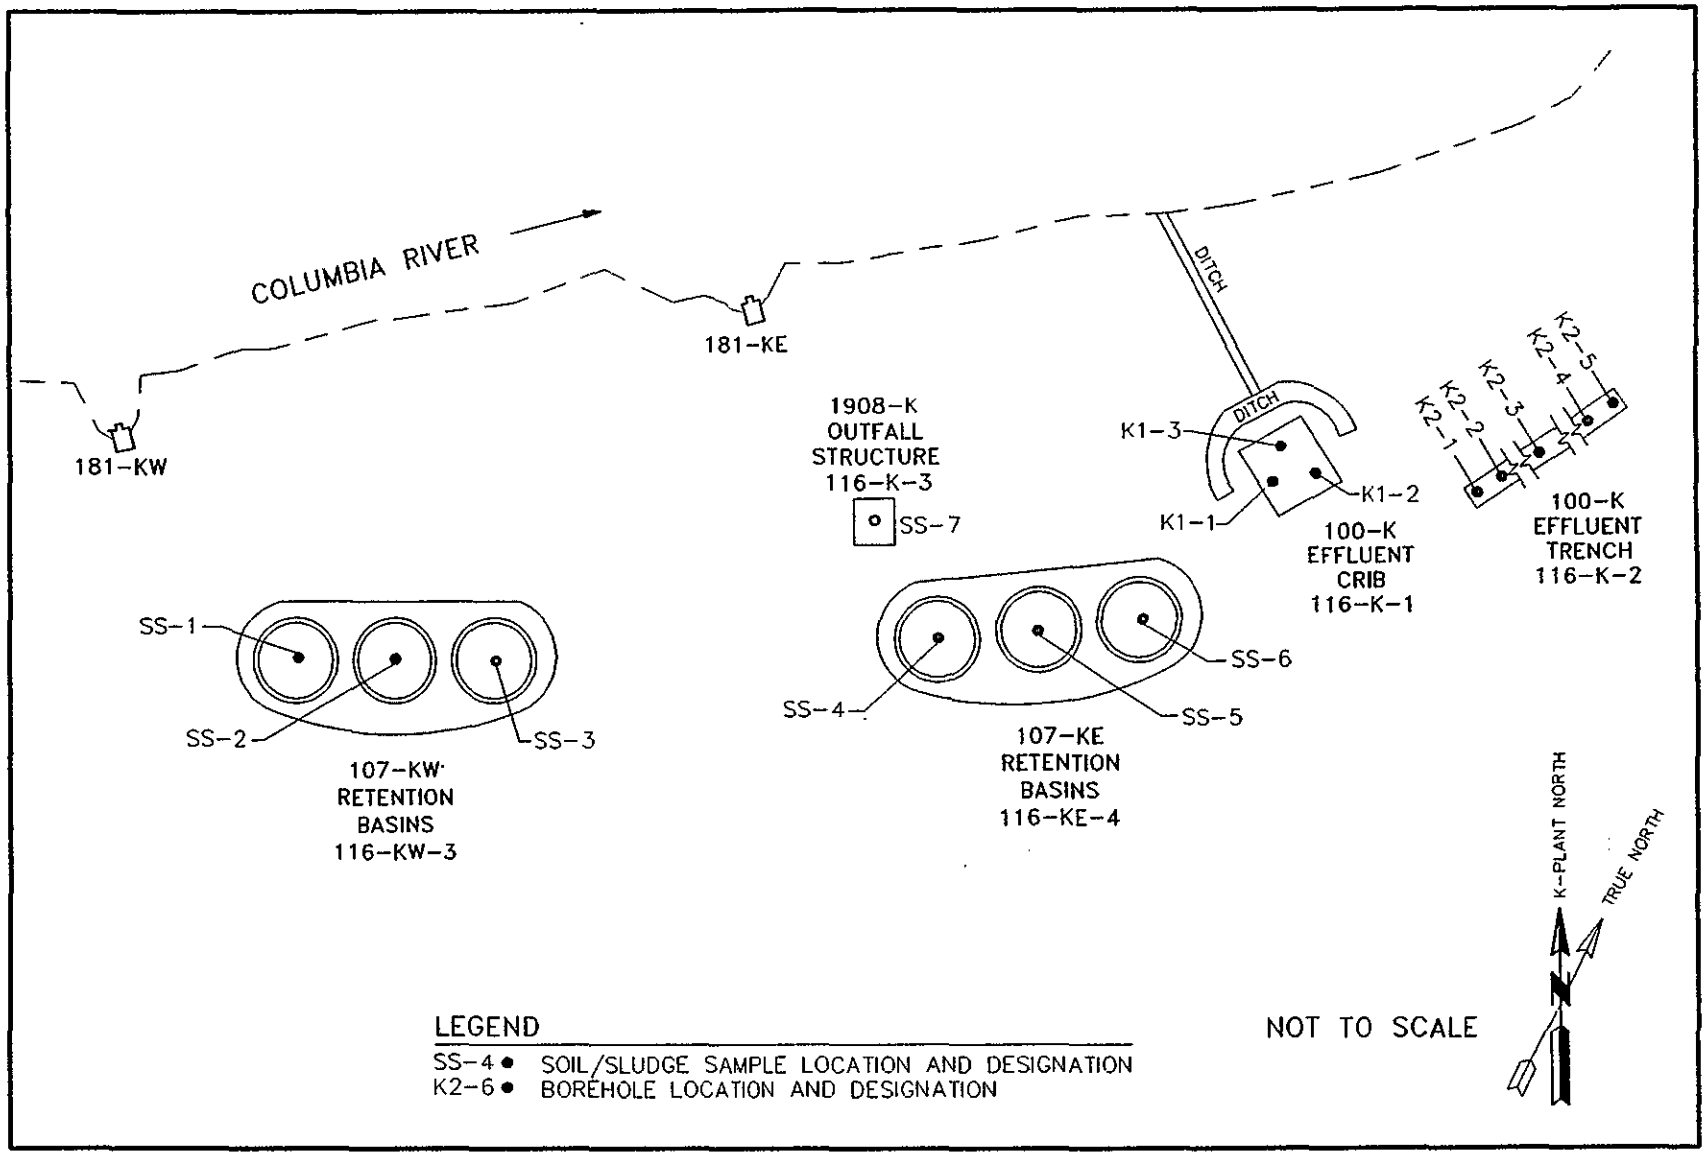

Figure FSP-1. Proposed Sampling Locations For 100-KR-1 Source Investigations.

will be decontaminated between boreholes as specified in EII 5.4 "Decontamination of Drilling Equipment" (WHC 1989), and the split spoon and stainless steel trowels and pans used to composite the sample will be decontaminated between samples as specified in EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989).

Since the depth of fill placed in the crib is poorly known, 2 ft (0.7 m) sampling intervals will be initiated from the surface but may extend below the top 20 ft (7 m). Field screening techniques will be used to identify the crib surface by attempting to recognize elevated levels of radioactivity that are expected. The Field Team Leader will make the decision to sample at 2 ft (0.7 m) intervals below the initial 20 ft (7 m), if necessary.

Because of the extreme drilling conditions encountered at the 100-K Area, it will not be mandatory to collect continuous samples beyond the top 20 ft (7 m) (or greater) interval. Instead, a 2 ft (0.7 m) interval may be collected per every 3 ft (0.9 m) of linear drilling.

3.3.7.1.3 Waste Unit 116-K-2 (Effluent Trench). Five soil borings (K2-1, 2, 3, 4, 5) will be drilled in the 116-K-2 effluent trench. If possible, the drill rig used in the 100-KR-4 ground water operable unit investigation will drill the 100-KR-1 boreholes. Drilling procedures will follow EII 6.7 "Ground Water Well and Borehole Drilling" (WHC 1989). Sampling will be conducted using a split spoon, and methods are described in EII 5.2 "Soil and Sediment Sampling" (WHC 1989). The five borings will be approximately evenly spaced (i.e., 1,300 ft [400 m] apart) from the influent end. Three of the five soil borings (K2-1, 2, 3) will be drilled from the surface of the ditch down to ground water. Since the approximate depth of the original ditch was 20 ft (7 m), sampling intervals will be 5 ft (1.5 m) from ground surface to 20 ft (7 m), 2 ft (0.7 m) intervals from 20 ft (7 m) to 40 ft (12 m) and 5 ft (1.5 m) intervals from 40 ft (12 m) to ground water. The three deeper holes will be located close to the head of the trench. The remaining two soil borings (K2-4, 5) will be sampled from ground surface to 40 ft (12 m) in the same intervals described above. As discussed under Section 3.3.7.1.2, continuous sampling through the 2 ft (0.7 m) intervals will not be required.

The drill rig will be decontaminated between boreholes as per EII 5.4 "Decontamination of Drilling Equipment" (WHC 1989), and the split spoon will be decontaminated between samples as required by EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989).

3.3.7.1.4 Waste Unit 116-K-3 (Outfall Structure). If sludge is found in the outfall structure, one sludge sample (SS-7) will be collected. A decontaminated stainless steel trowel will be used to collect material from surface to 6 in. (15 cm) as required by EII 5.2 "Soil and Sediment Sampling" (WHC 1989). One sample will be composited into a stainless steel pan. Because the structure is still being used, sampling procedures may need to be modified. Equipment will be decontaminated after each sample as required by EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989).

3.3.7.1.5 Effluent Discharge Pipelines and Valves. This investigation is intended to locate sludge deposits in the cooling water discharge pipelines. These sludge deposits may contain radionuclide or hazardous material, which would be released if the pipelines become severely corroded or are removed and disposed.

Radiological information collected from the site walk-over survey or surface radiation survey and the pipeline integrity assessment may reveal significant areas of radioactivity resulting from pipeline leaks. If sludge is found, that location will be targeted for further investigation.

Sludge sampling will conform to the standards set forth in Section 3.3.7.1.4 of this FSP. If sludge is found within the effluent pipelines and valves, two samples will be collected per continuous section using methods found in EII 5.2 "Soil and Sediment Sampling" (WHC 1989).

3.3.7.2 Geologic Logging. All boreholes will be logged by a qualified geologist and sampled at specified intervals. Borehole geologic logs will follow the guidelines specified in EII 9.1 "Geologic Logging" (WHC 1989). Drill cuttings and core samples will be screened with hand-held instruments to detect radiation and volatile organic compounds. Detailed geologic logging will not be performed on samples that indicate contamination to be present. General drilling observations will be noted such as occurrences of perched water, moisture, lithologic changes, sample intervals, and drilling problems. All of this information will be included on each borehole log.

3.3.7.3 Geophysical Logging. Each borehole will be geophysically logged after drilling. Geophysical logs will include gamma-gamma, neutron, epithermal neutron, and high resolution spectral gamma. Borehole geophysical logging is helpful in the correlation of sedimentary facies by measuring physical properties such as porosity, density, and water content. High-resolution spectral gamma logging permits the identification of gamma-emitting radionuclides. Geophysical logging will be conducted in accordance with

9 0 1 1 9 3 7 0 3 6 7

EII 5.6 "Control of Geophysical Logging" and EII 11.1 "Geophysical Logging" (in preparation) (WHC 1989) and/or as specified by subcontract procedures.

3.3.7.4 Drill Cutting Disposal. Soil cuttings containing low level and mixed radioactive waste will be contained, stored, and disposed of according to procedures to be developed. Soil cuttings containing hazardous wastes will be contained and disposed of in accordance with EII 4.1 "Nonradioactive Hazardous Waste Disposal" (WHC 1989). Soil cuttings containing unknown wastes will be packaged for storage and disposal in accordance with EII 4.2 "Interim Control of Unknown Waste" (WHC 1989). Storage or archive samples will be handled in accordance with Procedure EII 5.7A "Hanford Geotechnical Library Sample Control" (WHC 1989).

3.3.7.5 Borehole Abandonment. Soil boreholes will be sealed and abandoned as required by the state of Washington (WAC 173-160). Steel casing removed from the borehole will be decontaminated in accordance with EII 5.4 "Field Decontamination of Drilling Equipment" (WHC 1989). The boreholes will be pressure grouted, using a portland cement/bentonite slurry per EII 6.5 "Borehole Abandonment" (WHC 1989).

3.4 SUBTASK 2d - LABORATORY ANALYSIS

Analyses to be performed are listed in Table FSP-1 and are correlated with the sample intervals. The lists of specific analytes are contained in Table FSP-2. In general, the more rigorous analyses (long list) are performed on the samples expected to show higher levels of contamination; the indicator parameters and analytes of concern (short list) are performed on relatively less contaminated soils. Furthermore, Level IV and V analyses will be performed on a subset of the total samples.

Physical analyses will be performed on one sample per lithologic unit as determined by the field geologist. No sample will be sent for physical analysis if field screening indicates contamination to be present. A listing of physical test parameters is presented in Table FSP-2.

3.5 SUBTASK 2e - DATA EVALUATION

Data evaluation is not a field sampling or analytical technique and is described in Section 5.2.2.5 of the work plan.

4.0 TASK 3 - GEOLOGIC INVESTIGATION

The geological investigation will further characterize the geological structure and stratigraphy underlying the operable unit. Relevant data will be gathered under four subtasks. Because geological data needs overlap with those of the 100-KR-1 operable unit vadose investigation (Task 5) and the 100-KR-4 operable unit ground water investigation, the geological investigation subtasks involve a coordinated compilation of pertinent vadose zone and ground water information.

The four subtasks to be performed for the geologic investigations include:

- Data compilation and review
- Field activities
- Laboratory analysis
- Data evaluation.

4.1 SUBTASK 3a - DATA COMPILATION AND REVIEW

This subtask does not involve any field sampling. Details of the activities conducted for this subtask are provided in Section 5.2.3.1 of the work plan.

4.2 SUBTASK 3b - FIELD ACTIVITIES

The geologic investigation does not involve any specific borehole sites. Geologic information will be collected in conjunction with other source, vadose and ground water investigations. Two field activities will be conducted in the 100-KR-1 geologic investigation.

4.2.1 Surface Mapping

Surface geologic mapping will be conducted by a qualified geologist. The mapping will be plotted on the topographic map prepared under

Subtask 2b. Mapping will identify the types and areal extent of surficial deposits within and adjacent to the operable unit, including dune and sheet sand, alluvium, colluvium, and loess, as well as fly ash and backfill materials. The mapping will include the large areas of artificial fill and other unnatural features. Aerial photographs will be reviewed and information from the site walkover observations will be included. Relevant information from Section 3.3.7.2, geologic logging, will be incorporated into this mapping task.

4.2.2 Geologic Logging

All boreholes will be geologically logged, and this activity is discussed in Section 3.3.7.2 of this FSP.

4.3 SUBTASK 3c - LABORATORY ANALYSIS

Analysis of physical parameters will be performed on various samples (see Tables FSP-1 and 3) to characterize the vadose zone. The specific physical parameters to be analyzed are listed in Table FSP-2. The analysis will be performed for each lithologic unit encountered in the borehole. No samples will be sent for physical analyses if detectable levels of radioactivity or chemical contamination are noted during field screening.

4.4 SUBTASK 3d - DATA EVALUATION

This subtask does not involve any field work. Details of the activities associated with this subtask are provided in Section 5.2.3.4 of this work plan.

5.0 TASK 4 - SURFACE WATER AND SEDIMENTS INVESTIGATION

This task does not involve any field activity for the 100-KR-1 operable unit. The surface water and sediments investigation will be conducted as part of and is described in the 100-KR-4 operable unit work plan.

Table FSP-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Page - 1

Sample designation[a]	Sampling interval	Laboratory analyses[b] Long chemical analyses list[c]	Short chemical analyses list	Physical analyses[d]	Sampling Rationale
KW3-1	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-2	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-3	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KW3-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KW3-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KW3-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-1	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

Table FSP-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Sample designation[a]	Sampling interval	Laboratory analyses[b]: Long chemical analyses list[c]	Laboratory analyses[b]: Short chemical analyses list	Laboratory analyses[b]: Physical analyses[d]	Sampling Rationale
KE4-2	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KE4-3	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
KE4-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
KE4-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K1-4	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K1-5	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW2)		X	X	
K2-6	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

Table FSP-3. Proposed Samples for the 100-KR-1 Vadose Investigations.

Page - 3

Sample designation[a]	Sampling interval	Laboratory analyses[b]: Long chemical analyses list[c]	Laboratory analyses[b]: Short chemical analyses list	Laboratory analyses[b]: Physical analyses[d]	Sampling Rationale
K2-7	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	
K2-8	2-ft interval (surface to 20 ft)	X		X	Near surface soil and vadose characterization
	5-ft interval (20 ft to GW1)		X	X	

[a] Sample locations shown on Figure 5-2
[b] Analyses listed in Table 5-2
[c] Level IV and V analyses on two sample intervals, level III on remaining intervals
[d] Physical parameters will be analyzes for in each distinct lithologic unit if field screening methods do not detect contamination
GW1 = Ground water estimated at 80 ft
GW2 = Ground water estimated at 40 ft

6.0 TASK 5 - VADOSE INVESTIGATIONS

This task is designed to characterize the physical and chemical properties of the 100-KR-1 soils. The vadose zone investigation will involve the collection of soil samples from borings.

Four subtasks will be performed for the vadose investigation and include the following:

- Subtask 5a - Data compilation and review
- Subtask 5b - Field activities
- Subtask 5c - Laboratory analysis
- Subtask 5d - Data evaluation.

6.1 SUBTASK 5a - DATA COMPILATION AND REVIEW

This subtask does not involve any field sampling. Details of the activities conducted in this subtask are provided in Section 5.2.5.1 of the work plan.

6.2 SUBTASK 5b - FIELD ACTIVITIES

The objective of this subtask is to collect and analyze soil through the vadose zone within the 100-KR-1 operable unit to determine physical and chemical characteristics.

Field activities to be conducted for the vadose investigation include the following:

- Borehole siting
- Vadose and near surface soil sampling

6.2.1 Borehole Siting

Before beginning the vadose zone field investigation activities, the data generated from the surface surveys, as described under Task 2, will be reviewed to help site borehole locations. If the data is complete and adequate to determine borehole locations, no additional surveys will be performed. However, if survey coverage is incomplete, a site-specific survey(s) will be performed in conjunction with the borehole siting process.

The process of siting individual boreholes will be undertaken as part of the field activity process. After surface surveys data are reviewed, an evaluation of the general area on which boreholes are to be sited will be completed. Individual(s) cognizant of the capabilities and limitations of the drilling and sampling equipment used for the vadose zone investigation will conduct field observations. The primary purpose of the siting process is to evaluate access, health and safety concerns, and determine the most effective routes into and out of potential sites while creating a minimal amount of surface disturbance. Subsequent to completion of survey and siting activities the borehole locations will be staked.

6.2.2.1 Sampling Locations and Methods. Sampling will be done in the areas of retention basin leaks, effluent crib failure, and effluent trench overflow. Table FSP-3 presents the proposed sample designation, sampling intervals, laboratory analyses, and sampling rationale; Figure FSP-2 illustrates the proposed sample locations. Borehole locations are approximated and will be precisely located based on the procedures described in Section 6.2.1. The following sections present detailed sampling activities.

6.2.2.1.1 Area of Retention Basin Leaks. One borehole will be drilled adjacent to each of the six 107 retention basins. The six boreholes (KW3-1, 2, 3 and KE4-1, 2, 3) will be drilled and sampled from the ground surface to the water table. The top 20 ft (7 m) will be sampled at 2 ft (0.7 m) intervals and from 20 ft (7 m) to ground water at 5 ft (1.5 m) intervals.

In addition to the six boreholes adjacent to the basins, six boreholes (KW3-4, 5, 6 and KE4-4, 5, 6) will be drilled to ground water between the road north of the retention basins and the Columbia River. Locations for the boreholes, as shown in Figure FSP-2, are approximate and will be precisely located based on the surface radiation survey, walkover surveys, and accessibility. An attempt has been made to locate the boreholes in areas likely to show higher concentrations of contaminants by spotting boreholes on areas of fill or near washouts that were presumably formed during basin leak events.

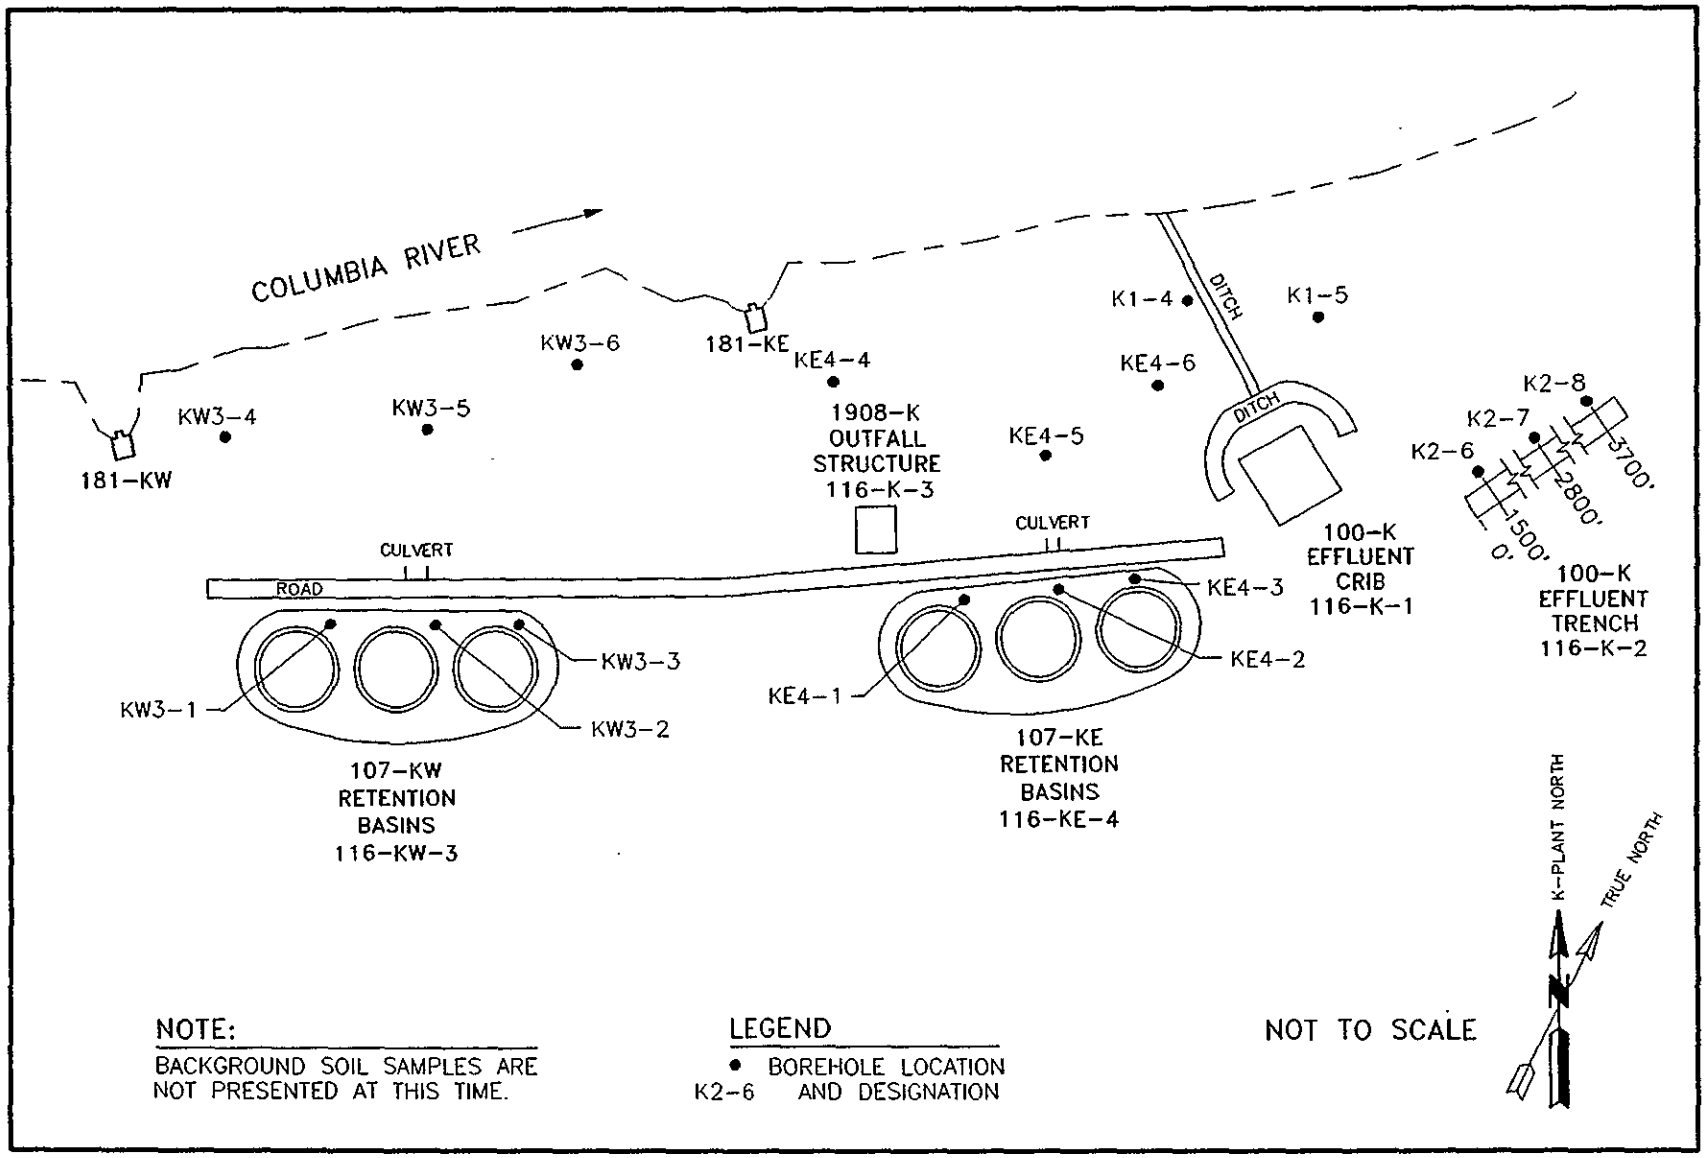

Figure FSP-2. Proposed Sampling Locations for Soil Investigation.

These boreholes will be sampled in the same manner as those near the retention basins: the top 20 ft (7 m) at 2 ft (0.7 m) intervals and the remainder at 5 ft (1.5 m) intervals. To avoid cross contamination of ground water by vadose zone contaminants, borings will not penetrate the water table (or capillary fringe) if significant levels of contamination are detected directly above this zone using field screening techniques.

Because of the extreme drilling conditions encountered at the 100-K Area, it will not be mandatory to collect continuous samples through the top 20 ft (7 m) (or greater) interval. Instead, a 2 ft (0.7 m) interval may be collected per every 3 ft (0.9 m) of linear drilling.

This biased sampling approach is designed to characterize the chemical and radiological nature of the vadose zone impacted by retention basin leaks. Based on the results of this effort, a sampling program may be initiated to further define the distribution of contaminants throughout the zone. Drilling, sampling, and decontamination procedures will proceed as discussed in Section 3.3.7.1.2 of this FSP.

6.2.2.1.2 Area of Effluent Crib Failure. Two boreholes (K1-4 and 5) will be drilled and sampled from the surface to the water table. As with other boreholes, discussed earlier, sampling will be at 2 ft (0.7 m) intervals from 0 to 20 ft (7 m) and at 5 ft (1.5 m) intervals from 20 ft (7 m) to ground water. A more extensive characterization effort may be undertaken based on the results of these analyses. Boreholes were sited in areas suspected of being most highly contaminated; one sited where effluents ran overland toward the river as a result of the crib breach, and the second sited adjacent to a ditch running from the crib to the river. As with other vadose zone borings, these drill holes will not penetrate the ground water if significant levels of contamination exist directly above the water table.

Because of the extreme drilling conditions encountered at the 100-K Area, it will not be mandatory to collect continuous samples through the top 20 ft (7 m) (or greater) interval. Instead, a 2 ft (0.7 m) interval may be collected per every 3 ft (0.9 m) of linear drilling. Drilling, sampling, and decontamination procedures will proceed as discussed in Section 3.3.7.1.2 of this FSP.

6.2.2.1.3 Area of Effluent Trench Overflow. Three areas of overflow are known to exist on the north side of the trench and are recognized by areas of graded fill. One borehole will be located on each washout area (K2-6, 7 and 8). Sampling will be done from the surface down to ground water and sampling intervals will be 2 ft (0.7 m) from ground surface to 20 ft (7 m) and

9 0 1 1 8 3 0 3 1 7

5 ft (1.5 m) intervals from 20 ft (7 m) to ground water. As noted above, continuous samples are not required through the 2 ft (0.7 m) sampling intervals due to the extreme drilling conditions likely to be encountered. Boreholes will not penetrate to ground water if significant levels of contamination are detected directly above the water table. Drilling, sampling, and decontamination procedures will proceed as discussed in Section 3.3.7.1.2 of this FSP.

6.2.2.2 Geologic Logging. Borehole geologic logs will record the applicable information as required by EII 9.1 "Geologic Logging" (WHC 1989) and is discussed in Section 3.3.7.2 of this FSP.

6.2.2.3 Geophysical Logging. Geophysical logging of all boreholes will proceed as discussed in Section 3.3.7.3 of this FSP.

6.2.2.4 Drill Cutting Disposal. All borehole cuttings will be properly disposed as discussed in Section 3.3.7.4 of this FSP.

6.2.2.5 Borehole Abandonment. All boreholes will be sealed and abandoned as required by the state of Washington and the procedures discussed in Section 3.3.7.5 of this FSP.

6.3 SUBTASK 5c - LABORATORY ANALYSIS

Analyses to be performed on each sample interval are listed in Table FSP-3. The lists of specific analytes is contained in Table FSP-2. In general, the more rigorous analyses (long list) are performed on the samples expected to show higher levels of contamination; the indicator parameters and analytes of concern (short list) are performed on relatively less contaminated soils. Furthermore, Level IV and V analyses will be performed on a subset of the total samples.

Physical analyses will be performed on one sample per lithologic unit as determined by the field geologist. No sample will be sent for physical analyses if field screening indicates contaminants to be present.

6.4 SUBTASK 5d - DATA EVALUATION

This subtask does not involve any field or laboratory activities and is discussed in Section 5.2.5.4 of the 100-KR-1 work plan.

7.0 TASK 6 - GROUND WATER INVESTIGATIONS

This task does not involve any field activity for the 100-KR-1 operable unit. This investigation will be conducted as part of the 100-KR-4 RI/FS.

8.0 TASK 7 - AIR INVESTIGATIONS

This task is designed to compile existing meteorological and air quality data as well as collecting new data. These data will be used to evaluate potential remedial action alternatives during the FS, conduct the risk assessment, and identify potential health hazards.

Four subtasks are involved in the air investigation.

- Subtask 7a - Data compilation and review
- Subtask 7b - Field sampling
- Subtask 7c - Laboratory analysis
- Subtask 7d - Data evaluation

8.1 Subtask 7a - DATA COMPILATION AND REVIEW

This subtask is not a field activity and is discussed in Section 5.2.7.1 of the work plan.

8.2 SUBTASK 7b - FIELD ACTIVITIES

Because of the large existing meteorological databases from the Hanford Meteorological Station (HMS), the nearby Station No. 6 wind tower, and the Pasco airport, no separate meteorological measurements are proposed for the 100-KR-1 operable unit project. Any real-time meteorological data needs during this project will be satisfied with data from these sites obtained in accordance with established station procedures.

There will be minimal disturbance of contaminated materials during the field sampling activities. However, air particulate sampling will be performed

9 1 1 0 6 9 1 3 0 2 6 1 9

near invasive activities of the 100-KR-1 operable unit that may generate particulate air emissions. Continuous air monitors will be located upwind and downwind for comparative purposes. In addition, personnel health physics air monitoring will be conducted at specific work sites. This air sampling will generally be performed at sites where the greatest potential for disturbing contaminated material exists, based on both the site and the work being performed.

Sampling will be performed for both airborne particulates and VOAs. Monitoring for VOAs will be performed using portable field instruments. Sampling for airborne particulates will be performed with high-volume air samplers.

8.3 SUBTASK 7c - LABORATORY ANALYSIS

The air sample filters will be analyzed for ^{60}Co, ^{137}Cs, ^{90}Sr, gross beta, and gross alpha. If significant concentrations of gross alpha (as defined by site-specific applicable relevant and appropriate requirements) are detected, samples will be composited and analyzed for ^{239}Pu.

8.4 SUBTASK 7d - DATA EVALUATION

This activity does not include any field work and is described in Section 5.2.7.4 of the work plan.

9.0 TASK 8 - ECOLOGICAL INVESTIGATION

The initial 100-KR-1 ecological field investigations will only involve a survey of terrestrial biota; the 100-KR-4 ecological investigations will concentrate on aquatic and riparian biota at the 100-K Area. The objectives of the terrestrial biota investigation are to:

- Establish the biological inventory at the operable unit
- Determine significant pathways and potentially affected species
- Provide information necessary to complete the risk assessment

- Provide information necessary to evaluate the potential biological effects of implementing the proposed remediation alternatives
- Provide information necessary to verify or refine the conceptual model.

The data collected from the terrestrial monitoring program will be used to determine the significant potential pathways of contaminant movement to humans, determine the critical habitat for species of special concern, and develop and refine conceptual models of human and environmental risk.

For the most efficient use of resources, the terrestrial biota studies will proceed incrementally and in conjunction with the ecological studies planned for the 100-KR-4 operable unit.

The biota investigation will include four subtasks:

- Subtask 8a - Compile and review existing data
- Subtask 8b - Field investigations
- Subtask 8c - Laboratory analysis
- Subtask 8d - Data evaluation.

9.1 SUBTASK 8a - COMPILE AND REVIEW EXISTING DATA

The discussion concerning this subtask can be found in Section 5.2.2.1 of the work plan.

9.2 SUBTASK 8b - FIELD ACTIVITIES

This subtask will supplement the literature review through an onsite terrestrial biological survey. This survey can be regarded as a qualitative, operable unit-specific verification of the 100-KR-1 terrestrial ecosystem information. The biologist in charge of this task will make the decision as to when a field survey is required to support Subtask 8a. Special searches will be made to locate clumps of wild asparagus. If asparagus plants occur in the 100-KR-1 operable unit, samples will be collected during the harvest season.

The survey will be conducted over the entire operable unit surface, including the riparian zone, and will be conducted as part of the site walkover survey described under Task 2. Major species present will be confirmed, to the extent practicable, under this subtask. Information gained from the survey will be entered onto the base map (or overlay).

Sampling done as part of the 100-KR-4 investigation will supply contaminant concentrations in plant tissues collected in the vicinity of the operable unit riparian zone and enable comparisons of these values with "control" areas. If values are significantly elevated over background control values, herbivorous animals will be harvested and their tissues analyzed for specific contaminants, e.g., ^{90}Sr in bone tissue and ^{137}Cs in muscle tissue. Low levels of contaminants found in plants may be indicative of elevated levels in wildlife. The animals selected for harvest would likely be mice-and/or cottontail rabbits because of their restricted home ranges. They are herbivores, and are usually available in numbers sufficient for sampling and monitoring. Biotic sampling will be performed per EII 5.3 "Biotic Sampling" (WHC 1989).

9.3 SUBTASK 8c - LABORATORY ANALYSIS

Asparagus will be analyzed for radionuclides. If animals are harvested they will be analyzed for specific contaminants identified in riparian zone plants as part of the 100-KR-4 ecological investigation.

9.4 SUBTASK 8d - DATA EVALUATION

This subtask does not involve any field sampling or measurements and is described under Section 5.2.8.4 of the work plan.

10.0 TASK 9 - CULTURAL RESOURCES INVESTIGATIONS

A cultural resource investigation has identified the location of surficial archaeological or historical sites listed on or eligible for the National Register of Historic Places. However, additional archaeological sites may exist along the Columbia River immediately adjacent to the 100-K Area and will be part of this investigation.

The task will involve verifying the locations of known sites by reviewing available data on historic land uses by local Indian tribes as well as early 20th century land use by pioneer farmers and settlers. The focus of the investigation will be to determine whether archaeological resources are present at proposed drilling sites. A Class 3 field survey will be conducted by a qualified archaeologist as part of the initial RI field activities. The Hanford Cultural Resource Management Plan (Chatters 1989) will be followed during the review process. No RI work will be performed in this area of known sites prior to completion of this task.

11.0 TASK 10 - DATA EVALUATION

Data gathered under the first nine tasks will be evaluated under this task. This task does not involve any field sampling or measurements, and it is discussed in Section 5.2.8 of the 100-KR-1 work plan.

12.0 TASK 11 - BASELINE RISK ASSESSMENT

Data gathered and evaluated under the first ten tasks will be used to generate a baseline risk assessment for the 100-KR-1 operable unit. This task does not involve any field sampling or measurements, and the risk assessment is discussed in Section 5.2.11 of the 100-KR-1 work plan.

13.0 TASK 12 - RI PHASE I REPORT: PRELIMINARY OPERABLE UNIT CHARACTERIZATION SUMMARY

This task consists of summarizing and presenting the results of Tasks 1 through 11, but it does not involve field sampling or measurements. The RI Phase I report is discussed in Section 5.2.12 of the work plan.

14.0 STANDARD FIELD PROCEDURES

Standard field procedures used in the 100-K Area field activities will strictly follow WHC's document, "Environmental Investigations and Site

Characterization Manual" (WHC 1989). Standard field procedures include sample designation, equipment and procedures, and handling.

14.1 SAMPLE DESIGNATION

Samples will be designated by a code, which includes a facility association code, type of sample with a sample number, depth, and analyses.

14.1.1. Facility Association

Each code will begin with a code identifying the facility with which it is associated. The WIDS number will be used for those facilities assigned a number. For those facilities not assigned a WIDS number (i.e., process effluent pipelines, and electric facilities), an abbreviation will be used followed by a number if more than one of these facilities is sampled. Examples of this coding are as follows:

- 116KW3 - Coding water retention basin waste unit 116-KW-3
- PEPX - The process effluent pipeline and number sampled

14.1.2 Type of Sample with Sample Number

The code described above will be followed by a code describing the type of sample and sample number as indicated below:

- SSX - Soil sample and sample number
- SLSX - Sludge sample and sample number
- BHX - Borehole sample and sample number
- SGX - Soil gas sample and sample number

14.1.3 Depth of Sample

The code described above will be followed by the depth of the sample in feet. If a depth range is sampled, then the greatest depth will be recorded, and if a surface sample is collected, then 00.0 will be recorded.

14.1.4 Analysis of Samples

The above codes will be followed by a code describing the required analyses or disposition (the number "2" will be appended for duplicate samples) of samples as follows:

- TCL - EPA target compound list
- TAL - EPA target analyte list
- PCB - PCBs
- SO - sulfamate and oxalate
- VOA - volatile organic analysis
- R - archive
- RAD - Radionuclides of concern
- MS - metals and radiation analysis
- AS - nonmetallic ion analysis
- SVS - semi-volatile organic analysis
- TS - physical analysis

Examples of the overall sample code are as follows:

- 116KW3-SS1-01.0-TCL (soil sample number 1, obtained from the cooling water retention basin waste unit 116-KW-3 at a 1.0 ft (0.3 m) depth for target compound list analysis.

If a Hanford Site or Westinghouse Hanford-specific sample identification or sample coding system is developed prior to field activities, then the Hanford system will be used instead of the system described above.

14.2 SAMPLE EQUIPMENT AND PROCEDURES

Details describing sampling equipment and procedures for most of the field sampling activities are described in the WHC manual on environmental investigations (WHC 1989), and include the following:

- EII 1.2 - Preparation and Revision of Environmental Investigation Instructions
- EII 1.4 - Deviation From Environmental Investigation Instructions
- EII 4.1 - Nonradioactive Hazardous Waste Disposal
- EII 4.2 - Interim Control of Unknown, Suspected Hazardous and Mixed Waste
- EII 3.2 - Health and Safety Monitoring Instruments
- EII 5.2 - Soil and Sediment Sampling
- EII 5.3 - Biotic Sampling
- EII 5.4 - Decontamination of Drilling Equipment
- EII 5.5 - Decontamination of Equipment for RCRA/CERCLA Sampling
- EII 5.6 - Control of Geophysical Logging
- EII 5.8 - Ground Water Sampling
- EII 5.9 - Soil Gas Sampling (in preparation)
- EII 5.12 - Air Quality Sampling
- EII 6.7 - Ground Water Well and Borehole Drilling
- EII 9.1 - Geologic Logging
- EII 13.1- Leak Detection Survey (in preparation)

Equipment and procedures for activities not described in the WHC document will be developed. The procedures will either be Westinghouse Hanford procedures developed in accordance with EII 1.2 "Preparation and Revision of Environmental Investigation Instructions" (WHC 1989), or participant contractor or subcontractor procedures approved and controlled as specified in Chapter 4.0 of the QAPP.

14.3 SAMPLE HANDLING

Field logs will be maintained to record all field observations and activities in accordance with EII 1.5 "Field Logbooks" (WHC 1989). Samples for laboratory analysis will be placed in containers and properly preserved in accordance with Chapter 4.0 of the QAPP. All samples for laboratory analysis will be transported under chain of custody in accordance with EII 5.1 "Chain of Custody" (WHC 1989), Chapter 5.0 of the QAPP, and EII 5.11 "Sample Packaging and Shipping" (WHC 1989).

THIS PAGE INTENTIONALLY
LEFT BLANK

Part 2

QUALITY ASSURANCE PROJECT PLAN

9 0 1 1 3 0 3 2 7

THIS PAGE INTENTIONALLY
LEFT BLANK

9 0 1 1 8 9 7 0 3 2 5

GLOSSARY

Accuracy: For the purposes of environmental investigations, accuracy may be interpreted as the measure of the bias in a system. Sampling accuracy is normally assessed through the evaluation of matrix spiked samples and reference samples.

Arithmetic Mean: The arithmetic mean is the sum of a set of n values divided by n.

Audit: For the purposes of environmental investigations, audits are considered to be systematic checks to verify the quality of operation of one or more elements of the total measurement system. In this sense, audits may be of two types: (1) performance audits, in which quantitative data are independently obtained for comparison with data routinely obtained in a measurement system, or (2) system audits, involving a qualitative onsite evaluation of laboratories or other organizational elements of the measurement system for compliance with established quality assurance program and procedure requirements. For environmental investigations at the Hanford Site, performance audit requirements are fulfilled by periodic submittal of blind samples to the primary laboratory, or the analysis of split samples by an independent laboratory. System audit requirements are implemented through the use of standard surveillance procedures.

Bias: Bias represents a systematic error that contributes to the difference between a population mean of a set of measurements and an accepted reference or true value.

Blind Sample: A blind sample refers to any type of sample routed to the primary laboratory for purposes of auditing performance relative to a particular sample matrix and analytical method. Blind samples are not specifically identified as such to the laboratory; they may be made from traceable standards, or may consist of sample material spiked with a known concentration of a known compound.

Coefficient of Variation: The coefficient of variation is the standard deviation divided by the mean, and is multiplied by 100 if expressed as a percentage.

Comparability: For the purposes of environmental investigations, comparability is an expression of the relative confidence with which one data set may be compared with another.

Completeness: For the purposes of environmental investigations, completeness may be interpreted as the percentage of measurements made, which are judged to be valid measurements.

Confidence Interval: Confidence intervals are applied to bound the value of a population parameter within a specified degree of confidence (i.e., the confidence coefficient), usually 90, 95, or 99%. The form of a confidence interval depends on the underlying assumptions and intentions. It assumes different values for different random samples, and requires specification of the number of observations on which the interval is based.

Deviation: For the purpose of environmental investigations, deviation refers to a planned departure from established criteria that may be required as a result of unforeseen field situations or that may be required to correct ambiguities in procedures that may arise in practical applications.

Equipment Blanks: Equipment blanks consist of pure deionized, distilled water washed through decontaminated sampling equipment and placed in containers identical to those used for actual field samples; they are used to verify the adequacy of sampling equipment decontamination procedures, and are normally collected at the same frequency as field duplicate samples.

Field Blanks: Field blanks consist of pure deionized, distilled water, transferred to a sample container at the site and preserved with the reagent specified for the analytes of interest; they are used to check for possible contamination originating with the reagent or the sampling environment, and are normally collected at the same frequency as field duplicate samples.

Field Duplicate Sample: Field duplicate samples are samples retrieved from the same sampling location using the same equipment and sampling technique, placed in separate identically prepared and preserved containers, and analyzed independently. Field duplicate samples are generally used to verify the repeatability or reproducibility of analytical data, and are normally analyzed with each analytical batch or every 20 samples, whichever is greater.

Geometric Mean: For a set of n positive numbers, the geometric mean is defined as the nth root of the product of their values. The geometric mean is used as a measure of central tendency for data from a log normal distribution.

Matrix Spiked Samples: Matrix spiked samples are a type of laboratory quality control sample; they are prepared by splitting a sample received from the field into two homogenous aliquots (i.e., replicate samples), and adding a known quantity of a representative analyte of interest to one aliquot to calculate percentage of recovery.

Nonconformance: A nonconformance is a deficiency in characteristic, documentation, or procedure that renders the quality of material, equipment, services, or activities unacceptable or indeterminate. When the deficiency is of a minor nature, does not effect a permanent or significant change in quality if it is not corrected, and can be brought into conformance with immediate corrective action, it shall not be categorized as a nonconformance. However, if the nature of the condition is such that it cannot be immediately and satisfactorily corrected, it shall be documented in compliance with approved procedures and brought to the attention of management for disposition and appropriate corrective action.

Precision: Precision is a measure of the repeatability or reproducibility of specific measurements under a given set of conditions. Specifically, it is a quantitative measure of the variability of a group of measurements compared to their average value. Precision is normally expressed in terms of standard deviation, but may also be expressed as the coefficient of variation (i.e., relative standard deviation) and range (i.e., maximum value minus minimum value). Precision is assessed by means of duplicate/replicate sample analysis.

Quality Assurance: For the purposes of environmental investigations, quality assurance refers to the total integrated quality planning, quality control, quality assessment, and corrective action activities that collectively ensure that the data from monitoring and analysis meets all end user requirements and/or the intended end use of the data.

Quality Assurance Project Plan: The quality assurance project plan is an orderly assembly of management policies, project objectives, methods, and procedures that defines how data of known quality will be produced for a particular project or investigation.

Quality Control: For the purposes of environmental investigations, quality assurance refers to the routine application of procedures and defined methods to the performance of sampling, measurement, and analytical processes.

Range: Range refers to the difference between the largest and smallest reported values in a sample, and is a statistic for describing the spread in a set of data.

Reference Samples: Reference samples are a type of laboratory quality control sample prepared from an independent, traceable standard at a concentration other than that used for analytical equipment calibration, but within the calibration range. Such reference samples are required for every analytical batch or every 20 samples, whichever is greater.

Relative Error: Relative error refers to the mean error of a set of measured data values as a percentage of the true value.

Replicate Sample: Replicate samples are two aliquots removed from the same sample container in the laboratory and analyzed independently.

Representativeness: For the purposes of environmental investigations, representativeness may be interpreted as the degree to which data accurately and precisely represent a characteristic of a population parameter, variations at a sampling point, or an environmental condition. Representativeness is a qualitative parameter which is most concerned with the proper design of a sampling program.

Significance Tests: Significance tests refer to a variety of methods used to check statistical hypotheses.

Skewness: Skewness is a measure of the asymmetry of a frequency distribution.

Split Sample: A split sample is produced through homogenizing a field sample and separating the sample material into two equal aliquots. Field split samples are usually routed to separate laboratories for independent analysis, generally for purposes of auditing the performance of the primary laboratory relative to a particular sample matrix and analytical method. See the glossary entry for audit above. In the laboratory, samples are generally split to create matrix spiked samples; see the glossary entry above.

Standard Deviation Estimate: The standard deviation estimate is the positive square root of the variance.

Trip Blanks: Trip blanks are a type of field quality control sample, consisting of pure deionized distilled water in a clean, sealed sample container, accompanying each batch of containers shipped to the sampling site and returned unopened to the laboratory. Trip blanks are used to identify any possible contamination originating from container preparation methods, shipment, handling, storage, or site conditions.

Validation: For the purposes of environmental investigations, validation refers to a systematic process of reviewing a body of data against a set of criteria to provide assurance that the data are acceptable for their intended use. Validation methods may include review of verification activities, editing, screening, cross-checking, or technical review.

Variance: Sample variance is a measure of the dispersion of a set of measurements; it is further defined as the sum of the squares of the individual deviations from the sample mean divided by one less that the number of results involved.

Verification: For the purposes of environmental investigations, verification refers to the process of determining whether procedures, processes, data, or documentation conform to specified requirements. Verification activities may include inspections, audits, surveillances, or technical review.

THIS PAGE INTENTIONALLY
LEFT BLANK

9 0 1 1 8 8 2 0 3 2 4

CONTENTS

1.0 Project Description QAPP-1
1.1 Project Objective QAPP-1
1.2 Background Information QAPP-1
1.3 Applicability and Relationship to the Westinghouse Hanford Company Quality Assurance Program QAPP-1
1.4 Schedule of Activities QAPP-3

2.0 Project Organization and Responsibilities QAPP-4
2.1 Technical Lead Responsibilities QAPP-4
2.2 Analytical Laboratories QAPP-4
2.3 Other Support Contractors QAPP-5

3.0 Quality Assurance Objectives for Measurements QAPP-5

4.0 Procedures QAPP-11
4.1 Approvals and Control QAPP-11
4.2 Sampling QAPP-12
4.3 Others QAPP-12
4.4 Changes QAPP-12

5.0 Sample Custody QAPP-13

6.0 Equipment Calibration QAPP-13

7.0 Analytical Methods QAPP-14

8.0 Data Reduction, Validation, and Reporting QAPP-15
8.1 Data Reduction and Data Package Preparation QAPP-15
8.2 Validation QAPP-16
8.3 Final Review and Records Management Considerations . . . QAPP-18

9.0 Internal Quality Control QAPP-19

10.0 Performance and System Audits QAPP-21

11.0 Preventive Maintenance QAPP-22

12.0 Data Assessment Procedures QAPP-22

13.0 Corrective Action QAPP-23

14.0 Quality Assurance Reports QAPP-23

15.0 References QAPP-24

FIGURE

QAPP 1. Location of 100-KR-1 Operable Unit QAPP-2

TABLES

QAPP 1. Precision, Accuracy, Completeness, and Target Detection Limits for Soil Samples and Surface Water Analysis QAPP-7

QAPP 2. Analytical Method and Handling Requirements for Soil Samples and Surface Water Samples QAPP-10

1.0 PROJECT DESCRIPTION

1.1 PROJECT OBJECTIVE

The primary objective of the environmental investigations in the 100-KR-1 operable unit is to further define the extent and location of sources of radioactive contamination and other inorganic, organic, and volatile and nonvolatile organic contaminants in the vadose zone and underlying aquifers. Data resulting from this investigation will be evaluated to determine the most feasible options for additional investigation, remediation or closure.

1.2 BACKGROUND INFORMATION

The 100-KR-1 operable unit is located in the north central part of the Hanford Site, Benton County, Washington, situated along the southern shoreline of the Columbia River as shown in Figure QAPP-1. Detailed background information regarding the history and present use of the unit is provided in Chapter 2.0 of the 100-KR-1 operable unit work plan.

1.3 APPLICABILITY AND RELATIONSHIP TO WESTINGHOUSE HANFORD COMPANY QUALITY ASSURANCE PROGRAM

This quality assurance project plan (QAPP) applies specifically to the Phase I field activities and laboratory analyses performed as part of the environmental investigations in 100-KR-1. It is an element of the sampling and analysis plan (SAP) prepared specifically for this phase of investigation, and is prepared in compliance with the Westinghouse Hanford QA program plan for Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA) remedial investigation/feasibility study (RI/FS) activities. This plan describes the means selected to implement the overall QA program requirements defined by the *Westinghouse Hanford Company Quality Assurance Manual*, WHC-CM-4-2, (WHC 1989a), as applicable to CERCLA RI/FS environmental investigations, while accommodating the specific requirements for work plan format and content agreed upon in the *Hanford Federal Facility Agreement and Consent Order* (Ecology et al. 1989). It contains a matrix of procedural resources from WHC-CM-4-2 and the *Environmental Investigations and Site Characterization Manual* (WHC-CM-7-7)

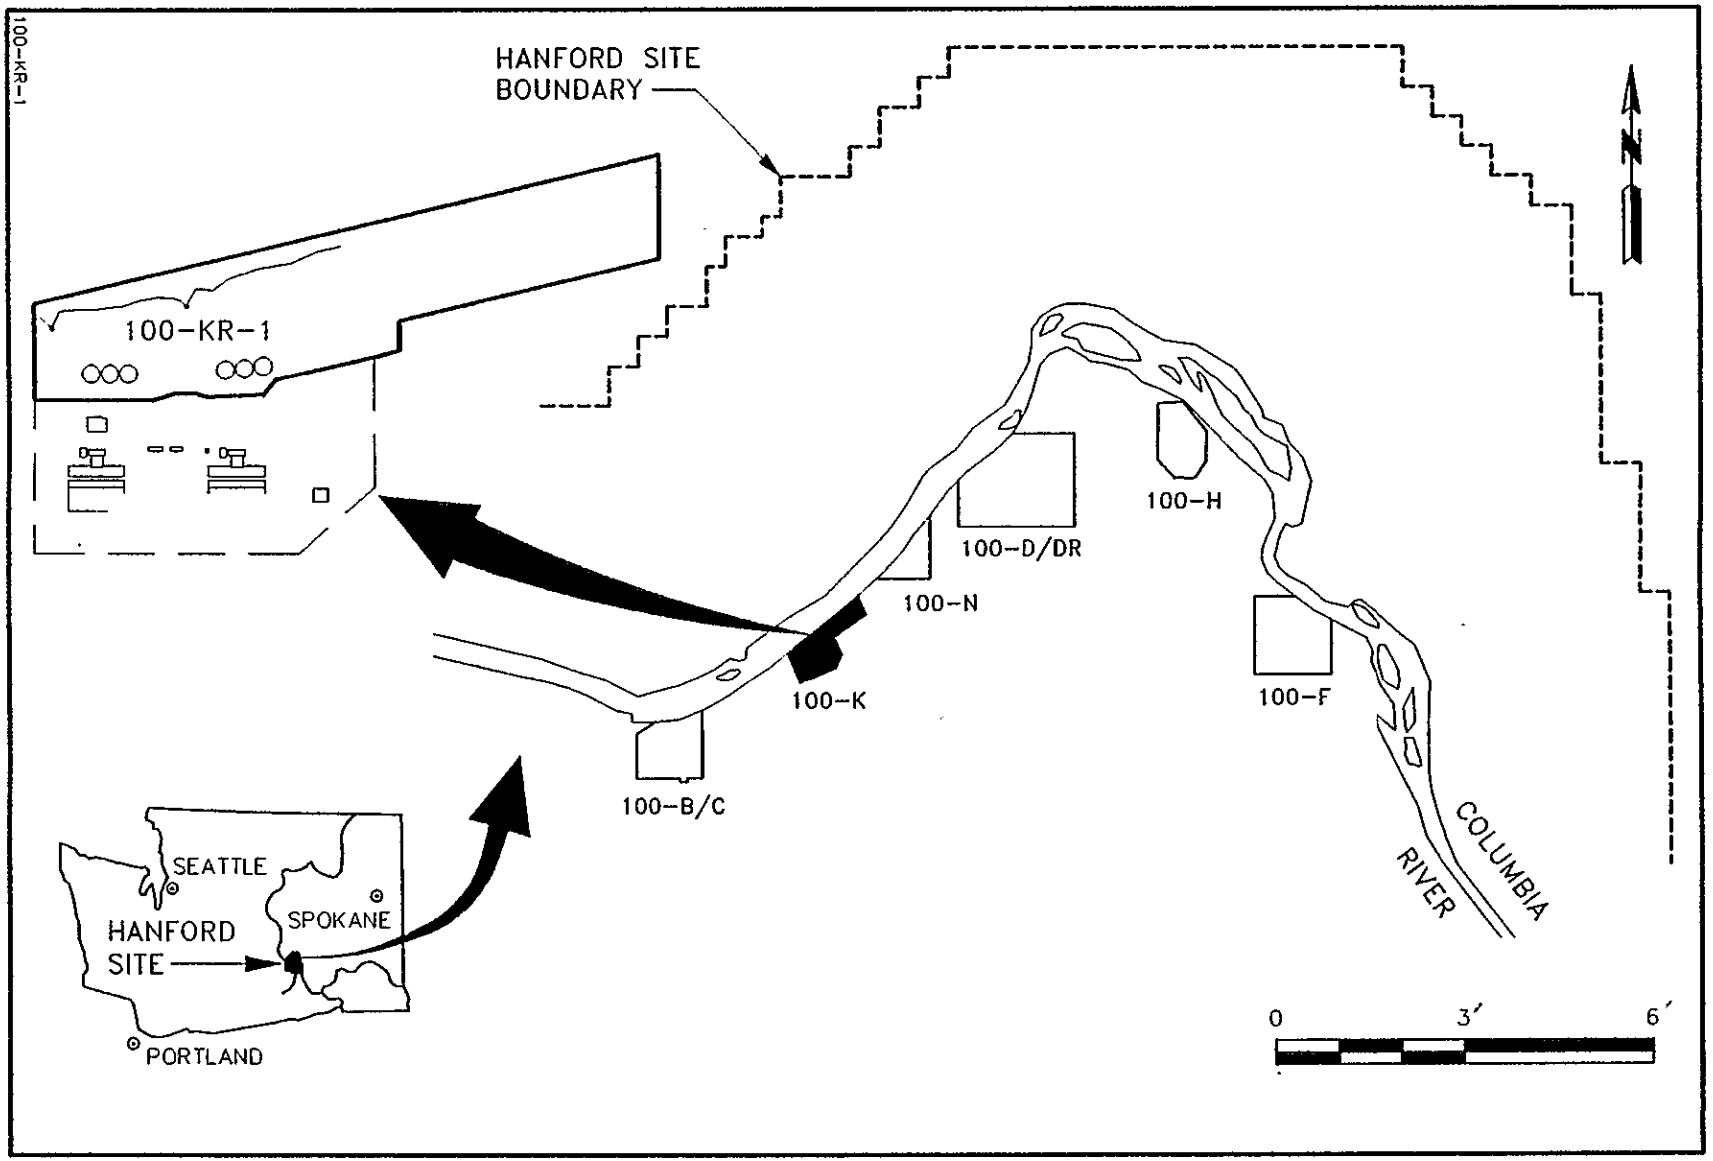

Figure QAPP-1. Northern Hanford Site and 100-K Area Operable Units.

(WHC 1989b). This plan is subject to mandatory review and revision control and shall be in compliance with quality requirements (QR) 6.0 "Document Control" from (WHC-CM-4-2) (WHC 1989a) and other standard Westinghouse Hanford Company (Westinghouse Hanford) document control procedures. All plans and procedure referenced in the QAPP are available for regulatory review on request by the direction of the Technical Lead.

1.4 SCHEDULE OF ACTIVITIES

The investigations that will be conducted in the 100-KR-1 operable unit will be subdivided into phases and a number of individual tasks. Because results of the task activity in an individual phase may significantly affect the technical activities planned for subsequent phases, this QAPP shall undergo mandatory review after completion of each phase and shall be updated or modified to accommodate any required revisions in the scope of work. This version of the QAPP applies specifically to Phase I of the RI.

Individual tasks for the Phase I are listed below. Detailed discussions are contained in Section 5.2 of the work plan and the field sampling plan (FSP).

- Task 1 - Project Management
- Task 2 - Source Investigations
- Task 3 - Geologic Investigations
- Task 4 - Source Water and Sediments Investigations
- Task 5 - Vadose Zone Investigations
- Task 6 - Ground Water Investigation
- Task 7 - Air Investigations
- Task 8 - Ecological Investigations
- Task 9 - Other
- Task 10 - Data Validation and Evaluation

- Task 11 - Baseline Risk Assessment
- Task 12 - Phase I RI Report

2.0 PROJECT ORGANIZATION AND RESPONSIBILITIES

2.1 TECHNICAL LEAD RESPONSIBILITIES

The Environmental Engineering, Technology, and Permitting Function of Westinghouse Hanford has primary responsibility for conducting this investigation. Organizational charts are included in the project management plan (PMP) for this operable unit that define personnel assignments and individual Westinghouse Hanford field team structures applicable to the various types of tasks included in the Phase I RI.

External participant contractors or subcontractors shall be evaluated and selected for certain portions of task activities at the direction of the Technical Lead in compliance with procedures QR 4.0 "Procurement Document Control," QI 4.1 "Procurement Document Control," quality instruction (QI) 4.2 "External Services Control," QR 7.0 "Control of Purchased Items and Services," QI 7.1 "Procurement Planning and Control," and QI 7.2 "Supplier Evaluation" (WHC 1989a). All contractor plans and procedures shall be approved prior to use, and shall be available for regulatory review after Westinghouse Hanford approval. All analytical procedures shall be reviewed and approved by the Westinghouse Hanford analytical laboratories organization.

2.2 ANALYTICAL LABORATORIES

A Westinghouse Hanford field sampling team will be assigned responsibility for screening all samples for gross alpha and beta/gamma radioactivity, and for separating samples into two groups for further analysis. Samples with an activity level greater than or equal to those derived from DOE Order 5480.11, *Radiation Protection for Occupational Workers* (DOE 1988) and 5400.5, *Radiation Protection of the Public and the Environment* (DOE 1990) will be routed to a Westinghouse Hanford or another Hanford Site participant contractor laboratory equipped and qualified to perform analysis of radioactive samples. For subcontractors or participant

contractors, applicable QR shall be invoked as part of the approved procurement document or work order. At the Technical Lead's direction, services of alternate qualified laboratories shall be procured for radioactive sample analysis (if onsite laboratory capacity is not available) and for the performance of split sample analysis. If such an option is selected, the QA plan and applicable analytical procedures from the alternate laboratory shall be approved by Westinghouse Hanford prior to their use. All analyses shall be coordinated through the Westinghouse Hanford Office of Sample Management (OSM) and shall be performed in compliance with Westinghouse Hanford-approved laboratory QA plans and analytical procedures, subject to the surveillance controls invoked by QI 7.3 "Source Surveillance and Inspection" (WHC 1989a).

2.3 OTHER SUPPORT CONTRACTORS

Procurement of all other contracted field activities shall be in compliance with standard Westinghouse Hanford procurement procedures requirements as discussed in Sections 2.1 and 4.1. All work shall be performed in compliance with Westinghouse Hanford-approved QA plans/procedures, subject to the controls of QI 7.3 "Source Surveillance and Inspection" (WHC 1989a) if the work is performed offsite. Onsite work is subject to controls identified in QI 10.4 "Surveillance" (WHC 1989a). Applicable QR shall be invoked as part of the approved procurement document or work order.

3.0 QUALITY ASSURANCE OBJECTIVES FOR MEASUREMENTS

Data quality objectives for the 100-KR-1 operable unit are summarized in Chapter 4.0 of the work plan. Additional analytical data based on soil and ground water sampling activities will be obtained and evaluated to further characterize the nature and extent of radioactive and hazardous contamination and to determine the most feasible options for remediation. Analytical data will be obtained at several different levels, based on the criteria provided in *Data Quality Objectives for Remedial Response Activities: Volume 1, Development Process* (EPA 1987), and are described below:

- Level V. Nonstandard methods will be required for analysis of radionuclides. Depending on the level of radioactivity noted in

screening, analysis will either be performed onsite by a qualified Westinghouse Hanford or participant contractor laboratory, or offsite by an approved subcontractor or participant contractor. Laboratories may or may not be contract laboratory program (CLP) laboratories, and new or modified analytical methods will be required. Detection limits, precision, and accuracy will be specific to the method, which must be prepared, reviewed, and approved prior to use in compliance with applicable Westinghouse Hanford procurement control procedures.

- Level IV. The CLP routine analytical services (RAS) methods will be required for selected organic and inorganic analyses as indicated in Table QAPP-1. All such analyses shall be performed onsite or offsite by a CLP-qualified laboratory, based on the results of Level I radiation screening. Participant contractor or subcontractor services shall be controlled through applicable Westinghouse Hanford procurement and work control procedures (Section 4.1).

- Level III. Level III analyses shall be acceptable for selected analytes using standard U.S. Environmental Protection Agency (EPA) and American Society for Testing and Materials (ASTM) methods, as shown in Table QAPP-1. Data validation requirements and intralaboratory quality control (QC) requirements shall be invoked that, in terms of data quality, approximate the requirements of the CLP for Level IV analysis.

- Level II. Field analysis is characterized by the use of portable analytical instruments which can be used onsite, or in a mobile laboratory stationed near the site. Methods such as x-ray fluorescence (XRF), specific conductance, headspace/gas chromatography (GC), solvent extraction/ GC, beta/gamma radiation quantification, and use of ion selective electrodes represent field analyses that will be conducted during the remedial investigation. Samples exhibiting above-background levels will necessitate laboratory analysis by Level III, IV, or V methods as appropriate.

Table QAPP-1. Precision, Accuracy, Completeness and Target Detection Limits for Groundwater and Surface Water Analyses

Page 1

Parameter	Analytical Method	Precision (Relative Percent Difference)	Accuracy (% Spike) Recovery	Completeness (%)	Target Detection Limit (ug/L)
Organic Compounds					
Target Compound List (TCL) Volatile Organics[a] (Purgeable Compounds)	624[d]	See Table 3-22	See Table 3-22	95	CLP[b]
TCL Semivolatile Extractable Acid Base/Neutral Compounds	625[d]	See Table 3-22	See Table 3-22	95	CLP[b]
TCL Pesticide/PCB	608[d]	See Table 3-22	See Table 3-22	95	CLP[b]
Target Analyte List (TAL) Metals (Total)					
Aluminum	CLP	±20	75-125	95	200
Antimony	CLP	±20	75-125	95	60
Arsenic	CLP	±20	75-125	95	10
Barium	CLP	±20	75-125	95	200
Beryllium	CLP	±20	75-125	95	5
Cadmium	CLP/213.2[d]	±20	75-125	95	1.1[c]
Calcium	CLP	±20	75-125	95	5000
Chromium, Total	CLP	±20	75-125	95	10
Chromium, Hexavalent	7196[e]	±20	75-125	95	10
Cobalt	CLP	±20	75-125	95	50
Copper	CLP/220.2[d]	±20	75-125	95	3[c]
Iron	CLP	±20	75-125	95	100
Lead	CLP	±20	75-125	95	3
Magnesium	CLP	±20	75-125	95	5000
Manganese	CLP	±20	75-125	95	15
Mercury	CLP	±20	75-125	95	0.2
Nickel	CLP	±20	75-125	95	40
Potassium	CLP	±20	75-125	95	5000
Selenium	CLP	±20	75-125	95	5
Silver	CLP/272.2[d]	±20	75-125	95	10
Sodium	CLP	±20	75-125	95	5000
Thallium	CLP	±20	75-125	95	10
Vanadium	CLP	±20	75-125	95	50
Zinc	CLP	±20	75-125	95	20
General Chemical					
Ammonia, as N	350.2	±20	NA	95	[f]
Alkalinity	310.1	±20	NA	95	[f]
Bicarbonate	403	±20	NA	95	[f]
Biochemical Oxygen Demand	405.1	±20	NA	95	[f]
Carbonate	403	±20	NA	95	[f]
Chemical Oxygen Demand	410.1	±20	NA	95	[f]
Chloride	325.3	±20	NA	95	[f]
Conductivity	NA	±20	NA	95	[f]
Dissolved Oxygen	NA	±20	NA	95	[f]
Fluoride	340.2	±20	NA	95	[f]
Hardness	130.2	±20	NA	95	[f]
Nitrate, as NO_3	353.2/353.3	±20	NA	95	[f]
pH	NA	±20	NA	95	[f]
Phosphate, as P	365.2/365.4	±20	NA	95	[f]
Sulfate	375.2/375.4	±20	NA	95	[f]
Total Dissolved Solids	160.1	±20	NA	95	[f]
Total Suspended Solids	160.2	±20	NA	95	[f]
Cyanide	335.2	±20	NA	95	[f]

Table QAPP-1. Precision, Accuracy, Completeness and Target Detection Limits for Groundwater and Surface Water Analyses

Parameter	Analytical Method	Precision (Relative Percent Difference)	Accuracy (% Spike) Recovery	Completeness (%)	Target Detection Limit (ug/L)
Radionuclides					
^{60}Cobalt	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{63}Nickel	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{137}Cesium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{152}Europium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{154}Europium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
Gross Alpha	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
Gross Beta	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{129}Iodine	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
Plutonium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{129}Strontium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{99}Technetium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
Tritium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
Uranium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{14}Carbon	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse
^{241}Americium	Westinghouse	Westinghouse	Westinghouse	Westinghouse	Westinghouse

[a] Denotes toxic pollutant.
[b] U.S. EPA Contract Laboratory Program, Statement of Work for Organics 288 and Inorganics 788. (EPA 1988c, 1989a)
[c] The detection limits for these elements should be lower than the CLP Detection limits for Chronic Quality Criteria.
[d] Methods for Chemical Analysis of Water and Wastes. EPA-60014-79-020. (EPA 1983a)
[e] Test Methods for Evaluating Solid Waste--Physical/Chemical Methods, 3rd edition, EPA SW-846, (EPA 1986)
[f] General chemical parameter detection limits are matrix- and laboratory-specific.

H:\1842\TABLES\KR4\QAPP\182

- Level I. Field screening is characterized by use of portable instruments which can provide real-time data to assist in the optimization of sampling point locations and for health and safety support. Soil samples shall undergo field screening to determine gross alpha and beta/gamma radiation and the presence of combustible and/or ionizable organic compounds. Samples exhibiting radioactivity greater than or equal to those derived from DOE Order 5480.11 (DOE 1988) and 5400 (DOE 1990) will be routed to an appropriately equipped and qualified on-site Westinghouse Hanford or participant contractor laboratory for analysis. Screening shall be performed by qualified Westinghouse Hanford health physics technicians as specified in governing procedures.

As noted in Section 4.6 of *Data Quality Objectives for Remedial Response Activities: Volume 1, Development Process* (EPA 1987), universal goals for precision, accuracy, representativeness, completeness, and comparability parameters cannot be practically established at the beginning of an investigation. Historical data are available, however, that may be used as minimum guidelines for selection or preparation of analytical methods appropriate for this investigation. Table QAPP-1 provides preliminary values, guidelines and reference sources for method detection limits, precision, and accuracy that are intended for use in initial procurement negotiations with the analytical laboratory. These preliminary values are based on the results of evaluation of the data quality objectives specified in Table QAPP-2, the reference specifications identified in Table QAPP-1 and the general performance capabilities currently expected for laboratories involved in environmental analyses. After individual laboratory statements of work are negotiated and procedures are developed and approved, Table QAPP-1 and this section shall be revised to reference approved detection limits, precision, and accuracy criteria as project requirements.

Goals for data representativeness are addressed qualitatively by the specification of sampling locations and intervals within the FSP. Objectives for this investigation shall require that contractually or procedurally established requirements for precision and accuracy be met for at least 90% of the total number of requested determinations. Failure to meet this criterion shall be documented in data summary reports and shall be considered in the validation process. Corrective action measures shall be initiated by the Technical Lead as appropriate. Approved analytical procedures shall require the use of the reporting techniques and units consistent with EPA reference methods listed in Table QAPP-1 to facilitate the comparability of data sets in terms of precision and accuracy.

TABLE QAPP-2. Analytical Method and Handling Requirements for Ground Water and Surface Water Samples.

Description	Method[a]	Container Requirement	Preservative	Holding Time
TCL volatile organics	624	3 40-mL amber glass	HCl pH<2 Cool 4°C	14 d
TCL semivolatile organics	625	2 80-oz amber glass	Cool 4°C	7 d
TCL pesticides/PCBs	608	1 80-oz amber glass	Cool 4°C	7 d
TAL Metals	CLP	1 1-L HDPE	HNO^3 pH<2 Cool 4° C	6 mo
Chromium, hexavalent	7196	250-mL HPDE	Cool 4°C	6 mo
Radionuclides	Westinghouse			
Oxalate	Westinghouse			
Sulfamate	Westinghouse			
Ammonia-N	350.2	1 1-L HDPE	H_2SO_4 pH<2 Cool 4° C	28 d
Alkalinity	310.1	1 250-mL HDPE	Cool 4°C	14 d
BOD	405.1	1 1-L HDPE	Cool 4°C	48 h
COD	410.1	1 125-mL HDPE	Cool 4°C H_2SO_4 pH<2	28 d
DO	NA	300-mL	None	Analyze immediately
Hardness	130.2	250-mL HDPE	HNO_3 pH<2 Cool 4°C	6 mo
Organic carbon	415.1	1 125-mL HDPE	HCl pH<2 Cool 4°C	28 d
Nitrate[b]	353.2/353.3	1 25-mL HDPE	Cool 4°C	48 h
Sulfate[b]	375.2/375.4	1 125-mL HDPE	Cool 4°C	28 d
Chloride[b]	325.3	1 125-mL HDPE	None	28 d
Fluoride[b]	340.2	1 500-mL HDPE	None	28 d
Total dissolved solids[b]	160.1	1 125-mL HDPE	Cool 4OC	7 d
Total suspended solids[b]	160.2	1 125-mL HDPE	Cool 4OC	7 d
Phosphate (ortho)[b]	365.2/365.4	1 125-mL HDPE	Cool 4°C	48 h
pH[b]	150.1	-	-	Field measurement
Conductivity[b]	120.1	-	-	Field measurement
Carbonate[b]	403	1 125-mL HDPE	Cool 4°C	14 d
Bicarbonate[b]	403	1 125-mL HDPE	Cool 4°C	14 d

[a] EPA 1982
[b] May be analyzed from the same aliquot.

TCL = Target compound list
HDPE = High-density polyethylene
BOD = Biochemical oxygen demand
COD = Chemical oxygen demand
DO = Dissolved oxygen
CLP = Contract laboratory program
H:\1842\TABLES\KR4\QAPP\186

4.0 PROCEDURES

4.1 APPROVALS AND CONTROL

4.1.1 Westinghouse Hanford

The Westinghouse Hanford procedures cited in this QAPP have been selected from the quality assurance program index included in a Westinghouse Hanford QA program plan for CERCLA RI/FS activities. Selected procedures include environmental investigations instructions (EII) from the *Environmental Investigations and Site Characterization Manual* (WHC 1989b), and QR and QI from the *Westinghouse Hanford Quality Assurance Manual* (WHC 1989a). Procedure approval, revision, and distribution control requirements applicable to EII are addressed in EII 1.2 "Preparation and Revision of Environmental Investigation Instructions" (WHC 1989b); requirements applicable to QI and QR are addressed in QR 5.0 "Instructions, Procedures, and Drawings," QI 5.1 "Preparation of Quality Assurance Documents," QR 6.0 "Document Control," and QI 6.1 "Quality Assurance Document Control" (WHC 1989a). Other procedures applicable to the preparation, review, approval, and revision of Hanford Analytical Laboratories organization procedures shall be as defined in the various procedures and manuals identified in the quality assurance program for CERCLA RI\FS activities. All procedures are available for regulatory review on request, at the direction of the Westinghouse Hanford Technical Lead.

4.1.2 Participant Contractor/Subcontractor

As noted in Section 2.1, participant contractor/subcontractor services shall be procured under the applicable requirements of QR 4.0 "Procurement Document Control," QI 4.1 "Procurement Document Control," QI 4.2 "External Services Control," QR 7.0 "Control of Purchased Items and Services," QI 7.1 "Procurement Planning and Control" and/or QI 7.2 "Supplier Evaluation" (WHC 1989a). Whenever such services require procedural controls, requirements for submittal of procedures for Westinghouse Hanford review and approval prior to use shall be included in the procurement document or work order, as applicable. In addition to the submittal of analytical procedures, analytical laboratories shall be required to submit the current version of their internal QA program plans.

4.2 SAMPLING

4.2.1 Soil Sampling

All soil sampling shall be performed in accordance with EII 5.2 "Soil and Sediment Sampling" (WHC 1989b). All drilling activities shall be in compliance with EII 6.7 "Ground Water Well and Borehole Drilling" (WHC 1989b). All boreholes shall be logged in compliance with EII 9.1 "Geologic Logging" (WHC 1989b). Test pit sampling shall be in accordance with the auger or grab sample techniques described in EII 5.2. Sample numbers, types location, and other site-specific considerations shall be as defined by the FSP. Documentation requirements are contained within individual EII and the data management plan (DMP). Sampling procedures applicability to individual Phase I tasks are shown in Table QAPP-2.

4.2.2 Sample Preparation and Handling

Sample container types, preservation requirements, preparation requirements, and special-handling requirements are defined by EII 5.2 "Soil and Sediment Sampling" and EII 5.11 "Sample Packaging and Shipping" (WHC 1989b).

4.3 OTHERS

Other procedures that will be required in this phase of the investigation are identified in Table QAPP-2, for each individual task. Documentation requirements shall be addressed within individual procedures and/or the DMP as appropriate. Analytical procedures are listed in Table QAPP-1.

4.4 CHANGES

Should deviations from established EII be required to accommodate unforeseen field situations, they may be authorized by the Field Team Leader in accordance with the requirements specified in EII 1.4 "Deviation from Environmental Investigation Instructions" (WHC 1989b). Documentation, review, and disposition of instruction change authorization forms are defined within EII 1.4. Other types of procedure change requests shall be documented as required by the Westinghouse Hanford procedures governing their preparation.

5.0 SAMPLE CUSTODY

All samples obtained during the course of this investigation shall be controlled as required by EII 5.1 "Chain of Custody" (WHC 1989b), from the point of origin to the analytical laboratory. Laboratory chain-of-custody procedures shall be reviewed and approved in compliance with the requirements of Section 4.1 of this QAPP, and shall ensure the maintenance of sample integrity and identification throughout the analytical process. At the direction of the Technical Lead, requirements for the return of residual sample materials after completion of analysis shall be defined in accordance with procedures defined in the procurement documentation to participant contractor/subcontractor laboratories. Chain-of-custody forms shall be initiated for returned residual samples as required by the approved procedures applicable within the participating laboratory. Results of analyses shall be traceable to original samples through the unique code or identifier specified in the FSP. All results of analyses shall be controlled as permanent project quality records as required by QR 17.0 "Quality Assurance Records" (WHC 1989a), EII 1.6 "Records Management" (WHC 1989b), and the DMP.

6.0 EQUIPMENT CALIBRATION

Calibration of all Westinghouse Hanford measuring and test equipment, whether in existing inventory or purchased for this investigation, shall be controlled as required by QR 12.0 "Control of Measuring and Test Equipment," QI 12.1 "Acquisition and Calibration of Portable Measuring and Test Equipment" (WHC 1989a), QI 12.2 "Measuring and Test Equipment Calibration by User" (WHC 1989a) and/or EII 3.1 "User Calibration of Health and Safety Measuring and Test Equipment" (WHC 1989b). Routine operational checks for Westinghouse Hanford field equipment shall be as defined within applicable EII or procedures; similar information shall be provided in Westinghouse Hanford-approved participant contractor or subcontractor procedures.

Calibration of Westinghouse Hanford, participant contractor, or subcontractor laboratory equipment used for Level III analysis shall be as defined by applicable standard analytical methods, subject to Westinghouse Hanford review and approval. Calibration of Westinghouse Hanford, participant contractor, or subcontractor

laboratory equipment used for Level V analysis shall be as defined by the Westinghouse Hanford-approved analytical method.

7.0 ANALYTICAL METHODS

Analytical methods or procedures for each analytical level identified in Table QAPP-1 and Chapter 3.0 shall be selected or developed and approved prior to use in compliance with appropriate Westinghouse Hanford procedure and/or procurement control requirements. As noted in Section 4.6 of *Data Quality Objectives for Remedial Response Activities: Volume 1, Development Process* (EPA 1987), universal goals for precision, accuracy, representativeness, completeness and comparability cannot be practically specified at the beginning of an investigation. Historical data for precision and accuracy are available for many analytes of interest, however, and shall be used as minimum guidelines for selection or preparation of analytical methods appropriate for this investigation. Table QAPP-1 provides general guidelines and reference sources for method detection limits, precision and accuracy as available for each analyte of interest sorted by the required analytical level. Where guidelines are not available, statistical guidelines appropriate for determining precision and accuracy shall be developed, included in procedures, and submitted for Westinghouse Hanford review and approval. Once individual laboratory statements of work are negotiated and procedures are approved, Table QAPP-1 shall be revised to include actual method references and approved detection limit, precision, and accuracy criteria as project requirements.

All analytical procedures approved for use in this investigation shall require the use of standard reporting techniques and units to facilitate the comparability of data sets in terms of precision and accuracy. All approved procedures shall be retained in the project quality records and shall be available for review on request, at the direction the Westinghouse Hanford Technical Lead.

9 0 1 1 8 3 0 2 5 0

8.0 DATA REDUCTION, VALIDATION, AND REPORTING

8.1 DATA REDUCTION AND DATA PACKAGE PREPARATION

All analytical laboratories shall be responsible for preparing a report summarizing the results of analysis and for preparing a detailed data package that includes all information necessary to perform data validation. Data summary report format and data package content shall be defined in the laboratories' analytical methods/internal QA program plans, subject to Westinghouse Hanford review and approval requirements as noted in Section 4.1. As a minimum, data packages shall include the following:

- Sample receipt and tracking documentation, including identification of the organization and individuals performing the analysis, the names and signatures of the responsible analysts, sample holding time requirements, references to applicable chain-of-custody procedures, and the dates of sample receipt, extraction, and analysis

- Instrument calibration documentation, including equipment type and model, with continuing calibration data for the time period in which the analysis was performed

- QC data, as appropriate for the methods used, including matrix spike/matrix spike duplicate data, recovery percentages, precision data, laboratory blank data, and identification of any nonconformances that may have affected the laboratory's measurement system during the time period in which the analysis was performed

- The analytical results or data deliverables, including reduced data, reduction formulas or algorithms, and identification of data outliers or deficiencies.

Other supporting information, such as initial calibration data, reconstructed ion chromatographs, spectrograms, traffic reports, and raw data, need not be included in the submittal of individual data packages unless specifically required to support validation report preparation for the CLP statements of work (EPA 1988c, 1989a) methods as defined in Section 8.2.3. All sample data, however, shall be retained by

the analytical laboratory and made available for systems or program audit purposes upon request by Westinghouse Hanford, U.S. Department of Energy-Richland Operations Office (DOE-RL), or regulatory agency representatives. Such data shall be retained by the analytical laboratory through the duration of their contractual statement of work, at which point it shall be turned over to Westinghouse Hanford for archiving.

The completed data package shall be reviewed and approved by the analytical laboratory's QA manager prior to submittal to Westinghouse Hanford for validation. The requirements of this section shall be included in procurement documentation or work orders, as appropriate, in compliance with the standard Westinghouse Hanford procurement control procedures referenced in Section 4.1.

8.2 VALIDATION

Validation of the completed data package may be performed by qualified Westinghouse Hanford personnel from the OSM, other Westinghouse Hanford organizations, or a qualified, independent, participant contractor or subcontractor in accordance with established procedures that follow EPA guidelines (1988a and b). Selection of qualified reviewers and assignment of validation responsibilities shall be as directed by the Westinghouse Hanford Technical Lead and shall be defined in procurement documentation or work orders as appropriate.

8.2.1 Level II Validation Report Preparation

Level II screening analyses performed for this investigation are noted in Chapter 3.0 and Table QAPP-1. All procedures shall include specific requirements for validation report preparation that are appropriate for the particular procedure and equipment type, and shall be reviewed and approved by Westinghouse Hanford prior to implementation in compliance with the standard Westinghouse Hanford procurement control procedures referenced in Section 4.1.

8.2.2 Level III Validation Report Preparation

All validation report requirements for Level III and Level V analyses shall be established within individual methods requirements, subject to Westinghouse Hanford review and approval as discussed in Section 4.1. Validation report requirements shall be in general compliance with the guidelines provided in EPA guidelines for Level IV analyses, modified as necessary to accommodate the allowances of the applicable reference methods listed for each analyte of interest in Table QAPP-1. In general, for organic analyses, validation reports shall be prepared documenting overchecks of the following areas as recommended in *Laboratory Data Validation Functional Guidelines for Evaluating Organics Analyses* (EPA 1988a):

- Data summary narrative
- Sample holding times
- Gas chromatograph/mass spectrometer tuning and mass calibration requirements
- Continuing calibration requirements
- Method blank sample requirements
- Surrogate recovery requirements
- Matrix spike/matrix spike duplicate requirements
- Internal standards performance requirements
- Target compound identification requirements
- Target compound quantification requirements and reported detection limits
- Any tentatively identified compounds, library search, assessment, and quantification requirements
- Overall data assessment requirements.

For inorganic analyses, validation reports shall be prepared documenting overchecks of the following areas, as recommended in *Laboratory Data Validation Functional Guidelines for Evaluating Inorganics Analyses* (EPA 1988b):

- Data summary narrative
- Sample holding times
- Continuing calibration requirements
- Method blank sample requirements
- Interference check sample requirements
- Laboratory control sample requirements
- Duplicate sample analysis
- Matrix spike sample requirements
- Atomic absorption QC requirements
- Inductively coupled plasma serial dilution requirements
- Overall data assessment requirements.

8.3 FINAL REVIEW AND RECORDS MANAGEMENT CONSIDERATIONS

All validation reports and supporting analytical data packages shall be subjected to a final technical review by a qualified reviewer at the direction of the Westinghouse Hanford Technical Lead, prior to submittal to the regulatory agencies or inclusion in reports or technical memoranda. All validation reports, data packages, and review comments shall be retained as permanent project quality records in compliance with EII 1.6 "Records Management" (WHC 1989b), QR 17.0 "Quality Assurance Records" (WHC 1989a), and the DMP.

9.0 INTERNAL QUALITY CONTROL

All analytical samples shall be subject to in-process QC measures in both the field and laboratory. Unless otherwise specified in the approved FSP, the following minimum field QC requirements apply for Level III and V analyses. These requirements are adapted from *Test Methods for Evaluating Solid Waste* (EPA 1986), as modified by the proposed rule changes included in the Federal Register, Volume 54, No. 13 (EPA 1989b).

- Field duplicate samples. For each shift of sampling activity under an individual sampling subtask, a minimum of 5% of the total collected samples shall be duplicated, or one duplicate shall be collected for every 20 samples, whichever is greater. Duplicate samples shall be retrieved from the same sampling location using the same equipment and sampling technique, and shall be placed into two identically prepared and preserved containers. All field duplicates shall be analyzed independently as an indication of gross errors in sampling techniques.

- Split samples. At the Technical Lead's direction, field or field duplicate samples may be split in the field and sent to an alternative laboratory as a performance audit of the primary laboratory. Split samples shall be analyzed by the independent laboratory compliance with approved methods based on the same reference standards that are invoked for the primary laboratory. For this investigation, performance requirements shall be met by analyzing a minimum of one split sample for each analytical method identified in Table QAPP-1.

- Blind samples. At the Technical Lead's direction, blind reference samples may be introduced into any sampling round as a performance and audit of the primary laboratory. Blind sample type shall be as directed by the Technical Lead and may be from traceable standards or from routine samples spiked with a known concentration of a known compound. For this investigation, performance requirements shall be met by analyzing a minimum of one blind sample for each analytical method identified in Table QAPP-1.

- Field blanks. Field blanks shall consist of pure deionized distilled water, transferred into a sample container at the site and preserved with the reagent specified for the analytes of interest. Field blanks are used as a check on reagent and environmental contamination, and shall be collected at the same frequency as field duplicate samples.

- Equipment blanks. Equipment blanks shall consist of pure deionized distilled water washed through decontaminated sampling equipment and placed in containers identical to those used for actual field samples. Equipment blanks are used to verify the adequacy of sampling equipment decontamination procedures, and shall be collected at the same frequency as field duplicate samples.

- Trip blanks. At the Technical Lead's direction, trip blanks may be introduced into any sampling round. Trip blanks consist of pure deionized distilled water added to one clean sample container, accompanying a batch of containers shipped to the sampling activity. Trip blanks shall be returned unopened to the laboratory, and are prepared as a check on possible contamination originating from container preparation methods, shipment, handling, storage, or site conditions. In compliance with standard Westinghouse Hanford procurement procedures, requirements for trip blank preparation shall be included in procurement documents of work orders to the sample container supplier and/or preparer.

The internal QC checks performed by analytical laboratories for Level III and Level V laboratory analyses shall meet the following minimum requirements.

- Matrix spiked samples. Matrix spiked samples require the addition of a known quantity of a representative analyte of interest to the sample as a measure of recovery percentage. The spike shall be made in a replicate of a field sample. Replicate samples are separate aliquots removed from the same sample container in the laboratory. Spike compound selection, quantities, and concentrations shall be described in the analytical procedures submitted for Westinghouse Hanford review and approval. At the direction of the Technical Lead, one sample shall be spiked per analytical batch, or once every 20 samples, whichever is greater, when required.

- QC reference samples and appropriate QA requirements. A QC reference sample shall be prepared from an independent standard at a concentration other than that used for calibration, but within the calibration range. Reference samples may be required as an independent check on analytical technique and methodology, and if required, shall be run with every analytical batch, or every 20 samples, whichever is greater.

Other requirements specific to laboratory analytical equipment calibration are included in Chapter 6.0.

The minimum requirements of this section shall be invoked in procurement documents or work orders in compliance with standard Westinghouse Hanford procedures as noted in Section 4.1.

10.0 PERFORMANCE AND SYSTEM AUDITS

As noted in Section 5.12 and Appendix A of *Interim Guidelines and Specifications for Preparing Quality Assurance Project Plans*, (EPA 1983b), audits in environmental investigations are considered to be systematic checks that verify the quality of operation of one or more elements of the total measurement system. System audit requirements shall be implemented through the use of procedure QI 10.4 "Surveillance" (WHC 1989a). Surveillances will be performed regularly throughout the course of the work plan activities. All quality affecting activities are subject to surveillance.

Additional performance and system audits will be scheduled as a consequence of corrective action requirements, or may be performed upon request by the Quality Coordinator, the Technical Lead, DOE-RL, Ecology, or the EPA. Any discrepancies observed during the evaluation of performance results during surveillance activities that cannot be immediately corrected to the satisfaction of the investigator shall be documented on a surveillance report and resolved in compliance with procedure QI 10.4 "Surveillance" (WHC 1989a). In addition, at the direction of the Westinghouse Hanford Environmental QA Officer, all aspects of 100-KR-1 project activities may also be evaluated as part of routine environmental restoration program-wide QA audits under the procedural requirements of WHC-CM-4-2 (WHC 1989a). Program audits shall be conducted in compliance with QR 18.0 "Audits," QI 18.1 "Audit Programming and Scheduling" and QI 18.2 "Planning, Performing, Reporting, and

Follow-up of Quality Audits" by auditors qualified in compliance with QI 2.5 "Qualification of Quality Assurance Program Audit Personnel" (WHC 1989a).

11.0 PREVENTIVE MAINTENANCE

All measurement and testing equipment used in the field and laboratory that directly affect the quality of the analytical data shall be subject to preventive maintenance measures that ensure minimization of measurement system downtime. For this investigation, such measures are confined to laboratory equipment because all field measurements are related either to the measurement of the sample interval or to the determination of radiological or other health and safety hazards. Laboratories shall be responsible for performing or managing the maintenance of their analytical equipment; maintenance requirements, spare parts lists, and instructions shall be included in individual methods or in laboratory QA plans, subject to Westinghouse Hanford review and approval. When samples are analyzed using EPA reference methods, the requirements for preventive maintenance of laboratory analytical equipment as defined by the reference method shall apply.

12.0 DATA ASSESSMENT PROCEDURES

Characterization data from this phase of the investigation will be assessed at two levels. As previously discussed in Chapter 8.0, analytical data shall first be compiled and reduced by the laboratory and validated in a manner appropriate for the individual analytical level. As discussed in Chapter 5.0 of the work plan, and as directed by the Technical Lead, various statistical and probabilistic techniques may be selected for use in the process of data comparison and analysis. Statistical methods may include one or more of the standard methods and formulae, or other appropriate methods at the discretion of the Technical Lead. In all cases, however, the statistical methodologies and assumptions to be used in the evaluation shall be defined by written directions that are signed, dated, and retained as project quality records in compliance with EII 1.6 "Records Management" (WHC 1989b). Applicable directions shall be documented in the final report for this phase of the characterization of 100-KR-1 produced in Task 10.

13.0 CORRECTIVE ACTION

Corrective action requests required as a result of surveillance reports, nonconformance reports, or audit activity shall be documented and dispositioned as required by QR 16.0 "Corrective Action," QI 16.1 "Trending/Trend Analysis," and QI 16.2 "Corrective Action Reporting," (WHC 1989a). Primary responsibilities for corrective action resolution are assigned to the Technical Lead and the Quality Coordinator.

Other measurement systems, procedures, or plan corrections that may be required as a result of routine review processes shall be resolved as required by governing procedures or shall be referred to the Technical Lead for resolution. Copies of all surveillance, nonconformance, audit, and corrective action documentation shall be routed to the project QA records upon completion or closure.

14.0 QUALITY ASSURANCE REPORTS

As previously stated in Chapters 10.0 and 13.0, project activities shall be regularly assessed by auditing and surveillance processes. Surveillance, nonconformance, audit, and corrective action documentation shall be routed to the project quality records upon completion or closure of the activity. A report such as that described in QI 16.1 "Trending/Trend Analysis" (WHC 1989a), summarizing all audit, surveillance, and instruction change authorization activity (see Section 4.4), as well as any associated corrective actions, shall be prepared by the Quality Coordinator at the completion of Phase I or annually beginning 1 yr after approval of the work plan, whichever is sooner. The report(s) shall be submitted to the Technical Lead for incorporation into the final report prepared at the end of Phase I of the investigation. The final report shall include an assessment of the overall adequacy of the total measurement system with regard to the data quality objectives of the investigation.

15.0 REFERENCES

DOE, 1988, *Radiation Protection for Occupational Workers*, DOE Order 5480.11, U.S. Department of Energy, Washington, D.C.

DOE, 1990, *Radiation Protection of the Public and the Environment*, DOE Order 5400.5, U.S. Department of Energy, Washington, D.C.

Ecology et al. 1989, *Hanford Federal Facility Agreement and Consent Order*, Washington Department of Ecology, U.S. Environmental Protection Agency, and U.S. Department of Energy, Olympia, Washington.

EPA, 1982, *Prescribed Procedures for the Measurement of Radioactivity in Drinking Water*, EPA-600/4-80-032, U.S. Environmental Protection Agency/ Environmental Monitoring and Support Laboratory, Cincinnati, Ohio.

EPA, 1983a, *Methods for Chemical Analysis of Water and Wastes*, EPA-60014-79-020, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1983b, *Interim Guidelines and Specifications for Preparation of Quality Assurance Project Plans*, QAMS-005/80, U.S. Environmental Protection Agency/Office of Exploratory Research, Washington, D.C.

EPA, 1986, *Test Methods for Evaluating Solid Wastes*, SW-846, third edition, U.S. Environmental Protection Agency/Office of Solid Waste and Emergency Response, Washington, Washington, D.C.

EPA, 1987, *Data Quality Objectives for Remedial Response Activities: Volume I, Development Process*, EPA-540/6-87-003, Office of Emergency and Remedial Response and Office of Waste Programs Enforcement, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1988a, *Laboratory Data Validation Functional Guidelines for Evaluating Organics Analyses*, Hazardous Site Evaluation Division, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1988b, *Laboratory Data Validation Functional Guidelines for Evaluating Inorganics Analyses*, Hazardous Site Evaluation Division, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1988c, *USEPA Contract Laboratory Program Statement of Work for Organic Analysis*, Sample Management Office, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1989a, *USEPA Contract Laboratory Program Statement of Work for Inorganic Analysis*, Sample Management Office, U.S. Environmental Protection Agency, Washington, D.C.

EPA, 1989b, *Hazardous Waste Management System; Testing and Monitoring Activities* Proposed Rule in Federal Register, Vol. 54, No. 13, pp. 3212-3228.

WHC 1989a, *Westinghouse Hanford Company Quality Assurance Manual*, WHC-CM-4-2, Westinghouse Hanford Company, Richland, Washington.

WHC, 1989b, *Environmental Investigations and Site Characterization Manual*, WHC-CM-7-7, Westinghouse Hanford Company, Richland, Washington.

THIS PAGE INTENTIONALLY
LEFT BLANK

Attachment 2

HEALTH AND SAFETY PLAN

9 0 1 1 8 9 0 3 5 2

THIS PAGE INTENTIONALLY
LEFT BLANK

9 0 1 1 3 3 0 3 5 3

CONTENTS

Page

1.0 General Considerations and Requirements HSP-1
1.1 Introduction HSP-1
1.2 Designated Safety Personnel HSP-2
1.3 Medical Surveillance HSP-4
1.4 Training HSP-5
1.5 Requirements for Use of Respiratory Protection HSP-6

2.0 General Procedures HSP-7
2.1 General Work Safety Practices HSP-7
2.2 Confined Space/Test Pit Entry HSP-11

3.0 Site Background HSP-12

4.0 Scope of Work and Potential Hazards HSP-14
4.1 Potential Hazards HSP-14
4.2 Assessment and Mitigation of Potential Hazards HSP-16

5.0 Environmental and Personal Monitoring HSP-17
5.1 Volatile Organic Compounds Monitoring HSP-18
5.2 Airborne Radioactive Materials and Radiation Monitoring HSP-19

6.0 Personal Protective Clothing and Respiratory Protection HSP-20
6.1 Personal Protective Equipment HSP-20
6.2 Heat Stress HSP-21
6.3 Hypothermia HSP-22

7.0 Site Control HSP-22

8.0 Decontamination Procedures HSP-23
8.1 Personnel Decontamination HSP-24
8.2 Equipment Decontamination HSP-24
8.3 Sampling and Monitoring Equipment HSP-25
8.4 Respiratory Protection Equipment HSP-25
8.5 Heavy Equipment HSP-26

9.0 Contingency and Emergency Response Plans HSP-26
9.1 Procedure for Personnel Injured in Exclusion Zone HSP-28
9.2 Procedure for Personal Injury in Support Area HSP-29
9.3 Procedures for Fire and Explosions HSP-30
9.4 Procedure for Personal Protective Equipment Failure HSP-31
9.5 Procedure for Failure of Other Equipment HSP-31
9.6 Emergency Escape Routes HSP-31
9.7 Response Action to Chemical Exposure HSP-31
9.8 Emergency Telephone Numbers HSP-32

10.0 References HSP-33

FIGURE

HSP-1 Location of Hanford Emergency Facilities HSP-27

TABLE

HSP-1 Facilities Within the Boundaries of 100-KR-1 Operable Unit HSP-13

HSP-2 Chemical Waste Sites in 100-KR-1 (PNL 1988) HSP-14

1.0 GENERAL CONSIDERATIONS AND REQUIREMENTS

1.1 INTRODUCTION

The purpose of this task-specific health and safety plan (HSP) is to establish standard health and safety procedures for Westinghouse Hanford Company (Westinghouse Hanford) employees and contractors engaged in remedial investigation activities in the 100-KR-1 operable unit. These activities will include drilling and sampling boreholes, well installation, and environmental sampling in areas of known chemical and radiological contamination.

All employees of Westinghouse Hanford or any other contractors who are participating in onsite activities in the 100-KR-1 operable unit shall:

1. Read the HSP and attend a pre-job safety meeting to review and discuss the HSP.

2. Follow all health and safety procedures specified in this document and in the applicable pre-job safety plan (PJSP).

Each PJSP must be signed by all involved personnel. Employees are encouraged to bring any questions or concerns to the Site Safety Officer. The approved PJSP will serve as the agenda for a mandatory "tailgate" safety meeting before startup each day. Additional tailgate safety meetings or safety briefings will be held at any time it is deemed necessary by the Site Safety Officer, the Health Physics Technician, or the Field Team Leader.

A brief PJSP will be prepared for each work site (e.g., pond, trench, ditch, etc.) which will reiterate the following information for that specific site and task(s).

1. Inventory of suspected chemical and/or radiological hazards.

2. Discussion of existing and potential physical hazards.

3. Methods for mitigating known and potential site-specific hazards.

Each PJSP will be reviewed and approved by: the operable unit Technical Lead, the Field Team Leader, the Site Safety Officer, Environmental Health and

Pesticide Services Section, Industrial Safety and Fire Protection, Health Physics, the Technical Lead's manager, and the manager of any other Westinghouse Hanford personnel with work responsibilities at the site, as related to the particular PJSP. The PJSP will also be reviewed and signed for concurrence by any non-Westinghouse Hanford contractor whose personnel are participating at the job site.

The levels of protection and procedures specified in this plan are based on the best available information and represent the minimum health and safety requirements to be observed at all times by Westinghouse Hanford employees and contractors while engaged in tasks associated with this project. Should any situation arise which is judged to be beyond the scope of the monitoring, personal protection, or decontamination procedures specified here or in the PJSP, work activities will stop and all personnel will withdraw from the exclusion zone as directed by the Site Safety Officer, the Health Physics Technician, and the Field Team Leader. After review of the situation, the Site Safety Officer will determine the need to upgrade the level of protection as specified in the PJSP or to revise the health and safety procedures for this activity.

1.2 DESIGNATED SAFETY PERSONNEL

The Field Team Leader and Site Safety Officer are responsible for site safety and health. Specific individuals will be assigned on a task by task basis by project management, and their names will be properly recorded before the task is initiated.

All activities onsite must be cleared through the Field Team Leader. The Field Team Leader has responsibility for the following:

- Allocating and administering the resources to successfully comply with all technical and health and safety requirements
- Verifying that all permits, supporting documentation, and clearances are in place (i.e., electrical outage requests, welding permits, excavation permit, HSP, sampling plan, Radiation Work Permit, onsite/offsite radiation shipping records, etc.)
- Providing technical advice during routine operations and emergencies
- Informing the appropriate site management and safety personnel of the activities to be performed each day

9 0 1 1 3 3 3 3 6 7

- Resolving any conflicts that may arise between Radiation Work Permits and implementation of the HSP
- Handling of emergency response situations as may be required
- Conducting pre-job safety meeting and periodic tailgate safety meetings
- Interactions with adjacent building occupants and/or inquisitive public.

The Site Safety Officer shall act as the site safety and health supervisor and is responsible for implementing the HSP at the site. The Site Safety Officer shall:

- Prepare each PJSP
- Monitor chemical, physical, and (in conjunction with the Health Physics Technician) radiation hazards to assess the degree of hazard present; monitoring shall specifically include organic vapor detection, radiation screening, and confined space evaluation
- Determine protection levels, clothing, and equipment needed to ensure the safety of personnel in conjunction with the Health Physics Technician
- Monitor performance of all personnel to ensure that the required safety procedures are followed
- Halt operations immediately, if necessary, because of safety and/or health concerns
- Conduct safety briefings as necessary
- At the Field Team Leader's request, prepare summary reports of health and safety activities at the conclusion of each task.

The Health Physics Technician is responsible for assuring that all radiological monitoring and protection procedures are being followed as specified in the appropriate Radiation Work Permit. Industrial hygiene and safety personnel will provide safety with an overview during drilling operations consistent with Westinghouse Hanford policy and provide technical advice as requested. Also, an additional industrial hygienist and Health Physics Technician may be requested to

provide downwind sampling for hazardous materials and radiological contaminants, respectively, and other analyses as required.

The ultimate responsibility and ultimate authority for employee health and safety lies with the employee and the employee's colleagues. Each employee is responsible for exercising the utmost care and good judgment in protecting personal health and safety and that of fellow employees. Should any employee observe a potentially unsafe condition or situation, it is the responsibility of that employee to immediately bring the observed condition to the attention of the appropriate health and safety personnel, as designated above. In the event of an immediately dangerous or life-threatening situation, the employee automatically has temporary 'stop-work' authority and the responsibility to immediately notify the Field Team Leader or Site Safety Officer. When work is temporarily halted because of a safety or health concern, personnel will exit the exclusion zone and meet at a predetermined place in the support zone. The Field Team Leader, Site Safety Officer, and Health Physics Technician will determine the next course of action.

1.3 MEDICAL SURVEILLANCE

All Westinghouse Hanford personnel and contractors engaged in onsite activities on 100-KR-1 must have baseline physical examinations and be participants in the Westinghouse Hanford (or an equivalent) hazardous waste worker medical surveillance program.

Medical examinations will be designed by the Hanford Environmental Health Foundation (HEHF) to identify any preexisting conditions that may place an employee at high risk, and will verify that each worker is physically able to perform the work required by this work plan without undue risk to personal health. The physician shall determine the existence of conditions that may reduce the effectiveness or prevent the employee's use of a self-contained breathing apparatus (SCBA). The physician shall also determine the presence of conditions that may pose undue risk to the employee while performing the physical tasks of this work plan using Level B personal protection equipment. This would include any condition that increases the employee's susceptibility to heat stress.

The examining physician's report will not include any nonoccupational diagnoses unless directly related to the employee's fitness for work required.

1.4 TRAINING

Before engaging in any onsite remedial investigation activities, each team member is required to have received 40 h of health and safety training related to hazardous waste site operations and at least 8 h of refresher training each year thereafter, as specified in 29 CFR 1910.120 (OSHA 1988a). At a minimum this training must include the following topics:

- Employee rights and responsibilities under the Occupational Safety and Health Administration (OSHA)
- Personal protection equipment and clothing, use and care, particularly fitting, operation, and use of cascade breathing air systems and SCBA
- Chemical and radiological hazard recognition
- Radiation worker training
- Emergency response, self-rescue, and first aid
- Vehicle operation, mandatory rules, and regulations
- Safe use of drilling and sampling equipment
- Handling, storage, and transportation of hazardous chemical and radioactive materials
- Site control and management
- Safe sampling techniques
- Site surveillance, observation, and safety plan development
- Proper decontamination methods for personnel, protective clothing, and equipment
- Use of field test equipment for radioactivity, explosivity, and other measurements as needed
- Communication procedures.

The Field Team Leader and Site Safety Officer will provide site-specific instructions regarding anticipated hazards, levels of protection, site monitoring, and operation of equipment as appropriate.

In addition, each inexperienced (never having performed site characterization) employee will be directly supervised by a trained, experienced person for a minimum of 3 d of field procedures. There are often several on-the-job trainees on a job site at the same time. Each will be training for a specific activity, usually with the experienced team member who is responsible for that activity. All members of the field team are supervised by the Field Team Leader and Site Safety Officer.

The Field Team Leader and the Site Safety Officer will receive an additional 8 h of training (in addition to the refresher training discussed above) to cover the following topics:

- Management of restricted and safe zones
- Rules for handling untrained site visitors
- Site management
- Other environmental, safety, and health topics which relate to the sampling and characterization effort.

1.5 REQUIREMENTS FOR USE OF RESPIRATORY PROTECTION

All employees of Westinghouse Hanford and subcontractors who may be required to use air-purifying or air-supplied respirators must be included in a medical surveillance program and be approved for the use of respiratory protection by an HEHF or other licensed physician. Each team member must be trained in the selection, limitations, and proper use and maintenance of respiratory protection (existing respiratory protection training may be applicable to the 40-h training requirement).

Before using any negative-pressure respirator, each employee must be fit-tested (within the past year) for the specific make, model, and size of respirator the individual will be using, according the Westinghouse Hanford fit testing procedures.

Beards (including a few days' growth), large sideburns, or moustaches which may interfere with a proper respirator seal are not permitted.

Subcontractors must provide evidence to Westinghouse Hanford that their medical surveillance and respiratory protection programs complies with 29 CFR 1910.120 (OSHA 1988a) and 29 CFR 1910.134 (OSHA 1988b), respectively.

2.0 GENERAL PROCEDURES

The following personal hygiene and work practice guidelines are intended to prevent injuries and adverse health effects. A hazardous waste site poses a multitude of health and safety concerns because of the variety and number of hazardous substances present. These guidelines represent the minimum standard procedures for reducing potential risks associated with this project and are to be followed by all job-site employees at all times.

2.1 GENERAL WORK SAFETY PRACTICES

2.1.1 Work Practices

- Eating, drinking, smoking, taking medications, chewing gum, etc., is prohibited within the exclusion zone. All sanitation facilities shall be located outside of the exclusion zone; decontamination is required before using such facilities.

- Personnel shall avoid direct contact with contaminated materials unless necessary for sample collection or required observation. Remote handling of casing, auger flights, etc. will be practiced whenever practical.

- While operating in the controlled zone, personnel shall use the "buddy system" or be in visual contact with someone outside of the controlled zone at all times.

- The buddy system will be used where appropriate for manual lifting.

- Requirements of Westinghouse Hanford radiation protection and Radiation Work Permit manuals shall be followed for all work involving radioactive materials or conducted within a radiologically controlled area.

- Work operations onsite shall not start before sunrise and shall cease at sunset, unless the entire control zone is adequately illuminated with artificial lighting. A new tour (shift) will man the drilling rig after completion of each shift.

- Do not handle soil, waste samples, or any other potentially contaminated items unless wearing the protective gloves specified in the PJSP.

- Whenever possible, stand upwind of excavations, boreholes, well casings, drilling spoils, etc., as indicated by an onsite windsock.

- Stand clear of the trench during excavation. Always approach the excavation from upwind.

- Be alert to potentially changing exposure conditions as evidenced by perceptible odors, unusual appearance of excavated soils, oily sheen on water, etc.

- Do not enter any test pit trench greater than 4 ft (1.3 m) in depth unless in accordance with procedures specified in the PJSP.

- Do not, <u>under any circumstances</u>, enter or ride in or on any backhoe bucket, materials hoist, or any other similar device not specifically designed for carrying human passengers.

- All drilling operations members must make a conscientious effort to remain aware of their own and other's positions in regards to rotating equipment, cat heads, u-joints, etc. Drilling operations members must be extremely careful when assembling, lifting, and carrying flights or pipe to avoid pinch-point injuries and collisions.

- Tools and equipment will be kept off the ground whenever possible to avoid tripping hazards and the spread of contamination.

9013830273

- Personnel not involved in operation of the drill rig or monitoring activities shall remain a safe distance from the rig as indicated by the Field Team Leader.

- Follow all provisions of each site-specific Hazardous Work Permit as addressed in the PJSP, including cutting and welding, confined space entry and excavation.

- Catalytic converters on the underside of vehicles are sufficiently hot to ignite dry prairie grass. Team members should not drive over dry grass that is higher than the ground clearance of the vehicle and should be aware of the potential fire hazard posed by catalytic converters at all times. Never allow a running vehicle to sit in a stationary location over dry grass or other combustible materials.

- Follow all provisions of each site-specific Radiation Work Permit.

- Team members will attempt to minimize truck tire disturbance of all stabilized sites.

2.1.2 Personal Protective Equipment

- Personal protective equipment will be selected specifically for the hazards identified in the PJSP. The Site Safety Officer is responsible for choosing the appropriate type and level of protection required for different activities at the job site.

- Levels of protection shall be appropriate to the hazard to avoid either excessive exposure or additional hazards imposed by excessive levels of protection. The PJSP will contain provisions for adjusting the level of protection as necessary. These personal protective equipment specifications must be followed at all times, as directed by the Field Team Leader, Health Physics Technician, and Site Safety Officer.

- Each employee must have available a hard hat, safety glasses, and substantial protective footwear to wear if specified in the PJSP.

- The exclusion zone around drilling or other noisy operations will be posted "Hearing Protection Required". The type of hearing protection to be worn will be specified in the PJSP with other personal protective equipment.

- Personnel should maintain a high level of awareness of the limitations in mobility, dexterity, and visual impairment inherent in the use of Level B and Level C personal protective equipment.

- Personnel should be alert to the symptoms of fatigue, heat stress, and cold stress and their effect on the normal caution and judgment of personnel.

- Life jackets must be worn and employees shall use the 'buddy system' for any activities over water (e.g., water column sampling of the Columbia River). Additional rescue equipment, such as a rope or pole, shall also be available.

2.1.3 Personal Decontamination

- The PJSP will describe in detail methods of personnel decontamination, including the use of contamination control corridors and step-off pads when appropriate.

- Thoroughly wash hands and face before eating or putting anything in the mouth, to avoid hand-to-mouth contamination.

- At the end of each work day or each job, disposable clothing shall be removed and placed in (chemical contamination) drums or plastic lined boxes as appropriate. Clothing that can be cleaned shall be sent to the Hanford Laundry.

- Individuals are expected to thoroughly shower before leaving the work site or Hanford Site if directed to do so by the Health Physics Technician, Site Safety Officer, or Field Team Leader.

2.1.4 Emergency Preparation

- A multipurpose dry chemical fire extinguisher, a fire shovel, a complete field first-aid kit (including bottles of eyewash solution), and a portable deluge shower shall be available at every drill site.

- Prearranged hand signals or other means of emergency communication will be established when respiratory protection equipment is to be worn, since this equipment seriously impairs speech communications.

- The Hanford Fire Department shall be notified prior to the start of a site investigation project. This notification shall include the location and nature of the various types of field work activities as described in the work plan. A site location map shall be included in this notification.

2.2 CONFINED SPACE/TEST PIT ENTRY

The following procedures apply to the entry of any confined space which, for the purpose of this document, shall be defined as any space having limited egress (access to an exit) and the potential for the presence or accumulation of a toxic or explosive atmosphere. This includes manholes, certain trenches (particularly those through waste disposal areas), and all test pits greater than 4 ft (1.3 m) in depth in potentially contaminated soil. If confined spaces are going to be entered as part of the work operations, a Hazardous Work Permit (filled out for confined space entry) must be obtained from Industrial Safety and Fire Protection.

The identified remedial investigation activities on 100-KR-1 should not require confined space entry. Nevertheless, the hazards associated with confined spaces are of such severity that all employees should be familiar with the safe work practices discussed below.

No employee shall enter any test pit or trench greater than 4 ft (1.3 m) in depth unless the sides are shored or laid back to a stable slope as specified in 29 CFR 1926.652 (OSHA 1988c) or equivalent state occupational health and safety regulations.

When an employee is required to enter a pit or trench 4 ft (1.3 m) or more in depth, an adequate means of access and egress, such as a slope of at least 2:1 to the bottom of the pit, or a secure ladder or steps shall be provided.

Before entering any confined space, including any test pit, the atmosphere will be tested for flammable gases, oxygen deficiency, and organic vapors. If other specific contamination, such as radioactive materials or other gases and vapors may be present, additional testing for those substances shall be conducted. Depending on the situation, the space may require ventilation and retesting before entry.

Any employee entering a confined or partially confined space must be equipped with an appropriate level of respiratory protection in keeping with the monitoring procedures discussed previously and the action levels for airborne contaminants (see Warnings and Action Levels in PJSP).

No employee shall enter any test pit requiring the use of Level B protection, unless a backup person also equipped with a pressure-demand SCBA is present. No backup person shall attempt any emergency rescue unless a second backup person equipped with a SCBA is present, or the appropriate emergency response authorities have been notified and additional help is on the way.

3.0 SITE BACKGROUND

The 100-K Area is located in the north central part of the Hanford Site and is situated along the southern shoreline of the Columbia River.

The 100-KR-1 operable unit is one of the four operable units located within the 100-K Area. Three of the 100-K operable units, including 100-KR-1, are source operable units (i.e., they contain sources of wastes and potential contamination). The fourth operable unit, 100-KR-4, is the ground water/surface water operable unit and includes the entire physical area of the 100-K Area and vicinity.

The 100-KR-1 operable unit is adjacent to the Columbia River shoreline between River Miles 381 and 382 and comprises approximately 0.23 mi^2 (0.6 km^2). Major facilities within the unit are inlet water structures, the 107-K cooling water retention basins, an outfall structure, and the effluent crib and trench.

The Hanford Federal Facility Agreement and Consent Order (Ecology et al. 1989) lists five contaminant sources in the 100-KR-1 operable unit. More recently, two river pumphouses have been assigned 100-KR-1 waste unit numbers. Table HSP-1 profiles the various waste units. Table HSP-2 provides the chemical inventory of these sites.

9 0 1 1 3 3 0 3 7 7

Table HSP-1. Facilities Within the Boundaries of the 100-KR-1 Operable Unit.

Facility designation	Name	Years in service	Facility purposes	Facility description
181-KE	River pump-house	1955-1971	Pump river water to water treatment plant	Reinforced-concrete intake structure
181-KW	River pump-house	1955-1970	Pump river water to water treatment plant	Reinforced-concrete intake structure
1904-K (116-K-3)	Outfall structure	1955-Present	Control effluent discharge from the 107-KE & 107-KW retention basins	Reinforced concrete structure; two steel inlet pipes, two 84 in. steel effluent pipes, overflow channel
107-KE (116-KE-4)	Retention basins	1955-1970	Provide retention of reactor cooling water prior to discharge into river	Three 250-ft-dia, 9,000,000-gal, welded carbon steel tanks, mounted on a reinforced concrete foundation
107-KW (116-KW-3)	Retention basins	1955-1971	Provide retention of reactor cooling water prior to discharge into river	Three 250-ft-dia, 9,000,000-gal, welded, carbon steel tanks, mounted on a reinforced concrete foundation
116-K-2	Effluent trench	1955-1971	Percolation of radioactive reactor cooling effluent	4,000-50-ft, gravel-lined percolation trench including four overflow areas
116-K-1	Effluent crib	1955	Percolation of radioactive reactor cooling effluent	200' x 200' x 20-ft percolation crib

Source: AEC 1964.

Table HSP-2. Chemical Waste Sites in 100-KR-1 (PNL 1988)

Waste Site	Chemical	Quantity (kg)
116-K-1	Sodium dichromate	40
116-K-2	Sodium dichromate	300,000
	Sulfuric acid	10,000
	Sulfamic acid	10,000
	Copper sulfate	500
116-KE-4	A,B	---
116-KW-3	A,B	---
116-K-3	A	---
181-KE	A	---
181-KW	A	---

[A]Waste site did not dispose chemicals
[B]Chemical data not available for leaks

4.0 SCOPE OF WORK AND POTENTIAL HAZARDS

While the information presented in Chapter 3.0 is believed to be representative of the constituents and quantities of wastes at the time of discharge, the present chemical nature, location, extent, and ultimate fate of these wastes in and around the liquid disposal facilities are largely unknown. The emphasis of the RI in 100-KR-1 will be to characterize the nature and extent of contamination in the vadose (unsaturated subsurface soil) zone.

4.1 POTENTIAL HAZARDS

Onsite tasks will involve noninvasive surface survey and sampling procedures and invasive soil sampling either directly in or immediately adjacent to areas known or suspected to contain potentially hazardous chemical substances, toxic metals, and radioactive materials.

Surface radiological contamination and fugitive dust will be the potential hazards of primary concern during noninvasive mapping and sampling activities.

Existing data indicate that hazardous substances that may be encountered during invasive sampling include radionuclides, heavy metals, and corrosives. In addition, volatile organics may be associated with certain facilities where solvents may have been discharged.

As discussed previously, this project will involve the following:

- Nonintrusive source investigations
- Drilling boreholes directly adjacent to liquid waste disposal ponds and trenches, and soil sampling
- Source sampling

The degree of the potential occupational hazards is expected to be similar for each of the designated tasks. The likelihood of encountering hazardous chemical or radioactive substances will clearly be greatest during intrusions into and through the strata in the vicinity of the liquid waste disposal facilities.

Potential hazards include:

1. External radiation (gamma, and to a lesser extent, beta) from radioactive materials in the soil
2. Internal radiation due to radionuclides present in contaminated soil entering the body by ingestion or through open cuts and scratches
3. Internal radiation due to inhalation of particulate (dust) contaminated with radioactive materials
4. Inhalation of toxic vapors or gases such as volatile organics or ammonia
5. Inhalation or ingestion of particulate (dust) contaminated with inorganic or organic chemicals, and toxic metals
6. Dermal exposure to soil and/or ground water contaminated with radionuclides
7. Dermal exposure to soil and/or ground water contaminated with inorganic or organic chemicals, and toxic metals

8. Physical hazards such as noise, heat stress, and cold stress

9. Slips, trips, falls, bumps, cuts, pinch points, falling objects, other overhead hazards, crushing injuries, etc., typical of every construction-related job site

10. Unknown and/or unexpected underground utilities.

4.2 ASSESSMENT AND MITIGATION OF POTENTIAL HAZARDS

The likelihood of significant exposure (100 mR/h or greater) to external radiation is remote and can be readily monitored and controlled by limiting exposure time, increasing distance, and employing shielding as required.

Internal radiation via inhalation or inadvertent ingestion of contaminated dust is a realistic concern and must be continuously evaluated by the Health Physics Technician. Appropriate respiratory protection, protective clothing, and decontamination procedures will be implemented as necessary to reduce potential inhalation, ingestion, and dermal exposure to acceptable levels.

Exposure to toxic chemical substances via the dermal exposure route is not expected to pose a significant problem for the designated tasks, given the use of proper protective clothing. The appropriate level of personal protective clothing and respiratory protection will vary from soil sampling during drilling operations to sampling Columbia River water. In general, all activities conducted within an exclusion zone will require Level D-2. These levels of protection will be upgraded or downgraded as appropriate, based on real-time hazard evaluation and action levels.

Chemical exposure via inhalation of contaminated dust is not expected to pose a significant hazard because of the relatively low concentrations of chemicals in soil and low concentration of dust in the ambient air. Activities that result in high levels of airborne particulate (i.e., dusty operations) will require respiratory protection.

Similarly, airborne concentrations of toxic gases/vapors are not expected to exceed applicable permissible exposure limits. As mentioned above, however, the interactions and fate of these compounds are not well characterized. The Site Safety Officer will periodically monitor airborne levels of toxic vapors and gases with direct reading field instruments selected for the anticipated hazards. A detailed monitoring

plan, with frequency and location of measurements, specific chemical hazards, and type and mode of detection instrument to be used will be included in each PJSP. Air monitoring with direct reading instruments will be carried out continuously in the event of the detection of breathing zone concentrations greater than background levels. Respiratory protection will be employed as appropriate. Warning levels and action levels will be designated in the PJSPs.

The Site Safety Officer and Field Team Leader must make every effort to identify any and all underground utilities in the vicinity of all intrusive operations such as drilling or trenching. Should the work crew encounter an unanticipated underground utility, work shall be halted until the nature and status of the line is determined.

5.0 ENVIRONMENTAL AND PERSONAL MONITORING

The Site Safety Officer shall be present at all times during work activities. Air quality monitoring equipment will be used during the field activities to quantify exposure of vapors and gases which pose risks. This equipment is intended to provide adequate warning and allow appropriate action to be taken to prevent harmful exposure to chemical and radiological contaminants released into the work environment. The air monitoring program will consist of monitoring air for contaminant vapor/gases in the vicinity of boreholes and breathing zones, and monitoring the general area for radiation. A Health Physics Technician must be onsite at all times and will observe the action levels and procedures specified in the Radiation Work Permit and appropriate as low as reasonably achievable (ALARA) plans. Core samples will also be monitored to determine levels of radioactivity and occupational risks before actual sample collection. As indicated above, the decision to modify the level of protection will be made by the Site Safety Officer, the Health Physics Technician, and the Field Team Leader. This decision will be based on, but not limited to the following:

- Interpretation of organic vapor, gas, and radiation detection instrument readings by Health Physics Technician and health and safety personnel
- Visual observation such as wind, dust, discoloration, etc.
- Unusual odors or those characteristic of contaminants

- Measurement with other sampling devices such as O_2 and explosive level meters

- Information specific to the individual sites (i.e., known or suspected chemical contaminants and levels of each)

- Physical characteristics of the work environment such as temperature and pH.

Air sampling may be required downwind of the referenced waste sites to monitor particulates and vapors before job startup. Siting of such sampling devices will be determined by Health Physics, Site Safety Officer, and HEHF (if appropriate). Any time that personnel sampling is required to determine exposure levels, it must be done by HEHF. Discrete sampling of ambient air within the work zone and breathing zone will be conducted using a direct reading instrument, as specified in the PJSP, and other methods as deemed appropriate (e.g., pumps with tubes, O_2 meters, etc.). The following standards will be used in determining critical levels:

- *Radionuclide Concentrations in Air*, DOE Order 5480.1b Chapter XI (DOE 1986)

- *Air Contaminants - Permissible Exposure Limits*, 29 CFR 1910.1000 (OSHA 1989)

- *Threshold Limit Values and Biological Exposure Indices for 1989-1990* (ACGIH 1990)

- *Occupational Safety and Health Standards*, 29 CFR 1910.120 (OSHA 1988a)

- *Pocket Guide to Chemical Hazards*, (NIOSH 1985), recommended exposure limits for substances that do not have either a threshold limit value or a permissible exposure limit.

5.1 VOLATILE ORGANIC COMPOUNDS MONITORING

Although there is no record of disposal of volatile organic compounds in the 100-KR-1 operable unit, this section is included since it is the policy of Westinghouse Hanford to monitor for these compounds at all waste sites for safety reasons. The Site

Safety Officer shall have a direct reading instrument, as specified in the PJSP, onsite at all times and will establish "background readings" upwind of any excavation, spoils pile, borehole, etc.

Instruments used by the Site Safety Officer will be calibrated according to environmental investigation instruction (EII) 3.1 "User Calibration of Health and Safety M&TE" (WHC 1989). Instruments used to monitor organic vapors and gases will be checked for calibration daily before and after use, according to the manufacturer's recommended or approved method, with certified calibration gas. Calibration information will be recorded in the field logbook at the time of calibration. Field instruments will be calibrated at field ambient temperature. Conditions such as unusual humidity or temperatures that may affect instrument performance will be recorded in the field logbook.

Each PJSP will contain action levels based on the hazards identified for that activity. The PJSP action levels may be lower, but will not be higher than, the following:

> A consistent reading in the breathing zone that is up to 2.5 p/m above the upwind background level for 5 min shall be the action level for donning air-purifying respirators equipped with the appropriate cartridges. Any indication of cartridge "breakthrough" must be reported to the Site Safety Officer immediately. The Site Safety Officer and Field Team Leader will evaluate the situation and determine the action to be taken. Any breathing zone readings consistently greater than 2.5 p/m above background for 10 min or greater than 10 p/m other than for a brief peak will be the action level for temporarily discontinuing work, and upgrading the level of respiratory protection to Level B SCBAs or airlines as specified in the PJSP. Warning and action levels will be based on criteria referenced in DOE/RL Order 5480.10A (DOE/RL 1988).

5.2 AIRBORNE RADIOACTIVE MATERIALS AND RADIATION MONITORING

An onsite Health Physics Technician will monitor airborne radioactive contamination levels and external radiation levels. Action levels will be consistent with derived air concentrations and applicable guidelines as specified in the Health Physics radiation protection manual.

Appropriate respiratory protection shall be required when conditions are such that the airborne contamination levels may exceed an 8-h derived air concentration (i.e., the presence of high levels of uncontained, loose contamination on exposed surfaces or operations which may raise excessive levels of dust contaminated with airborne radioactive materials, such as excavation and/or drilling under extremely dry conditions).

Specific conditions requiring the use of respiratory protection because of radioactive materials in air will be incorporated into the Radiation Work Permit. If, in the judgment of the Health Physics Technician, any of these conditions arise, work shall cease until appropriate respiratory protection is provided.

6.0 PERSONAL PROTECTIVE CLOTHING AND RESPIRATORY PROTECTION

The following scheme will be used to designate the required level(s) of personal protective equipment and respiratory protection: the alphabetical designations 'B,' 'C,' and 'D,' shall refer to levels of respiratory protection (i.e., pressure-demand air supplying respirators with escape provisions, air-purifying respirators, and no respiratory protection, respectively). Since potential dermal exposure hazards may independently require a wide variety of personal protective clothing, regardless of an approved level of respiratory protection, the numerical designations '1,' '2,' and '3' will be used to specify the level of protective clothing that is to be employed (i.e., the level of protective equipment can be completely defined by a designation of 'C-2,' 'B-1,' etc.).

6.1 PERSONAL PROTECTIVE EQUIPMENT

The level of personal protective equipment required initially at the site during excavation, drilling, and sampling activities will be specified in the unique PJSP for each job within the operable unit. Personal protective clothing and respiratory protection shall be selected to limit exposure to anticipated chemical and radiological hazards. Work practices and engineering controls as described in the PJSP will also be used to control exposure, since a personal protection equipment ensemble alone

cannot protect against all hazards. The following guidelines will be used to specify personal protective equipment ensembles, based on the potential hazards determined in the PJSP:

Occupational Safety and Health Standards, 29 CFR 1910.120 (OSHA 1988a)

Occupational Safety and Health Guidance Manual for Hazardous Waste Site Activities (NIOSH et al. 1985).

6.2 HEAT STRESS

Working in protective clothing can greatly increase the likelihood of heat fatigue, heat exhaustion, and heat stroke, the latter a life-threatening condition. If temperatures at the site are above 65°F, the wet bulb globe temperature index shall be monitored to assess the potential for heat stress. Work/rest periods will be adjusted according to the standards stated in current threshold limit values (ACGIH 1990). Sufficient cool water and disposable drinking cups will be provided in the rest area. Engineering controls, such as solar shielding, also will be applied when and where appropriate.

If the wet bulb globe temperature index exceeds 77°F, employees shall use the 'buddy system' to monitor each other's pulse rate at the start of each rest period. If the pulse rate exceeds 110 beats per minute, the employee shall take an oral temperature with a clean disposable colorimetric oral thermometer. If the oral temperature exceeds 99.6°F, the next work period shall be shortened by one third. The pulse rate and oral temperature shall be monitored again at the beginning of the next rest period. If the oral temperature exceeds 99.6°F, the work period shall again be shortened by one third, etc., until the oral temperature is below 99.6°F.

All employees are to be alert to the possibility and symptoms of heat stress. Should any of the following symptoms occur--extreme fatigue, cramps, dizziness, headache, nausea, profuse sweating, pale clammy skin--the employee is to immediately leave the work area, rest, cool off, and drink plenty of cool water. The Site Safety Officer and the Field Team Leader shall be immediately informed of the problem, and shall obtain emergency medical assistance as needed.

6.3 HYPOTHERMIA

Working in extreme cold and exposed areas may create a risk of hypothermia. Portable heaters, insulated work clothing, and access to a heated vehicle or other enclosure may be provided, as needed to help mitigate cold stress. All employees should be alert to the symptoms, which include increasing disorientation and impaired judgement, shivering, weakness, numbness, drowsiness, and low body temperature. Unconsciousness may result if the symptoms are undetected. Should any employee observe behavior that indicates such symptoms, escort the victim out of the work area to a vehicle or other heated, protected area. Notify the Site Safety Officer and Field Team Leader, who shall obtain emergency medical assistance.

7.0 SITE CONTROL

The Field Team Leader, Site Safety Officer, and Health Physics Technician are designated to coordinate access control and security on the site. A temporary exclusion zone will be established (a minimum of a 25-ft [8-m] radius) at each digging or drilling location. The exclusion zone will be clearly marked with radiation zone rope and "Controlled Area" or "Surface Contamination Area" signs. If the exclusion zone is to be established for greater than 90 d, then chain, not rope, will be used. The size and shape of the exclusion zone will be dictated by the types of hazards expected, the climatic conditions, and specific drilling and sampling operations required. The ground surface of the area immediately around the drill hole, the corridors to the command post, and the decontamination area and escape route will be covered with appropriate material to reduce contamination of personnel and equipment. Exclusion zone boundaries will be increased or decreased based upon results of field monitoring, environmental changes, or work technique changes. The site Radiation Work Permit and the contractor's standard operating procedures for radiation protection will also dictate the boundary size and shape. Portable sanitation facilities shall be located outside of the exclusion zone. No unauthorized person shall be allowed within the controlled zone and no authorized person shall be allowed within the exclusion zone unless equipped with the required level of personal protective equipment and respiratory protection. All personnel who enter the exclusion zone will be required to go through decontamination procedures (radiological and chemical) before leaving the zone. All team members must be surveyed for radioactive contamination upon leaving the exclusion zone.

9 0 1 1 3 1 0 3 0 9 7

The onsite command post and staging area will be established near the exclusion zone on the upwind side, as determined by an onsite windsock, if physically possible. Exact location for the command post is to be determined just before start of work. Vehicle access, availability of utilities (power and telephone), wind direction, and proximity to sample locations should be considered in establishing command post location.

8.0 DECONTAMINATION PROCEDURES

Remedial investigation activities will require entry into areas of known chemical and radiological contamination. Consequently, it is likely that personnel and equipment will be contaminated with hazardous chemical and radiological substances.

During drilling and sampling activities at the site, potential sources of contamination include but are not limited to airborne vapors, gases, dust, mists and aerosols; splashes and spills; walking through contaminated areas; and handling contaminated equipment. All personnel who enter the exclusion zone will be required to go through decontamination procedures upon leaving the zone. Decontamination areas shall be located upwind of the work area (based on the recorded predominant wind direction) and shall be sufficiently distant from the work site, so as to allow for errant wind gusts, which may occasionally blow in from the work site. The procedures discussed below are intended to be compatible with EII procedures, EII 5.4 "Decontamination of Drilling Equipment", and EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989).

Decontamination procedures shall be consistent with Level B and Level C decontamination protocol. Specific decontamination procedures will provided in the PJSP. The following are examples of the equipment and facilities that may be used:

1. Decontamination garbage/dirty equipment bags
2. Decontamination pad/corridor cover (kraft paper)
3. Emergency response pressurized water tank with wand and adjustable spray nozzle
4. Bagging and taping material
5. Emergency water deluge and eyewash bottles
6. Detergent, brush, and bucket
7. Barrels

8. Step out pads
9. Sponges, wipes, and rags
10. Tables and stands.

8.1 PERSONNEL DECONTAMINATION

All personnel who access the exclusion and contamination reduction zones of the project will process through decontamination at the end of any given work shift or any other time they leave the respective zones. A decontamination corridor will be established within the exclusion zone for each task of the campaign. Clothing that is disposable will be removed in such a manner that outer layers are removed first and placed in containers which will be sealed when full or at the end of each day. Nondisposable clothing (such as special work procedure) that can be cleaned will be removed, bagged, and sent to the laundry. All wash liquids used for decontamination purposes must be properly disposed of per applicable state/federal regulations. After removing outer protective clothing, each team member must be surveyed by a Health Physics Technician before proceeding to an uncontrolled area. If radioactive contamination is detected, the individual involved shall be escorted to an appropriate decontamination area by the Health Physics Technician. At the Health Physics Technician's discretion, nasal smears may be taken for counting/analysis. Health Physics Dosimetry shall also be notified, and the determination for further bio-assay, if needed, will be made at that time. Site-specific radiation decontamination procedures will be provided in the Radiation Work Permit and PJSP.

8.2 EQUIPMENT DECONTAMINATION

Equipment decontamination methods will generally consist of washing or steam cleaning with a detergent/water or other decontamination solution, as specified in the field sampling plan (FSP). Rinsing with a diluted nitric acid solution may be necessary to remove metal oxides and hydroxides. Field contamination of drilling equipment, where applicable, shall be performed within impoundments in the decontamination zone to ensure that all wash liquids are captured. All wash liquids used for decontamination purposes must be properly disposed of per applicable state/federal regulations.

Downhole drilling equipment shall be decontaminated before use on another borehole/as required to assure the safety of personnel and prevent cross contamination of samples.

Equipment which is radiologically contaminated beyond the limits specified in the Radiation Work Permit shall not be decontaminated in the field. Such equipment shall be transported to the 2705-T Building for decontamination before reuse.

8.3 SAMPLING AND MONITORING EQUIPMENT

All possible measures should be taken by personnel to prevent or limit the contamination of any sampling and monitoring equipment used. In general, air-monitoring instruments will not be contaminated by chemicals unless splashed or set down on contaminated areas. Any delicate instrument that cannot be easily decontaminated should be protected while it is being used by placing it in a bag and using tape to secure the bag around the instrument. Openings in the bag can be made for sample intake, electrical connections, etc. Personnel performing field maintenance procedures on air-monitoring instruments should be aware of the fact that instruments may become contaminated internally if air containing high concentrations of radioactive particulate is drawn through the instrument.

Foreign material, which collects within the probe tip and on the face of the lamp on the HNU (a trademark of HNU Systems, Inc.) photoionization detector, may be chemically or radioactively contaminated, and should be handled appropriately when disassembling the probe or cleaning the lamp. A similar situation exists with the readout probe and metallic frit filters in the sampling line of the organic vapor analyzer. All instruments and equipment must be surveyed by the Health Physics Technician for the purpose of radiological contamination control before removal from the exclusion zone. Items with detectable levels of contamination must be controlled as radioactive material or controlled or regulated equipment.

Sampling devices require special cleaning and decontamination as detailed in EII 5.5 "Decontamination of Equipment for RCRA/CERCLA Sampling" (WHC 1989). When appropriate, disposable sampling equipment will be used to eliminate the need for decontamination liquids.

8.4 RESPIRATORY PROTECTION EQUIPMENT

Respiratory protection will be specified in the PJSP. There is a high potential for airline hoses to become contaminated; therefore, whenever possible, hoses should be covered with plastic. If grossly contaminated, they may have to be discarded. Cleaning and decontamination of face pieces will be performed by the mask cleaning

station (i.e., Hanford Laundry). Maintenance of special respiratory protection equipment (i.e., SKA PAK - a trademark of Figgie International) is performed by Personal Protective Equipment Unit in MO-412, 200 West Area.

8.5 HEAVY EQUIPMENT

All possible measures will be taken to prevent or limit the contamination of heavy equipment. Those parts of drilling equipment that become contaminated, such as auger flights, will be double bagged and taken to the 2705-T Building for decontamination before reuse to minimize personnel contamination potential and cross contamination of samples between boreholes.

9.0 CONTINGENCY AND EMERGENCY RESPONSE PLANS

The following procedures have been established to deal with emergency situations that might occur during drilling or sampling operations. As a general rule, in the event of an unanticipated, potentially hazardous situation as indicated by instrument readings, visible contamination, unusual or excessive odors, etc., team members shall temporarily cease operations and move upwind to a predesignated safe area. Any individual leaving a radiologically controlled area needs to be released by a Health Physics Technician, even if that individual is going to the first aid station (Figure HSP-1) or the hospital. If this cannot be accomplished, for whatever reason, the Health Physics Technician must accompany the individual to the first aid station or the hospital.

A two-way radio will be operational and be manned by the Field Team Leader to maintain contact with the team's base station. When feasible, personnel in the exclusion zone will maintain line-of-sight with the Field Team Leader. Any failure of radio communications will require evaluation by the Site Safety Officer and the Field Team Leader of whether personnel shall leave the exclusion zone. Communications from rig to rig or site to site will also be provided so that the Site Safety Officer or Field Team Leader can respond to an emergency. In addition, a series of three 1-s horn blasts from a truck in the support zone is the emergency signal for all personnel to the leave the exclusion zone.

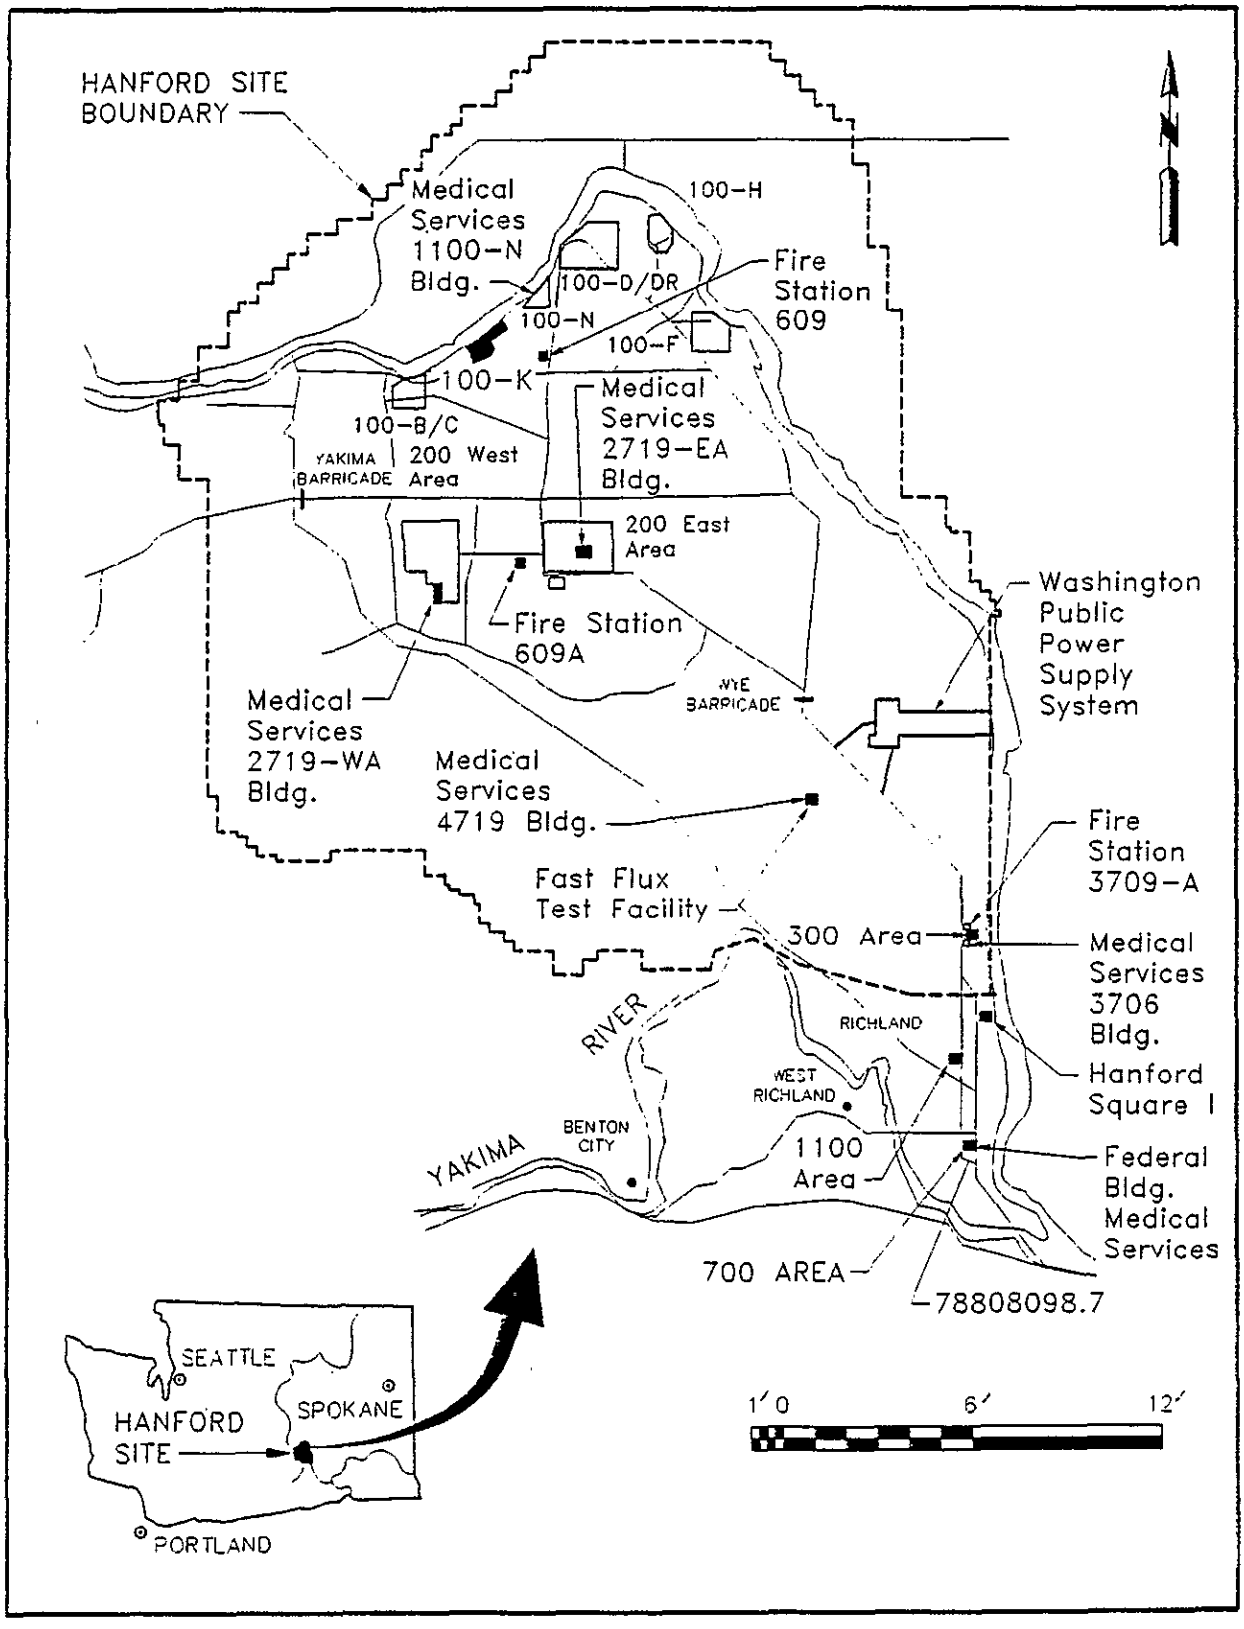

Figure HSP-1. Location of Hanford Emergency Facilities.

The following standard hand signals will be used in all cases:

■ Hand gripping throat	Out of air, can't breathe
■ Grip partner's wrist or both hands around waist	Leave area immediately
■ Hands on top of head	Need assistance
■ Thumbs up	OK, affirmative
■ Thumbs down	No, negative.

The Site Safety Officer is directly responsible for providing safety recommendations on the site to the site emergency coordinator. The site emergency coordinator for the 100-KR-1 drilling operations will be the Field Team Leader.

The site emergency coordinator will be responsible for the evacuation, emergency treatment, emergency transport of field personnel as necessary, and for the notification of the appropriate Hanford Site facility emergency response units and management staff.

Emergency communications will be maintained during all onsite field activities by two-way radio contact. If an emergency occurs, such as fire or explosion, all onsite personnel should exit the site in an upwind direction and assemble in a predesignated area. All emergency response actions for each job will be covered in the tailgate meeting with the PJSP. If an onsite injury occurs, team members should employ the following procedures.

9.1 PROCEDURE FOR PERSONNEL INJURED IN EXCLUSION ZONE

Designated emergency response members of the field team shall be trained and certified in first aid and cardiopulmonary resuscitation. If an injury occurs, the designated team members will provide appropriate assistance. Only trained, certified personnel should attempt to give first aid. If able, the injured person should proceed through decontamination to the nearest available source of first aid.

Upon notification of a serious injury in the exclusion zone, the emergency signal of three 1-s horn blasts will be sounded. All site personnel will assemble at the decontamination line. The Site Safety Officer and Field Team Leader should evaluate the nature of the injury and the extent of decontamination possible before the injured person is moved to the support area. No person should reenter the exclusion zone until the cause of the injury is determined and measures taken to prevent recurrence.

Should any employee exhibit erratic behavior or fall unconscious because of apparent heat illness, the emergency three horn blasts shall be sounded and the Field Team Leader shall immediately call for an ambulance. Designated first aid personnel, if within the exclusion zone, shall immediately proceed through decontamination with the victim, as follows:

1. Remove victim's outer protective clothing and discard
2. Remove own outer protective clothing and discard
3. Remove victim's inner protective clothing and discard
4. Remove own inner protective clothing and discard
5. Proceed with first aid for heat illness.

In extremely cold or exposed working situations, if an employee shows increasing disorientation or any other symptoms of hypothermia, follow the basic emergency and decontamination procedures for heat stroke, then proceed with first aid for hypothermia.

9.2 PROCEDURE FOR PERSONAL INJURY IN SUPPORT AREA

Upon notification of an injury in the support area, the Field Team Leader and the Site Safety Officer will assess the situation. If the cause of the injury or loss of the injured person does not affect the performance or safety of site personnel, operations may continue, with initiation of first aid and summoning of medical assistance as discussed above. If the injury increases the risk to others, the emergency signal of three 1-s horn blasts will be sounded and all site personnel shall move to the decontamination area for further instructions. Activities onsite will stop until the hazardous condition (if any) is evaluated and reduced to an acceptable level.

9.3 PROCEDURES FOR FIRE AND EXPLOSIONS

The dry chemical fire extinguishers, which are required on all field vehicles, are effective for fires involving ordinary combustibles (wood, grass, etc.), flammable liquids, and electrical equipment. They are appropriate for small, localized fires such as a drum of burning refuse, small burning gasoline spill, vehicle engine fire, etc. No attempt should be made to use the provided extinguishers for well-established fires or large areas/volumes of flammable liquids.

In the case of fire, prevention is the best contingency plan. Smoking in the exclusion zone is strictly prohibited and smoking materials, where permitted, should be extinguished with care.

In the event of a fire or explosion, the following steps are to be taken.

1. Immediately notify site emergency personnel and the local fire department by contacting the Hanford Patrol by phone (811) or by radio (station 1) to relay message.

2. If the situation can be readily controlled with available resources without jeopardizing personal health and safety or the health and safety of other site personnel, take immediate action to do so.

If the fire cannot be readily controlled, take the following steps.

1. Upon discovery of a fire or explosion onsite, the emergency signal of three 1-s horn blasts will be sounded and all site personnel will assemble upwind of the fire at the decontamination line. The fire department will be called and all personnel will move to a safe distance from the involved area. Again, based on the individual tailgate meetings, a decision to send all personnel immediately out of the exclusion area may be an option.

2. Isolate the fire to prevent spreading, if possible.

3. Clear the area of all personnel working in the immediate vicinity.

9.4 PROCEDURE FOR PERSONAL PROTECTIVE EQUIPMENT FAILURE

If any site worker experiences a failure or alteration of protective equipment that may jeopardize the level of protection provided by the equipment, that person and that person's buddy shall immediately proceed through decontamination and leave the exclusion zone. In the event of respiratory protection failure, the primary concern will be getting the person to breathable air, and decontamination will be secondary. Reentry shall not be permitted until the equipment has been repaired or replaced, or the conditions leading to the problem are adequately evaluated and corrected.

9.5 PROCEDURE FOR FAILURE OF OTHER EQUIPMENT

If onsite monitoring equipment fails to operate properly, the Field Team Leader and Site Safety Officer shall be notified and then determine the effect of the failure on continuing operations. If the failure may compromise health and safety procedures or jeopardize the safety of personnel, all personnel shall leave the exclusion zone until the equipment is repaired or replaced.

9.6 EMERGENCY ESCAPE ROUTES

In the event that an emergency situation prevents exiting the exclusion zone by way of the decontamination area, exit the exclusion zone in any direction, preferably upwind, avoiding any barriers. Site-specific situations will be covered in more detail in the PJSP.

9.7 RESPONSE ACTION TO CHEMICAL EXPOSURE

Responses of this nature will be covered in the PJSP. Designated first aid field team members will be briefed on these procedures from the PJSP, and only those designated individuals will treat the exposed person. The Site Safety Officer or Field Team Leader should be notified of any chemical exposure incidents as soon as possible, so that appropriate actions may be taken to prevent further exposure.

9.8 EMERGENCY TELEPHONE NUMBERS

Local Resources:	Hanford Emergency Response Team	375-2400
Ambulance:	Hanford Fire Department will dispatch the ambulance	375-2400
Hospital:	Kadlec Hospital, Richland	946-4611
Police (Local or State):	Hanford Patrol	375-2400
Fire Department:	Hanford Fire Department	375-2400
Poison Control Center:		800-572-5842

EMERGENCY CONTACTS

Industrial Safety:	P. A. Wright (PNL) H. N. Bowers (WHC)	376-1634 373-3948
Health Physics:	J. R. Berry (PNL) J. B. Levine (WHC)	376-3057 373-1333
Field Team Leaders:	PNL or WHC	
Environmental Reporting:	W. J. Bjorklund (PNL) TBD (WHC)	376-4781 TBD

10.0 REFERENCES

ACGIH, 1990, *Threshold Limit Values and Biological Exposure Indices for 1989-1990*, American Conference of Governmental Industrial Hygienists, Cincinnati, Ohio.

AEC, 1964, *Catalog of Hanford Buildings and Facilities*, Atomic Energy Commission, GE Study Group for the Economic Development of Richland, Richland, Washington.

DOE, 1986, *Environment, Safety & Health Program for DOE Operations*, DOE Order 5480.1b, U.S. Department of Energy, Washington, D.C.

DOE/RL, 1988, *Industrial Hygiene Program*, DOE/RL Order 5480.10A, U.S. Department of Energy, Richland Operations, Richland, Washington.

Ecology et al. 1989, *Hanford Federal Facility Agreement and Consent Order*, Washington Department of Ecology, U.S. Environmental Protection Agency, and U.S. Department of Energy, Olympia, Washington.

NIOSH, 1985, *Pocket Guide to Chemical Hazards*, National Institute for Occupational Safety and Health, U.S. Department of Health and Human Services, Public Health Service, Centers for Disease Control, Washington, D.C.

NIOSH/OSHA/USCG/EPA, 1985, *Occupational Safety and Health Guidance Manual for Hazardous Waste Site Activities*, prepared by National Institute for Occupational Safety and Health, Occupational Safety and Health Administration, U.S. Coast Guard, and U.S. Environmental Protection Agency, Washington, D.C.

OSHA, 1988a, *Occupational Safety and Health Standards*, Title 29, Code of Federal Regulations, Part 1910.120, Occupational Safety and Health Administration, Washington, D.C.

OSHA, 1988b, *Occupational Safety and Health Standards*, Title 29, Code of Federal Regulations, Part 1910.134, Occupational Safety and Health Administration, Washington, D.C.

OSHA, 1988c, *Safety and Health Regulations for Construction*, Title 29, Code of Federal Regulations, Part 1926.652, Occupational Safety and Health Administration, Washington, D.C.

OSHA, 1989, *Occupational Safety and Health Standards*, Title 29, Code of Federal Regulations, Part 1910.1000, Occupational Safety and Health Administration, Washington, D.C.

PNL, 1988 *Environmental Monitoring at Hanford for 1987,* PNL-6464, Pacific Northwest Laboratory, Richland, Washington.

WHC, 1989, *Environmental Investigations and Site Characterizations Manual*, WHC-CM-7-7, Richland, Washington.

Attachment 3

PROJECT MANAGEMENT PLAN

9011330400

THIS PAGE INTENTIONALLY
LEFT BLANK

9 0 1 1 3 3 0 4 0 1

CONTENTS

1.0 Introduction PMP-1

2.0 Project Organization and Responsibilities PMP-1
2.1 Interface of Regulatory Authorities and the U.S. Department of Energy PMP-1
2.2 Project Organization and Responsibilities PMP-2

3.0 Documentation and Records PMP-7

4.0 Financial and Project Tracking Requirements PMP-7
4.1 Management Control PMP-7
4.2 Meetings and Progress Reports PMP-12

5.0 References PMP-14

FIGURES:

PMP-1 Project Organization for Hanford Site RI/FS Projects . . . . . PMP- 3
PMP-2 Example Project Organization for 100-KR-1 RI/FS Contractor Team . . . . . PMP- 5
PMP-3 Hanford Site Technical Resources for Conducting RI/FS . . . . . PMP- 6
PMP-4 The Hanford Site Soil Sampling Team . . . . . PMP- 8
PMP-5 The Hanford Site Biological Sampling Team . . . . . PMP- 9
PMP-6 The Hanford Site Physical and Geophysical Survey Team PMP-10
PMP-7 The Hanford Site Vadose Zone Drilling and Sampling Team PMP-11

THIS PAGE INTENTIONALLY
LEFT BLANK

1.0 INTRODUCTION

This project management plan (PMP) defines the administrative and institutional tasks necessary to support the Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA) remedial investigation/feasibility study (RI/FS) for the 100-KR-1 operable unit at the Hanford Site. This plan defines the responsibilities of the various participants, the organizational structure, and the project tracking and reporting procedures.

The U.S. Environmental Protection Agency (EPA), the Washington Department of Ecology (Ecology), and the U.S. Department of Energy (DOE) have entered into an agreement (the Hanford Federal Facility Agreement and Consent Order) for remedial actions and corrective activities on the Hanford Site (Ecology et al., 1989). An action plan, which implements and is an attachment to the agreement, defines EPA and Ecology regulatory integration and the methods and processes to be used to implement the agreement. This PMP is in accordance with the provisions of the action plan dated May 1989. Any revisions to the action plan that would result in changes to project management requirements would supersede the provisions of this plan.

2.0 PROJECT ORGANIZATION AND RESPONSIBILITIES

2.1 INTERFACE OF REGULATORY AUTHORITIES AND THE DOE

The 100-KR-1 operable unit consists of inactive waste management units to be remediated under CERCLA. The EPA has been designated as the lead regulatory agency as defined in the agreement (Ecology et al. 1989). Accordingly, EPA is responsible for overseeing remedial action activity at this unit and ensuring that the applicable authorities of both EPA and Ecology are applied. The specific responsibilities of EPA, Ecology, and the DOE are detailed in the action plan.

2.2 PROJECT ORGANIZATION AND RESPONSIBILITIES

The project organization for implementing remedial activities at the Hanford Site is shown in Figure PMP-1. The following sections describe the responsibilities of the individuals shown in this figure.

Project Manager. The EPA, DOE, and Ecology have each designated one individual as project manager, who will serve as the primary point of contact for all activities to be carried out under the agreement and the action plan. The responsibilities of the project managers are given in Section 4 of the action plan.

Unit Manager. As shown in Figure PMP-1, the EPA, DOE, and Ecology will each designate an individual as a unit manager for the 100-KR-1 operable unit.

The unit manager from EPA will serve as the lead unit manager. The EPA unit manager will be responsible for regulatory oversight of all RI/FS activities required for the 100-KR-1 operable unit.

The unit manager from Ecology will be responsible for making decisions related to issues for which the supporting regulatory agency maintains authority. All such decisions will be made in consideration of recommendations made by the EPA unit manager.

The unit manager from DOE will be directly responsible for supervising the RI/FS activities at the 100-KR-1 operable unit. These responsibilities include maintaining and controlling the schedule and budget and keeping the EPA and Ecology unit managers informed as to the status of the RI/FS, particularly the status of agreements and commitments.

Quality Assurance Officer. The QA officer is responsible for monitoring overall environmental restoration program activities through establishment of Hanford Site QA auditing program controls that may be appropriately applied to RI/FS activities. The QA officer is specifically vested with the organizational independence and authority to identify conditions adverse to quality and to systematically seek effective corrective action.

Quality Coordinator. The quality coordinator is responsible for coordinating and monitoring performance of the QAPP requirements by means of internal surveillance techniques and by auditing, as directed by the QA officer. The quality coordinator

9 0 1 1 9 8 7 0 4 0 4

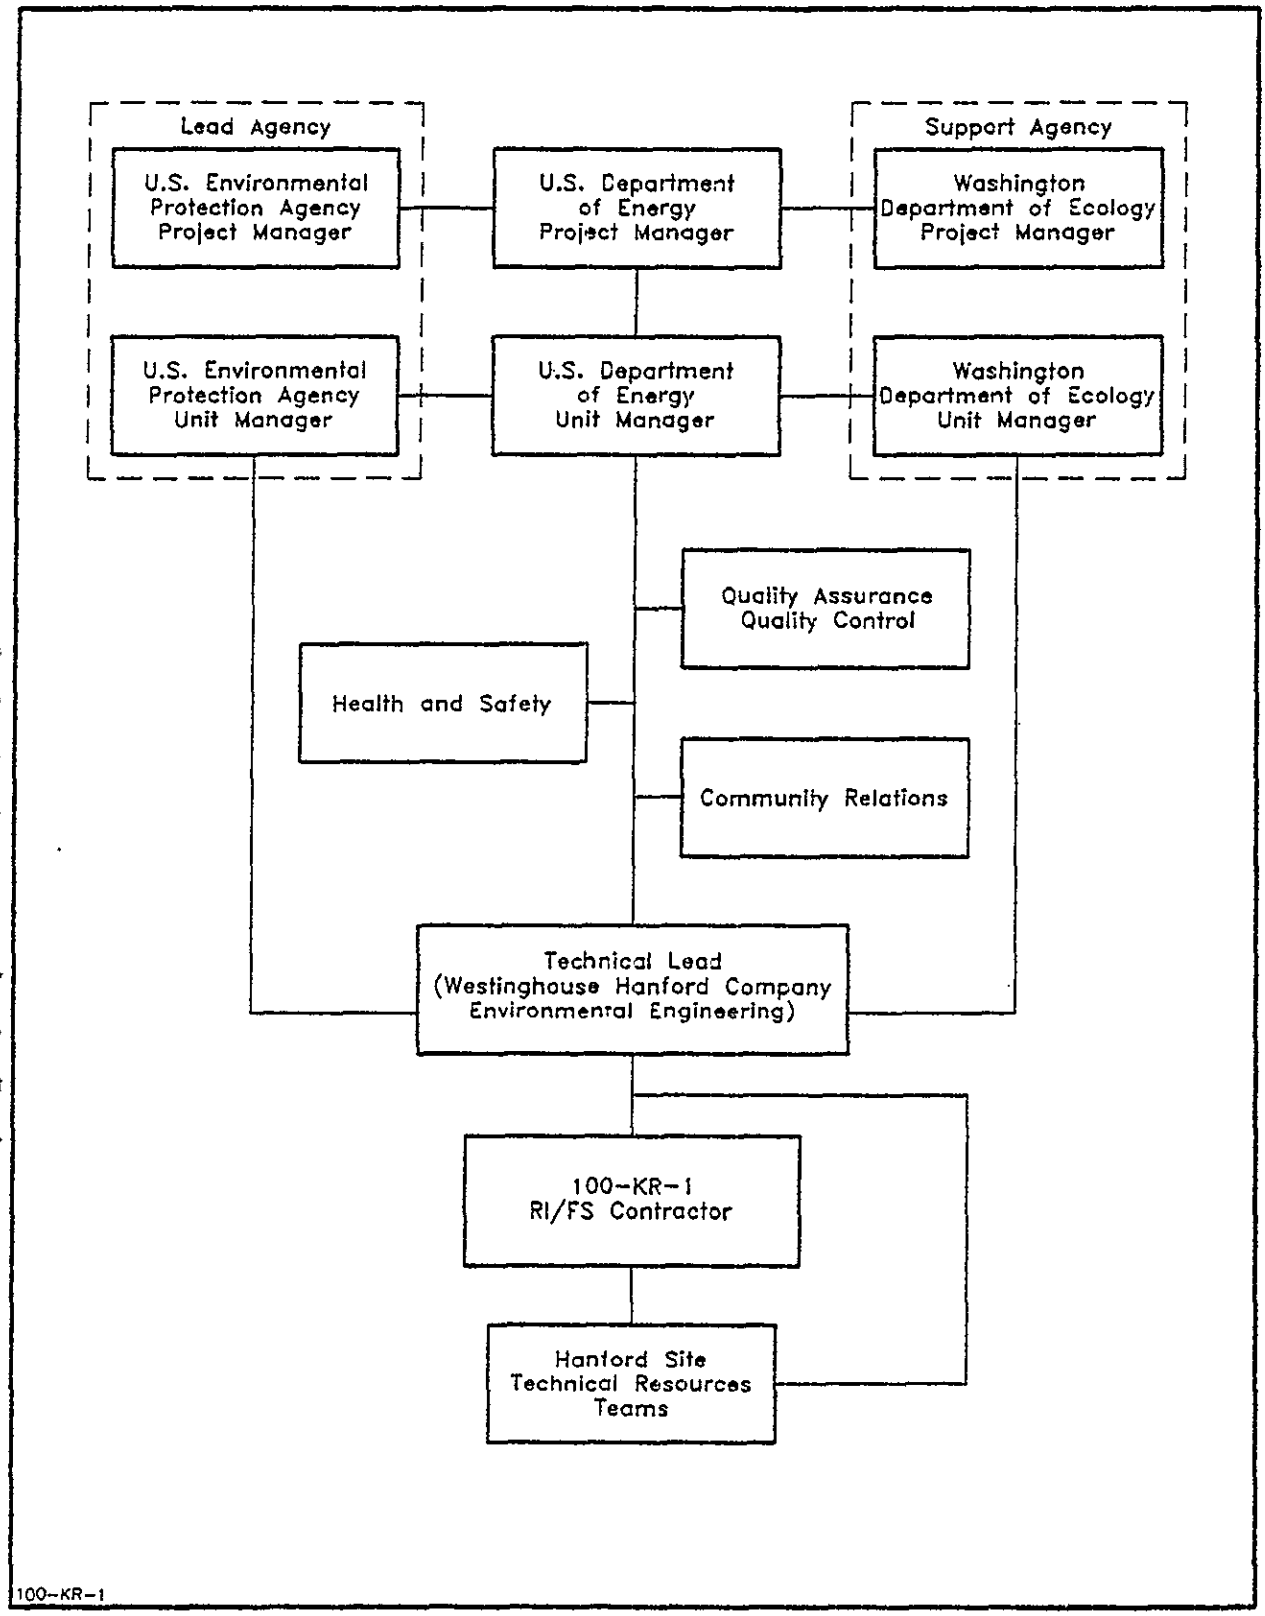

FIGURE PMP-1. Project Organization for Hanford Site RI/FS Projects.

retains the necessary organizational independence and authority to identify conditions adverse to quality and to inform the technical lead of needed corrective action.

Health and Safety Officer. The health and safety officer is responsible for monitoring all potential health and safety hazards, including those associated with radioactive, volatile, and/or toxic compounds during sample handling and sampling decontamination activities. The health and safety officer has the responsibility and authority to halt field activities resulting from unacceptable nonradioactive health and safety hazards. In concert with the health physics technician, the health and safety officer also has authority total field activities resulting from unacceptable radioactive health and safety hazards.

Technical Lead. The technical lead will be a designated person within the Westinghouse Hanford Environmental Engineering Group. The responsibilities of the technical lead will be to plan, authorize, and control work so that it can be completed on schedule and within budget, and to ensure that all planning and work performance activities are technically sound.

Remedial Investigation and Feasibility Study Coordinators. The RI and FS coordinators will be responsible for coordinating all activities related to the RI and FS, respectively, including data collection, analysis, and reporting. The RI and FS coordinators will be responsible for keeping the technical lead informed as to the RI and FS work status and any problems that may arise.

RI/FS Contractor. Figure PMP-1 also shows the organizational relationship of an offsite RI/FS contractor. If an offsite contractor is used to perform the RI/FS, the contractor would assume most responsibilities of the RI and FS coordinators, as described above. In this instance, the contractor will be directly responsible for planning data collection activities and of analyzing and reporting the results of the data-gathering in the RI and FS reports. However, the Westinghouse Hanford Environmental Engineering Group coordinator would retain the responsibility for securing and managing the field sampling efforts of the Hanford Site technical resource teams, described below. Figure PMP-2 shows a sample organizational structure for an RI/FS contractor team.

Hanford Site Technical Resources. The various technical resources available on the Hanford Site for performing the RI field studies are shown in Figure PMP-3. These resources will be responsible for performing data collection activities and analyses, and for reporting the results of specific technical activities related to the RI.

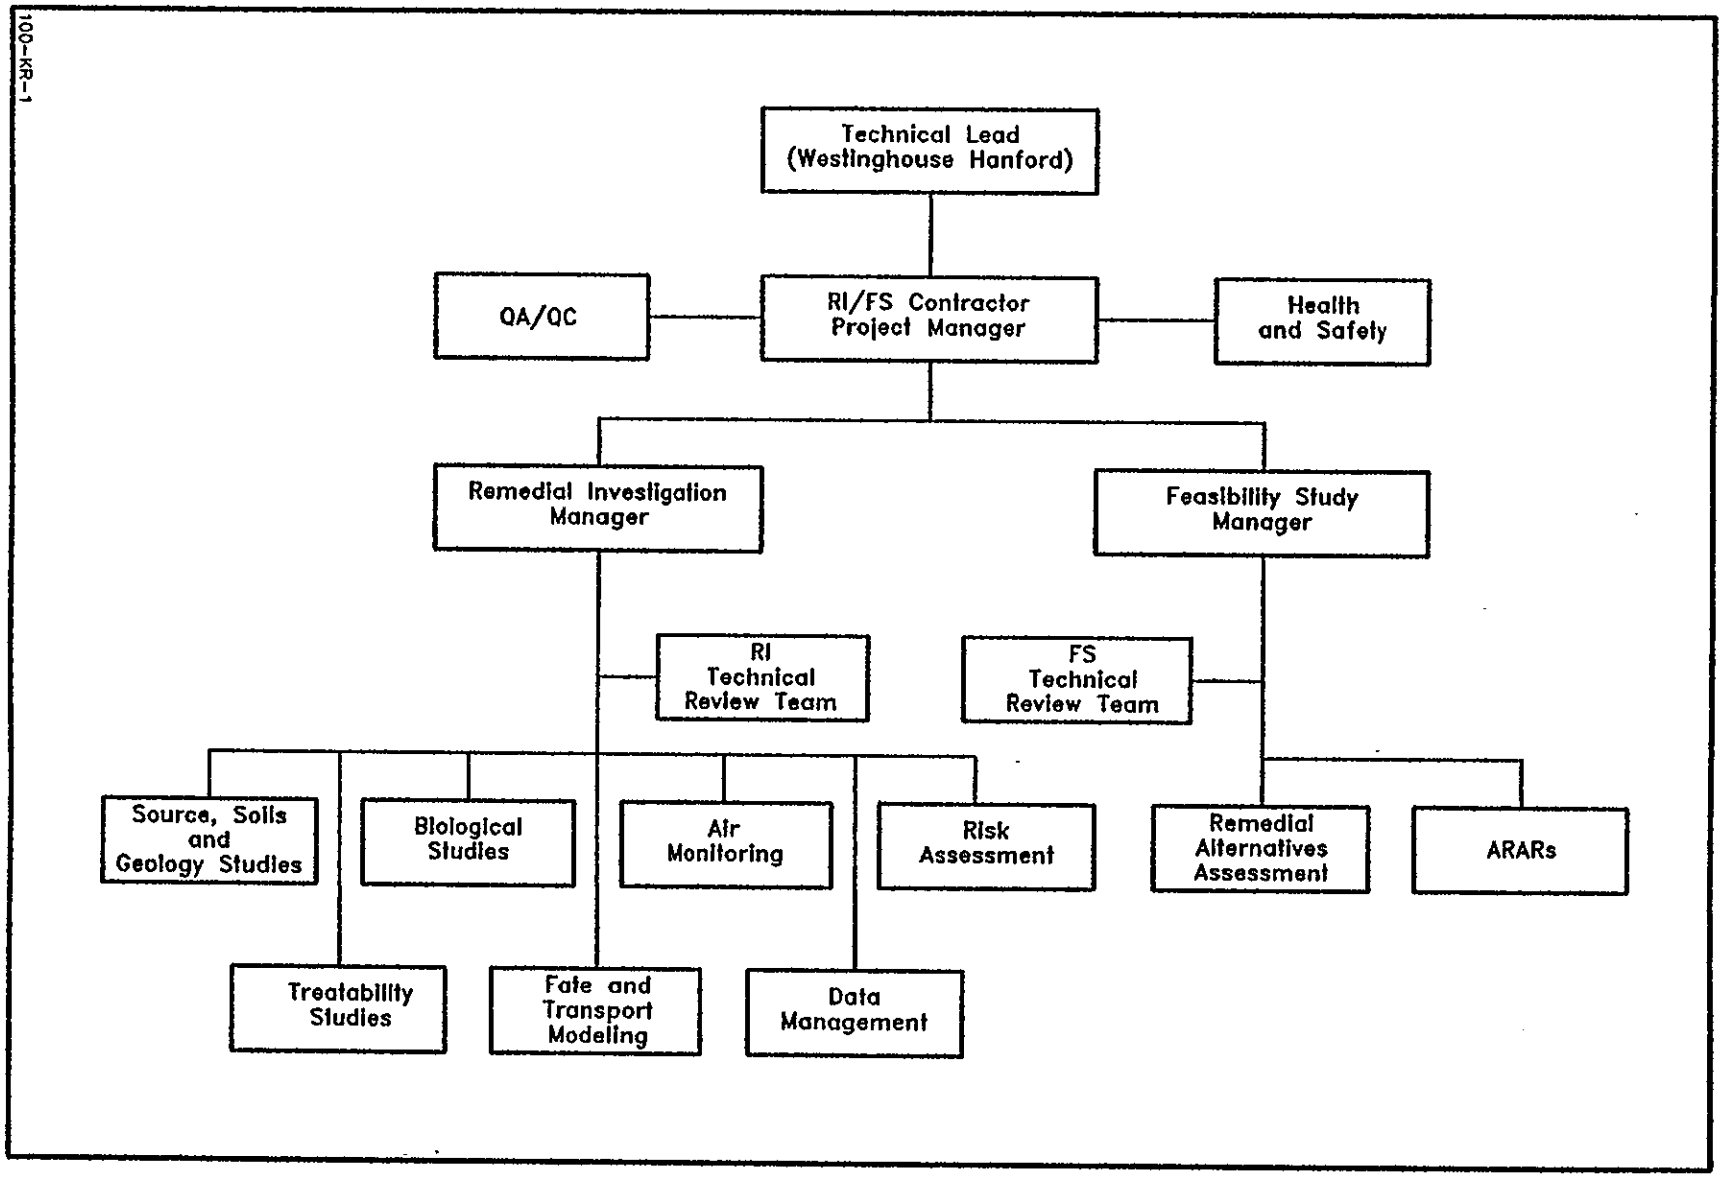

FIGURE PMP-2. Example Project Organization, 100-KR-1 RI/FS Contractor Team.

Subject/Activity	TECHNICAL RESOURCES	
	Remedial Investigation	Feasibility Study
Hydrology and geology	Westinghouse Hanford [a]/Geosciences; PNL [b]/Earth and Environmental Sciences Center	Westinghouse Hanford/ Geosciences
Toxicology and risk/endangerment assessment	Westinghouse Hanford/Environmental Technology; PNL/Earth and Environmental Sciences Center; PNL/Life Sciences Center	Westinghouse Hanford/ Environmental Technology
Environmental chemistry	Westinghouse Hanford/Geosciences; PNL/Earth and Environmental Sciences Center	Westinghouse Hanford/ Geosciences
Geotechnical and civil engineering	Westinghouse Hanford/Geosciences (Planning); PNL/Earth and Environmental Sciences Center	N/A
Geotechnical and civil engineering	N/A	Westinghouse Hanford/ Environmental Engineering PNL/Waste Technology Center
Ground water treatment engineering	N/A	Westinghouse Hanford/ Environmental Engineering PNL/Waste Technology Center
Waste stabilization and treatment	N/A	Westinghouse Hanford/ Environmental Engineering PNL/Waste Technology Center
Surveying	Kaiser Engineers Hanford	N/A
Soil and water	Westinghouse Hanford/Environmental Engineering/Environmental Field Services/Office of Sample Management and subcontractor; PNL/Earth and Environmental Services Center/Materials and Chemical Services Center	N/A
Drilling and well installation	Westinghouse Hanford/Geosciences/ Environmental field services; Kaiser Engineers	N/A
Radiation protection	Westinghouse Hanford/Health Physics	N/A

[a] Westinghouse Hanford = Westinghouse Hanford Company
[b] PNL = Pacific Northwest Laboratory

100-KR-1

FIGURE PMP-3. Hanford Site Technical Resources for Conducting RI/FS.

Figures PMP-4 through -7 show the detailed organizational structure of specific technical teams. Internal and external work orders and subcontractor task orders will be written by the Westinghouse Hanford technical lead to use these technical resources, which are under the control of the technical lead. Statements of work will be provided to the technical teams and will include a discussion of authority and responsibility, a schedule with clearly defined milestones, and a task description including specific requirements. Each technical team will keep the RI coordinator informed on the RI work status performed by that group and of any problems that may arise.

3.0 DOCUMENTATION AND RECORDS

All RI/FS plans and reports will be categorized as either primary or secondary documents as described in the action plan. The process for document review and comment is as described in Section 9 of the action plan. Changes in the work schedule, as well as minor field changes, can be made without having to process a formal revision. The process for making these changes is stated in the action plan. Administrative records, which must be maintained to support the Hanford Site CERCLA activities, will be in accordance with Section 9 of the action plan.

4.0 FINANCIAL AND PROJECT TRACKING REQUIREMENTS

4.1 MANAGEMENT CONTROL

Westinghouse Hanford will have the overall responsibility for planning and controlling the RI/FS activities, and providing effective technical, cost, and schedule baseline management. If an offsite RI/FS contractor is used, the contractor will assume the direct day-to-day responsibilities for these management functions. The management control system used for this project must meet the requirements of DOE Order 4700.1, *Project Management System* (DOE 1987), and DOE Order 2250.1B, *Cost and Schedule Control Systems Criteria for Contract Performance Measurement* (DOE 1985). The Westinghouse Hanford Management Control System (MCS) meets these requirements. The primary goals of the Westinghouse Hanford MCS are to provide methods for planning, authorizing, and controlling work so that it can be

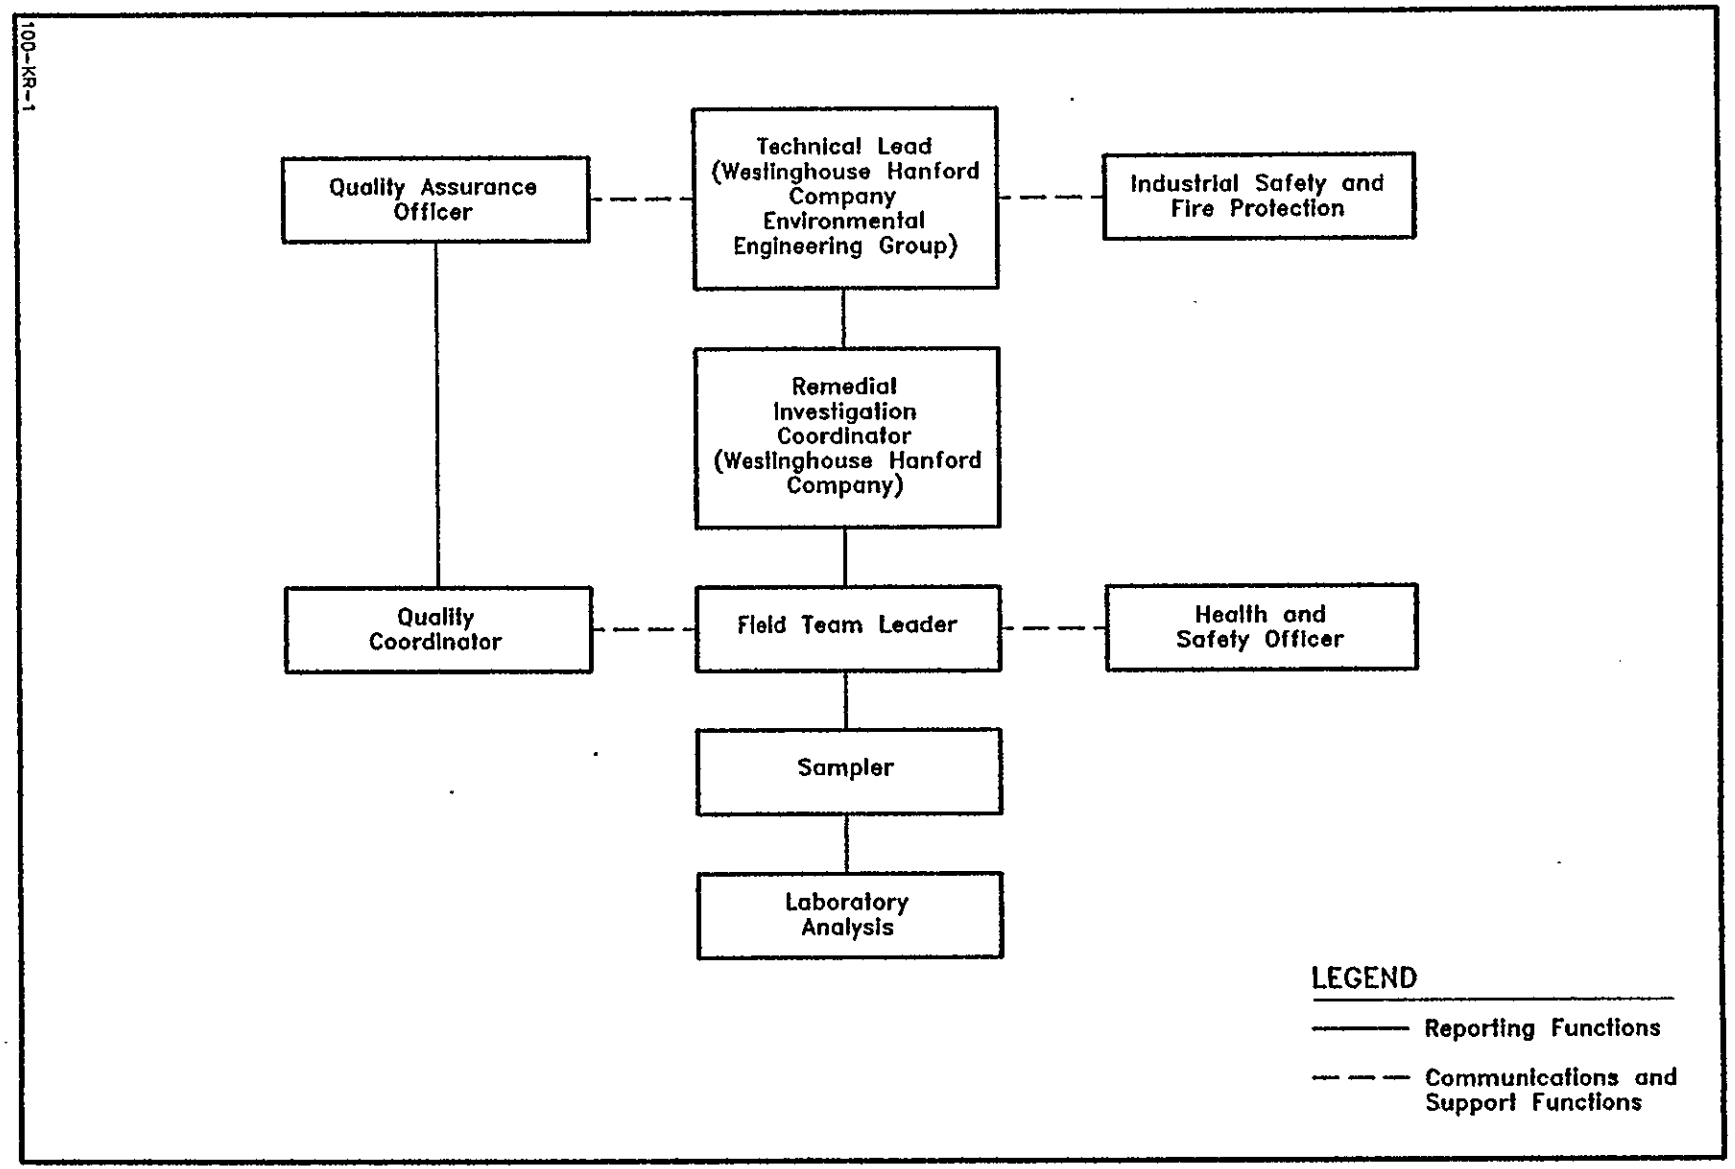

FIGURE PMP-4. The Hanford Site Soil Sampling Team.

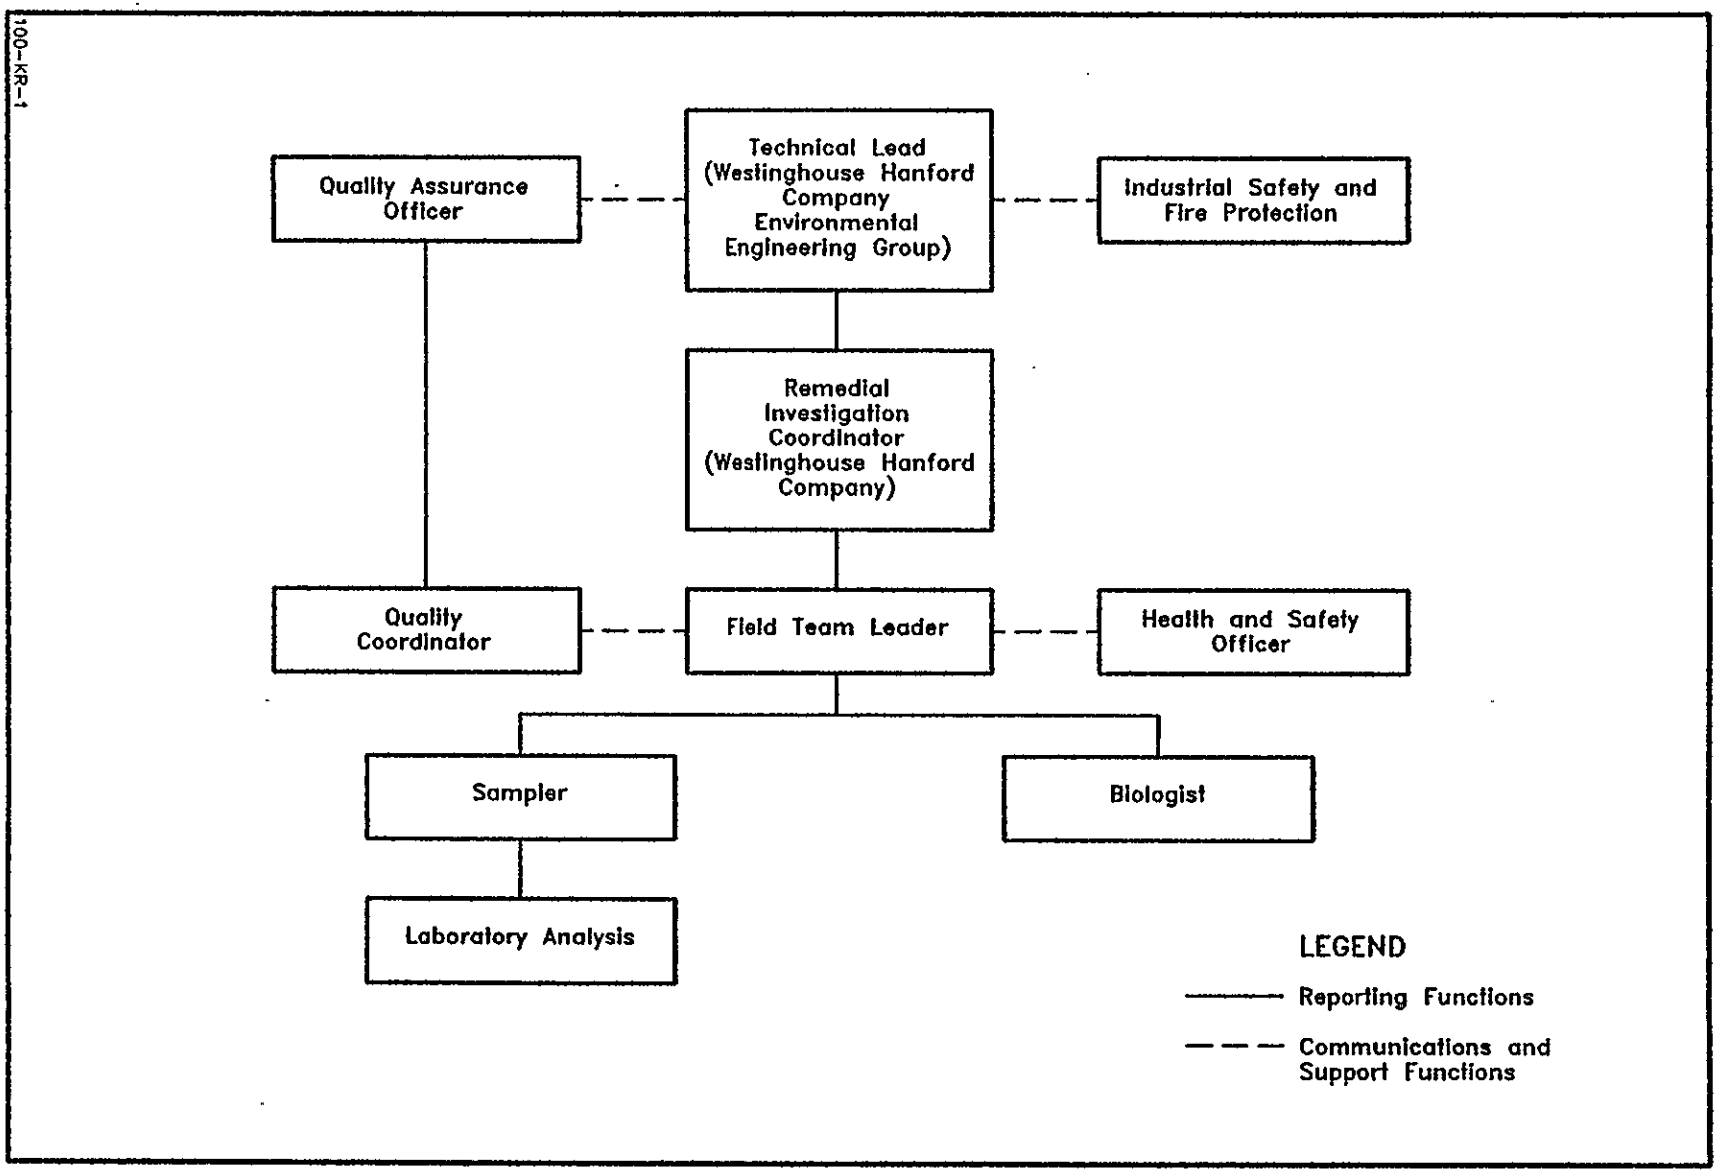

FIGURE PMP-5. The Hanford Site Biological Sampling Team.

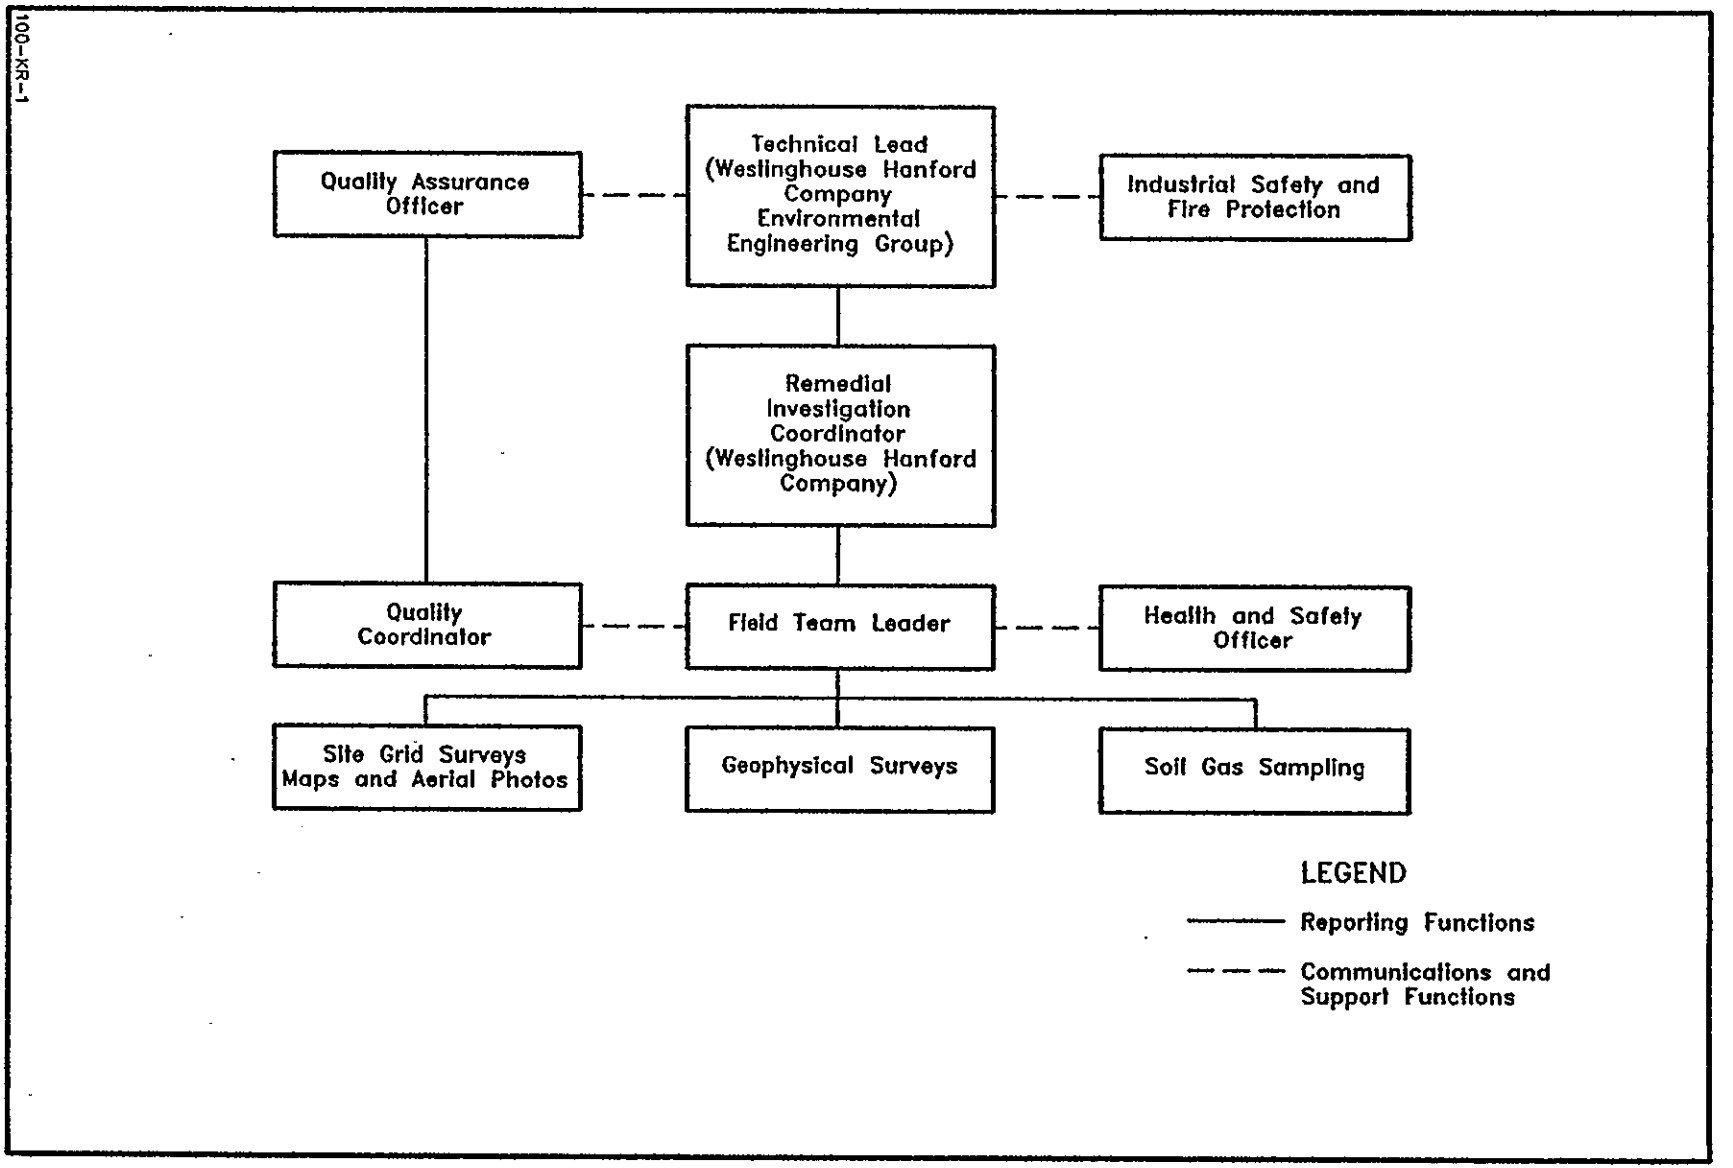

FIGURE PMP-6. The Hanford Site Physical and Geophysical Survey Team.

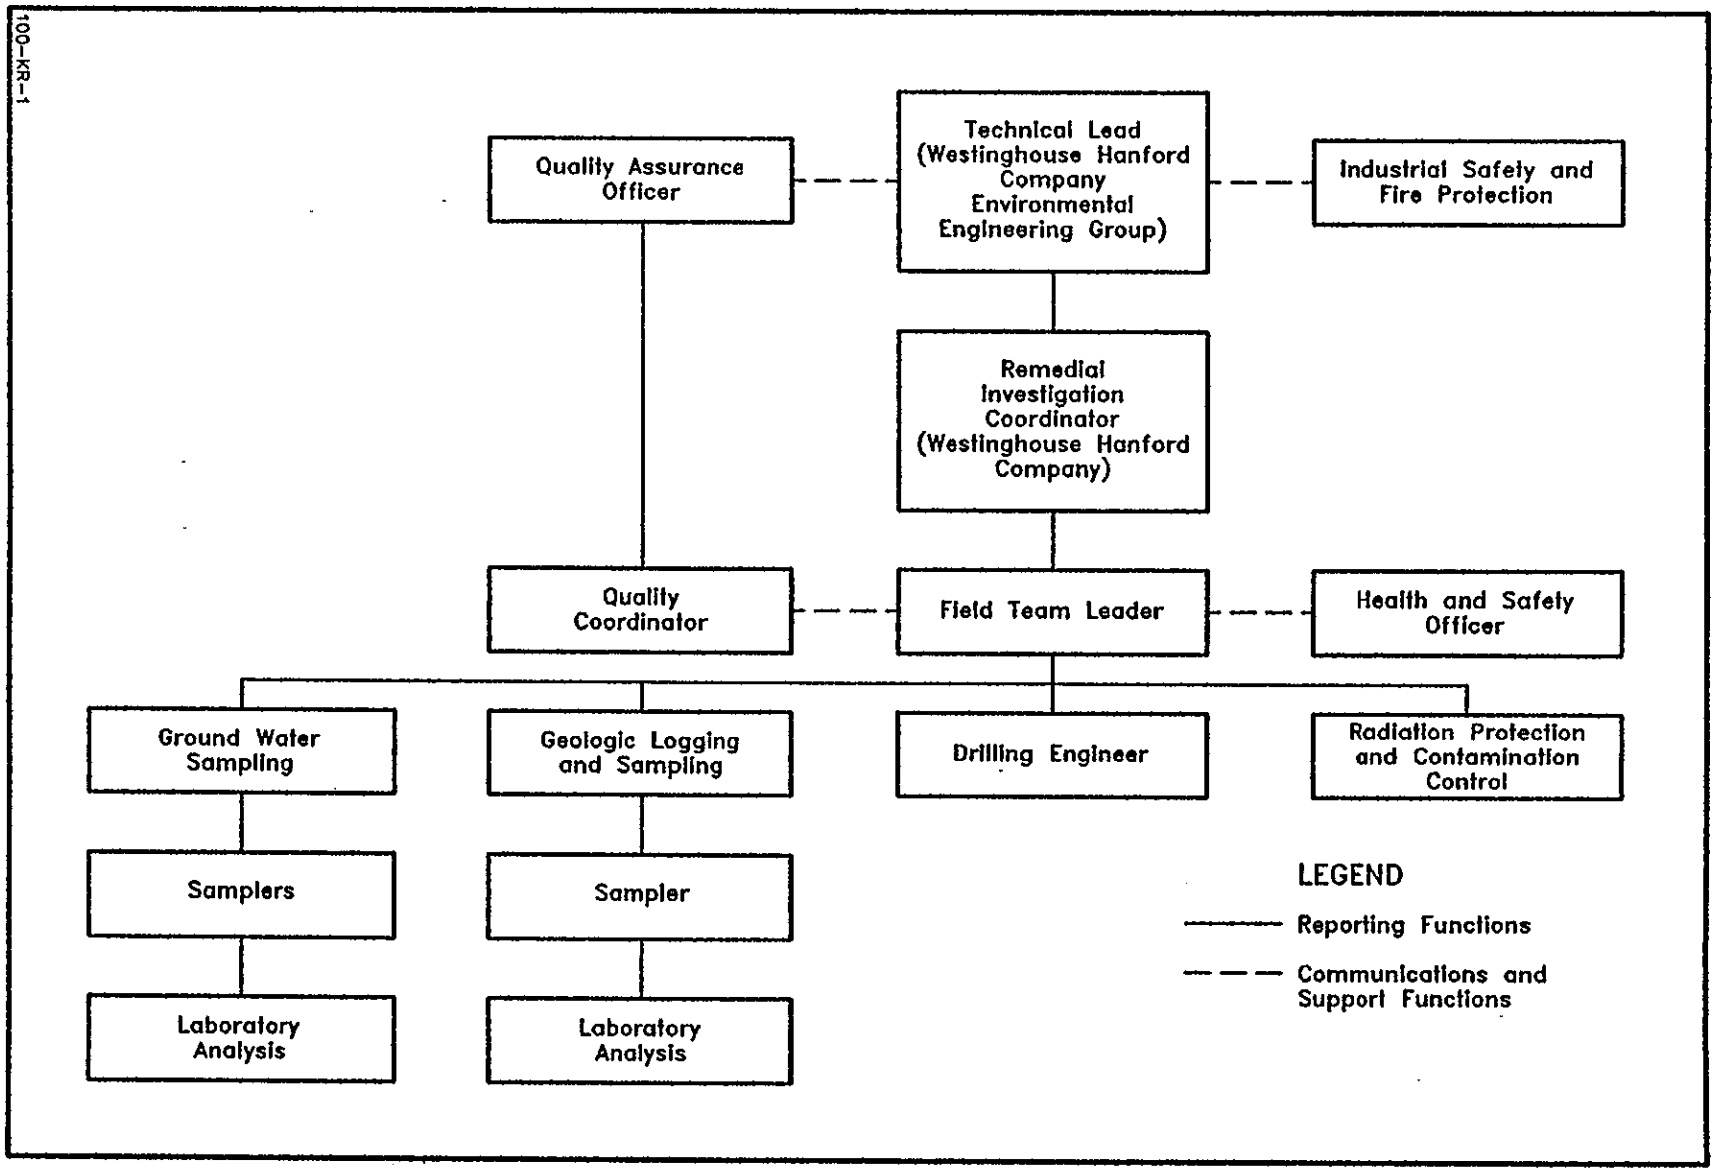

FIGURE PMP-7. The Hanford Site Drilling and Sampling Team.

completed on schedule and within budget, and to ensure that all planning and work performance activities are technically sound and in conformance with management and quality requirements.

The RI/FS schedule for the 100-KR-1 operable unit and major milestones are described in Section 6.0 of the work plan. The schedule in the work plan will be the primary vehicle for the unit lead and technical lead to track the progress of the RI/FS for the 100-KR-1 operable unit. The RI/FS schedule must be consistent with the work schedule contained in the action plan.

The RI/FS schedule in the work plan will be updated at least annually, to expand the new current fiscal year and the follow-on year. In addition, any approved schedule changes would be incorporated at this time, if not previously incorporated. This update will be performed in the fourth quarter of the previous fiscal year (e.g., July to September) for the upcoming current fiscal year. The work schedule can be revised at any time during the year if the need arises, but the changes would be restricted to major changes that would not be suitable for the change control process.

4.2 MEETINGS AND PROGRESS REPORTS

Both project and unit managers must meet periodically to discuss progress, review plans, and address any issues that have arisen. The project managers' meeting will take place at least quarterly.

Unit managers shall meet monthly to discuss progress, address issues, and review near-term plans pertaining to their respective operable units and/or treatment, storage, and disposal (TSD) groups/units. The meetings shall be technical in nature, with emphasis on technical issues and work progress. The assigned DOE unit manager for the 100-KR-1 operable unit will be responsible for preparing revisions to the RI/FS schedule prior to the meeting. The schedule shall address all ongoing activities associated with the operable unit, including actions on specific source units (e.g., sampling). This schedule will be provided to all parties and reviewed at the meeting. Any agreements and commitments (within the unit manager's level of authority) resulting from the meeting will be prepared and signed by all parties as soon as possible after the meeting. Meeting minutes will be issued by the DOE unit manager and will summarize the discussion at the meeting, with information copies

given to the project managers. The minutes will be issued within 5 working days following the meeting. The minutes will include, at a minimum, the following:

- Status of previous agreements and commitments
- Any new agreements and commitments
- Schedules (with current status noted)
- Any approved changes signed off at the meeting.

Project coordinators for each operable unit also will meet on a monthly basis to share information and to discuss progress and problems.

The DOE shall issue a quarterly progress report for the Hanford Site within 45 days following the end of each quarter. Quarters end on March 30, June 30, September 30, and December 31. The quarterly progress reports will be placed in the public information repositories. The report shall include the following:

- Highlights of significant progress and problems
- Technical progress with supporting information, as appropriate
- Problem areas with recommended solutions (This will include any anticipated delays in meeting schedules, the reason(s) for the potential delay, and actions to prevent or minimize the delay)
- Significant activities planned for the next quarter
- Work schedules (with current status noted).

5.0 REFERENCES

DOE, 1985, *Cost and Schedule Control Systems Criteria for Contract Performance Measurement*, DOE Order 2250.1B, U.S. Department of Energy, Washington, D.C.

DOE, 1987, *Project Management System*, DOE Order 4700.1, U.S. Department Of Energy, Washington, D.C.

Washington Department of Ecology, U.S. Environmental Protection Agency, and U.S. Department of Energy, May 1989, *Hanford Federal Facility Agreement and Consent Order*, 89-10.

9 0 1 1 3 9 3 0 4 1 6

Attachment 4

DATA MANAGEMENT PLAN

9 0 1 1 3 3 0 4 1 7

THIS PAGE INTENTIONALLY
LEFT BLANK

9 1 4 0 3 8 8 1 1 0 6

CONTENTS

1.0 Introduction and Objectives DMP-1
1.1 Introduction DMP-1
1.2 Objectives DMP-1

2.0 Types of Data DMP-2
2.1 Data Types DMP-2
2.2 Data Collection DMP-2
2.3 Data Storage and Access DMP-12
2.4 Data Quantity DMP-13

3.0 Data Management Plan DMP-13
3.1 Objective DMP-13
3.2 Organizations Controlling Data DMP-13
3.3 Databases DMP-25

4.0 Environmental Information Management Plan DMP-26

5.0 Hanford Environmental Information System DMP-27
5.1 Objective DMP-27
5.2 Integration of 100-KR-1 Data into HEIS DMP-28

6.0 References DMP-28

FIGURES

DMP-1 General Data Management Plan for 100-KR-1 Work Plan Task Data DMP-22
DMP-2 General Data Management Plan for 100-KR-1 Work Plan Task Data After Implementation of HEIS DMP-29

TABLES

DMP-1 Procedures Applicable to Work Plan Tasks DMP-3
DMP-2 Personnel and Compliance Procedures DMP-11
DMP-3 Estimated Quantity of Samples for Operable Unit Characterization DMP-14

THIS PAGE INTENTIONALLY
LEFT BLANK

1.0 INTRODUCTION AND OBJECTIVES

1.1 INTRODUCTION

An extensive amount of data will be generated over the next several years in connection with the Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA) remedial investigation/feasibility study (RI/FS) process for the 100-KR-1 operable unit. The quality of these data is extremely important to the full remediation of the operable unit as agreed upon by the U.S. Department of Energy (DOE), U.S. Environmental Protection Agency (EPA), Washington Department of Ecology (Ecology), and interested parties.

This data management plan (DMP) addresses management of data generated from the 100-KR-1 operable unit work plan, field sampling plan (FSP), quality assurance project plan (QAPP), and health and safety plan (HSP) activities.

Development of a comprehensive plan for the management of all environmental data generated at the Hanford Site is under way. The *Environmental Information Management Plan* (EIMP) (Steward 1989), released in March 1989, describes activities in the Environmental Data Management Center (EDMC) and provides a description of the long-range goals for management of scientific and technical data. The EIMP is currently under review and is expected to be revised and expanded in fiscal year 1990.

1.2 OBJECTIVES

This DMP describes the process for accessing and tracking the receipt, storage, and control of validated data, records, documents, correspondence, and other information associated with the 100-KR-1 RI/FS.

This DMP addresses the following itemizations:

- Types of data to be collected
- Plans for managing data
- Organizations controlling data

- Databases used to store the data
- Environmental Information Management Plan (EIMP)
- Hanford Environmental Information System (HEIS).

2.0 TYPES OF DATA

2.1 DATA TYPES

General data types include field logbooks, verified sample analyses, historic data, chain-of-custody forms, quality assurance/quality control (QA/QC) data, reports, memoranda/meeting minutes, telephone conference memoranda, archived samples, raw sample data, videotapes, magnetic media, paper tapes, personnel training records, exposure records, respiratory protection fitting records, personnel health and safety records, and compliance and regulatory data. Table DMP-1 lists the data types and applicable procedures by work plan task. Table DMP-2 lists data types and procedures for health and safety planning, as well as for regulatory compliance activities.

2.2 DATA COLLECTION

Data will be collected according to the FSP and the QAPP. Table DMP-1 lists controlling procedures for data collection and handling before turnover of responsibility to the organization responsible for data storage. All procedures for data collection will be approved in compliance with applicable Westinghouse Hanford Company (Westinghouse Hanford) procedures. Where Westinghouse Hanford environmental investigations instructions (EII) are referenced, they will be the latest approved versions from the *Environmental Investigations and Site Characterizations Manual* (WHC 1989).

Table DMP-1. Site Characterization

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC[a]	Database or Controlling Organization: Others
OPERABLE UNIT CHARACTERIZATION				
Task 1 - Project Management (Addressed in Project Management Plan)				
Task 2 - Source Investigations				
Subtask 2a - Data Compilation	Historic: Engineering plans, reports	EII 1.6	X	
	Telephone conversations	EII 1.6	X	
	Memoranda/ minutes	EII 1.6	X	
Subtask 2b - Maps	Aerial photographs	EII 1.6	X	
	Logbooks	EII 1.5	X	
	Magnetic media and supporting documentation	EII 1.6	X	
	Maps	EII 1.6	X	
Subtask 2c - Field Activities	Logbooks	EII 1.5	X	
	Magnetic media and supporting documentation	EII 1.6	X	
	Chart Recordings	EII 1.6	X	
	Chain of custody	EII 5.1	X	
	QA/QC		X	OSM[b]
Subtask 2d - Laboratory Analysis	Validated sample analysis	EII 1.5	X	
	QA/QC	EII 1.6	X	
Subtask 2e - Data Evaluation	Log books	EII 1.5	X	
	QA/QC	EII 1.0	X	
Task 3 - Geological Investigations				
Subtask 3a - Data Compilation	Technical memos	EII 1.6	X	
	Geological logs	EII 9.1	X	

Table DMP-1. Site Characterization

Page 2

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC[a]	Database or Controlling Organization: Others
Subtask 3b - Field Activities	Aerial photographs	EII 1.6	X	
	Log books	EII 1.5	X	
		EII 11.1	X	
	Magnetic media and supporting documentation	EII 1.6	X	
		EII 1.6	X	
	Chart recordings	EII 1.6	X	
	Core/cutting samples	EII 5.2	X	
	Chain of custody	EII 1.5	X	
	QA/QC			OSM
	Geophysical surveys	EII 11.2	X	
Subtask 3c - Laboratory Analysis	Validated sample analysis	EII 1.6	X	
	QA/QC	EII 1.6	X	OSM
Subtask 3d - Data Evaluation	Log books	EII 1.5	X	
	QA/QC	EII 1.6	X	
Task 4 - Surface Water and Sediments Investigations (See Data Management for 100-KR-4 Operable Unit)				
Task 5 - Vadose Investigations				
Subtask 5a - Data Compilation	Technical memos	EII 1.6	X	
	Geological logs	EII 9.1	X	
Subtask 5b - Field Activities	Aerial photographs	EII 1.6	X	
	Log books	EII 1.5	X	
		EII 11.1	X	
	Magnetic media and supporting documentation	EII 1.6	X	
		EII 1.6	X	
	Chart recordings	EII 1.6	X	
	Core/cutting samples	EII 5.2	X	
	Chain of custody	EII 1.5	X	
	QA/QC			OSM
	Geophysical surveys	EII 11.2	X	
	Borehole logs	EII 9.1	X	
Subtask 5c - Laboratory Analysis	Validated sample analysis	EII 1.6	X	
	QA/QC	EII 1.6	X	OSM

Table DMP-1. Site Characterization

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC[a]	Database or Controlling Organization: Others
Subtask 5d - Data Evaluation	Log books	EII 1.5	X	
	QA/QC	EII 1.6	X	
Task 6 - Ground Water Investigations	(See Data Management Plan for 100-KR-4 Operable Unit)			
Task 7 - Air Investigations				
Subtask 7a - Data Compilation	Technical memos	EII 1.6	X	
	Historic reports	PNL-6509		
Subtask 7b - Field Activities	Aerial photographs	EII 1.6	X	
	Log books	EII 1.5	X	
		EII 11.1	X	
	Magnetic media	EII 1.6	X	
	and supporting documentation	EII 1.6	X	
	QA/QC			OSM
Subtask 7c - Laboratory Analysis	Validated sample analysis	EII 1.6	X	
	QA/QC	EII 1.6	X	OSM
Subtask 7d - Data Evaluation	Log books	EII 1.5	X	
	QA/QC	EII 1.6	X	
Task 8 - Ecological Investigations				
Subtask 8a - Data Compilation	Technical memos	EII 1.6	X	
Subtask 8b - Field Activities	Aerial photographs	EII 1.6	X	
	Log books	EII 1.5	X	
		EII 11.1	X	
	Magnetic media	EII 1.6	X	
	and supporting documentation	EII 1.6	X	
	Chart recordings	EII 1.6	X	
	Chain of custody	EII 1.5	X	
	QA/QC			OSM
Subtask 8c - Laboratory Analysis	Validated sample analysis	EII 1.6	X	
	QA/QC	EII 1.6	X	OSM

Table DMP-1. Site Characterization

Page 4

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC[a]	Database or Controlling Organization: Others
Subtask 8d - Data Evaluation	Log books	EII 1.5	X	
	QA/QC	EII 1.6	X	
Task 9 - Cultural Resource Investigations	Hanford Plan	PNL-6942		
Task 10 - Data Evaluations	Technical memos	EII 1.6	X	
Task 11 - Baseline Risk Assessment	Technical memos	EII 1.6	X	
	Computer models	EII 1.6	X	
	Magnetic media and supporting documentation	EII 1.6	X	
Task 12 - Report				
Subtask 12a - Prepare	Report	EII 1.6	X	
Subtask 12b - Review/Approval	Approval	EII 1.6	X	

FS PHASE I/II REMEDIAL ALTERNATIVES DEVELOPMENT

Task 1 - Project Management (Addressed in Project Management Plan)				
Task 2 - Alternatives Development				
Subtask 2a - Develop Objectives	Technical memos	EII 1.6	X	
Subtask 2b - Develop General Response Actions	Technical memos	EII 1.6	X	
Subtask 2c - Identify Potential Technologies	Technical memos	EII 1.6	X	
Subtask 2d - Evaluate Process Options	Technical memos	EII 1.6	X	
Subtask 2e - Assemble Alternatives	Technical memos	EII 1.6	X	

Table DMP-1. Site Characterization

Page 5

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC[a]	Database or Controlling Organization: Others
Subtask 2f - Identify/Action-Specific ARARs	Technical memos	EII 1.6	X	
Task 3 - Alternatives Screening				
Subtask 3a - Refine Objectives	Technical memos	EII 1.6	X	
Subtask 3b - Define Alternatives	Technical memos	EII 1.6	X	
Subtask 3c - Screen Alternatives	Technical memos	EII 1.6	X	
Subtask 3d - Identify/Action-Specific ARARs	Technical memos	EII 1.6	X	
Subtask 3e - Evaluate Data Needs	Technical memos	EII 1.6	X	
Task 4 - Report				
Subtask 4a - Prepare	Report	EII 1.6	X	
Subtask 4b - Review/Approval	Approval	EII 1.6	X	

RI PHASE II OPERABLE UNIT CHARACTERIZATION AND TREATABILITY

Task 1 - Project Management (Addressed in Project Management Plan)				
Task 2 - Source Investigations				
Subtask 2a - Data Compilation and Review	Technical Memos	EII 1.6	X	
Subtask 2b - Field Activities	Technical memos	EII 1.6	X	
Subtask 2c - Other	TBD			
Task 3 - Geologic Investigations				
Subtask 3a - Field Activities	Technical memos	EII 1.6	X	

Table DMP-1. Site Characterization

Page 6

Work Plan Task	Data Type	Procedure	Database or Controlling Organization: EDMC*	Database or Controlling Organization: Others
Subtask 3b - Laboratory Analysis	Technical memos	EII 1.6	X	
Subtask 3c - Data Evaluation	Technical memos	EII 1.6	X	
Task 4 - Surface Water and Sediments Investigations (See Data Management Plan for 100-KR-4 Operable Unit)				
Task 5 - Vadose Zone Investigations				
Subtask 5a - Field Activities	Technical memos	EII 1.6	X	
Subtask 5b - Laboratory Analysis	Technical memos	EII 1.6	X	
Subtask 5c - Data Evaluation	Technical memos	EII 1.6	X	
Task 6 - Ground Water Investigations (See Data Management Plan for 100-KR-4 Operable Unit)				
Task 7 - Air Investigations				
Subtask 7a - Field Activities	Technical memos	EII 1.6	X	
Subtask 7b - Laboratory Analysis	Technical memos	EII 1.6	X	
Subtask 7c - Data Evaluation	Technical memos	EII 1.6	X	
Task 8 - Ecological Investigations				
Subtask 8a - Field Activities	Technical memos	EII 1.6	X	
Subtask 8b - Laboratory Analysis	Technical memos	EII 1.6	X	
Subtask 8c - Data Evaluation	Technical memos	EII 1.6	X	
Task 9 - Treatability Work Plan Development	Work Plan	EII 1.6	X	
Task 10 - Treatability Work Plan Implementation	Pilot and test data/ Log books	EII 1.5	X	
	Sample analysis	EII 1.6	X	
	Magnetic media	EII 1.6	X	
	Technical memos	EII 1.6	X	

Table DMP-1. Site Characterization

Work Plan Task	Data Type	Procedure	Database or Controlling Organization	
			EDMC*	Others
Task 11 - Cultural Resource Investigations	Plan	PNL-6942		
Task 12 - Data Evaluation	Log books QA/QC	EII 1.5 EII 1.6	X X	
Task 13 - Baseline Risk Assessment	Technical memos	EII 1.6	X	
Task 14 Report				
Subtask 14a - Prepare	Report	EII 1.6	X	
Subtask 14b - Review/Approve	Report	EII 1.6	X	
FS PHASE III REMEDIAL ALTERNATIVES ANALYSIS				
Task 1 - Define Alternatives	Technical memos	EII 1.6	X	
Task 2 - Alternative Analysis	Technical memos	EII 1.6	X	
Task 3 - Compare Alternatives	Technical memos	EII 1.6	X	
Task 4 - Report				
Subtask 4a - Prepare	Report	EII 1.6	X	
Subtask 4b - Review/Approve	Report	EII 1.6	X	
Task 5 - Corrective Action Plan	Plan	EII 1.6	X	
NEPA				
Task 1 - Analyze	Technical memos	EII 1.6	X	
Task 2 - Prepare	Report	EII 1.6	X	

Table DMP-1. Site Characterization

Page 8

Work Plan Task	Data Type	Procedure	Database or Controlling Organization	
			EDMC[a]	Others
Task 3 - Review/Approve	Report	EII 1.6	X	
CLOSURE PERMITS				
Task 1 - Prepare	Report	EII 1.6	X	
Task 2 Review/Approve	Report	EII 1.6	X	
INTERIM REMEDIAL ACTIONS	Technical memos To be determined	EII 1.6	X	

[a] EDMC - Environmental data management center
[b] OSM - Office of sample management

H:\1842\TABLES\KR1\DMP\177

Table DMP-2. Management of Related Administrative Data.

Category	Data type	Controlling Document/ Procedure	Database or Controlling Organization				
			TRI	HEHF	ORE	EDMC	EHPSS
Personnel	Personnel training and and qualifications	See Section 3.0					
	Occupational exposure records (non-radiologic)	EII 2.2		X			X
	Radiological exposure records	See Section 3.0				X	
	Respiratory protection fitting						X
	Personal health and safety records	EII 2.1		X			X
Compliance/ regulatory	Applicable or relevant and appropriate requirements/screening levels	EII 1.6				X	
	Guidance document tracking	EII 1.6				X	
	Compliance issues	EII 1.6				X	
	Problem resolution	EII 1.6				X	
	Administrative record	TPA-AP-06-RO & TPA-AP-10-RO				X	

TRI - Training Record Information System
HEHF - Hanford Environmental Health Foundation
ORE - Occupation Radiation Exposure
EDMC - Environmental Data Management Center
EHPSS - Environmental Health and Pesticide Services Section

H:\1842\TABLES\KR1\DMP\178

2.3 DATA STORAGE AND ACCESS

Data will be handled and stored according to procedures approved in compliance with applicable Westinghouse Hanford procedures. Data controlling organizations are listed in Table DMP-1 and Table DMP-2. The EDMC is the central file collection and processing facility. All files entering the EDMC will be indexed, recorded and placed into safe and secure storage. Data designated for placement into the administrative record will be copied, placed into the Hanford Site Administrative Record File, and distributed by the EDMC to the user community.

The following data types will reside in locations other than the EDMC.

Data type	Data location
■ QA/QC laboratory data	Office of Sample Management (Westinghouse Hanford Company)
■ Archived sample index	Office of Sample Management (Westinghouse Hanford Company)
■ Archived samples	Laboratory performing analyses (see the archived sample index)
■ Training records	Technical Training Support Section (Westinghouse Hanford Company)
■ Meteorological data	Hanford Meteorological Station (Pacific Northwest Laboratory)
■ Health and safety	Hanford Environmental Health Foundation records
■ Personal protection fitting	Environmental Health and Pesticide Services Section (Westinghouse Hanford Company)
■ Radiological exposure	Pacific Northwest Laboratory.

2.4 DATA QUANTITY

Data quantities are described in the work plan and the FSP. Estimated data quantities by operable unit work plan task, as shown in Table DMP-3, are provided for the purpose of data volume and planning work load.

3.0 DATA MANAGEMENT

3.1 OBJECTIVE

A considerable amount of data will be generated through the implementation of the 100-KR-1 operable unit work plan, FSP, and HSP. The QAPP provides the specific procedural direction and control for obtaining and analyzing samples in conformance with requirements to ensure quality data results. The FSP provides the detailed logistical methods to be employed in selecting the location, depth, frequency of collection, etc., of media to be sampled and the methods to be employed to obtain samples of the selected media for cataloging, shipment, and analysis.

Figure DMP-1 displays the general DMP outline for data generated through 100-KR-1 activities.

3.2 ORGANIZATIONS CONTROLLING DATA

This section describes the organizations that will receive data generated from 100-KR-1 activities.

3.2.1 Environmental Engineering Section

The Westinghouse Hanford Environmental Engineering Section provides the Technical Lead. The Technical Lead is responsible for maintaining and transmitting data to the designated storage facility.

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 1

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
OPERABLE UNIT CHARACTERIZATION						
Task 1 - Project Management (Addressed in Project Management Plan)						
Task 2 - Source Investigations						
Subtask 2a - Data Compilation	Historic: Engineering plans, reports	25				
	Personal Interviews	10				
	Memoranda/minutes	10				
Subtask 2b - Maps	Aerial photographs	10				
	Logbooks	1				
	Magnetic media and supporting documentation	1				
	Maps	5				
Subtask 2c - Field Activities	Logbooks	4				
	Magnetic media and supporting documentation	4				
	Chart Recordings					
	Chain of custody	14	60	185	7	
	QA/QC	10	14	185		
Subtask 2d - Laboratory Analysis	Validated sample analysis	1		185	7	1295
	QA/QC	1		185	7	1295
Subtask 2e - Data Evaluation	Log books	1				
	QA/QC	1				
Task 3 - Geological Investigations						
Subtask 3a - Data Compilation	Reports/Documents	10				
	Geological logs	30				

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 2

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 3b - Field Activities	Aerial photographs	4				
	Log books	4				
	Magnetic media and supporting documentation	4				
	Chart recordings					
	Core/cutting samples					
	Chain of custody	10	31	185	6	
	QA/QC	10		45		
	Geophysical surveys	17				
Subtask 3c - Laboratory Analysis	Validated sample analysis	1		45	6	270
	QA/QC	1		45	6	270
Subtask 3d - Data Evaluation	Log books	1				
	QA/QC	1				
Task 4 - Surface Water and Sediments Investigations (See Data Management for 100-KR-4 Operable Unit)						
Task 5 - Vadose Investigations						
Subtask 5a - Data Compilation	Technical memos	10				
	Geological logs	10				
Subtask 5b - Field Activities	Aerial photographs	4				
	Log books	4				
	Magnetic media and supporting documentation	4				
	Chart recordings	17				
	Core/cutting samples		17	310		
	Chain of custody	10	17	310		
	QA/QC	10	17	310		
	Geophysical surveys	17	17			
	Borehole logs	17				
Subtask 5c - Laboratory Analysis	Validated sample analysis	1		310	7	
	QA/QC	1		310	7	

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 3

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 5d - Data Evaluation	Log books	1				2170
	QA/QC	1				2170
Task 6 - Ground Water Investigations	(See Data Management Plan for 100-KR-4 Operable Unit)					
Task 7 - Air Investigations						
Subtask 7a - Data Compilation	Technical memos	1				
	Historic reports	5				
Subtask 7b - Field Activities	Aerial photographs	1				
	Log books	1				
	Magnetic media and supporting documentation	1				
	QA/QC	1				
Subtask 7c - Laboratory Analysis	Validated sample analysis	31				
	QA/QC	31				
Subtask 7d - Data Evaluation	Log books	1				
	QA/QC	1				
Task 8 - Ecological Investigations						
Subtask 8a - Data Compilation	Technical memos	1				
Subtask 8b - Field Activities	Aerial photographs	10				
	Log books	1				
	Magnetic media and supporting documentation	1				
	Chart recordings					
	Chain of custody	5				
	QA/QC	5	TBD	TBD	TBD	TBD
Subtask 8c - Laboratory Analysis	Validated sample analysis					
	QA/QC					

Table DMP-3. Site Characterization - Estimated Data Quantity

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 8d - Data Evaluation	Log books QA/QC	1 1				
Task 9 - Cultural Resource Investigations	Hanford Plan	1				
Task 10 - Data Evaluations	Technical memos	1				
Task 11 - Baseline Risk Assessment	Technical memos Computer models Magnetic media and supporting documentation	1 4 4				
Task 12 - Report						
Subtask 12a - Prepare	Report	1				
Subtask 12b - Review/Approval	Approval	1				

FS PHASE I/II REMEDIAL ALTERNATIVES DEVELOPMENT

Task 1 - Project Management (Addressed in Project Management Plan)						
Task 2 - Alternatives Development						
Subtask 2a - Develop Objectives	Technical memos	1				
Subtask 2b - Develop General Response Actions	Technical memos	1				
Subtask 2c - Identify Potential Technologies	Technical memos	1				
Subtask 2d - Evaluate Process Options	Technical memos	3				
Subtask 2e - Assemble Alternatives	Technical memos	1				

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 5

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 2f - Identify/Action-Specific ARARs	Technical memos	1				
Task 3 - Alternatives Screening						
Subtask 3a - Refine Objectives	Technical memos	1				
Subtask 3b - Define Alternatives	Technical memos	1				
Subtask 3c - Screen Alternatives	Technical memos	1				
Subtask 3d - Identify/Action-Specific ARARs	Technical memos	1				
Subtask 3e - Evaluate Data Needs	Technical memos	1				
Task 4 - Report						
Subtask 4a - Prepare	Report	1				
Subtask 4b - Review/Approval	Approval	1				
RI PHASE II OPERABLE UNIT CHARACTERIZATION AND TREATABILITY						
Task 1 - Project Management (Addressed in Project Management Plan)						
Task 2 - Source Investigations						
Subtask 2a - Data Compilation and Review	Technical Memos	1				
Subtask 2b - Field Activities	Technical memos	1				
Subtask 2c - Other	TBD	TBD				
Task 3 - Geologic Investigations						
Subtask 3a - Field Activities	Technical memos	1				
Subtask 3b - Laboratory Analysis	Technical memos	1				

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 6

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 3c - Data Evaluation	Technical memos	1				
Task 4 - Surface Water and Sediments Investigations						
Subtask 4a - Field Activities	Technical memos	1				
Subtask 4b - Laboratory Analysis	Technical memos	1				
Subtask 4c - Data Evaluation	Technical memos	1				
Task 5 - Vadose Zone Investigations						
Subtask 5a - Field Activities	Technical memos	1				
Subtask 5b - Laboratory Analysis	Technical memos	1				
Subtask 5c - Data Evaluation	Technical memos	1				
Task 6 - Ground Water Investigations						
Subtask 6a - Field Activities	Technical memos	1				
Subtask 6b - Laboratory Analysis	Technical memos	1				
Subtask 6c - Data Evaluation	Technical memos	1				
Task 7 - Air Investigations						
Subtask 7a - Field Activities	Technical memos	1				
Subtask 7b - Laboratory Analysis	Technical memos	1				
Subtask 7c - Data Evaluation	Technical memos	1				
Task 8 - Ecological Investigations						
Subtask 8a - Field Activities	Technical memos	1				
Subtask 8b - Laboratory Analysis	Technical memos	1				

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 7

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 8c - Data Evaluation	Technical memos	1				
Task 9 - Treatability Work Plan Development	Work Plan	Unknown				
Task 10 - Treatability Work Plan Implementation	Pilot and test data/ Log books Sample analysis Magnetic media Technical memos	Unknown				
Task 11 - Cultural Resource Investigations	Plan	1				
Task 12 - Data Evaluation	Log books QA/QC	1				
Task 13 - Baseline Risk Assessment	Technical memos	1				
Task 14 Report						
Subtask 14a - Prepare	Report	1				
Subtask 14b - Review/Approve	Report	1				
FS PHASE III REMEDIAL ALTERNATIVES ANALYSIS						
Task 1 - Define Alternatives	Technical memos	1				
Task 2 - Alternative Analysis	Technical memos	1				
Task 3 - Compare Alternatives	Technical memos	1				
Task 4 - Report						
Subtask 4a - Prepare	Report	1				

Table DMP-3. Site Characterization - Estimated Data Quantity

Page 8

Work Plan Task	Data Type	Estimated No. of Documents/ Articles	Estimated No. of Sample Locations	Estimated Total No. of Samples	Estimated No. of Analyses/ Per Sample	Estimated Total No. of Data Points
Subtask 4b - Review/Approve	Report	1				
Task 5 - Corrective Action Plan	Plan	1				
NEPA						
Task 1 - Analyze	Technical memos	1				
Task 2 - Prepare	Report	1				
Task 3 - Review/Approve	Report	1				
CLOSURE PERMITS						
Task 1 - Prepare	Report	1				
Task 2 Review/Approve	Report	1				
INTERIM REMEDIAL ACTIONS	Technical memos To be determined	TBD				

[a] EDMC - Environmental data management center
[b] OSM - Office of sample management

H:\1842\TABLES\KR1\DMP\179

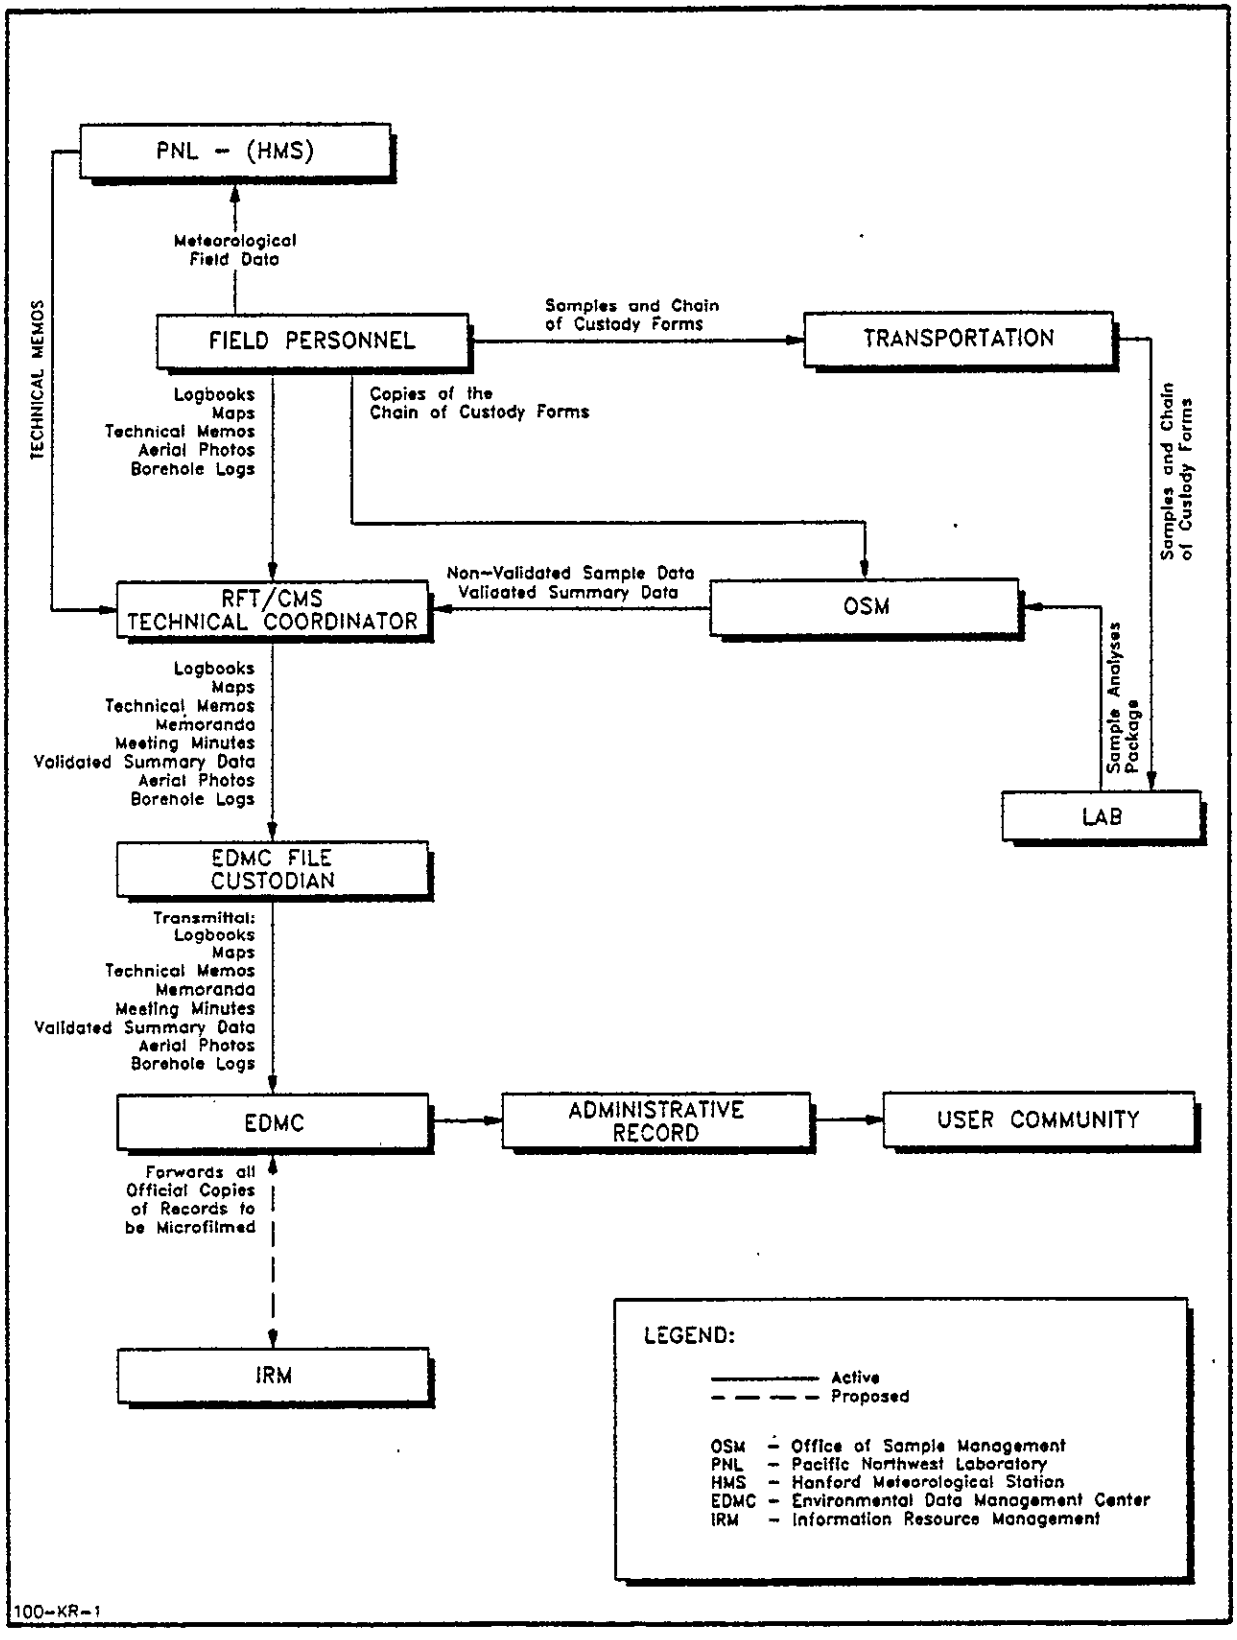

Figure DMP-1. General Data Management Plan for 100-KR-1 Work Plan Task Data.

3.2.2 Office of Sample Management

The Westinghouse Hanford Office of Sample Management (OSM) will validate all data packages received from the laboratory. Validated summary data will be forwarded to the Technical Lead for use and submittal to the EDMC. Nonvalidated or preliminary data will be forwarded to the Technical Lead upon request. Preliminary data will be clearly labeled as such. The OSM will maintain raw sample data, QA/QC laboratory data and the archived sample index.

3.2.3 Environmental Data Management Center

The EDMC is the Westinghouse Hanford Environmental Division's central facility and service that provides a file management system for processing environmental information. The EDMC manages and controls the Administrative Record Public Access Room. Data transmittal to the EDMC is governed by the following procedures:

- EII 1.6, "Records Management" (WHC 1989)
- TPA-AP-06-R0, Predecisional Draft, "Clearance and Release of Administrative Record Documentation" (DOE/RL et al. 1990b)
- TPA-AP-07-R0, Predecisional Draft, "Information Transmittals and Receipt Control" (DOE-RL et al. 1990b)
- TPA-AP-10-R0, "Administrative Record Management" (DOE-RL et al. 1990c)
- WHC-EP-0219, *Environmental Information Management Plan* (Steward 1989).

Procedures addressing record control before transmittal to EDMC will be developed in fiscal year 1990.

3.2.4 Information Resource Management

The Information Resource Management (IRM) is the designated records custodian (permanent storage) for Westinghouse Hanford. The procedural link between the EDMC and the IRM is being developed.

3.2.5 Hanford Environmental Health Foundation

The Hanford Environmental Health Foundation (HEHF) performs the analyses on the nonradiological health and exposure data and forwards summary reports to the Fire and Protection Group and the Environmental Health and Pesticide Services Section (EHPSS) within the Westinghouse Hanford Environmental Division. Nonradiological and health exposure data are maintained also for other site contractors (Pacific Northwest Laboratory [PNL] and Kaiser Engineers Hanford [KEH]) associated with 100-KR-1 activities. The HEHF provides summary data to the appropriate site contractor. The preparation of health and safety plans is addressed in EII 2.1 and occupational health monitoring is covered in EII 2.2. Data management procedures are currently under development.

3.2.6 Environmental Health and Pesticide Services Section

The Westinghouse Hanford EHPSS maintains personal protection equipment fitting records as well as nonradiological health and exposure summary reports provided by HEHF for Westinghouse Hanford Environmental Division and subcontractor personnel.

3.2.7 Technical Training Support Section

The Westinghouse Hanford Technical Training Support Section provides instructions on development of training programs, and maintains training records.

3.2.8 Pacific Northwest Laboratory

The PNL operates the Hanford Meteorological Station (HMS) that collects and maintains meteorological data. Additionally, PNL collects and maintains radiation exposure data. Data management is discussed in the *Hanford Meteorological Data Collection System and Data Base* (Andrews 1988).

3.3 DATABASES

This section addresses databases that will receive data generated from 100-KR-1 activities.

3.3.1 Meteorological Data

The HMS, controlled by PNL, collects and maintains meteorological data. This database contains meteorological data dating from 1943 to present. The *Hanford Meteorological Data Collection System and Data Base* (Andrews 1988) is the document that explains meteorological data management.

3.3.2 Nonradiological Exposure and Medical Records

The HEHF collects and maintains data for all nonradiological exposure records and medical records.

3.3.3 Radiological Exposure Records

The PNL collects and maintains data on occupational radiation exposure. This database contains respiratory personnel protection equipment fitting records, work restrictions, and radiation exposure information.

3.3.4 Training Records

Training records for Westinghouse Hanford and subcontractor personnel are managed by the Westinghouse Hanford Technical Training Support Section. Other Hanford Site contractors (PNL and KEH) maintain their own personnel training records.

3.3.5 Environmental Information/ Administrative Record

Westinghouse Hanford EDMC personnel manage environmental information and the administrative record. The administrative record provides an index and key information on all data transmitted to the EDMC. This database is used to assist in data retrieval and to produce index lists as required.

3.3.6 Sample Status Tracking

The OSM maintains the sample status tracking database. This database contains information about each sample. Information maintained includes sample number, ship data, receipt data, and laboratory identification.

4.0 ENVIRONMENTAL INFORMATION MANAGEMENT PLAN

The EIMP (Steward 1989) was issued in March 1989 and is currently under review. The EIMP is expected to be revised and expanded in fiscal year 1990. The first part of the EIMP provides an overview of the Westinghouse Hanford Environmental Division's working files management system and addresses the management of information transmitted to the EDMC, the Environmental Division's designated file manager, in support of Environmental Restoration Program activities. An overview is presented of the EDMC's location, operating mechanics, field file support services, automated support services, and the composition and compilation of an agency-required administrative record.

The second part of the EIMP addresses future plans for management of scientific and technical data. The planning and control activities affecting data are

discussed. These activities include data collection, analysis, integration, transfer, storage, retrieval, and presentation.

5.0 HANFORD ENVIRONMENTAL INFORMATION SYSTEM

5.1 OBJECTIVE

The HEIS is being developed by PNL for Westinghouse Hanford as a primary resource for computerized storage, retrieval, and analysis of quality-assured technical data associated with CERCLA RI/FS activities and Resource Conservation and Recovery Act of 1976 (RCRA) facility investigation/corrective measure study (RFI/CMS) activities being undertaken at the Hanford Site. The HEIS will provide a means of interactive access to data sets. Implementation of HEIS will serve to facilitate data consistency, quality, traceability, and security within a single controlled database. The HEIS is expected to be operational by September 1990.

The following is a list of data subjects proposed to be entered into HEIS:

- Geologic
- Geophysics
- Atmospheric
- Biotic
- Site Characterization
- Soil Gas
- Waste Site Information
- Surface Monitoring
- Ground Water.

Existing databases that are proposed to be incorporated, in whole or in part, within HEIS include the Waste Information Data System (WIDS), and the Hanford Groundwater Database.

Considerable resources are being devoted to completing development and implementing HEIS in fiscal year 1990. The HEIS is accompanied by a detailed operator and procedure manual that is being prepared by PNL for Westinghouse Hanford.

5.2 INTEGRATION OF 100-KR-1 DATA INTO HEIS

All data collected before the implementation of HEIS will be handled and stored according to the DMP described in Chapter 3.0. Figure DMP-2 outlines the general data management for data collected after implementation of HEIS. Data collected prior to implementing HEIS will be entered eventually into HEIS as time and resources allow.

6.0 REFERENCES

Andrews, G. L., 1988, *Hanford Meteorological Data Collection System and Data Base*, PNL-6509, Pacific Northwest Laboratory, Richland, Washington.

DOE-RL, EPA, and Ecology, 1990a Predecisional draft, *Clearance and Release of Administrative Record Documentation*, TPA-AP-06-R0, U.S. Department of Energy-Richland Operations Office, U.S. Environmental Protection Agency, and Washington State Department of Ecology, Richland, Washington.

DOE-RL, EPA, and Ecology, 1990b Predecisional draft, *Information Transmittals and Receipt Control*, TPA-AP-07-R0, U.S. Department of Energy-Richland Operations Office, U.S. Environmental Protection Agency, and Washington State Department of Ecology, Richland, Washington.

DOE-RL, EPA, and Ecology, 1990c Predecisional draft, *Administrative Record Management*, TPA-AP-10-R0, U.S. Department of Energy-Richland Operations Office, U.S. Environmental Protection Agency, and Washington State Department of Ecology, Richland, Washington.

Steward, J. C., 1989, *Environmental Information Management Plan*, WHC-EP-0219, Westinghouse Hanford Company, Richland, Washington.

WHC, 1989, *Environmental Investigations and Site Characterizations Manual*, WHC-CM-7-7, Westinghouse Hanford Company, Richland, Washington.

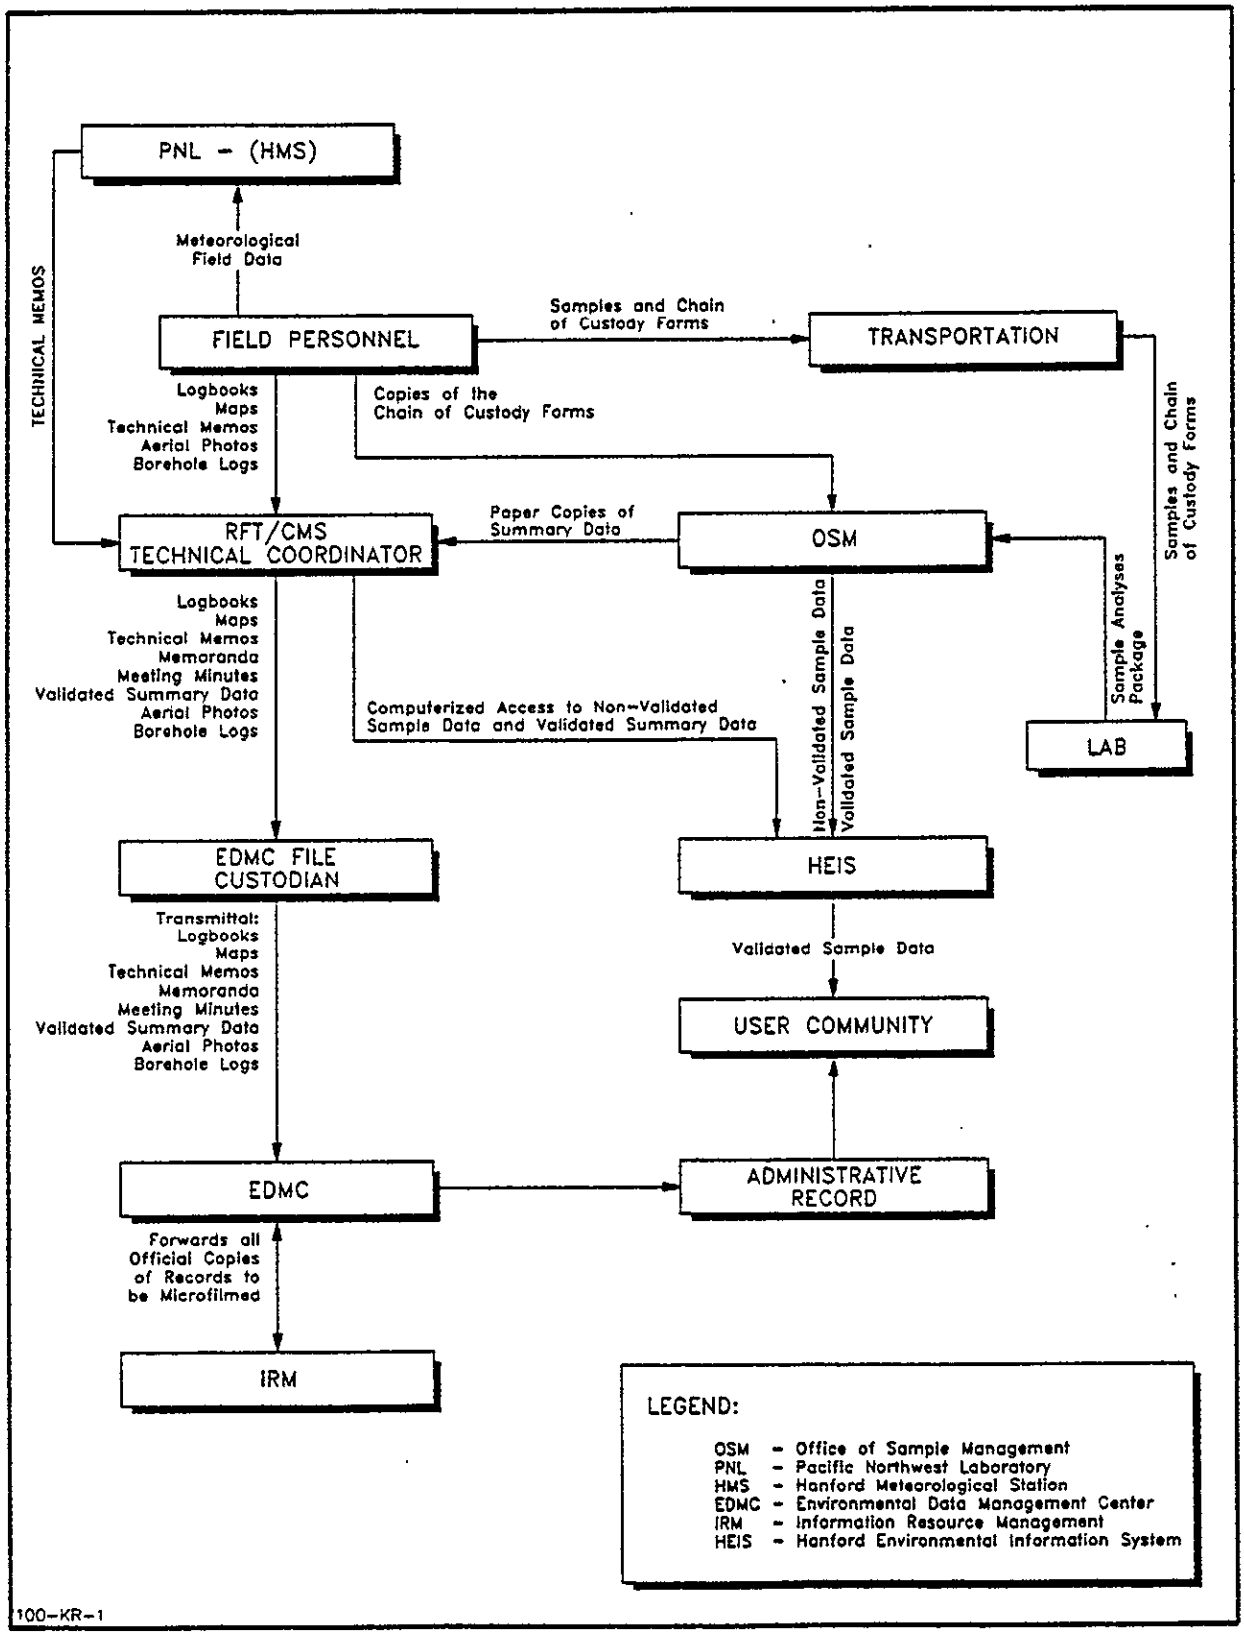

Figure DMP-2. General Data Management Plan for 100-K-1 Work Plan Task Data After Implementation of HEIS.

9 0 1 1 3 3 0 4 4 3

THIS PAGE INTENTIONALLY
LEFT BLANK

Attachment 5

COMMUNITY RELATIONS PLAN

9011830449

THIS PAGE INTENTIONALLY
LEFT BLANK

1.0 INTRODUCTION

A community relations plan (CRP) has been developed for the Hanford Site Environmental Restoration Program. Because community relations activities are so interrelated among operable units, a decision was made to develop a single CRP that will have the capability to address specific individual concerns associated with each operable unit, but will still provide continuity and general coordination of all the Environmental Restoration Program activities with regard to community involvement. The site-wide CRP discusses Hanford Site background information, history of community involvement at the Hanford Site, and community concerns regarding the Hanford Site. It also delineates the community relations program that the U.S. Department of Energy-Richland Operations Office, the U.S. Environmental Protection Agency-Region 10 Office, and the Washington Department of Ecology will cooperatively implement throughout the cleanup of all the operable units at the Hanford Site. All community relations activities associated with the 100-KR-1 operable unit work plan will be conducted under this overall Hanford Site CRP.

9 0 1 1 0 3 5 0 4 5 0

THIS PAGE INTENTIONALLY
LEFT BLANK
